

# EMERYSTATION 2

1010	Drive Piles	1d	0	05NOV99 A	10JAN00 A	47d	0
1000	Notice to Proceed	1d	0	08NOV99 A	06MAR00	85d	0
1120	Building Permit Foundation	1d	1d	06MAR00	06MAR00	0	0

## AREA 1A

1110	Suvery & Stake Site	1d	0	05NOV99 A	08NOV99 A	2d	0
1090	Structural Steel Submittals	10d	3d	07DEC99 A	08MAR00	64d	0
1020	Rebar Submittals Foundation	10d	0	01FEB00 A	07FEB00 A	5d	0
2070	Schedule Soil testing	2d	1d	02MAR00 A	06MAR00	2d	0
2050	Soil Contaminants Testing	5d	5d	08MAR00 A	13MAR00	0	0
2030	Hazmat Certified / Plan By Owner <i>HAS PLAN</i>	5d	5d	14MAR00	20MAR00	0	0
1730	Notice to begin Foundation	1d	1d	20MAR00	20MAR00	0	0
1130	Mobilize Foundation Crew	1d	1d	21MAR00	21MAR00	0	0
1580	Demo A.C	3d	3d	21MAR00	23MAR00	0	0
2420	Pot Hole Subgrade for Contaminations	2d	2d	21MAR00	22MAR00	0	0
3570	Stockpile Spoils for Test Results	2d	2d	23MAR00	24MAR00	0	0
3650	Off Haul Spoils from Subgrade	2d	2d	27MAR00	28MAR00	0	0
1140	Layout Pile Caps & GB Area 1A	3d	3d	29MAR00	31MAR00	0	0
3710	Cut Subgrade	3d	3d	29MAR00	31MAR00	0	0
2160	Demo As Required Existing Foundation	3d	3d	31MAR00	04APR00	0	0
1170	Excavate Pile Caps & GB Area 1A	5d	5d	04APR00	10APR00	0	0
1200	Place Pile Dowels Area 1A	2d	2d	07APR00	10APR00	0	0

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 1A  
 © Primavera Systems, Inc.

**WBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- Early start point
- Early finish point
- Target start point
- Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

# EMERYSTATION 2

1230	Resteel Pile Caps & GB Area 1A	6d	6d	07APR00	14APR00	0
1030	Plumbing Submittals Foundation	10d	10d	10APR00	21APR00	0
1040	Electrical Submittals Foundation	10d	10d	10APR00	21APR00	0
1080	Fire Sprinkler Submittals Foundation	10d	10d	10APR00	21APR00	0
1100	Concrete Mix Design Foundation	10d	10d	10APR00	21APR00	0
3450	Pull Test Pile Dowels	1d	1d	12APR00	12APR00	0
1260	Form Pile Caps Area 1A	4d	4d	13APR00	18APR00	0
1290	Set Bolts Area 1A	4d	4d	17APR00	20APR00	0
1320	Survey Bolts Area 1A	1d	1d	20APR00	20APR00	0
1350	POUR PILE CAPS COMPLETE AREA 1A	1d	1d	21APR00	21APR00	0
1355	POUR GB where possible (no Drag Steel at	1d	1d	21APR00	21APR00	0
1380	Clean up Subgrade Area 1A	1d	1d	24APR00	24APR00	0
1780	Weld Rebar to Base Plates Area 1A	5d	5d	09MAY00	15MAY00	0
1500	Complete Grade Beams / To Col. Drag Steel	2d	2d	16MAY00	17MAY00	0

## AREA 1B

1160	Layout Pile Caps & GB Area 1B	3d	3d	24MAR00	28MAR00	0
2080	Demo As Required Existing Foundation	2d	2d	29MAR00	30MAR00	0
1180	Excavate Pile Caps & GB Area 1B	5d	5d	31MAR00	06APR00	0
1210	Place Pile Dowels Area 1B	2d	2d	05APR00	06APR00	0
1240	Resteel Pile Caps & G.B Area 1B	6d	6d	07APR00	14APR00	0
3460	Pull Test Pile Dowels	1d	1d	10APR00	10APR00	0
1270	Form Pile Caps Area 1B	4d	4d	14APR00	19APR00	0
1300	Set Bolts Area 1B	4d	4d	18APR00	21APR00	0

- ▼ Resteel Pile Caps & GB Area 1A
- ▼ Plumbing Submittals Foundation
- ▼ Electrical Submittals Foundation
- ▼ Fire Sprinkler Submittals Foundation
- ▼ Concrete Mix Design Foundation
- ▼ Pull Test Pile Dowels
- ▼ Form Pile Caps Area 1A
- ▼ Set Bolts Area 1A
- ▼ Survey Bolts Area 1A
- ▼ POUR PILE CAPS COMPLETE AREA 1A
- ▼ POUR GB where possible (no Drag Steel at Col)
- ▼ Clean up Subgrade Area 1A
- ▼ Weld Rebar to Base Plates Area 1A
- ▼ Complete Grade Beams / To Col. Drag Steel

- ▼ Layout Pile Caps & GB Area 1B
- ▼ Demo As Required Existing Foundation
- ▼ Excavate Pile Caps & GB Area 1B
- ▼ Place Pile Dowels Area 1B
- ▼ Resteel Pile Caps & G.B Area 1B
- ▼ Pull Test Pile Dowels
- ▼ Form Pile Caps Area 1B
- ▼ Set Bolts Area 1B

**Start date** 08NOV99  
**Finish date** 08MAR01  
**Data date** 06MAR00  
**Run date** 14MAR00  
**Page number** 2A  
 © Primavera Systems, Inc.

**WBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

# EMERYSTATION 2

1330	Survey Bolts Area 1B	1d	1d	21APR00	21APR00	0	▽ Survey Bolts Area 1B
1360	POUR PILE CAPS COMPLETE AREA 1B	1d	1d	24APR00	24APR00	0	▽ POUR PILE CAPS COMPLETE AREA 1B
2020	POUR GB where possible ( no Drag Steel at	1d	1d	24APR00	24APR00	0	▽ POUR GB where possible ( no Drag Steel at Col)
1390	Clean up Subgrade Area 1B	1d	1d	25APR00	25APR00	0	▽ Clean up Subgrade Area 1B
1790	Weld Rebar to Base Plates Area 1B	5d	5d	12MAY00	18MAY00	0	▽ Weld Rebar to Base Plates Area 1B
2010	Complete Grade Beams / To Col. Drag Steel	2d	2d	19MAY00	22MAY00	0	▽ Complete Grade Beams / To Col. Drag Steel
<b>AREA 2</b>							
1150	Layout Pile Caps & GB Area 2	3d	3d	03APR00	05APR00	0	▽ Layout Pile Caps & GB Area 2
2240	Demo As Required Existing Foundation	3d	3d	05APR00	07APR00	0	▽ Demo As Required Existing Foundation
1190	Excavate Pile Caps & GB Area 2	6d	6d	07APR00	14APR00	0	▽ Excavate Pile Caps & GB Area 2
1220	Place Pile Dowels Area 2	3d	3d	12APR00	14APR00	0	▽ Place Pile Dowels Area 2
1250	Resteeel Pile Caps & G.B Area 2	7d	7d	13APR00	21APR00	0	▽ Resteeel Pile Caps & G.B Area 2
1280	Form Pile Caps Area 2	4d	4d	18APR00	21APR00	0	▽ Form Pile Caps Area 2
3490	Pull Test Pile Dowels	1d	1d	18APR00	18APR00	0	▽ Pull Test Pile Dowels
1310	Set Bolts Area 2	4d	4d	20APR00	25APR00	0	▽ Set Bolts Area 2
1340	Survey Bolts Area 2	1d	1d	25APR00	25APR00	0	▽ Survey Bolts Area 2
1370	POUR PILE CAPS COMPLETE AREA 1B	1d	1d	26APR00	26APR00	0	▽ POUR PILE CAPS COMPLETE AREA 1B
1420	POUR GB where possible (no Drag Steel at	1d	1d	26APR00	26APR00	0	▽ POUR GB where possible (no Drag Steel at Col)
1400	Clean up Subgrade Area 1B	2d	2d	27APR00	28APR00	0	▽ Clean up Subgrade Area 1B
3170	Weld Rebar to Base Plates Area 2	5d	5d	05JUN00	09JUN00	0	▽ Weld Rebar to Base Plates Area 2
2040	Complete Grade Beams / To Col. Drag Steel	2d	2d	12JUN00	13JUN00	0	▽ Complete Grade Beams / To Col. Drag Steel
<b>AREA 1A</b>							
1410	SME Mobilize / Erect Crane	3d	3d	01MAY00	03MAY00	0	▽ SME Mobilize / Erect Crane

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 3A  
 © Primavera Systems, Inc.

**WBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<div style="font-size: 8px;">                     ▬ Early bar                      ▽ Early start point                      ▽ Early finish point                      ◆ Target start point                      ◆ Target finish point                      ▬ Target bar                      ▬ Progress bar                      ▬ Critical bar                      ▬ Summary bar                      ◆ Start milestone point                      ◆ Finish milestone point                 </div>

# EMERYSTATION 2

1430	SME ERECT AREA 1A 2ND FLR	2d	2d	04MAY00	05MAY00	0	▽ SME ERECT AREA 1A 2ND FLR
1440	SME ERECT AREA 1A 3RD FLR	1d	1d	08MAY00	08MAY00	0	▽ SME ERECT AREA 1A 3RD FLR
2250	Spread Deck 2nd flr	1d	1d	08MAY00	08MAY00	0	▽ Spread Deck 2nd flr
1660	Deck Area 1A Complete 2nd flr	3d	3d	09MAY00	11MAY00	0	▽ Deck Area 1A Complete 2nd flr
2260	Weld Connections 2nd flr	1d	1d	09MAY00	09MAY00	0	▽ Weld Connections 2nd flr
2270	Spread Metal Deck 3rd flr	1d	1d	09MAY00	09MAY00	0	▽ Spread Metal Deck 3rd flr
5810	Pour Manlift Pad Area 1A	1d	1d	09MAY00	09MAY00	0	▽ Pour Manlift Pad Area 1A
6050	Erect Stair Tower Area 1A	1d	1d	09MAY00	09MAY00	0	▽ Erect Stair Tower Area 1A
2280	Weld Splice Connections 3rd flr	2d	2d	10MAY00	11MAY00	0	▽ Weld Splice Connections 3rd flr
1670	Deck Area 1A Complete 3rd flr	3d	3d	11MAY00	15MAY00	0	▽ Deck Area 1A Complete 3rd flr
1450	SME ERECT AREA 1A 4TH FLR	2d	2d	12MAY00	15MAY00	0	▽ SME ERECT AREA 1A 4TH FLR
1460	SME ERECT AREA 1A 5TH FLR	1d	1d	16MAY00	16MAY00	0	▽ SME ERECT AREA 1A 5TH FLR
2350	Spread Metal Deck 4th flr	1d	1d	16MAY00	16MAY00	0	▽ Spread Metal Deck 4th flr
6040	Erect Manlift Area 1A	1d	1d	16MAY00	16MAY00	0	▽ Erect Manlift Area 1A
1680	Deck Area 1A Complete 4th flr	3d	3d	17MAY00	19MAY00	0	▽ Deck Area 1A Complete 4th flr
2430	Weld Connections 4th flr	1d	1d	17MAY00	17MAY00	0	▽ Weld Connections 4th flr
2440	Spread Metal Deck 5th flr	1d	1d	17MAY00	17MAY00	0	▽ Spread Metal Deck 5th flr
2450	Weld Splice Connections 5th flr	2d	2d	18MAY00	19MAY00	0	▽ Weld Splice Connections 5th flr
1690	Deck Area 1A Complete 5th flr	3d	3d	19MAY00	23MAY00	0	▽ Deck Area 1A Complete 5th flr
1470	SME ERECT AREA 1A 6TH FLR	2d	2d	22MAY00	23MAY00	0	▽ SME ERECT AREA 1A 6TH FLR
1480	SME ERECT AREA 1A ROOF	1d	1d	24MAY00	24MAY00	0	▽ SME ERECT AREA 1A ROOF
1570	Spread Metal Deck 6th flr	1d	1d	24MAY00	24MAY00	0	▽ Spread Metal Deck 6th flr
1490	SME ERECT AREA 1A PENTHOUSE	1d	1d	25MAY00	25MAY00	0	▽ SME ERECT AREA 1A PENTHOUSE

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	4A
© Primavera Systems, Inc.	

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

## EMERYSTATION 2

1700	Deck Area 1A Complete 6th flr	3d	3d	25MAY00	29MAY00	0	∇ Deck Area 1A Complete 6th flr
2460	Weld Connections 6th flr	1d	1d	25MAY00	25MAY00	0	∇ Weld Connections 6th flr
2470	Spread Metal Deck Roof	1d	1d	25MAY00	25MAY00	0	∇ Spread Metal Deck Roof
1710	Deck Area 1A Complete Roof	3d	3d	26MAY00	30MAY00	0	∇ Deck Area 1A Complete Roof
2490	Weld Connections Roof	1d	1d	26MAY00	26MAY00	0	∇ Weld Connections Roof
2640	Weld connections Penthouse	1d	1d	26MAY00	26MAY00	0	∇ Weld connections Penthouse
1720	Deck Area 1A Complete Penthouse	1d	1d	29MAY00	29MAY00	0	∇ Deck Area 1A Complete Penthouse
<b>AREA 1B</b>							
1510	SME ERECT AREA 1B 2ND FLR	2d	2d	09MAY00	10MAY00	0	∇ SME ERECT AREA 1B 2ND FLR
1520	SME ERECT AREA 1B 3RD FLR	1d	1d	11MAY00	11MAY00	0	∇ SME ERECT AREA 1B 3RD FLR
2480	Spread Deck 2nd flr	1d	1d	11MAY00	11MAY00	0	∇ Spread Deck 2nd flr
2650	Weld Connections 2nd flr	1d	1d	12MAY00	12MAY00	0	∇ Weld Connections 2nd flr
2660	Deck Area 1B Complete 2nd flr	3d	3d	12MAY00	16MAY00	0	∇ Deck Area 1B Complete 2nd flr
2670	Spread Metal Deck 3rd flr	1d	1d	12MAY00	12MAY00	0	∇ Spread Metal Deck 3rd flr
1530	SME ERECT AREA 1B 4TH FLR	2d	2d	17MAY00	18MAY00	0	∇ SME ERECT AREA 1B 4TH FLR
1540	SME ERECT AREA 1B 5TH FLR	1d	1d	19MAY00	19MAY00	0	∇ SME ERECT AREA 1B 5TH FLR
2060	Relocate Stair Tower Area 1B	1d	1d	19MAY00	19MAY00	0	∇ Relocate Stair Tower Area 1B
2680	Weld Splice Connections 3rd flr	2d	2d	19MAY00	22MAY00	0	∇ Weld Splice Connections 3rd flr
2690	Deck Area 1B Complete 3rd flr	3d	3d	19MAY00	23MAY00	0	∇ Deck Area 1B Complete 3rd flr
2700	Spread Metal Deck 4th flr	1d	1d	19MAY00	19MAY00	0	∇ Spread Metal Deck 4th flr
2850	Weld Connections 4th flr	1d	1d	22MAY00	22MAY00	0	∇ Weld Connections 4th flr
2860	Deck Area 1B Complete 4th flr	3d	3d	22MAY00	24MAY00	0	∇ Deck Area 1B Complete 4th flr
2870	Spread Metal Deck 5th flr	1d	1d	22MAY00	22MAY00	0	∇ Spread Metal Deck 5th flr

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 5A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<ul style="list-style-type: none"> <li>■ Early bar</li> <li>∇ Early start point</li> <li>∇ Early finish point</li> <li>◆ Target start point</li> <li>◆ Target finish point</li> <li>■ Target bar</li> <li>■ Progress bar</li> <li>■ Critical bar</li> <li>■ Summary bar</li> <li>◆ Start milestone point</li> <li>◆ Finish milestone point</li> </ul>

# EMERYSTATION 2

1550	SME ERECT AREA 1B 6TH FLR	2d	2d	26MAY00	29MAY00	0	▽ SME ERECT AREA 1B 6TH FLR
1560	SME ERECT AREA 1B ROOF	1d	1d	30MAY00	30MAY00	0	▽ SME ERECT AREA 1B ROOF
2880	Weld Splice Connections 5th flr	2d	2d	30MAY00	31MAY00	0	▽ Weld Splice Connections 5th flr
2890	Deck Area 1B Complete 5th flr	3d	3d	30MAY00	01JUN00	0	▽ Deck Area 1B Complete 5th flr
2900	Spread Metal Deck 6th flr	1d	1d	30MAY00	30MAY00	0	▽ Spread Metal Deck 6th flr
2910	Weld Connections 6th flr	1d	1d	31MAY00	31MAY00	0	▽ Weld Connections 6th flr
3050	Deck Area 1B Complete 6th flr	3d	3d	31MAY00	02JUN00	0	▽ Deck Area 1B Complete 6th flr
3060	Spread Metal Deck Roof	1d	1d	31MAY00	31MAY00	0	▽ Spread Metal Deck Roof
3070	Weld Connections Roof	2d	2d	01JUN00	02JUN00	0	▽ Weld Connections Roof
3080	Deck Area 1B Complete Roof	3d	3d	01JUN00	05JUN00	0	▽ Deck Area 1B Complete Roof
<b>AREA 2</b>							
1590	SME ERECT AREA 2 2ND FLR	2d	2d	31MAY00	01JUN00	0	▽ SME ERECT AREA 2 2ND FLR
1600	SME ERECT AREA 2 3RD FLR	1d	1d	02JUN00	02JUN00	0	▽ SME ERECT AREA 2 3RD FLR
1800	Spread Deck 2nd flr	1d	1d	02JUN00	02JUN00	0	▽ Spread Deck 2nd flr
1610	SME ERECT AREA 2 4TH FLR	2d	2d	05JUN00	06JUN00	0	▽ SME ERECT AREA 2 4TH FLR
1810	Weld Connections 2nd flr	1d	1d	05JUN00	05JUN00	0	▽ Weld Connections 2nd flr
1820	Deck Area 2 Complete 2nd flr	3d	3d	05JUN00	07JUN00	0	▽ Deck Area 2 Complete 2nd flr
1830	Spread Metal Deck 3rd flr	1d	1d	05JUN00	05JUN00	0	▽ Spread Metal Deck 3rd flr
1840	Weld Splice Connections 3rd flr	2d	2d	06JUN00	07JUN00	0	▽ Weld Splice Connections 3rd flr
1850	Deck Area 2 Complete 3rd flr	3d	3d	06JUN00	08JUN00	0	▽ Deck Area 2 Complete 3rd flr
1620	SME ERECT AREA 2 5TH FLR	1d	1d	07JUN00	07JUN00	0	▽ SME ERECT AREA 2 5TH FLR
3090	Spread Metal Deck 4th flr	1d	1d	07JUN00	07JUN00	0	▽ Spread Metal Deck 4th flr
1630	SME ERECT AREA 2 6TH FLR	2d	2d	08JUN00	09JUN00	0	▽ SME ERECT AREA 2 6TH FLR

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	6A
© Primavera Systems, Inc.	

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<ul style="list-style-type: none"> <li>■ Early bar</li> <li>▽ Early start point</li> <li>▽ Early finish point</li> <li>◆ Target start point</li> <li>◆ Target finish point</li> <li>■ Progress bar</li> <li>■ Critical bar</li> <li>■ Summary bar</li> <li>◆ Start milestone point</li> <li>◆ Finish milestone point</li> </ul>

## EMERYSTATION 2

3270	Weld Connections 4th flr	1d	1d	08JUN00	08JUN00	0
3280	Deck Area 2 Complete 4th flr	3d	3d	08JUN00	12JUN00	0
3290	Spread Metal Deck 5th flr	1d	1d	08JUN00	08JUN00	0
1860	Deck Area 2 Complete 5th flr	3d	3d	09JUN00	13JUN00	0
3300	Weld Splice Connections 5th flr	1d	1d	09JUN00	09JUN00	0
1640	SME ERECT AREA 2 ROOF	1d	1d	12JUN00	12JUN00	0
3310	Spread Metal Deck 6th flr	1d	1d	12JUN00	12JUN00	0
1650	SME ERECT AREA 2 PENTHOUSE	1d	1d	13JUN00	13JUN00	0
3320	Weld Connections 6th flr	1d	1d	13JUN00	13JUN00	0
3330	Deck Area 2 Complete 6th flr	3d	3d	13JUN00	15JUN00	0
3350	Spread Metal Deck Roof	1d	1d	13JUN00	13JUN00	0
1740	Deck Area 2 Complete Roof	3d	3d	14JUN00	16JUN00	0
1750	Spread Metal Deck Penthouse	1d	1d	14JUN00	14JUN00	0
1760	Weld Connections Penthouse	2d	2d	14JUN00	15JUN00	0
3360	Weld Connections 6th flr	1d	1d	14JUN00	14JUN00	0
1770	Metal Deck Complete Penthouse	1d	1d	15JUN00	15JUN00	0

▽ Weld Connections 4th flr
▽ Deck Area 2 Complete 4th flr
▽ Spread Metal Deck 5th flr
▽ Deck Area 2 Complete 5th flr
▽ Weld Splice Connections 5th flr
▽ SME ERECT AREA 2 ROOF
▽ Spread Metal Deck 6th flr
▽ SME ERECT AREA 2 PENTHOUSE
▽ Weld Connections 6th flr
▽ Deck Area 2 Complete 6th flr
▽ Spread Metal Deck Roof
▽ Deck Area 2 Complete Roof
▽ Spread Metal Deck Penthouse
▽ Weld Connections Penthouse
▽ Weld Connections 6th flr
▽ Metal Deck Complete Penthouse

### AREA 1A

5830	MEPS Underground Work Area 1A	3d	3d	31MAY00	02JUN00	0
5840	Rock/Sand Subgrade Area 1A	1d	1d	05JUN00	05JUN00	0
5850	Edge Form Area 1A	3d	3d	06JUN00	08JUN00	0
5870	Install Embeds Area 1A	2d	2d	08JUN00	09JUN00	0
5860	Resteel S.O.G Area 1A	3d	3d	09JUN00	13JUN00	0
5880	Inspection SOG Area 1A	1d	1d	13JUN00	13JUN00	0

▽ MEPS Underground Work Area 1A
▽ Rock/Sand Subgrade Area 1A
▽ Edge Form Area 1A
▽ Install Embeds Area 1A
▽ Resteel S.O.G Area 1A
▽ Inspection SOG Area 1A

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 7A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- ▬ Target bar
- ▬ Progress bar
- ▬ Critical bar
- ▬ Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

# EMERYSTATION 2

5890	POUR SOG AREA 1A	1d	1d	14JUN00	14JUN00	0		▽ POUR SOG AREA 1A
<b>AREA 1B</b>								
5900	MEPS Underground Work Area 1B	3d	3d	05JUN00	07JUN00	0		▽ MEPS Underground Work Area 1B
5910	Rock/Sand Subgrade Area 1B	1d	1d	08JUN00	08JUN00	0		▽ Rock/Sand Subgrade Area 1B
5920	Edge Form Area 1B	3d	3d	09JUN00	13JUN00	0		▽ Edge Form Area 1B
5940	Install Embeds Area 1B	2d	2d	13JUN00	14JUN00	0		▽ Install Embeds Area 1B
5930	Resteel S.O.G Area 1B	3d	3d	14JUN00	16JUN00	0		▽ Resteel S.O.G Area 1B
5950	Inspection SOG Area 1B	1d	1d	16JUN00	16JUN00	0		▽ Inspection SOG Area 1B
5960	POUR SOG AREA 1B	1d	1d	19JUN00	19JUN00	0		▽ POUR SOG AREA 1B
<b>AREA 2</b>								
5970	MEPS Underground Work Area 2	3d	3d	15JUN00	19JUN00	0		▽ MEPS Underground Work Area 2
5980	Rock/Sand Subgrade Area 2	1d	1d	20JUN00	20JUN00	0		▽ Rock/Sand Subgrade Area 2
5990	Edge Form Area 2	3d	3d	21JUN00	23JUN00	0		▽ Edge Form Area 2
6010	Install Embeds Area 2	2d	2d	23JUN00	26JUN00	0		▽ Install Embeds Area 2
6000	Resteel S.O.G Area 2	3d	3d	26JUN00	28JUN00	0		▽ Resteel S.O.G Area 2
6020	Inspection SOG Area 2	1d	1d	28JUN00	28JUN00	0		▽ Inspection SOG Area 2
6030	POUR SOG AREA 2	1d	1d	29JUN00	29JUN00	0		▽ POUR SOG AREA 2
<b>AREA 1 1ST FLR</b>								
2920	Weld Brace Frames Area 1 1st flr	4d	4d	15JUN00	20JUN00	0		▽ Weld Brace Frames Area 1 1st flr
3380	Resteel S.S Columns Area 1	2d	2d	20JUN00	21JUN00	0		▽ Resteel S.S Columns Area 1
3390	Form Columns Area 1 1st flr	2d	2d	21JUN00	22JUN00	0		▽ Form Columns Area 1 1st flr
3420	Pour Columns Area 1 1st flr	1d	1d	22JUN00	22JUN00	0		▽ Pour Columns Area 1 1st flr
3430	Strip Columns Area 1 1st flr	1d	1d	23JUN00	23JUN00	0		▽ Strip Columns Area 1 1st flr

**Start date** 08NOV99  
**Finish date** 08MAR01  
**Data date** 06MAR00  
**Run date** 14MAR00  
**Page number** 8A  
 © Primavera Systems, Inc.

**WECOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<ul style="list-style-type: none"> <li>■ Early bar</li> <li>▽ Early start point</li> <li>▽ Early finish point</li> <li>◆ Target start point</li> <li>◆ Target finish point</li> <li>■ Progress bar</li> <li>■ Critical bar</li> <li>■ Summary bar</li> <li>◆ Start milestone point</li> <li>◆ Finish milestone point</li> </ul>



# EMERYSTATION 2

3100	Fireproof Steel Area 1 1st flr	4d	4d	26JUN00	29JUN00	0
3810	Electrical Rough in Area 1 1st flr	1d	1d	05JUL00	05JUL00	0
4290	Fire Sprinklers Rough in Area 1 1st flr	3d	3d	05JUL00	07JUL00	0
6120	HVAC Rough in Area 1 1st flr	1d	1d	05JUL00	05JUL00	0
3440	Install CMU Walls Area 1	4d	4d	06JUL00	11JUL00	0
3340	Metal Stud Framing Area 1 1st flr	3d	3d	11JUL00	13JUL00	0
4050	Plumbing Rough in Area 1 1st flr	2d	2d	12JUL00	13JUL00	0
4530	Sheetrock Area 1 1st flr	3d	3d	24OCT00	26OCT00	0
4770	Tape & Texture Area 1 1st flr	5d	5d	27OCT00	02NOV00	0

- ▼ Fireproof Steel Area 1 1st flr
- ▼ Electrical Rough in Area 1 1st flr
- ▼ Fire Sprinklers Rough in Area 1 1st flr
- ▼ HVAC Rough in Area 1 1st flr
- ▼ Install CMU Walls Area 1
- ▼ Metal Stud Framing Area 1 1st flr
- ▼ Plumbing Rough in Area 1 1st flr
- ▼ Sheetrock Area 1 1st flr
- ▼ Tape & Texture Area 1 1st flr

## AREA 1 2ND FLR

1085	Fire Proofing / Safing Submittals Approved	10d	10d	18MAY00	31MAY00	0
2090	Layout & Install MEPS AREA 1 2nd flr	2d	2d	25MAY00	26MAY00	0
2290	Install Embeds Area 1 2nd flr	2d	2d	25MAY00	26MAY00	0
1870	Resteel Deck Area 1 2nd flr	2d	2d	26MAY00	29MAY00	0
2500	Deck Inspection Area 1 2nd flr	1d	1d	29MAY00	29MAY00	0
2710	POUR DECK AREA 1 2ND FLR	1d	1d	30MAY00	30MAY00	0
3250	Precast Pre-Weld	4d	4d	31MAY00	05JUN00	0
2930	Weld Brace Frames Area 1 2nd flr	4d	4d	02JUN00	07JUN00	0
3110	Fireproof Steel Area 1 2nd flr	4d	4d	08JUN00	13JUN00	0
3580	HVAC Rough in Area 1 2nd flr	3d	3d	14JUN00	16JUN00	0
3820	Electrical Rough in Area 1 2nd flr	1d	1d	14JUN00	14JUN00	0
4060	Plumbing Rough in Area 1 2nd flr	1d	1d	14JUN00	14JUN00	0
4300	Fire Sprinklers Rough in Area 1 2nd flr	3d	3d	14JUN00	16JUN00	0

- ▼ Fire Proofing / Safing Submittals Approved
- ▼ Layout & Install MEPS AREA 1 2nd flr
- ▼ Install Embeds Area 1 2nd flr
- ▼ Resteel Deck Area 1 2nd flr
- ▼ Deck Inspection Area 1 2nd flr
- ▼ POUR DECK AREA 1 2ND FLR
- ▼ Precast Pre-Weld
- ▼ Weld Brace Frames Area 1 2nd flr
- ▼ Fireproof Steel Area 1 2nd flr
- ▼ HVAC Rough in Area 1 2nd flr
- ▼ Electrical Rough in Area 1 2nd flr
- ▼ Plumbing Rough in Area 1 2nd flr
- ▼ Fire Sprinklers Rough in Area 1 2nd flr

## AREA 1 3RD FLR

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	9A
© Primavera Systems, Inc.	

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▼ Early start point
- ▼ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start reflection point
- ◆ Finish reflection point

# EMERYSTATION 2

2100	Layout & Install MEPS AREA 1 3rd flr	2d	2d	29MAY00	30MAY00	0	▽ Layout & Install MEPS AREA 1 3rd flr
2300	Install Embeds Area 1 3rd flr	2d	2d	29MAY00	30MAY00	0	▽ Install Embeds Area 1 3rd flr
1880	Resteeel Deck Area 1 3rd flr	2d	2d	30MAY00	31MAY00	0	▽ Resteeel Deck Area 1 3rd flr
2510	Deck Inspection Area 1 3rd flr	1d	1d	31MAY00	31MAY00	0	▽ Deck Inspection Area 1 3rd flr
2720	POUR DECK AREA 1 3RD FLR	1d	1d	01JUN00	01JUN00	0	▽ POUR DECK AREA 1 3RD FLR
3470	Percast Pre-Weld	4d	4d	02JUN00	07JUN00	0	▽ Percast Pre-Weld
2940	Weld Brace Frames Area 1 3rd flr	4d	4d	06JUN00	09JUN00	0	▽ Weld Brace Frames Area 1 3rd flr
3120	Fireproof Steel Area 1 3rd flr	4d	4d	14JUN00	19JUN00	0	▽ Fireproof Steel Area 1 3rd flr
3590	HVAC Rough in Area 1 3rd flr	3d	3d	20JUN00	22JUN00	0	▽ HVAC Rough in Area 1 3rd flr
3830	Electrical Rough in Area 1 3rd flr	1d	1d	20JUN00	20JUN00	0	▽ Electrical Rough in Area 1 3rd flr
4070	Plumbing Rough in Area 1 3rd flr	1d	1d	20JUN00	20JUN00	0	▽ Plumbing Rough in Area 1 3rd flr
4310	Fire Sprinklers Rough in Area 1 3rd flr	3d	3d	20JUN00	22JUN00	0	▽ Fire Sprinklers Rough in Area 1 3rd flr
<b>AREA 1 4TH FLR</b>							
2110	Layout & Install MEPS AREA 1 4th flr	2d	2d	31MAY00	01JUN00	0	▽ Layout & Install MEPS AREA 1 4th flr
2310	Install Embeds Area 1 4th flr	2d	2d	31MAY00	01JUN00	0	▽ Install Embeds Area 1 4th flr
1890	Resteeel Deck Area 1 4th flr	2d	2d	01JUN00	02JUN00	0	▽ Resteeel Deck Area 1 4th flr
2520	Deck Inspection Area 1 4th flr	1d	1d	02JUN00	02JUN00	0	▽ Deck Inspection Area 1 4th flr
2730	POUR DECK AREA 1 4TH FLR	1d	1d	05JUN00	05JUN00	0	▽ POUR DECK AREA 1 4TH FLR
3500	Precast Pre-Weld	4d	4d	06JUN00	09JUN00	0	▽ Precast Pre-Weld
2950	Weld Brace Frames Area 1 4th flr	4d	4d	08JUN00	13JUN00	0	▽ Weld Brace Frames Area 1 4th flr
3130	Fireproof Steel Area 1 4th flr	4d	4d	20JUN00	23JUN00	0	▽ Fireproof Steel Area 1 4th flr
3600	HVAC Rough in Area 1 4th flr	3d	3d	26JUN00	28JUN00	0	▽ HVAC Rough in Area 1 4th flr
3840	Electrical Rough in Area 1 4th flr	1d	1d	26JUN00	26JUN00	0	▽ Electrical Rough in Area 1 4th flr

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 10A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<ul style="list-style-type: none"> <li>■ Early bar</li> <li>▽ Early start point</li> <li>▽ Early finish point</li> <li>◆ Target start point</li> <li>◆ Target finish point</li> <li>■ Target bar</li> <li>■ Progress bar</li> <li>■ Critical bar</li> <li>■ Summary bar</li> <li>◆ Start milestone point</li> <li>◆ Finish milestone point</li> </ul>

# EMERYSTATION 2

4080	Plumbing Rough in Area 1 4th flr	1d	1d	26JUN00	26JUN00	0				▽ Plumbing Rough in Area 1 4th flr
4320	Fire Sprinklers Rough in Area 1 4th flr	1d	1d	26JUN00	26JUN00	0				▽ Fire Sprinklers Rough in Area 1 4th flr
<b>AREA 1 5TH FLR</b>										
2120	Layout & Install MEPS AREA 1 5th flr	2d	2d	02JUN00	05JUN00	0				▽ Layout & Install MEPS AREA 1 5th flr
2320	Install Embeds Area 1 5th flr	2d	2d	02JUN00	05JUN00	0				▽ Install Embeds Area 1 5th flr
1900	Resteel Deck Area 1 5th flr	2d	2d	05JUN00	06JUN00	0				▽ Resteel Deck Area 1 5th flr
2530	Deck Inspection Area 1 5th flr	1d	1d	06JUN00	06JUN00	0				▽ Deck Inspection Area 1 5th flr
2740	POUR DECK AREA 1 5TH FLR	1d	1d	07JUN00	07JUN00	0				▽ POUR DECK AREA 1 5TH FLR
3640	Precast Pre-Weld	4d	4d	08JUN00	13JUN00	0				▽ Precast Pre-Weld
2960	Weld Brace Frames Area 1 5th flr	3d	3d	13JUN00	15JUN00	0				▽ Weld Brace Frames Area 1 5th flr
3140	Fireproof Steel Area 1 5th flr	4d	4d	26JUN00	29JUN00	0				▽ Fireproof Steel Area 1 5th flr
3610	HVAC Rough in Area 1 5th flr	3d	3d	05JUL00	07JUL00	0				▽ HVAC Rough in Area 1 5th flr
3850	Electrical Rough in Area 1 5th flr	1d	1d	05JUL00	05JUL00	0				▽ Electrical Rough in Area 1 5th flr
4090	Plumbing Rough in Area 1 5th flr	1d	1d	05JUL00	05JUL00	0				▽ Plumbing Rough in Area 1 5th flr
4330	Fire Sprinklers Rough in Area 1 5th flr	3d	3d	05JUL00	07JUL00	0				▽ Fire Sprinklers Rough in Area 1 5th flr
<b>AREA 1 6TH FLR</b>										
2130	Layout & Install MEPS AREA 1 6th flr	2d	2d	06JUN00	07JUN00	0				▽ Layout & Install MEPS AREA 1 6th flr
2330	Install Embeds Area 1 6th flr	2d	2d	06JUN00	07JUN00	0				▽ Install Embeds Area 1 6th flr
1910	Resteel Deck Area 1 6th flr	1d	1d	09JUN00	09JUN00	0				▽ Resteel Deck Area 1 6th flr
2540	Deck Inspection Area 1 6th flr	1d	1d	09JUN00	09JUN00	0				▽ Deck Inspection Area 1 6th flr
2750	POUR DECK AREA 1 6TH FLR	1d	1d	12JUN00	12JUN00	0				▽ POUR DECK AREA 1 6TH FLR
3510	Precast Pre-Weld	4d	4d	13JUN00	16JUN00	0				▽ Precast Pre-Weld
2970	Weld Brace Frames Area 1 6th flr	3d	3d	16JUN00	20JUN00	0				▽ Weld Brace Frames Area 1 6th flr
3150	Fireproof Steel Area 1 6th flr	4d	4d	05JUL00	10JUL00	0				▽ Fireproof Steel Area 1 6th flr

**Start date** 08NOV99  
**Finish date** 08MAR01  
**Data date** 06MAR00  
**Run date** 14MAR00  
**Page number** 11A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<div style="font-size: 8px;">           ■ Early bar            ▽ Early start point            ▽ Early finish point            ◆ Target start point            ◆ Target finish point            ■ Target bar            ■ Progress bar            ■ Critical bar            — Summary bar            ◆ Start milestone point            ◆ Finish milestone point         </div>

# EMERYSTATION 2

3620	HVAC Rough in Area 1 6th flr	3d	3d	11JUL00	13JUL00	0			▽ HVAC Rough in Area 1 6th flr
3860	Electrical Rough in Area 1 6th flr	1d	1d	11JUL00	11JUL00	0			▽ Electrical Rough in Area 1 6th flr
4100	Plumbing Rough in Area 1 6th flr	1d	1d	11JUL00	11JUL00	0			▽ Plumbing Rough in Area 1 6th flr
4340	Fire Sprinklers Rough in Area 1 6th flr	3d	3d	11JUL00	13JUL00	0			▽ Fire Sprinklers Rough in Area 1 6th flr
<b>AREA 1 MECH / ROOF</b>									
2140	Layout & Install MEPS AREA 1 Mech. flr	2d	2d	08JUN00	09JUN00	0			▽ Layout & Install MEPS AREA 1 Mech. flr
2340	Install Embeds Area 1 Mech. flr	2d	2d	08JUN00	09JUN00	0			▽ Install Embeds Area 1 Mech. flr
1920	Resteel Deck Area 1 Roof	2d	2d	13JUN00	14JUN00	0			▽ Resteel Deck Area 1 Roof
2550	Deck Inspection Area 1 Mech. flr	1d	1d	14JUN00	14JUN00	0			▽ Deck Inspection Area 1 Mech. flr
2760	POUR DECK AREA 1 MECH. FLR	1d	1d	15JUN00	15JUN00	0			▽ POUR DECK AREA 1 MECH. FLR
3160	Fireproof Steel Area 1 Mech. flr	2d	2d	16JUN00	19JUN00	0			▽ Fireproof Steel Area 1 Mech. flr
3400	Metal Stud Framing Area 1 Mech. Room	2d	2d	20JUN00	21JUN00	0			▽ Metal Stud Framing Area 1 Mech. Room
3630	HVAC Rough in Area 1 Mech. flr	2d	2d	20JUN00	21JUN00	0			▽ HVAC Rough in Area 1 Mech. flr
3870	Electrical Rough in Area 1 Mech. flr	3d	3d	20JUN00	22JUN00	0			▽ Electrical Rough in Area 1 Mech. flr
4110	Plumbing Rough in Area 1 Mech. flr	2d	2d	20JUN00	21JUN00	0			▽ Plumbing Rough in Area 1 Mech. flr
4350	Fire Sprinklers Rough in Area 1 Mech. flr	2d	2d	20JUN00	21JUN00	0			▽ Fire Sprinklers Rough in Area 1 Mech. flr
<b>AREA 1 PENTHOUSE</b>									
2150	Layout & Install MEPS Area 1 Penthouse	2d	2d	12JUN00	13JUN00	0			▽ Layout & Install MEPS Area 1 Penthouse
1930	Resteel Deck Area 1 Penthouse	1d	1d	14JUN00	14JUN00	0			▽ Resteel Deck Area 1 Penthouse
2560	Deck Inspection Area 1 Penthouse	1d	1d	14JUN00	14JUN00	0			▽ Deck Inspection Area 1 Penthouse
2770	POUR DECK AREA 1 PENTHOUSE	1d	1d	15JUN00	15JUN00	0			▽ POUR DECK AREA 1 PENTHOUSE
<b>AREA 2 1ST FLR</b>									
2980	Weld Brace Frames Area 2 1st flr	3d	3d	05JUL00	07JUL00	0			▽ Weld Brace Frames Area 2 1st flr
7200	Resteel S.S Columns Area 2	2d	2d	07JUL00	10JUL00	0			▽ Resteel S.S Columns Area 2

**Start date** 08NOV99  
**Finish date** 08MAR01  
**Data date** 06MAR00  
**Run date** 14MAR00  
**Page number** 12A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<ul style="list-style-type: none"> <li>■ Early bar</li> <li>▽ Early start point</li> <li>▽ Early finish point</li> <li>◆ Target start point</li> <li>◆ Target finish point</li> <li>■ Target bar</li> <li>■ Progress bar</li> <li>■ Critical bar</li> <li>— Standstill bar</li> <li>◆ Start milestone point</li> <li>◆ Finish milestone point</li> </ul>

# EMERYSTATION 2

7210	Fourm Columns Area 2 1st flr	2d	2d	10JUL00	11JUL00	0		
7230	Pour Columns Area 2 1st flr	1d	1d	11JUL00	11JUL00	0	∇ Fourm Columns Area 2 1st flr	
7220	Strip Columns Area 2 1st flr	1d	1d	12JUL00	12JUL00	0	∇ Pour Columns Area 2 1st flr	
3180	Fireproof Steel Area 2 1st flr	4d	4d	13JUL00	18JUL00	0	∇ Strip Columns Area 2 1st flr	
3040	HVAC Rough in Area 2 1st flr	1d	1d	19JUL00	19JUL00	0	∇ Fireproof Steel Area 2 1st flr	
3260	Electrical Rough in Area 2 1st flr	1d	1d	19JUL00	19JUL00	0	∇ HVAC Rough in Area 2 1st flr	
4370	Fire Sprinklers Rough in Area 2 1st flr	3d	3d	19JUL00	21JUL00	0	∇ Electrical Rough in Area 2 1st flr	
3370	Install CMU Walls Area 2 1st flr	4d	4d	20JUL00	25JUL00	0	∇ Fire Sprinklers Rough in Area 2 1st flr	
3410	Metal Stud Framing Area 2 1st flr	3d	3d	26JUL00	28JUL00	0	∇ Install CMU Walls Area 2 1st flr	
4130	Plumbing Rough in Area 2 1st flr	2d	2d	27JUL00	28JUL00	0	∇ Metal Stud Framing Area 2 1st flr	
4610	Sheetrock Area 2 1st flr	3d	3d	27OCT00	31OCT00	0	∇ Plumbing Rough in Area 2 1st flr	
4850	Tape Area 2 1st flr	5d	5d	01NOV00	07NOV00	0	∇ Shetrock Area 2 1st flr	
<b>AREA 2 2ND FLR</b>								
2170	Layout & Install MEPS Area 2 2nd flr	2d	2d	09JUN00	12JUN00	0	∇ Layout & Install MEPS Area 2 2nd flr	
2360	Install Embeds Area 2 2nd flr	1d	1d	09JUN00	09JUN00	0	∇ Install Embeds Area 2 2nd flr	
1940	Resteel Deck Area 2 2nd flr	1d	1d	13JUN00	13JUN00	0	∇ Resteel Deck Area 2 2nd flr	
2570	Deck Inspection Area 2 2nd flr	1d	1d	14JUN00	14JUN00	0	∇ Deck Inspection Area 2 2nd flr	
2780	POUR DECK AREA 2 2ND FLR	1d	1d	14JUN00	14JUN00	0	∇ POUR DECK AREA 2 2ND FLR	
3520	Precast Pre-Weld	4d	4d	15JUN00	20JUN00	0	∇ Precast Pre-Weld	
2990	Weld Brace Frames Area 2 2nd flr	3d	3d	19JUN00	21JUN00	0	∇ Weld Brace Frames Area 2 2nd flr	
3190	Fireproof Steel Area 2 2nd flr	3d	3d	22JUN00	26JUN00	0	∇ Fireproof Steel Area 2 2nd flr	
3660	HVAC Rough in Area 2 2nd flr	2d	2d	27JUN00	28JUN00	0	∇ HVAC Rough in Area 2 2nd flr	
4380	Fire Sprinklers Rough in Area 2 2nd flr	3d	3d	27JUN00	29JUN00	0	∇ Fire Sprinklers Rough in Area 2 2nd flr	
<b>AREA 2 3RD FLR</b>								

**Start date** 08NOV99  
**Finish date** 08MAR01  
**Data date** 06MAR00  
**Run date** 14MAR00  
**Page number** 13A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	■ Early bar ∇ Early start point ∇ Early finish point ◆ Target start point ◆ Target finish point ■ Progress bar ■ Critical bar ■ Summary bar ◆ Start milestone point ◆ Finish milestone point

# EMERYSTATION 2

2370	Install Embeds Area 2 3rd flr	1d	1d	12JUN00	12JUN00	0	
2180	Layout & Install MEPS Area 2 3rd flr	2d	2d	13JUN00	14JUN00	0	▽ Install Embeds Area 2 3rd flr
1950	Resteel Deck Area 2 3rd flr	1d	1d	15JUN00	15JUN00	0	▽ Layout & Install MEPS Area 2 3rd flr
2580	Deck Inspection Area 2 3rd flr	1d	1d	15JUN00	15JUN00	0	▽ Resteel Deck Area 2 3rd flr
2790	POUR DECK AREA 2 3RD FLR	1d	1d	16JUN00	16JUN00	0	▽ Deck Inspection Area 2 3rd flr
3530	Precast Pre-Weld	4d	4d	19JUN00	22JUN00	0	▽ POUR DECK AREA 2 3RD FLR
3000	Weld Brace Frames Area 2 3rd flr	3d	3d	21JUN00	23JUN00	0	▽ Precast Pre-Weld
3200	Fireproof Steel Area 2 3rd flr	3d	3d	26JUN00	28JUN00	0	▽ Weld Brace Frames Area 2 3rd flr
3670	HVAC Rough in Area 2 3rd flr	2d	2d	29JUN00	05JUL00	0	▽ Fireproof Steel Area 2 3rd flr
4390	Fire Sprinklers Rough in Area 2 3rd flr	3d	3d	29JUN00	06JUL00	0	▽ HVAC Rough in Area 2 3rd flr
<b>AREA 2 4TH FLR</b>							
2380	Install Embeds Area 2 4th flr	1d	1d	13JUN00	13JUN00	0	▽ Fire Sprinklers Rough in Area 2 3rd flr
2190	Layout & Install MEPS Area 2 4th flr	2d	2d	15JUN00	16JUN00	0	▽ Install Embeds Area 2 4th flr
1960	Resteel Deck Area 2 4th flr	1d	1d	19JUN00	19JUN00	0	▽ Layout & Install MEPS Area 2 4th flr
2590	Deck Inspection Area 2 4th flr	1d	1d	19JUN00	19JUN00	0	▽ Resteel Deck Area 2 4th flr
2800	POUR DECK AREA 2 4TH FLR	1d	1d	20JUN00	20JUN00	0	▽ Deck Inspection Area 2 4th flr
3540	Precast Pre-Weld	4d	4d	21JUN00	26JUN00	0	▽ POUR DECK AREA 2 4TH FLR
3010	Weld Brace Frames Area 2 4th flr	3d	3d	23JUN00	27JUN00	0	▽ Precast Pre-Weld
3210	Fireproof Steel Area 2 4th flr	3d	3d	28JUN00	05JUL00	0	▽ Weld Brace Frames Area 2 4th flr
3680	HVAC Rough in Area 2 4th flr	3d	3d	06JUL00	10JUL00	0	▽ Fireproof Steel Area 2 4th flr
4400	Fire Sprinklers Rough in Area 2 4th flr	2d	2d	06JUL00	07JUL00	0	▽ HVAC Rough in Area 2 4th flr
<b>AREA 2 5TH FLR</b>							
2390	Install Embeds Area 2 5th flr	1d	1d	14JUN00	14JUN00	0	▽ Fire Sprinklers Rough in Area 2 4th flr
2200	Layout & Install MEPS Area 2 5th flr	2d	2d	19JUN00	20JUN00	0	▽ Install Embeds Area 2 5th flr
▽ Layout & Install MEPS Area 2 5th flr							

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 14A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

# EMERYSTATION 2

1970	Resteel Deck Area 2 5th Flr	1d	1d	21JUN00	21JUN00	0		▽ Resteel Deck Area 2 5th Flr
2600	Deck Inspection Area 2 5th flr	1d	1d	21JUN00	21JUN00	0		▽ Deck Inspection Area 2 5th flr
2810	POUR DECK AREA 2 5TH FLR	1d	1d	22JUN00	22JUN00	0		▽ POUR DECK AREA 2 5TH FLR
3550	Precast Pre-Weld	4d	4d	23JUN00	28JUN00	0		▽ Precast Pre-Weld
3020	Weld Brace Frames Area 2 5th flr	3d	3d	26JUN00	28JUN00	0		▽ Weld Brace Frames Area 2 5th flr
3220	Fireproof Steel Area 2 5th flr	3d	3d	29JUN00	06JUL00	0		▽ Fireproof Steel Area 2 5th flr
3690	HVAC Rough in Area 2 5th flr	3d	3d	07JUL00	11JUL00	0		▽ HVAC Rough in Area 2 5th flr
4410	Fire Sprinklers Rough in Area 2 5th flr	2d	2d	07JUL00	10JUL00	0		▽ Fire Sprinklers Rough in Area 2 5th flr
<b>AREA 2 6TH FLR</b>								
2400	Install Embeds Area 2 6th flr	1d	1d	15JUN00	15JUN00	0		▽ Install Embeds Area 2 6th flr
2210	Layout & Install MEPS Area 2 6th flr	1d	1d	21JUN00	21JUN00	0		▽ Layout & Install MEPS Area 2 6th flr
1980	Resteel Deck Area 2 6th flr	1d	1d	22JUN00	22JUN00	0		▽ Resteel Deck Area 2 6th flr
2610	Deck Inspection Area 2 6th flr	1d	1d	22JUN00	22JUN00	0		▽ Deck Inspection Area 2 6th flr
2820	POUR DECK AREA 2 6TH FLR	1d	1d	23JUN00	23JUN00	0		▽ POUR DECK AREA 2 6TH FLR
3560	Precast Pre-Weld	4d	4d	26JUN00	29JUN00	0		▽ Precast Pre-Weld
3030	Weld Brace Frames Area 2 6th flr	3d	3d	10JUL00	12JUL00	0		▽ Weld Brace Frames Area 2 6th flr
3230	Fireproof Steel Area 2 6th flr	3d	3d	13JUL00	17JUL00	0		▽ Fireproof Steel Area 2 6th flr
3700	HVAC Rough in Area 2 6th flr	3d	3d	18JUL00	20JUL00	0		▽ HVAC Rough in Area 2 6th flr
4420	Fire Sprinklers Rough in Area 2 6th flr	2d	2d	18JUL00	19JUL00	0		▽ Fire Sprinklers Rough in Area 2 6th flr
<b>AREA 2 MECH/ROOF</b>								
2410	Install Embeds Area 2 Mech. flr	1d	1d	16JUN00	16JUN00	0		▽ Install Embeds Area 2 Mech. flr
2220	Layout & Install MEPS Area 2 Mech. flr	3d	3d	22JUN00	26JUN00	0		▽ Layout & Install MEPS Area 2 Mech. flr
1990	Resteel Deck Area 2 Roof	2d	2d	27JUN00	28JUN00	0		▽ Resteel Deck Area 2 Roof
2620	Deck Inspection Area 2 Mech. flr	1d	1d	28JUN00	28JUN00	0		▽ Deck Inspection Area 2 Mech. flr

**Start date** 08NOV99  
**Finish date** 08MAR01  
**Data date** 06MAR00  
**Run date** 14MAR00  
**Page number** 15A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	▽ Early bar ▽ Early start point ◆ Early finish point ◆ Target start point ◆ Target finish point ▽ Target bar ▽ Progress bar ▽ Critical bar ▽ Summary bar ◆ Start milestone point ◆ Finish milestone point

# EMERYSTATION 2

3240	Form Curbs & Pads	3d	3d	29JUN00	06JUL00	0
2830	POUR DECK AREA 2 ROOF	1d	1d	07JUL00	07JUL00	0
3730	Install Lower Main Roofing System Roof	9d	9d	11OCT00	23OCT00	0

▼▼ Form Curbs & Pads
▼ POUR DECK AREA 2 ROOF
▼▼ Install Lower Main Roofing System Roof

AREA 2 PENTHOUSE						
2230	Layout & Install MEPS Area 2 Penthouse	2d	2d	23JUN00	26JUN00	0
2000	Resteel Deck Area 2 Penthouse	1d	1d	27JUN00	27JUN00	0
2630	Deck Inspection Area 2 Penthouse	1d	1d	27JUN00	27JUN00	0
2840	POUR DECK AREA 2 ELEVATOR SLAB	1d	1d	07JUL00	07JUL00	0
3480	Metal Stud Framing Area 2 Penthouse	5d	5d	10JUL00	14JUL00	0
4440	Fire Sprinklers Rough in Area 2 Penthouse	2d	2d	10JUL00	11JUL00	0
3960	Electrical Rough in Area 2 Penthouse	3d	3d	12JUL00	14JUL00	0
3720	HVAC Rough in Area 2 Penthouse	2d	2d	13JUL00	14JUL00	0
4200	Plumbing Rough in Area 2 Penthouse	2d	2d	13JUL00	14JUL00	0
4680	Sheetrock Area 2 Penthouse	3d	3d	17JUL00	19JUL00	0
4690	Install Penthouse Exterior Skin	7d	7d	20JUL00	28JUL00	0
4720	Mechanical Shop drawings	10d	10d	20JUL00	02AUG00	0
4710	Mechanical installation	20d	20d	03AUG00	30AUG00	0
4700	Install Upper Roofing System Penthouse	7d	7d	07SEP00	15SEP00	0

▼ Layout & Install MEPS Area 2 Penthouse
▼ Resteel Deck Area 2 Penthouse
▼ Deck Inspection Area 2 Penthouse
▼ POUR DECK AREA 2 ELEVATOR SLAB
▼ Metal Stud Framing Area 2 Penthouse
▼ Fire Sprinklers Rough in Area 2 Penthouse
▼ Electrical Rough in Area 2 Penthouse
▼ HVAC Rough in Area 2 Penthouse
▼ Plumbing Rough in Area 2 Penthouse
▼ Sheetrock Area 2 Penthouse
▼ Install Penthouse Exterior Skin
▼ Mechanical Shop drawings
▼ Mechanical installation
▼ Install Upper Roofing System Penthouse

AREA 1						
8730	Stair Shop Drawings	40d	33d	01MAR00 A	19APR00	3d
8740	Stair Shop Drawing Review	20d	20d	20APR00	17MAY00	0
8750	Stair Fabrication	40d	40d	18MAY00	17JUL00	0
8760	Install Stair #2	6d	6d	18JUL00	25JUL00	0

▼ Stair Shop Drawings
▼ Stair Shop Drawing Review
▼ Stair Fabrication
▼ Install Stair #2

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	16A
© Primavera Systems, Inc.	

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<ul style="list-style-type: none"> <li>■ Early bar</li> <li>▽ Early start point</li> <li>▽ Early finish point</li> <li>◆ Target start point</li> <li>◆ Target finish point</li> <li>■ Progress bar</li> <li>■ Critical bar</li> <li>— Summary bar</li> <li>◆ Start milestone point</li> <li>◆ Finish milestone point</li> </ul>



## EMERYSTATION 2

8190	Frame Stair Shaft 2nd flr	2d	2d	26JUL00	27JUL00	0
8370	Frame Stair Shaft 3rd flr	2d	2d	28JUL00	31JUL00	0
8380	Frame Stair Shaft 4th flr	2d	2d	01AUG00	02AUG00	0
8390	Frame Stair Shaft 5th flr	2d	2d	03AUG00	04AUG00	0
8410	Frame Stair Shaft 6th flr	2d	2d	07AUG00	08AUG00	0
5410	Frame Stair Shaft 1st flr	2d	2d	09AUG00	10AUG00	0
8070	Sheetrock inside of stair shaft	3d	3d	18SEP00	20SEP00	0
7370	Tape Stair #2	6d	6d	21SEP00	28SEP00	0
5820	Install Handrails	2d	2d	29SEP00	02OCT00	0
5090	Paint Stair 2	2d	2d	03OCT00	04OCT00	0
5790	Hang Doors stair 2	2d	2d	05OCT00	06OCT00	0
7400	Electrical / Life Safety Finish Work Stair 2	1d	1d	05OCT00	05OCT00	0

- ∇ Frame Stair Shaft 2nd flr
- ∇ Frame Stair Shaft 3rd flr
- ∇ Frame Stair Shaft 4th flr
- ∇ Frame Stair Shaft 5th flr
- ∇ Frame Stair Shaft 6th flr
- ∇ Frame Stair Shaft 1st flr
- ∇ Sheetrock inside of stair shaft
- ∇ Tape Stair #2
- ∇ Install Handrails
- ∇ Paint Stair 2
- ∇ Hang Doors stair 2
- ∇ Electrical / Life Safety Finish Work Stair 2

**AREA 2**

8770	Install Stair #1	6d	6d	26JUL00	02AUG00	0
8420	Frame Stair Shaft 2nd flr	2d	2d	03AUG00	04AUG00	0
8440	Frame Stair Shaft 3rd flr	2d	2d	07AUG00	08AUG00	0
8460	Frame Stair Shaft 4th flr	2d	2d	09AUG00	10AUG00	0
8570	Frame Stair Shaft 5th flr	2d	2d	11AUG00	14AUG00	0
8630	Frame Stair Shaft 6th flr	2d	2d	15AUG00	16AUG00	0
8640	Frame Stair Shaft Roof	2d	2d	17AUG00	18AUG00	0
8430	Frame Stair Shaft 1st flr	2d	2d	21AUG00	22AUG00	0
8720	Sheetrock inside stair shaft	1d	1d	18SEP00	18SEP00	0
7380	Tape Stair 1	6d	6d	19SEP00	26SEP00	0

- ∇ Install Stair #1
- ∇ Frame Stair Shaft 2nd flr
- ∇ Frame Stair Shaft 3rd flr
- ∇ Frame Stair Shaft 4th flr
- ∇ Frame Stair Shaft 5th flr
- ∇ Frame Stair Shaft 6th flr
- ∇ Frame Stair Shaft Roof
- ∇ Frame Stair Shaft 1st flr
- ∇ Sheetrock inside stair shaft
- ∇ Tape Stair 1

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 17A  
 © Primavera Systems, Inc.

**WECOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ∇ Early start point
- ∇ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

# EMERYSTATION 2

6060	Install Handrails	2d	2d	27SEP00	28SEP00	0
5100	Paint Stair 1	2d	2d	29SEP00	02OCT00	0
5780	Hang Doors Stair 1	2d	2d	03OCT00	04OCT00	0
7390	Electrical / Life Safety Finish Work Stair 1	1d	1d	03OCT00	03OCT00	0

- ▽ Install Handrails
- ▽ Paint Stair 1
- ▽ Hang Doors Stair 1
- ▽ Electrical / Life Safety Finish Work Stair 1

## AREA 2 2ND FLR

5070	Frame Restrooms	3d	3d	27JUN00	29JUN00	0
6150	Rough Plumbing Restrooms	2d	2d	29JUN00	05JUL00	0
6160	Rough Electrical Restrooms	2d	2d	29JUN00	05JUL00	0
7240	Rough HVAC Restrooms	1d	1d	29JUN00	29JUN00	0
7250	Complete Sprinkler Drops	1d	1d	29JUN00	29JUN00	0
7260	Sheetrock Restrooms	2d	2d	24OCT00	25OCT00	0
7270	Tape & Texture Restrooms	5d	5d	26OCT00	01NOV00	0
5020	Tile Restrooms 2nd flr	4d	4d	02NOV00	07NOV00	0
5010	Paint Restrooms 2nd flr	2d	2d	08NOV00	09NOV00	0
5080	Finish Plumbing Restrooms 2nd flr	3d	3d	10NOV00	14NOV00	0
5120	Finish Electrical Restrooms 2nd flr	1d	1d	10NOV00	10NOV00	0
5240	Finish HVAC Restrooms 2ND flr	1d	1d	10NOV00	10NOV00	0
5360	Set Counter Tops Restrooms 2nd flr	1d	1d	10NOV00	10NOV00	0
5550	Hang Doors Restrooms 2nd flr	1d	1d	10NOV00	10NOV00	0
5610	Protect Doors Restrooms 2nd flr	1d	1d	13NOV00	13NOV00	0
5300	Partitions/Dispensers Restrooms 2ND flr	1d	1d	15NOV00	15NOV00	0
5490	Set Mirrors Restrooms 2nd flr	1d	1d	15NOV00	15NOV00	0

- ▽ Frame Restrooms
- ▽ Rough Plumbing Restrooms
- ▽ Rough Electrical Restrooms
- ▽ Rough HVAC Restrooms
- ▽ Complete Sprinkler Drops
- ▽ Sheetrock Restrooms
- ▽ Tape & Texture Restrooms
- ▽ Tile Restrooms 2nd flr
- ▽ Paint Restrooms 2nd flr
- ▽ Finish Plumbing Restrooms 2nd flr
- ▽ Finish Electrical Restrooms 2nd flr
- ▽ Finish HVAC Restrooms 2ND flr
- ▽ Set Counter Tops Restrooms 2nd flr
- ▽ Hang Doors Restrooms 2nd flr
- ▽ Protect Doors Restrooms 2nd flr
- ▽ Partitions/Dispensers Restrooms 2ND flr
- ▽ Set Mirrors Restrooms 2nd flr

## AREA 2 3RD FLR

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	18A
© Primavera Systems, Inc.	

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

## EMERYSTATION 2

7280	Frame Restrooms	3d	3d	29JUN00	06JUL00	0
7290	Rough Plumbing Restrooms	2d	2d	06JUL00	07JUL00	0
7300	Rough Electrical Restrooms	2d	2d	06JUL00	07JUL00	0
7310	Rough HVAC Restrooms	1d	1d	06JUL00	06JUL00	0
7320	Complete Sprinkler Drops	1d	1d	06JUL00	06JUL00	0
7330	Sheetrock Restrooms	2d	2d	26OCT00	27OCT00	0
7340	Tape & Texture Restrooms	5d	5d	30OCT00	03NOV00	0
5190	Tile Restrooms 3rd flr	4d	4d	06NOV00	09NOV00	0
5030	Paint Restrooms 3rd flr	2d	2d	10NOV00	13NOV00	0
5250	Finish Plumbing Restrooms 3rd flr	3d	3d	14NOV00	16NOV00	0
5310	Finish Electrical Restrooms 3rd flr	1d	1d	14NOV00	14NOV00	0
5440	Finish HVAC Restrooms 3rd flr	1d	1d	14NOV00	14NOV00	0
5560	Set Counter Tops Restrooms 3rd flr	1d	1d	14NOV00	14NOV00	0
5680	Hang Doors Restrooms 3rd flr	1d	1d	14NOV00	14NOV00	0
5730	Protect Doors Restrooms 3rd flr	1d	1d	15NOV00	15NOV00	0
5500	Partitions/Dispensers Restrooms 3rd flr	1d	1d	17NOV00	17NOV00	0
5620	Set Mirrors Restrooms 3rd flr	1d	1d	17NOV00	17NOV00	0

- ▣ Frame Restrooms
- ▣ Rough Plumbing Restrooms
- ▣ Rough Electrical Restrooms
- ▣ Rough HVAC Restrooms
- ▣ Complete Sprinkler Drops
  
- ▣ Sheetrock Restrooms
- ▣ Tape & Texture Restrooms
- ▣ Tile Restrooms 3rd flr
- ▣ Paint Restrooms 3rd flr
- ▣ Finish Plumbing Restrooms 3rd flr
- ▣ Finish Electrical Restrooms 3rd flr
- ▣ Finish HVAC Restrooms 3rd flr
- ▣ Set Counter Tops Restrooms 3rd flr
- ▣ Hang Doors Restrooms 3rd flr
- ▣ Protect Doors Restrooms 3rd flr
- ▣ Partitions/Dispensers Restrooms 3rd flr
- ▣ Set Mirrors Restrooms 3rd flr

### AREA 2 4TH FLR

7350	Frame Restrooms	3d	3d	06JUL00	10JUL00	0
7360	Rough Plumbing Restrooms	2d	2d	10JUL00	11JUL00	0
7410	Rough Electrical Restrooms	2d	2d	10JUL00	11JUL00	0
7420	Rough HVAC Restrooms	1d	1d	10JUL00	10JUL00	0
7430	Complete Sprinkler Drops Restrooms	1d	1d	10JUL00	10JUL00	0

- ▣ Frame Restrooms
- ▣ Rough Plumbing Restrooms
- ▣ Rough Electrical Restrooms
- ▣ Rough HVAC Restrooms
- ▣ Complete Sprinkler Drops Restrooms

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	19A
© Primavera Systems, Inc.	

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<ul style="list-style-type: none"> <li>▣ Early bar</li> <li>▣ Early start point</li> <li>▣ Early finish point</li> <li>◆ Target start point</li> <li>◆ Target finish point</li> <li>▣ Target bar</li> <li>▣ Progress bar</li> <li>▣ Critical bar</li> <li>▣ Summary bar</li> <li>◆ Start milestone point</li> <li>◆ Finish milestone point</li> </ul>

## EMERYSTATION 2

7440	Sheetrock Restrooms	2d	2d	30OCT00	31OCT00	0
7450	Tape & Texture Restrooms	5d	5d	01NOV00	07NOV00	0
5200	Tile Restrooms 4th flr	4d	4d	08NOV00	13NOV00	0
5040	Paint Restrooms 4th flr	2d	2d	14NOV00	15NOV00	0
5260	Finish Plumbing Restrooms 4th flr	2d	2d	16NOV00	17NOV00	0
5320	Finish Electrical Restrooms 4th flr	1d	1d	16NOV00	16NOV00	0
5450	Finish HVAC Restrooms 4th flr	1d	1d	16NOV00	16NOV00	0
5570	Set Counter Tops Restrooms 4th flr	1d	1d	16NOV00	16NOV00	0
5690	Hang Doors Restrooms 4th flr	1d	1d	16NOV00	16NOV00	0
5740	Protect Doors Restrooms 4th flr	1d	1d	17NOV00	17NOV00	0
5510	Partitions/Dispensers Restrooms 4th flr	1d	1d	20NOV00	20NOV00	0
5630	Set Mirrors Restrooms 4th flr	1d	1d	20NOV00	20NOV00	0

- ▽ Sheetrock Restrooms
- ▽ Tape & Texture Restrooms
- ▽ Tile Restrooms 4th flr
- ▽ Paint Restrooms 4th flr
- ▽ Finish Plumbing Restrooms 4th flr
- ▽ Finish Electrical Restrooms 4th flr
- ▽ Finish HVAC Restrooms 4th flr
- ▽ Set Counter Tops Restrooms 4th flr
- ▽ Hang Doors Restrooms 4th flr
- ▽ Protect Doors Restrooms 4th flr
- ▽ Partitions/Dispensers Restrooms 4th flr
- ▽ Set Mirrors Restrooms 4th flr

**AREA 2 5TH FLR**

5750	Frame Restrooms	3d	3d	07JUL00	11JUL00	0
7460	Rough Plumbing Restrooms	2d	2d	11JUL00	12JUL00	0
7470	Rough Electrical Restrooms	2d	2d	11JUL00	12JUL00	0
7480	Rough HVAC Restrooms	1d	1d	11JUL00	11JUL00	0
7490	Complete Sprinkler Drops Restrooms	1d	1d	11JUL00	11JUL00	0
7500	Sheetrock Restrooms	2d	2d	01NOV00	02NOV00	0
7510	Tape & Texture Restrooms	5d	5d	03NOV00	09NOV00	0
5210	Tile Restrooms 5th flr	8d	8d	10NOV00	21NOV00	0
5050	Paint Restrooms 5th flr	2d	2d	22NOV00	23NOV00	0
5270	Finish Plumbing Restrooms 5th flr	2d	2d	27NOV00	28NOV00	0

- ▽ Frame Restrooms
- ▽ Rough Plumbing Restrooms
- ▽ Rough Electrical Restrooms
- ▽ Rough HVAC Restrooms
- ▽ Complete Sprinkler Drops Restrooms
- ▽ Sheetrock Restrooms
- ▽ Tape & Texture Restrooms
- ▽ Tile Restrooms 5th flr
- ▽ Paint Restrooms 5th flr
- ▽ Finish Plumbing Restrooms 5th flr

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	20A
© Primavera Systems, Inc.	

**WECOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

# EMERYSTATION 2

5330	Finish Electrical Restrooms 5th flr	1d	1d	27NOV00	27NOV00	0
5460	Finish HVAC Restrooms 5th flr	1d	1d	27NOV00	27NOV00	0
5580	Set Counter Tops Restrooms 5th flr	1d	1d	27NOV00	27NOV00	0
5700	Hang Doors Restrooms 5th flr	1d	1d	27NOV00	27NOV00	0
5720	Protect Doors Restrooms 5th flr	1d	1d	28NOV00	28NOV00	0
5520	Partitions/Dispensers Restrooms 5th flr	1d	1d	29NOV00	29NOV00	0
5640	Set Mirrors Restrooms 5th flr	1d	1d	29NOV00	29NOV00	0

- ▽ Finish Electrical Restrooms 5th flr
- ▽ Finish HVAC Restrooms 5th flr
- ▽ Set Counter Tops Restrooms 5th flr
- ▽ Hang Doors Restrooms 5th flr
- ▽ Protect Doors Restrooms 5th flr
- ▽ Partitions/Dispensers Restrooms 5th flr
- ▽ Set Mirrors Restrooms 5th flr

## AREA 2 6TH FLR

7520	Frame Restrooms	3d	3d	18JUL00	20JUL00	0
7530	Rough Plumbing Restrooms	2d	2d	20JUL00	21JUL00	0
7540	Rough Electrical Restrooms	2d	2d	20JUL00	21JUL00	0
7550	Rough HVAC Restrooms	1d	1d	20JUL00	20JUL00	0
7560	Complete Sprinkler Drops Restrooms	1d	1d	20JUL00	20JUL00	0
7570	Sheetrock Restrooms	2d	2d	03NOV00	06NOV00	0
7580	Tape & Texture Restrooms	5d	5d	07NOV00	13NOV00	0
5220	Tile Restrooms 6th flr	8d	8d	14NOV00	23NOV00	0
5060	Paint Restrooms 6th flr	2d	2d	27NOV00	28NOV00	0
5280	Finish Plumbing Restrooms 6th flr	2d	2d	29NOV00	30NOV00	0
5340	Finish Electrical Restrooms 6th flr	2d	2d	29NOV00	30NOV00	0
5470	Finish HVAC Restrooms 6th flr	1d	1d	29NOV00	29NOV00	0
5590	Set Counter Tops Restrooms 6th flr	1d	1d	29NOV00	29NOV00	0
5710	Hang Doors Restrooms 6th flr	1d	1d	29NOV00	29NOV00	0
5770	Protect Doors Restrooms 6th flr	1d	1d	30NOV00	30NOV00	0

- ▽ Frame Restrooms
- ▽ Rough Plumbing Restrooms
- ▽ Rough Electrical Restrooms
- ▽ Rough HVAC Restrooms
- ▽ Complete Sprinkler Drops Restrooms
- ▽ Sheetrock Restrooms
- ▽ Tape & Texture Restrooms
- ▽ Tile Restrooms 6th flr
- ▽ Paint Restrooms 6th flr
- ▽ Finish Plumbing Restrooms 6th flr
- ▽ Finish Electrical Restrooms 6th flr
- ▽ Finish HVAC Restrooms 6th flr
- ▽ Set Counter Tops Restrooms 6th flr
- ▽ Hang Doors Restrooms 6th flr
- ▽ Protect Doors Restrooms 6th flr

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 21A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

# EMERYSTATION 2

5530	Partitions/Dispensers Restrooms 6th flr	1d	1d	01DEC00	01DEC00	0		▽ Partitions/Dispensers Restrooms 6th flr
5650	Set Mirrors Restrooms 6th flr	1d	1d	01DEC00	01DEC00	0		▽ Set Mirrors Restrooms 6th flr
<b>AREA 2 1ST FLR</b>								
6210	Frame Elevator Shaft & Lobby	3d	3d	19JUL00	21JUL00	0		▽ Frame Elevator Shaft & Lobby
6240	MEPS Rough in Elevator Lobby	2d	2d	21JUL00	24JUL00	0		▽ MEPS Rough in Elevator Lobby
7630	Set Elevator Door Frames	1d	1d	28NOV00	28NOV00	0		▽ Set Elevator Door Frames
6220	Rock Elevator Lobby	4d	4d	29NOV00	04DEC00	0		▽ Rock Elevator Lobby
6230	Tape Elevator Lobby	5d	5d	05DEC00	11DEC00	0		▽ Tape Elevator Lobby
5110	Paint Elevator Lobby 1st flr	2d	2d	12DEC00	13DEC00	0		▽ Paint Elevator Lobby 1st flr
6250	MEPS Finish Work Elevator Lobby	3d	3d	14DEC00	18DEC00	0		▽ MEPS Finish Work Elevator Lobby
<b>AREA 2 2ND FLR</b>								
6260	Frame Elevator Shaft & Lobby	3d	3d	27JUN00	29JUN00	0		▽ Frame Elevator Shaft & Lobby
6280	MEPS Rough in Elevator Lobby	2d	2d	29JUN00	05JUL00	0		▽ MEPS Rough in Elevator Lobby
7640	Set Elevator Door Frames	1d	1d	28NOV00	28NOV00	0		▽ Set Elevator Door Frames
6270	Rock Elevator Lobby	3d	3d	29NOV00	01DEC00	0		▽ Rock Elevator Lobby
6290	Tape Elevator Lobby	5d	5d	04DEC00	08DEC00	0		▽ Tape Elevator Lobby
5130	Paint Elevator Lobby 2nd flr	1d	1d	11DEC00	11DEC00	0		▽ Paint Elevator Lobby 2nd flr
6420	MEPS Finish Work Elevator Lobby	3d	3d	12DEC00	14DEC00	0		▽ MEPS Finish Work Elevator Lobby
<b>AREA 2 3RD FLR</b>								
6470	Frame Elevator Shaft & Lobby	3d	3d	29JUN00	06JUL00	0		▽ Frame Elevator Shaft & Lobby
6490	MEPS Rough in Elevator Lobby	2d	2d	06JUL00	07JUL00	0		▽ MEPS Rough in Elevator Lobby
7650	Set Elevator Door Frames	1d	1d	29NOV00	29NOV00	0		▽ Set Elevator Door Frames
6480	Rock Elevator Lobby & Shaft	3d	3d	04DEC00	06DEC00	0		▽ Rock Elevator Lobby & Shaft

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 22A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

# EMERYSTATION 2

6500	Tape Elevator Lobby	5d	5d	07DEC00	13DEC00	0
6460	Paint Elevator Lobby 3rd flr	1d	1d	14DEC00	14DEC00	0
6510	MEPS Finish Work Elevator Lobby	3d	3d	15DEC00	19DEC00	0

**AREA 2 4TH FLR**

6300	Frame Elevator Shaft & Lobby	3d	3d	06JUL00	10JUL00	0
6360	MEPS Rough in Elevator Lobby	2d	2d	10JUL00	11JUL00	0
7660	Set Elevator Door Frames	1d	1d	29NOV00	29NOV00	0
6330	Rock Elevator Lobby	3d	3d	07DEC00	11DEC00	0
6390	Tape Elevator Lobby	5d	5d	12DEC00	18DEC00	0
5140	Paint Elevator Lobby 4th flr	1d	1d	19DEC00	19DEC00	0
6430	MEPS Finish Work Elevator Lobby	3d	3d	20DEC00	22DEC00	0

**AREA 2 5TH FLR**

6310	Frame Elevator Shaft & Lobby	3d	3d	07JUL00	11JUL00	0
6370	MEPS Rough in Elevator Lobby	2d	2d	11JUL00	12JUL00	0
7670	Set Elevator Door Frames	1d	1d	30NOV00	30NOV00	0
6340	Rock Elevator Lobby & Shaft	3d	3d	12DEC00	14DEC00	0
6400	Tape Elevator Lobby	5d	5d	15DEC00	21DEC00	0
5150	Paint Elevator Lobby 5th flr	1d	1d	22DEC00	22DEC00	0
6440	MEPS Finish Work Elevator Lobby	3d	3d	02JAN01	04JAN01	0

**AREA 2 6TH FLR**

6320	Frame Elevator Shaft & Lobby	3d	3d	18JUL00	20JUL00	0
6380	MEPS Rough in Elevator Lobby	2d	2d	20JUL00	21JUL00	0
7680	Set Elevator Door Frames	1d	1d	30NOV00	30NOV00	0
6350	Rock Elevator Lobby & Shaft	3d	3d	15DEC00	19DEC00	0

- ▼ Tape Elevator Lobby
- ▼ Paint Elevator Lobby 3rd flr
- ▼ MEPS Finish Work Elevator Lobby

- ▼ Frame Elevator Shaft & Lobby
- ▼ MEPS Rough in Elevator Lobby
- ▼ Set Elevator Door Frames
- ▼ Rock Elevator Lobby
- ▼ Tape Elevator Lobby
- ▼ Paint Elevator Lobby 4th flr
- ▼ MEPS Finish Work Elevator Lobby

- ▼ Frame Elevator Shaft & Lobby
- ▼ MEPS Rough in Elevator Lobby
- ▼ Set Elevator Door Frames
- ▼ Rock Elevator Lobby & Shaft
- ▼ Tape Elevator Lobby
- ▼ Paint Elevator Lobby 5th flr
- ▼ MEPS Finish Work Elevator Lobby

- ▼ Frame Elevator Shaft & Lobby
- ▼ MEPS Rough in Elevator Lobby
- ▼ Set Elevator Door Frames
- ▼ Rock Elevator Lobby & Shaft

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	23A
© Primavera Systems, Inc.	

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

# EMERYSTATION 2

6410	Tape Elevator Lobby	5d	5d	20DEC00	03JAN01	0
5160	Paint Elevator Lobby 6th flr	1d	1d	04JAN01	04JAN01	0
6450	MEPS Finish Work Elevator Lobby	3d	3d	05JAN01	09JAN01	0

### ELEVATOR 1

7620	Hoist Elevator Machine Beams	1d	1d	13JUN00	13JUN00	0
7590	Hoist Elevator Machine Equipment	1d	1d	10JUL00	10JUL00	0
6540	Install Machine Room Equipment	10d	10d	18SEP00	29SEP00	0
6520	Install Rails	4d	4d	24OCT00	27OCT00	0
7600	Temp Power to Elevators	5d	5d	24OCT00	30OCT00	0
6550	Install Electrical & Switch Gear	10d	10d	30OCT00	10NOV00	0
6530	Build / Install Car Platform	10d	10d	13NOV00	27NOV00	0
6570	Cable Up Car	7d	7d	16NOV00	27NOV00	0
7610	Place all Signage for Temp Elevator	1d	1d	27NOV00	27NOV00	0
6630	Switch to Permanent Power	1d	1d	28NOV00	28NOV00	0
6700	Temp Construction Car Inspection	2d	2d	28NOV00	29NOV00	0
7690	Remove Man Lift	1d	1d	30NOV00	30NOV00	0
8860	Install Stone Floors	5d	5d	23JAN01	29JAN01	0

### ELEVATOR 2

6580	Install Machine Room Equipment	10d	10d	02OCT00	13OCT00	0
6600	Install Rails	4d	4d	30OCT00	02NOV00	0
6590	Install Electrical & Switch Gear	10d	10d	13NOV00	27NOV00	0
6610	Build / Install Car Platform	10d	10d	28NOV00	11DEC00	0
6620	Cable Up Car	7d	7d	01DEC00	11DEC00	0
7700	Complete finish Work	4d	4d	12DEC00	15DEC00	0

Tape Elevator Lobby  
 Paint Elevator Lobby 6th flr  
 MEPS Finish Work Elevator Lobby

Hoist Elevator Machine Beams  
 Hoist Elevator Machine Equipment  
 Install Machine Room Equipment  
 Install Rails  
 Temp Power to Elevators  
 Install Electrical & Switch Gear  
 Build / Install Car Platform  
 Cable Up Car  
 Place all Signage for Temp Elevator  
 Switch to Permanent Power  
 Temp Construction Car Inspection  
 Remove Man Lift  
 Install Stone Floors

Install Machine Room Equipment  
 Install Rails  
 Install Electrical & Switch Gear  
 Build / Install Car Platform  
 Cable Up Car  
 Complete finish Work

Start date	08NOV99
Finish date	08MAR01
Data date	06MAR00
Run date	14MAR00
Page number	24A
© Primavera Systems, Inc.	

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- Early start point
- Early finish point
- Target start point
- Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point



# EMERYSTATION 2

Activity ID	Activity Description	Duration	Start	End	Start	End	0	Notes
8850	Install Stone Floors	5d	5d	16JAN01	22JAN01		0	▼ Install Stone Floors
<b>ELEVATOR 3</b>								
6640	Install Machine Room Equipment	10d	10d	16OCT00	27OCT00		0	▼ Install Machine Room Equipment
6660	Install Rails	4d	4d	03NOV00	08NOV00		0	▼ Install Rails
6650	Install Electrical & Switch Gear	10d	10d	28NOV00	11DEC00		0	▼ Install Electrical & Switch Gear
6670	Build / Install Car Platform	10d	10d	12DEC00	02JAN01		0	▼ Build / Install Car Platform
6680	Cable Up Car	7d	7d	15DEC00	02JAN01		0	▼ Cable Up Car
6690	Complete Finish Work	4d	4d	03JAN01	08JAN01		0	▼ Complete Finish Work
8780	Install Stone Floors	5d	5d	09JAN01	15JAN01		0	▼ Install Stone Floors
8690	Schedule State Inspection	5d	5d	30JAN01	05FEB01		0	▼ Schedule State Inspection
<b>AREA 2 1ST FLR</b>								
6710	Metal Stud Framing	1d	1d	26JUL00	26JUL00		0	▼ Metal Stud Framing
6720	MEPS Rough In	1d	1d	27JUL00	27JUL00		0	▼ MEPS Rough In
6730	Sheetrock	1d	1d	28JUL00	28JUL00		0	▼ Sheetrock
6740	Tape	5d	5d	31JUL00	04AUG00		0	▼ Tape
5380	Paint Elect/Phone Room 1st flr	1d	1d	07AUG00	07AUG00		0	▼ Paint Elect/Phone Room 1st flr
5800	Hang Temp Door Electrical Rooms	1d	1d	08AUG00	08AUG00		0	▼ Hang Temp Door Electrical Rooms
6770	Install Switch Gear & Panels	5d	5d	08AUG00	14AUG00		0	▼ Install Switch Gear & Panels
6200	Protect Doors	1d	1d	09AUG00	09AUG00		0	▼ Protect Doors
6760	Install F.T Plywood Mounting Boards	1d	1d	15AUG00	15AUG00		0	▼ Install F.T Plywood Mounting Boards
6070	Hang Doors Elect/Phone Rooms	1d	1d	24OCT00	24OCT00		0	▼ Hang Doors Elect/Phone Rooms
<b>AREA 2 2ND FLR</b>								
6780	Metal Stud Framing	1d	1d	27JUN00	27JUN00		0	▼ Metal Stud Framing

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 25A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	Legend
08MAR00			DJD	■ Early bar ▼ Early start point ▽ Early finish point ◆ Target start point ◆ Target finish point ■ Target bar ■ Progress bar ■ Critical bar ■ Summary bar ◆ Start milestone point ◆ Finish milestone point

# EMERYSTATION 2

6790	MEPS Rough In	1d	1d	28JUN00	28JUN00	0
6800	Sheetrock	2d	2d	29JUN00	05JUL00	0
6810	Tape	5d	5d	06JUL00	12JUL00	0
5350	Paint Elect/Phone Room 1st flr	1d	1d	13JUL00	13JUL00	0
6840	Install Switch Gear & Panels	5d	5d	14JUL00	20JUL00	0
5670	Hang Temp Door Electrical Rooms	1d	1d	21JUL00	21JUL00	0
6830	Install F.T Plywood Mounting Boards	1d	1d	21JUL00	21JUL00	0
6080	Hang Doors Elect/Phone Rooms	1d	1d	24OCT00	24OCT00	0

- ▽ MEPS Rough In
- ▽ Sheetrock
- ▽ Tape
- ▽ Paint Elect/Phone Room 1st flr
- ▽ Install Switch Gear & Panels
- ▽ Hang Temp Door Electrical Rooms
- ▽ Install F.T Plywood Mounting Boards
- ▽ Hang Doors Elect/Phone Rooms

## AREA 2 3RD FLR

6850	Metal Stud Framing	1d	1d	29JUN00	29JUN00	0
6860	MEPS Rough In	1d	1d	05JUL00	05JUL00	0
6870	Sheetrock	2d	2d	06JUL00	07JUL00	0
6880	Tape	5d	5d	10JUL00	14JUL00	0
5370	Paint Elect/Phone Room 3rd flr	1d	1d	17JUL00	17JUL00	0
6910	Install Switch Gear & Panels	5d	5d	18JUL00	24JUL00	0
5760	Hang Temp Door Electrical Room	1d	1d	25JUL00	25JUL00	0
6900	Install F.T Plywood Mounting Boards	1d	1d	25JUL00	25JUL00	0
6090	Hang Doors Elect/Phone Rooms	1d	1d	24OCT00	24OCT00	0

- ▽ Metal Stud Framing
- ▽ MEPS Rough In
- ▽ Sheetrock
- ▽ Tape
- ▽ Paint Elect/Phone Room 3rd flr
- ▽ Install Switch Gear & Panels
- ▽ Hang Temp Door Electrical Room
- ▽ Install F.T Plywood Mounting Boards
- ▽ Hang Doors Elect/Phone Rooms

## AREA 2 4TH FLR

6920	Metal Stud Framing	1d	1d	06JUL00	06JUL00	0
6960	MEPS Rough In	1d	1d	07JUL00	07JUL00	0
7000	Sheetrock	2d	2d	10JUL00	11JUL00	0
7040	Tape	5d	5d	12JUL00	18JUL00	0
5430	Paint Elect/Phone Room 4th flr	1d	1d	19JUL00	19JUL00	0

- ▽ Metal Stud Framing
- ▽ MEPS Rough In
- ▽ Sheetrock
- ▽ Tape
- ▽ Paint Elect/Phone Room 4th flr

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 26A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- Early start point
- Early finish point
- Target start point
- Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

# EMERYSTATION 2

7160	Install Switch Gear & Panels	5d	5d	20JUL00	26JUL00	0
6170	Hang Temp Door Electrical Room	1d	1d	27JUL00	27JUL00	0
7120	Install F.T Plywood Mounting Boards	1d	1d	27JUL00	27JUL00	0
5480	Hang Doors Elect/Phone Rooms	1d	1d	24OCT00	24OCT00	0

**AREA 2 5TH FLR**

6930	Metal Stud Framing	1d	1d	07JUL00	07JUL00	0
6970	MEPS Rough In	1d	1d	10JUL00	10JUL00	0
7010	Sheetrock	2d	2d	12JUL00	13JUL00	0
7050	Tape	5d	5d	14JUL00	20JUL00	0
5390	Paint Elect/Phone Room 5th flr	1d	1d	21JUL00	21JUL00	0
7170	Install Switch Gear & Panels	4d	4d	24JUL00	27JUL00	0
7130	Install F.T Plywood Mounting Boards	1d	1d	28JUL00	28JUL00	0
8870	Hang Temp Door Electrical Room	1d	1d	28JUL00	28JUL00	0
6180	Hang Doors Elect/Phone Rooms	1d	1d	25OCT00	25OCT00	0

**AREA 2 6TH FLR**

6940	Metal Stud Framing	1d	1d	18JUL00	18JUL00	0
6980	MEPS Rough In	1d	1d	19JUL00	19JUL00	0
7020	Sheetrock	2d	2d	20JUL00	21JUL00	0
7060	Tape	5d	5d	24JUL00	28JUL00	0
5400	Paint Elect/Phone Room 6th flr	1d	1d	31JUL00	31JUL00	0
7180	Install Switch Gear & Panels	5d	5d	01AUG00	07AUG00	0
7140	Install F.T Plywood Mounting Boards	1d	1d	08AUG00	08AUG00	0
7150	Hang Temp Door Electrical Room	1d	1d	08AUG00	08AUG00	0
6190	Hang Doors Elect/Phone Rooms	1d	1d	26OCT00	26OCT00	0

- ▣ Install Switch Gear & Panels
- ▽ Hang Temp Door Electrical Room
- ▽ Install F.T Plywood Mounting Boards
- ▽ Hang Doors Elect/Phone Rooms

- ▽ Metal Stud Framing
- ▽ MEPS Rough In
- ▽ Sheetrock
- ▣ Tape
- ▽ Paint Elect/Phone Room 5th flr
- ▣ Install Switch Gear & Panels
- ▽ Install F.T Plywood Mounting Boards
- ▽ Hang Temp Door Electrical Room
- ▽ Hang Doors Elect/Phone Rooms

- ▽ Metal Stud Framing
- ▽ MEPS Rough In
- ▽ Sheetrock
- ▣ Tape
- ▽ Paint Elect/Phone Room 6th flr
- ▣ Install Switch Gear & Panels
- ▽ Install F.T Plywood Mounting Boards
- ▽ Hang Temp Door Electrical Room
- ▽ Hang Doors Elect/Phone Rooms

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 27A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- ▣ Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- ▣ Target bar
- ▣ Progress bar
- ▣ Critical bar
- ▣ Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point



# EMERYSTATION 2

## PRECAST

7760	Embed Layout Drawings	10d	5d	28FEB00 A	10MAR00	5d
6890	Precast Shop Drawings	25d	25d	13MAR00	14APR00	0
7770	Shop Drawings Submittals	30d	30d	17APR00	26MAY00	0
7780	City Approval Shop Drawings	10d	10d	15MAY00	26MAY00	0
6990	Fabricate Panels	60d	60d	29MAY00	23AUG00	0
7030	Mobilize Crane	1d	1d	24AUG00	24AUG00	0
7070	Erect Precast at East Lobby	7d	7d	25AUG00	04SEP00	0
7190	Erect Precast at West Lobby	6d	6d	05SEP00	12SEP00	0
7080	Plumb & Line Precast	60d	60d	06SEP00	29NOV00	0
7740	Erect Precast at Roof	15d	15d	13SEP00	03OCT00	0
7090	Weld Off Connections	60d	60d	27SEP00	20DEC00	0
7750	Erect Precast Balance of Building	30d	30d	04OCT00	14NOV00	0

## GLASS SYSTEM

7800	Award Glazing Contract	20d	15d	01FEB00 A	24MAR00	24d
7790	Glass Shop Drawings	40d	40d	27MAR00	19MAY00	0
7810	Shop Drawing Approval	25d	25d	01MAY00	02JUN00	0
7820	Fabricate Glazing System	65d	65d	05JUN00	06SEP00	0
7100	Hoist Mullions / Glass	3d	3d	25AUG00	29AUG00	0
7110	Install Curtainwalls & Caulking	40d	40d	12SEP00	06NOV00	0
7710	Glazing & Metal Doors 1st flr	15d	15d	31OCT00	20NOV00	0
7830	Glazing & Metal Doors 2nd flr	20d	20d	07NOV00	05DEC00	0
7880	Caulking	50d	50d	21NOV00	07FEB01	0

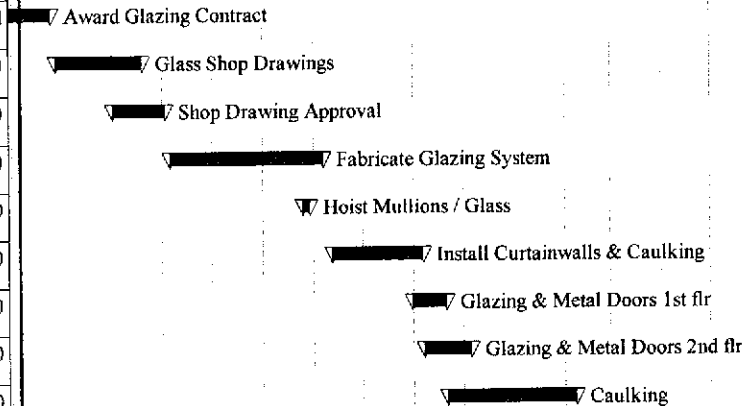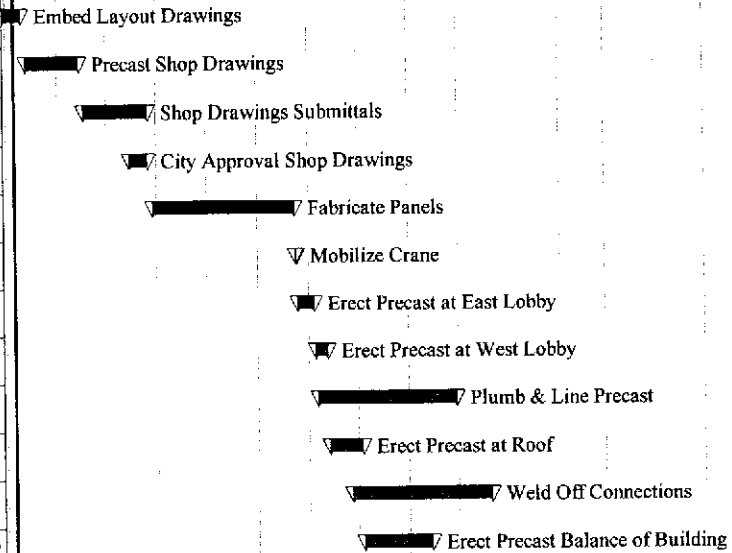

Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 28A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Standstill bar
- Start milestone point
- Finish milestone point

# EMERYSTATION 2

7840	Glazing & Metal Doors 3rd flr	18d	18d	06DEC00	08JAN01	0	▣ Glazing & Metal Doors 3rd flr
7850	Glazing & Metal Doors 4th flr	18d	18d	05JAN01	30JAN01	0	▣ Glazing & Metal Doors 4th flr
7860	Glazing & Metal Doors 5th flr	18d	18d	29JAN01	21FEB01	0	▣ Glazing & Metal Doors 5th flr
7870	Glazing & Metal Doors 6th flr	18d	18d	13FEB01	08MAR01	0	▣ Glazing & Metal Doors 6th flr

SHELL							
7720	Lobby Design Complete	20d	20d	06MAR00	31MAR00	0	▣ Lobby Design Complete
7890	Frame Walls & Soffits Lobby	10d	10d	24OCT00	06NOV00	0	▣ Frame Walls & Soffits Lobby
7900	Rough MEPS Lobby	10d	10d	24OCT00	06NOV00	0	▣ Rough MEPS Lobby
7730	Water Tight Lobby	1d	1d	07NOV00	07NOV00	0	▣ Water Tight Lobby
7910	Sheetrock Lobby	15d	15d	07NOV00	28NOV00	0	▣ Sheetrock Lobby
7920	Tape Lobby	10d	10d	23NOV00	07DEC00	0	▣ Tape Lobby
7930	Paint Lobby	10d	10d	22DEC00	12JAN01	0	▣ Paint Lobby
8050	MEPS Finish Trim Work	10d	10d	12FEB01	23FEB01	0	▣ MEPS Finish Trim Work
8040	Carpet Lobby	8d	8d	26FEB01	07MAR01	0	▣ Carpet Lobby

STONE							
7980	Award Stone Contract	10d	10d	15MAY00	26MAY00	0	▣ Award Stone Contract
7940	Stone Shop Drawings	30d	30d	29MAY00	12JUL00	0	▣ Stone Shop Drawings
7950	Stone Shop Drawings Approved	15d	15d	13JUL00	02AUG00	0	▣ Stone Shop Drawings Approved
7960	Fabrication & Shipping	65d	65d	03AUG00	01NOV00	0	▣ Fabrication & Shipping
7970	Install Stone Lobby	35d	35d	02NOV00	21DEC00	0	▣ Install Stone Lobby

WOOD							
7990	Award Wood Contract	10d	10d	12JUN00	23JUN00	0	▣ Award Wood Contract
8000	Wood Panel Shop Drawings	40d	40d	26JUN00	23AUG00	0	▣ Wood Panel Shop Drawings


**Start date** 08NOV99  
**Finish date** 08MAR01  
**Data date** 06MAR00  
**Run date** 14MAR00  
**Page number** 29A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved	
08MAR00			DJD	<ul style="list-style-type: none"> <li>▣ Early bar</li> <li>▽ Early start point</li> <li>▽ Early finish point</li> <li>◆ Target start point</li> <li>◆ Target finish point</li> <li>▣ Target bar</li> <li>▣ Progress bar</li> <li>▣ Critical bar</li> <li>▣ Summary bar</li> <li>◆ Start milestone point</li> <li>◆ Finish milestone point</li> </ul>


# EMERYSTATION 2

8010	Wood Shop Drawings Approved	15d	15d	24AUG00	13SEP00	0
8020	Fabrication & Shipping	60d	60d	14SEP00	07DEC00	0
8030	Install Wood Panels Lobby	30d	30d	22DEC00	09FEB01	0



### BUILDING START UP

8700	Start Up Duration	20d	20d	26JAN01	22FEB01	0
8710	Life Safety Testing	15d	15d	07FEB01	27FEB01	0



Start date 08NOV99  
 Finish date 08MAR01  
 Data date 06MAR00  
 Run date 14MAR00  
 Page number 30A  
 © Primavera Systems, Inc.

**WEBCOR BUILDERS**

Date	Revision	Checked	Approved
08MAR00			DJD

- Early bar
- ▽ Early start point
- ▽ Early finish point
- ◆ Target start point
- ◆ Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point
