


ID	Task Name	Duration	Start	Finish	Predecessors	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March
1	MEETINGS AT ACDEH																			
2	May 17, 2017 Meeting at ACDEH (1:30pm - 3:30pm)	0 days	Wed 5/17/17	Wed 5/17/17																
3	Jun. 14, 2017 Meeting at ACDEH (1pm - 3pm)	0 days	Wed 6/14/17	Wed 6/14/17																
4																				
5	GEOTRACKER CONFIRMATION																			
6	First Quarter 2017 Verification of Required Document Upload	0 days	Fri 3/31/17	Fri 3/31/17																
7	Second Quarter 2017 Verification of Required Document Upload	0 days	Fri 6/30/17	Fri 6/30/17																
8	Third Quarter 2017 Verification of Required Document Upload	0 days	Fri 9/29/17	Fri 9/29/17																
9	Fourth Quarter 2017 Verification of Required Document Upload	0 days	Fri 12/29/17	Fri 12/29/17																
10																				
11	SITE INVESTIGATIONS																			
12	Benzene Excavation / Cement Treated Base (CTB) Area	217 days?	Thu 9/1/16	Fri 6/30/17																
13	Soil Excavation Implementation Report submitted to ACDEH	0 days	Thu 9/1/16	Thu 9/1/16																
14	Work Plan Addendum for Cement Treated Base (CTB) Investigation	11 days?	Tue 1/17/17	Wed 2/1/17																
15	Submit Draft to ACDEH (GeoTracker upload)	0 days	Tue 1/17/17	Tue 1/17/17																
16	ACDEH Review (committed to 30 days)	15 days?	Tue 1/17/17	Tue 1/31/17	15SS															
17	Received ACDEH Conditional Approval	0 days	Wed 2/1/17	Wed 2/1/17	16															
18	CTB Area Investigation	25 days	Mon 2/20/17	Fri 3/24/17																
19	Obtain Permit for CTB Sampling	5 days	Mon 2/20/17	Fri 2/24/17																
20	CTB Field Investigation	2 days	Mon 3/13/17	Tue 3/14/17	19															
21	CTB Sampling Results	2 days	Thu 3/23/17	Fri 3/24/17	20															
22	Soil Excavation Implementation Report Addendum	58 days?	Wed 4/12/17	Fri 6/30/17																
23	Submit CTB Investigation Report dated 4/5/17 to ACDEH (GeoTracker upload)	0 days	Wed 4/12/17	Wed 4/12/17																
24	ACDEH Review (60 days)	60 days?	Wed 4/12/17	Sat 6/10/17	23SS															
25	<<ACDEH comment provided during 5/17/17 call	0 days	Wed 5/17/17	Wed 5/17/17																
26	<<Submit Response ACDEH Comments Letter to ACDEH (GeoTracker upload)	0 days	Tue 6/6/17	Tue 6/6/17	25															
27	Revisions to Draft	5 days	Mon 6/12/17	Fri 6/16/17	24															
28	Resubmittal to ACDEH	0 days	Fri 6/16/17	Fri 6/16/17	27															
29	ACDEH Review of Revised Draft (2 weeks)	14 days?	Sat 6/17/17	Fri 6/30/17	28															
30	ACDEH Approval	0 days	Fri 6/30/17	Fri 6/30/17	29															
31																				
32	INSTITUTIONAL CONTROLS																			
33	Deed Restriction	69 days?	Tue 2/14/17	Fri 5/19/17																
34	Submit Draft Deed Restriction to ACDEH (vial email)	0 days	Tue 2/14/17	Tue 2/14/17																
35	ACDEH Review (60 days)	60 days?	Tue 2/14/17	Fri 4/14/17	34SS															
36	Revisions to Draft	15 days	Mon 4/17/17	Fri 5/5/17	35															
37	Resubmittal to ACDEH	0 days	Fri 5/5/17	Fri 5/5/17	36															
38	ACDEH Review of Revised Draft (2 weeks)	14 days?	Sat 5/6/17	Fri 5/19/17	37															
39	ACDEH Approval and GeoTracker upload	0 days	Fri 5/19/17	Fri 5/19/17	38															
40	CC&R's	69 days?	Tue 6/6/17	Fri 9/8/17																
41	Submit Draft to ACDEH (via email)	0 days	Tue 6/6/17	Tue 6/6/17																
42	ACDEH Review (60 days)	60 days?	Tue 6/6/17	Fri 8/4/17	41SS															
43	Revisions to Draft	15 days	Mon 8/7/17	Fri 8/25/17	42															
44	Resubmittal to ACDEH	0 days	Fri 8/25/17	Fri 8/25/17	43															
45	ACDEH Review of Revised Draft (2 weeks)	14 days?	Sat 8/26/17	Fri 9/8/17	44															
46	ACDEH Approval and GeoTracker upload	0 days	Fri 9/8/17	Fri 9/8/17	45															
47																				
48																				

Project: State Street
Date: Wed 6/14/17

Task		Summary		External Milestone		Manual Task		Manual Summary		External Tasks		Deadline	
Split		Project Summary		Inactive Milestone		Duration-only		Start-only		External Milestone			
Milestone		External Tasks		Inactive Summary		Manual Summary Rollup		Finish-only		Progress			

Page 1

ID	Task Name	Duration	Start	Finish	Predecessors	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March
49	ENGINEERING CONTROLS																			
50	VMS O&M Plan	68 days	Wed 4/12/17	Fri 7/14/17																
51	Submitted VMS O&M Plan to ACDEH (GeoTracker upload)	0 days	Wed 4/12/17	Wed 4/12/17																
52	ACDEH Review (60 days)	60 days?	Wed 4/12/17	Sat 6/10/17 51SS																
53	Revisions	15 days	Mon 6/12/17	Fri 6/30/17 52																
54	Resubmittal to ACDEH	0 days	Fri 6/30/17	Fri 6/30/17 53																
55	ACDEH Review of Revised Plan (2 weeks)	14 days?	Sat 7/1/17	Fri 7/14/17 54																
56	ACDEH Approval	0 days	Fri 7/14/17	Fri 7/14/17 55																
57																				
58	Site Utility Work	146 days?	Mon 4/3/17	Mon 10/23/17																
59	Wet Utilities (Sewer, Strom & Water)	65 days	Mon 4/3/17	Sat 7/1/17																
60	Start Date for Site Utility Installation	0 days	Mon 4/3/17	Mon 4/3/17																
61	Sewer, Strom & Water Installation (weather permitting)	90 days	Mon 4/3/17	Sat 7/1/17 60																
62	Trench Plug on Sewer Main	1 day	Fri 4/14/17	Fri 4/14/17 61SS+2 days																
63	CQA of Trench Plug on Sewer Main	1 day	Fri 4/14/17	Fri 4/14/17 62SS																
64	Trench Plug on Storm Main (to be done concurrently with water main)	1 day	Mon 6/26/17	Mon 6/26/17																
65	CQA of Trench Plug on Storm Main	1 day	Mon 6/26/17	Mon 6/26/17 64SS																
66	Trench Plug on Water Main (to be done concurrently with storm main)	1 day	Mon 6/26/17	Mon 6/26/17 64SS																
67	CQA of Trench Plug on Water Main	1 day	Mon 6/26/17	Mon 6/26/17 66SS																
68	Utilities - PG&E, AT&T, CATV	25 days	Mon 7/3/17	Fri 8/4/17 59																
69	Subgrade Prep & Rock, Form & Pour Curb, Gutter & Sidewalk	18 days	Mon 8/7/17	Wed 8/30/17 68																
70	Pull & Splice Cable - PG&E and Street Lights	17 days?	Thu 8/31/17	Fri 9/22/17 69																
71	Test Sewer-USD & Water-ACWD, Video Sewer & Storm	10 days	Fri 9/22/17	Thu 10/5/17 70FS-1 day																
72	Final Rock Grade & Pave Streets	10 days	Fri 10/6/17	Thu 10/19/17 71																
73	Pave Streets	3 days	Thu 10/19/17	Mon 10/23/17 72FS-1 day																
74																				
75	Building 12																			
76	Row Home Construction (~9 months)	264 days?	Fri 4/28/17	Tue 1/16/18																
77	Foundation (~2 months)	40 days	Fri 4/28/17	Wed 6/7/17																
78	Start Date for Building 12 Foundation	0 days	Fri 4/28/17	Fri 4/28/17																
79	Subslab Barrier and Vent Pipe Installation	14 days	Tue 5/23/17	Mon 6/5/17 78																
80	CQA of Subslab Barrier and Vent Pipe Installation	14 days	Tue 5/23/17	Mon 6/5/17 79SS																
81	Pour Foundation Slab	0 days	Wed 6/7/17	Wed 6/7/17																
82	Trench Dam Installation (after streets paved)	5 days	Tue 10/24/17	Mon 10/30/17 73																
83	Trench Dam Installation (install during foundation pour)	5 days	Tue 10/24/17	Mon 10/30/17 73																
84	CQA of Trench Dam Installation	5 days	Tue 10/24/17	Mon 10/30/17 83SS																
85	Construction Completion Report-Part 1 (Subslab Installation)	81 days?	Fri 7/14/17	Tue 10/3/17																
86	Submit Draft to ACDEH (GeoTracker upload)	0 days	Fri 7/14/17	Fri 7/14/17 81FS+38 days																
87	ACDEH Review (60 days)	60 days?	Sat 7/15/17	Tue 9/12/17 86																
88	Revisions to Draft	7 days	Wed 9/13/17	Tue 9/19/17 87																
89	Resubmittal to ACDEH	0 days	Tue 9/19/17	Tue 9/19/17 88																
90	ACDEH Review of Revised Draft (2 weeks)	14 days?	Wed 9/20/17	Tue 10/3/17 89																
91	ACDEH Approval	0 days	Tue 10/3/17	Tue 10/3/17 90																
92	Framing to Roof Completion (~3 months)	97 days	Mon 6/12/17	Sat 9/16/17 77																
93	Start Date for Building 12 Framing	0 days	Mon 6/12/17	Mon 6/12/17																
94	Building 12 Framing	90 days	Mon 6/12/17	Sat 9/9/17 93																
95	Vent Riser Completion	10 days	Mon 9/4/17	Fri 9/15/17 93SS+60 days, 94SS+60 days																
96	CQA of Vent Risers	1 day	Sat 9/16/17	Sat 9/16/17 95																



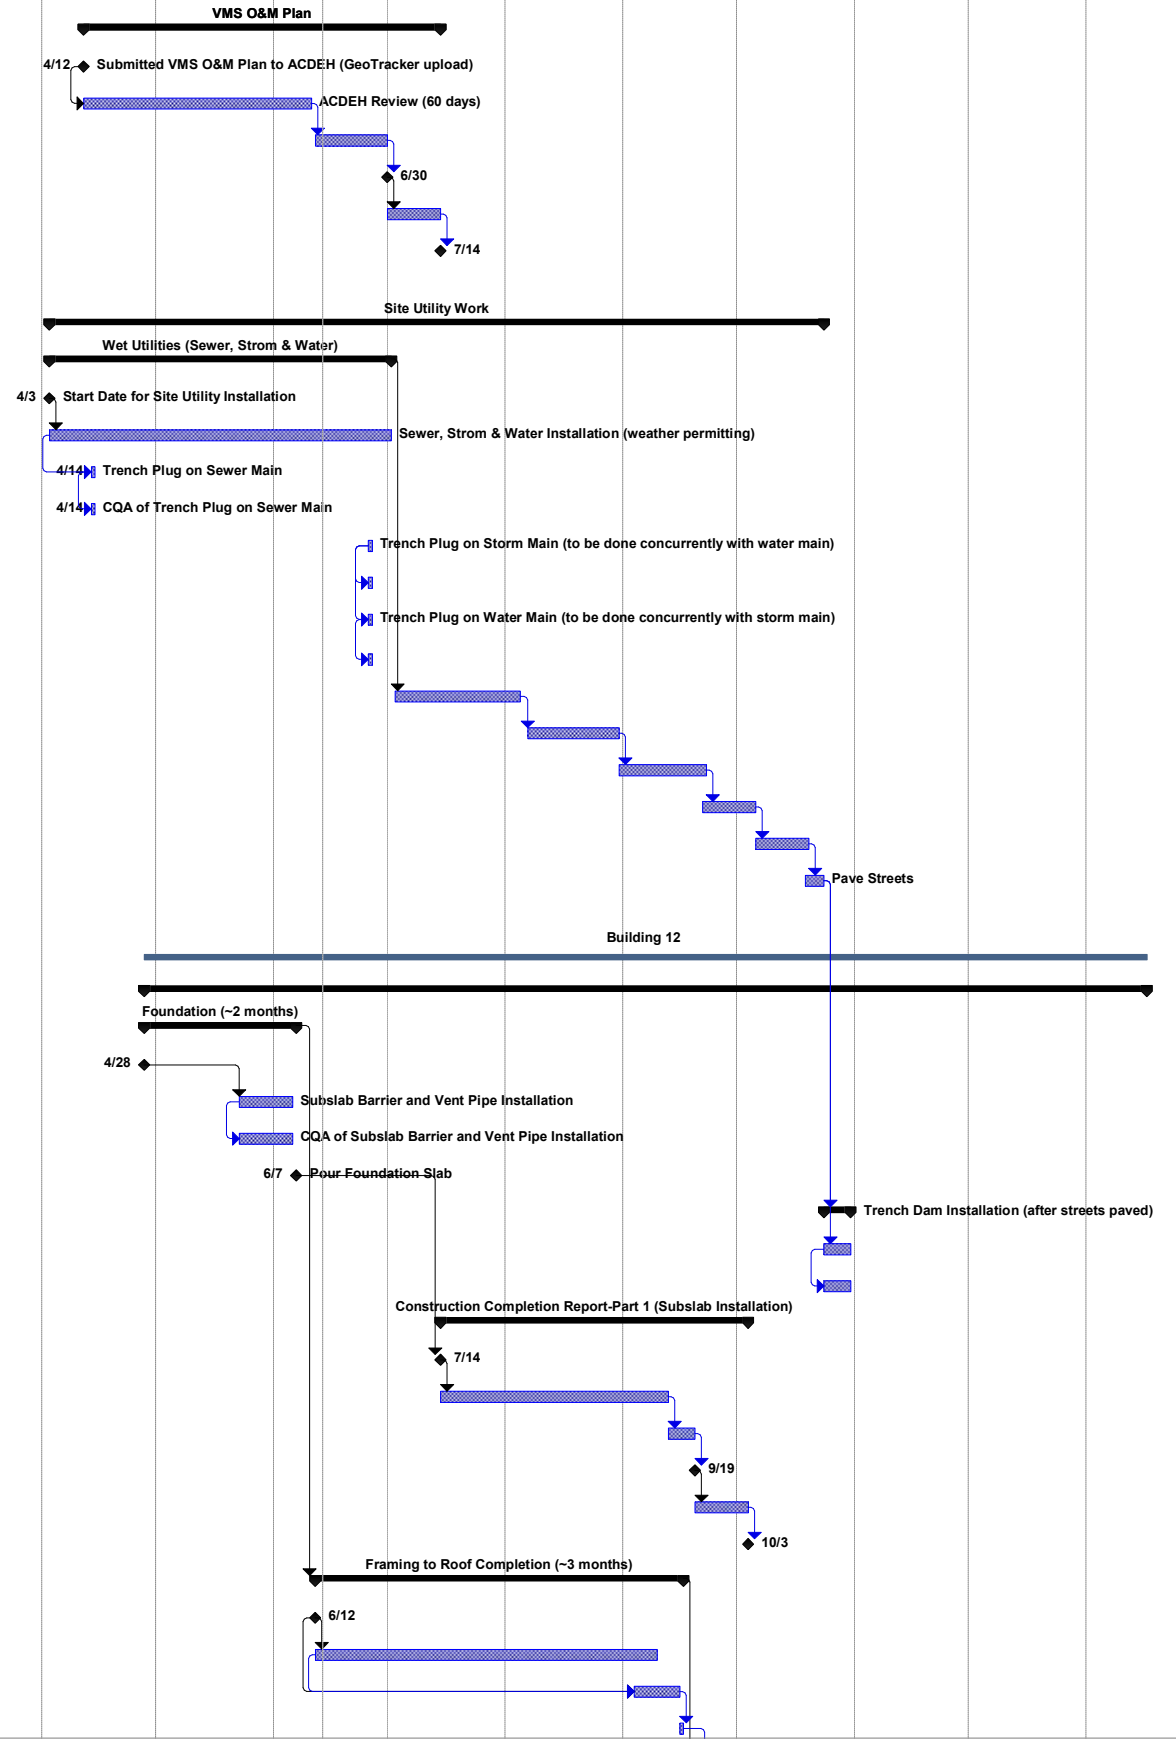


Project: State Street
Date: Wed 6/14/17

Task	Summary	External Milestone	Manual Task	Manual Summary	External Tasks	Deadline
Split	Project Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	
Milestone	External Tasks	Inactive Summary	Manual Summary Rollup	Finish-only	Progress	

Page 2

ID	Task Name	Duration	Start	Finish	Predecessors	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March
97	Construction Completion Report-Part 2 (Vent Risers)	81 days?	Sat 9/23/17	Wed 12/13/17																
98	Submit Draft to ACDEH (GeoTracker upload)	0 days	Sat 9/23/17	Sat 9/23/17	96FS+7 days															
99	ACDEH Review (60 days)	60 days?	Sun 9/24/17	Wed 11/22/17	98															
100	Revisions to Draft	7 days	Thu 11/23/17	Wed 11/29/17	99															
101	Resubmittal to ACDEH	0 days	Wed 11/29/17	Wed 11/29/17	100															
102	ACDEH Review of Revised Draft (2 weeks)	14 days?	Thu 11/30/17	Wed 12/13/17	101															
103	ACDEH Approval	0 days	Wed 12/13/17	Wed 12/13/17	102															
104	Interior/Exterior Rough & Finish	120 days	Sun 9/17/17	Sun 1/14/18	92															
105	Vent Riser Roof Cap Completion	5 days	Thu 11/16/17	Mon 11/20/17	104SS+60 days															
106	CQA of Vent Riser Roof Cap Completion	2 days	Tue 11/21/17	Wed 11/22/17	105															
107	VMS Performance Monitoring	1 day	Tue 11/28/17	Tue 11/28/17	106FS+5 days															
108	Construction Completion Report-Part 3 (Roof Completion)	35 days?	Tue 12/12/17	Tue 1/16/18																
109	Submit Draft to ACDEH (GeoTracker upload)	0 days	Tue 12/12/17	Tue 12/12/17	107FS+14 days															
110	ACDEH Review (2 weeks)	14 days	Wed 12/13/17	Tue 12/26/17	109															
111	Revisions to Draft (1 week)	7 days	Wed 12/27/17	Tue 1/2/18	110															
112	Resubmittal to ACDEH	0 days	Tue 1/2/18	Tue 1/2/18	111															
113	ACDEH Review of Revised Draft (2 weeks)	14 days?	Wed 1/3/18	Tue 1/16/18	112															
114	ACDEH Approval	0 days	Tue 1/16/18	Tue 1/16/18	113															
115	Building Ready for Occupancy	0 days	Fri 12/15/17	Fri 12/15/17	104,113															
116																				
117	Building 7	270 days	Tue 8/1/17	Fri 4/27/18																
118	Row Home Construction	270 days	Tue 8/1/17	Fri 4/27/18																
119	Foundation (~2 months)	35 days	Tue 8/1/17	Mon 9/4/17																
120	Estimated Start Date for Building 12 Foundation	0 days	Tue 8/1/17	Tue 8/1/17																
121	Subslab Barrier and Vent Pipe Installation	5 days	Thu 8/31/17	Mon 9/4/17	120SS+30 days															
122	CQA of Subslab Barrier and Vent Pipe Installation	5 days	Thu 8/31/17	Mon 9/4/17	121SS															
123	Pour Foundation Slab	0 days	Mon 9/4/17	Mon 9/4/17	122															
124																				
125	Building 10 (Schedule TBD Following Start of Building 7 Construction)	210 days	Sat 9/30/17	Fri 4/27/18	117SS+60 days															
126																				
127	Building 9 (Schedule TBD Following Start of Building 10 Construction)	210 days	Wed 11/29/17	Tue 6/26/18	125SS+60 days															
128																				
129	Building 8 (Schedule TBD Following Start of Building 9 Construction)	210 days	Sun 1/28/18	Sat 8/25/18	127SS+60 days															
130																				
131	Building 11 (Schedule TBD, to Follow Buildings 6, 1, 2, 3, 4 and 5)	210 days	Sun 1/1/17	Sat 7/29/17																
132																				
133	Building A Podium Construction (~20 months)	470 days?	Mon 1/9/17	Sun 10/28/18																
134	Shoring and Excavation	47 days	Mon 1/9/17	Fri 2/24/17																
135	Foundation (~6-7 months)	210 days	Wed 3/8/17	Tue 10/3/17	134															
136	Excavate Elevator Pits	6 days	Wed 4/5/17	Mon 4/10/17																
137	Elevator Pit Vapor Barrier Installation	4 days	Tue 4/11/17	Fri 4/14/17	136															
138	CQA of Elevator Pit Vapor Barrier Installation	4 days	Tue 4/11/17	Fri 4/14/17	137SS															
139	Framing (~13-14 months) thru Temp. Certificate of Occupancy	390 days	Wed 10/4/17	Sun 10/28/18	135															
140	VMS Construction Completion Report	67 days?	Fri 6/30/17	Mon 10/2/17																
141	Submit Draft to ACDEH (GeoTracker upload)	0 days	Fri 6/30/17	Fri 6/30/17																
142	ACDEH Review (60 days)	60 days?	Fri 6/30/17	Mon 8/28/17	141															
143	Revisions to Draft	15 days	Tue 8/29/17	Mon 9/18/17	142															
144	Resubmittal to ACDEH	0 days	Mon 9/18/17	Mon 9/18/17	143															

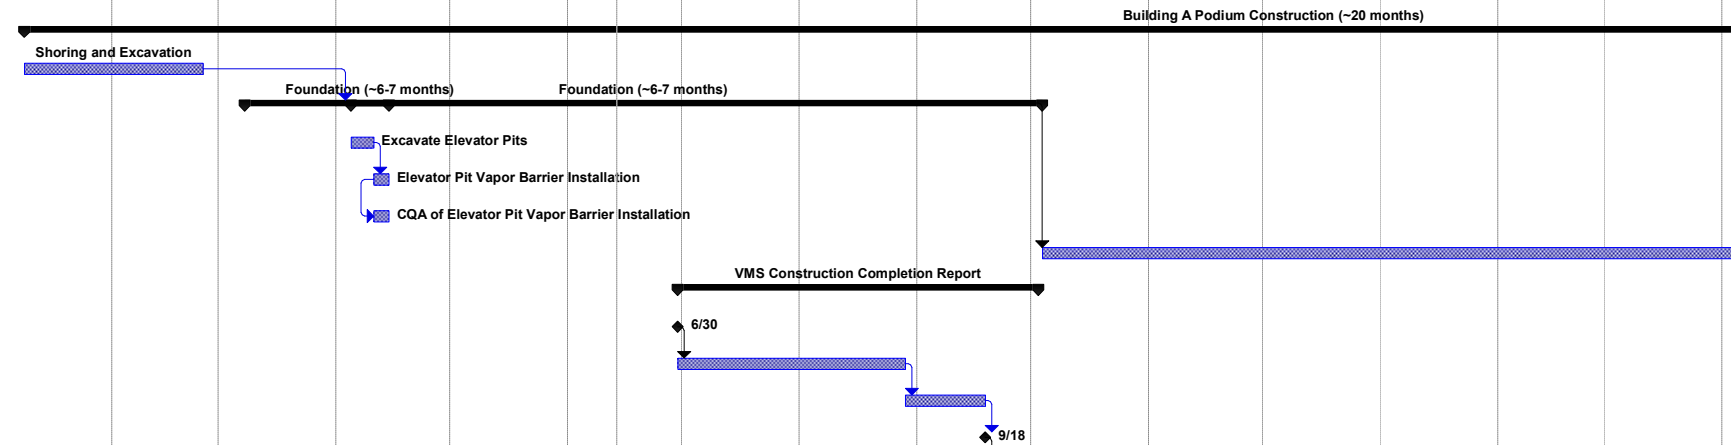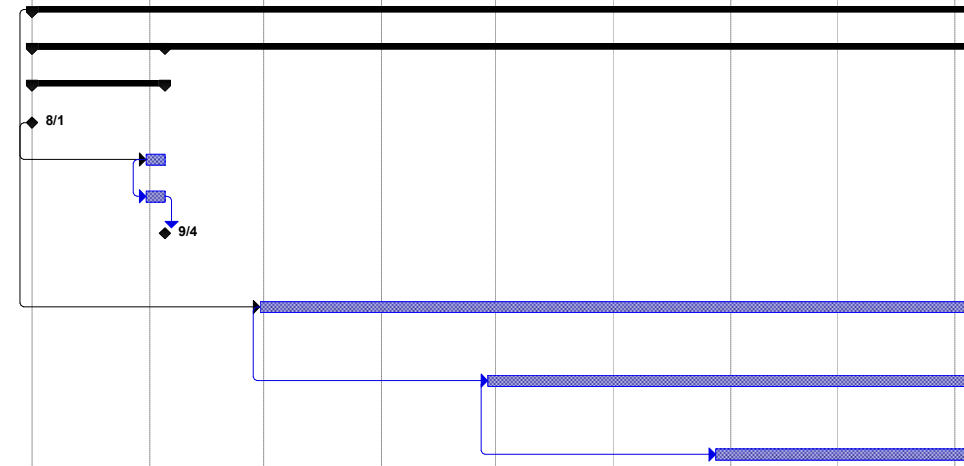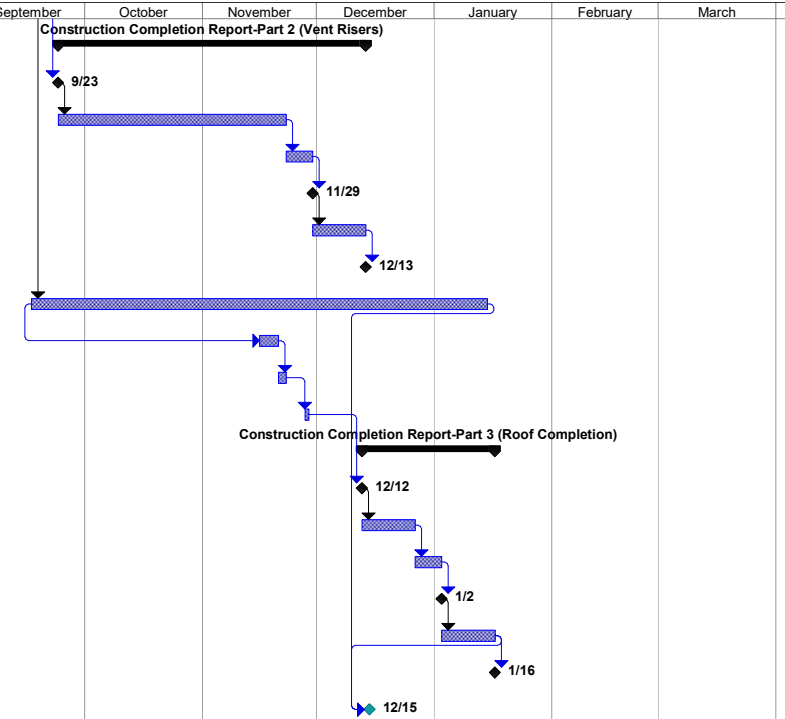

Project: State Street
Date: Wed 6/14/17

Task		Summary		External Milestone		Manual Task		Manual Summary		External Tasks		Deadline	
Split		Project Summary		Inactive Milestone		Duration-only		Start-only		External Milestone			
Milestone		External Tasks		Inactive Summary		Manual Summary Rollup		Finish-only		Progress			

Page 3

ID	Task Name	Duration	Start	Finish	Predecessors	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March
145	ACDEH Review of Revised Draft (2 weeks)	14 days?	Tue 9/19/17	Mon 10/2/17 144																
146	ACDEH Approval	0 days	Mon 10/2/17	Mon 10/2/17 145	145															
147	Building Ready for Occupancy	0 days	Sun 10/28/18	Sun 10/28/18 139,146																



Project: State Street
Date: Wed 6/14/17

Task	Summary	External Milestone	Manual Task	Manual Summary	External Tasks	Deadline
Split	Project Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	
Milestone	External Tasks	Inactive Summary	Manual Summary Rollup	Finish-only	Progress	
