



### EXPLANATION

- SS-6 ▲ Subslab Soil Gas Probe Location
- CSV-1 ✱ Former Crawl Space Gas Probe Location
- SG-1 ▲ Soil Gas Probe Location
- Air Flow Direction in 2" Diameter PVC Pipe
- ⇨ Subslab Air Flow Illustration
- ▬ 4' Diameter Slotted PVC for Air Inlet or Extraction
- 730 PCE Concentration in Subslab Gas ( $\mu\text{g}/\text{m}^3$ ), July 2-3, 2013 (unless otherwise noted)
- 10,000 PCE Isoconcentration Contour in Subslab Gas ( $\mu\text{g}/\text{m}^3$ )
- 210 (ESL) Environmental Screening Level for Residential Land Use Established by SFRWQCB is  $210 \mu\text{g}/\text{m}^3$


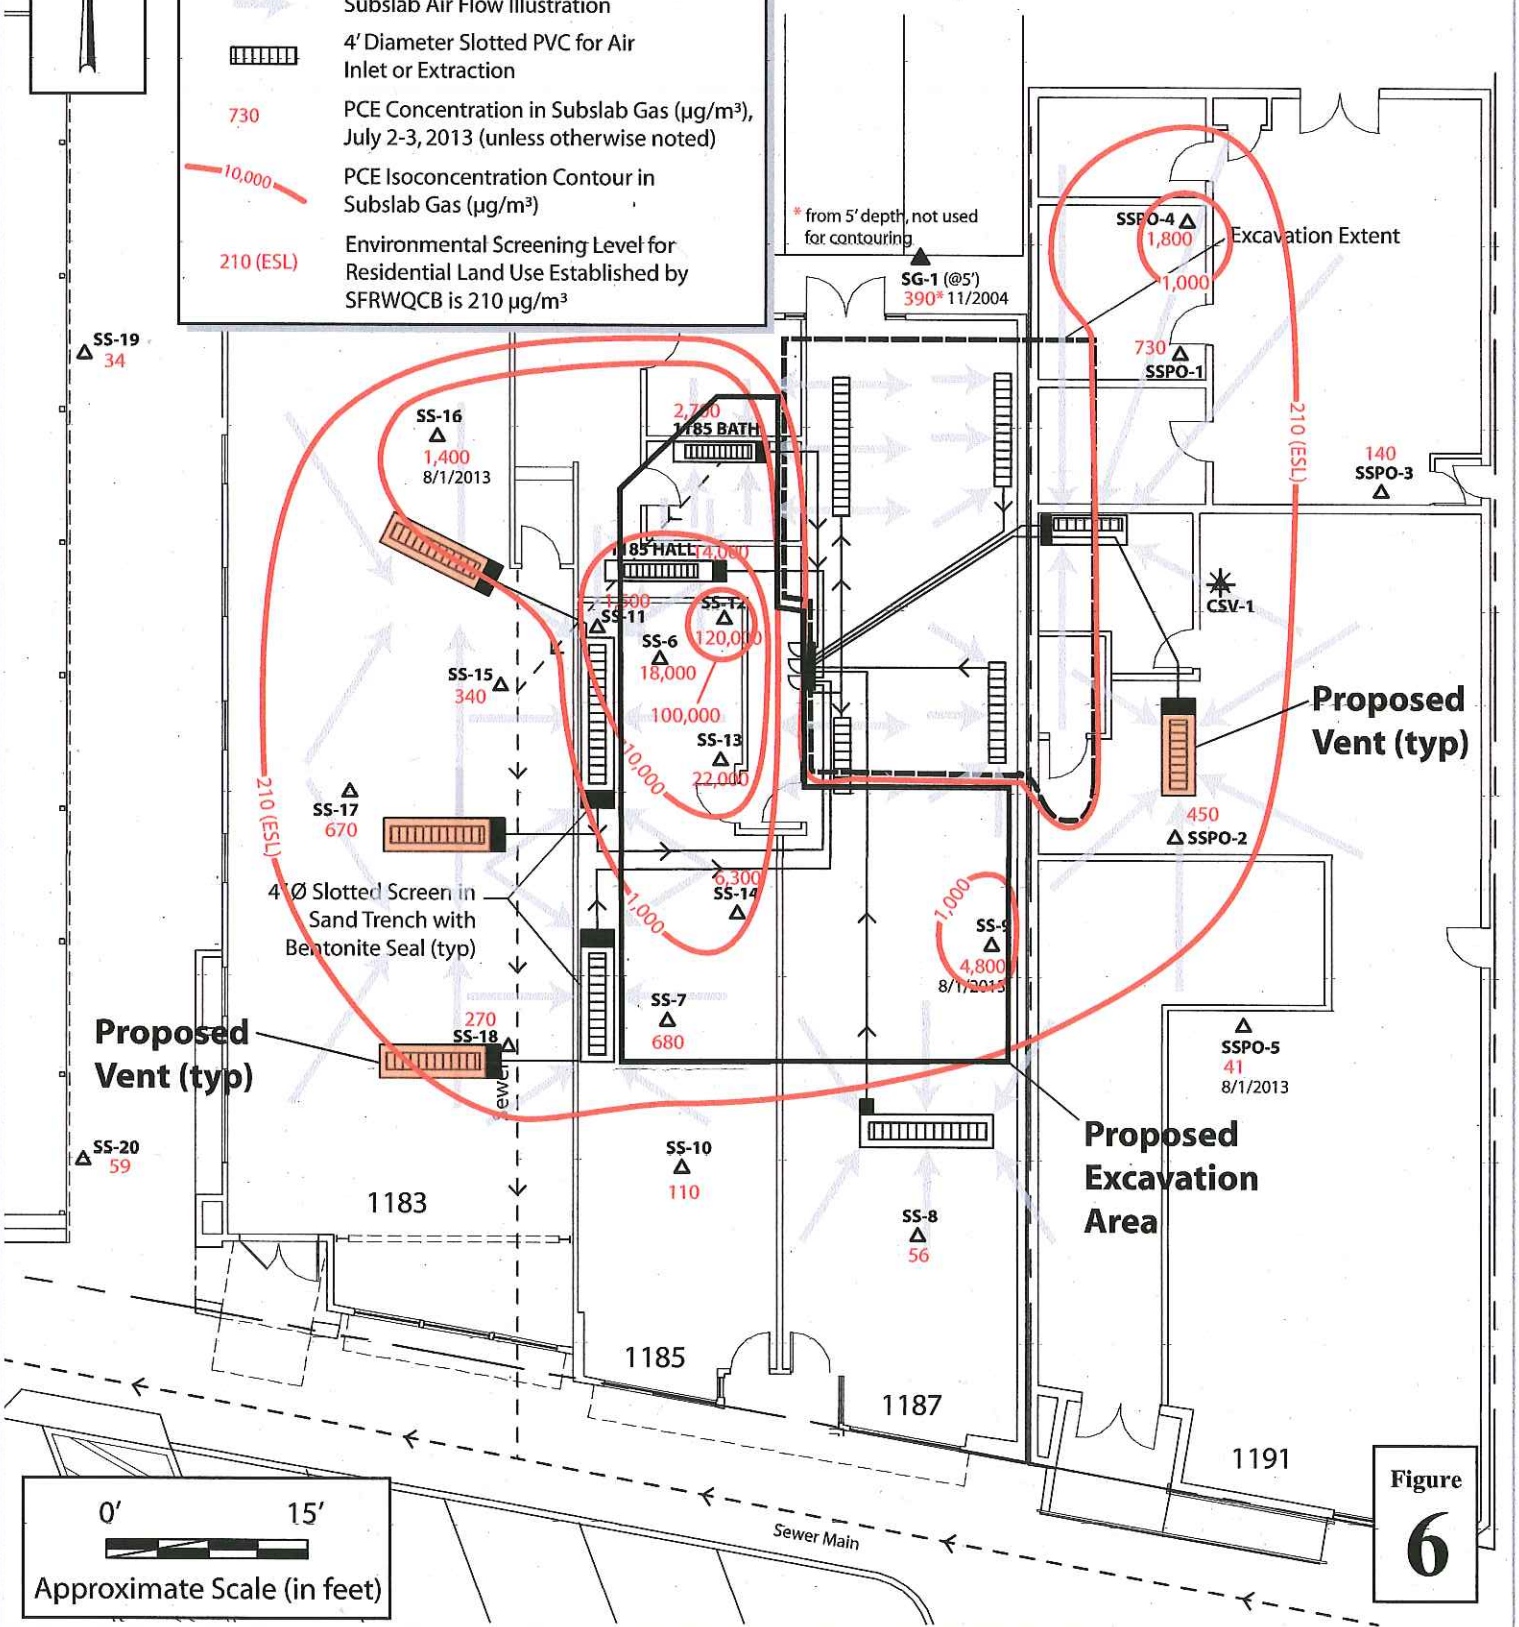


Figure  
**6**



1187 Solano Avenue, Albany (Former Albany 1-Hr Cleaners)

	Task	Comments	Start	End	Dur	2013					2014									
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
	<b>SOLANO INVESTIGATION AND CLEANUP</b>		8/5/13	10/1/14	292															
1	<b>INTERIM REMEDIATION</b>		8/5/13	9/24/13	36															
1.1	Excavate at 1185-1187	Final Soil Excavation	8/5/13	8/30/13	20															
1.2	Vent Pipe Install at 1183-1187		8/26/13	9/1/13	5															
1.3	Test Vent Pipe at 1183-1187		9/1/13	9/2/13																
1.4	Final Backfill and Compaction		9/1/13	9/5/13	3															
1.5	Preliminary Indoor Air Test 1185-1187		9/5/13	9/5/13	1															
1.6	Preliminary Plumbing for Tenant 1185-1187		9/6/13	9/10/13	3															
1.7	Slab Installation	Thin or Thick Slab?	9/10/13	9/12/13	3															
1.8	Vent Pipe Install at 1191		9/13/13	9/18/13	4															
1.9	Test Vent Pipe at 1191		9/19/13	9/24/13	4															
2	<b>INDOOR AIR TESTING</b>		8/30/13	11/4/13	45															
2.1	Workplan to ACEH		8/30/13	8/30/13	1															
2.2	Blow-down Tests		9/16/13	9/20/13	5															
2.3	GeoSeal Slab Penetrations at 1183-1191	Dentist Vacation	9/16/13	9/20/13	5															
2.4	Collect Air Samples 1181-1191	With HVAC. Without Venting.	9/25/13	9/25/13	1															
2.5	Collect Air Samples with Venting???	Test w/venting, if needed	9/26/13	10/7/13	8															
2.6	Air Sampling Report to ACEH		10/3/13	10/3/13	1															
2.7	ACEH Sample Report Review		10/4/13	11/4/13	21															
2.8	ACEH Response/Comfort Letter	Key Milestone	11/4/13	11/4/13	1															
3	<b>REPORTING</b>		9/24/13	1/14/14	76															
3.1	SWI/SCM/Interim Remediation Report		9/24/13	9/24/13	1															
3.2	FS/CAP		9/24/13	9/24/13	1															
3.3	ACEH Report Review		9/25/13	11/25/13	42															
3.4	ACEH Intent to Approve CAP/Comfort Letter		11/25/13	11/25/13	1															
3.5	30-Day Public Notice for CAP Approval		11/25/13	12/27/13	23															
3.6	ACEH CAP Approval after Comment Period		1/14/14	1/14/14	1															
4	<b>GEOSEAL SLAB TOP (after tenant plumbing)</b>		12/15/13	12/18/13	3															
5	<b>VENTILATION SYSTEM</b>		10/1/13	9/6/14	234															
5.1	Prepare Permit for BAAQMD		10/1/13	10/14/13	9															
5.2	BAAQMD Permit Review		10/15/13	12/13/13	42															
5.3	Permit Approval		12/14/13	12/16/13	1															
5.4	Install Equipment on Roof		12/22/13	12/30/13	5															
5.5	Startup Testing		1/2/14	1/8/14	5															
5.6	Operation & Maintenance (O&M) and Reporting		1/8/14	9/6/14	168															
5.7	Subslab Gas Monitoring (As needed)		1/8/14	9/6/14	168															
6	<b>GROUNDWATER MONITORING</b>		8/5/13	8/5/14	252															
7	<b>CASE CLOSURE</b>	When reach subslab gas goal?	10/1/14	10/1/14	1															
