


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Text1	Gantt Chart (2019-2021)																											
1	VMS Design & Approval	42 days	Wed 9/5/18	Thu 11/1/18				VMS Design & Approval																											
2	ACDEH Confirmation of VMS for Bldgs 12,17,18	1 day	Wed 9/5/18	Wed 9/5/18		ACDEH	Confirmed in mtg on 9/5/2018.	ACDEH Confirmation of VMS for Bldgs 12,17,18																											
3	ACDEH Distributes VMS Design Checklist	1 day	Thu 9/6/18	Thu 9/6/18	2	ACDEH		ACDEH Distributes VMS Design Checklist																											
4	GeoKinetics Prepare Design	10 days	Fri 9/7/18	Thu 9/20/18	3			GeoKinetics Prepare Design																											
5	ACDEH Review of VMS Design	10 days	Fri 9/21/18	Thu 10/4/18	4	ACDEH		ACDEH Review of VMS Design																											
6	Oakland Review of VMS Design	20 days	Fri 10/5/18	Thu 11/1/18	5			Oakland Review of VMS Design																											
7	Community Outreach	1 day	Thu 9/13/18	Thu 9/13/18				Community Outreach																											
8	Prescott Neighborhood Meeting	1 day	Thu 9/13/18	Thu 9/13/18				Prescott Neighborhood Meeting																											
9	Land Development & Foundation Construction	192 days	Wed 9/12/18	Thu 6/6/19				Land Development & Foundation Construction																											
10	Parcel B	149 days	Wed 9/12/18	Mon 4/8/19				Parcel B																											
11	Pad Grade & Rough A+B	15 days	Wed 9/12/18	Tue 10/2/18				Pad Grade & Rough A+B																											
12	Import Soil for Landscape Areas B only	3 days	Wed 9/19/18	Fri 9/21/18	11SS+5 days		West to inspect and document.	Import Soil for Landscape Areas B only																											
13	ACDEH Review of Import Soil for Landscape B	5 days	Wed 9/12/18	Tue 9/18/18	12FS-8 days	ACDEH		ACDEH Review of Import Soil for Landscape B																											
14	Notify ACDEH of Landscape Soil Placement B	1 day	Fri 9/14/18	Fri 9/14/18	12FS-6 days	ACDEH		Notify ACDEH of Landscape Soil Placement B																											
15	Pier Sets B	20 days	Wed 10/3/18	Tue 10/30/18	11			Pier Sets B																											
16	Pad Cleans	5 days	Wed 10/31/18	Tue 11/6/18	15			Pad Cleans																											
17	Plumbing Trenching Per Building	10 days	Wed 11/7/18	Tue 11/20/18	16			Plumbing Trenching Per Building																											
18	Bldg 12 Sub-Slab	15 days	Wed 11/7/18	Tue 11/27/18				Bldg 12 Sub-Slab																											
24	Bldg 17 Sub-Slab	15 days	Tue 11/20/18	Mon 12/10/18				Bldg 17 Sub-Slab																											
30	Bldg 18 Sub-Slab	15 days	Mon 12/3/18	Fri 12/21/18				Bldg 18 Sub-Slab																											
36	Pour Foundations 1 Building per week	1 day	Wed 12/12/18	Wed 12/12/18	40SS+15 days			Pour Foundations 1 Building per week																											
37	Pour 12	1 day	Thu 12/27/18	Thu 12/27/18	36FS+10 days			Pour 12																											

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Text1	Gantt Chart (2019-2021)																											
38	Pour 17	1 day	Fri 1/4/19	Fri 1/4/19	37FS+5 days			Gantt Chart showing Pour 17 on Jan 4, 2019.																											
39	Pour 18	1 day	Mon 1/14/19	Mon 1/14/19	38FS+5 days			Gantt Chart showing Pour 18 on Jan 14, 2019.																											
40	Foundations B	20 days	Wed 11/21/18	Tue 12/18/18	17			Gantt Chart showing Foundations B from Nov 21, 2018 to Dec 18, 2018.																											
41	Sewer B	15 days	Wed 10/31/18	Tue 11/20/18	15			Gantt Chart showing Sewer B from Oct 31, 2018 to Nov 20, 2018.																											
42	Storm B	12 days	Wed 11/21/18	Thu 12/6/18	41			Gantt Chart showing Storm B from Nov 21, 2018 to Dec 6, 2018.																											
43	Water B	10 days	Fri 12/7/18	Thu 12/20/18	42			Gantt Chart showing Water B from Dec 7, 2018 to Dec 20, 2018.																											
44	Joint Trench B	15 days	Fri 12/21/18	Thu 1/10/19	43			Gantt Chart showing Joint Trench B from Dec 21, 2018 to Jan 10, 2019.																											
45	Fine Grade B	5 days	Fri 1/11/19	Thu 1/17/19	44			Gantt Chart showing Fine Grade B from Jan 11, 2019 to Jan 17, 2019.																											
46	Haul Off B	2 days	Fri 1/18/19	Mon 1/21/19	45			Gantt Chart showing Haul Off B from Jan 18, 2019 to Jan 21, 2019.																											
47	90% Rock B	5 days	Tue 1/22/19	Mon 1/28/19	46			Gantt Chart showing 90% Rock B from Jan 22, 2019 to Jan 28, 2019.																											
48	Civil Concrete B	15 days	Tue 1/29/19	Mon 2/18/19	47			Gantt Chart showing Civil Concrete B from Jan 29, 2019 to Feb 18, 2019.																											
49	Final Rock B	3 days	Tue 2/19/19	Thu 2/21/19	48			Gantt Chart showing Final Rock B from Feb 19, 2019 to Feb 21, 2019.																											
50	Pave B	2 days	Fri 2/22/19	Mon 2/25/19	49			Gantt Chart showing Pave B from Feb 22, 2019 to Feb 25, 2019.																											
51	Raise Iron B	4 days	Tue 2/26/19	Fri 3/1/19	50			Gantt Chart showing Raise Iron B from Feb 26, 2019 to Mar 1, 2019.																											
52	Signage and Stripe B	5 days	Fri 3/1/19	Thu 3/7/19	50FF+8 days			Gantt Chart showing Signage and Stripe B from Mar 1, 2019 to Mar 7, 2019.																											
53	Landscapes B	30 days	Tue 2/26/19	Mon 4/8/19	50			Gantt Chart showing Landscapes B from Feb 26, 2019 to Apr 8, 2019.																											
54	<b>Parcel A</b>	<b>142 days</b>	<b>Wed 11/21/18</b>	<b>Thu 6/6/19</b>				Gantt Chart showing Parcel A from Nov 21, 2018 to Jun 6, 2019.																											
55	Pads A	15 days	Wed 12/5/18	Tue 12/25/18	40FS-10 days			Gantt Chart showing Pads A from Dec 5, 2018 to Dec 25, 2018.																											
56	Import Soil for Landscape Areas	3 days	Mon 12/10/18	Wed 12/12/18	55SS+3 days		West to inspect and document.	Gantt Chart showing Import Soil for Landscape Areas from Dec 10, 2018 to Dec 12, 2018.																											
57	ACDEH Review of Import Soil for Landscape A	5 days	Mon 12/3/18	Fri 12/7/18	56FS-8 days	ACDEH		Gantt Chart showing ACDEH Review of Import Soil for Landscape A from Dec 3, 2018 to Dec 7, 2018.																											
58	Notify ACDEH of Landscape Soil Placement A	1 day	Wed 12/5/18	Wed 12/5/18	56FS-6 days	ACDEH		Gantt Chart showing Notify ACDEH of Landscape Soil Placement A on Dec 5, 2018.																											
59	Pier Sets A	20 days	Wed 12/26/18	Tue 1/22/19	55			Gantt Chart showing Pier Sets A from Dec 26, 2018 to Jan 22, 2019.																											

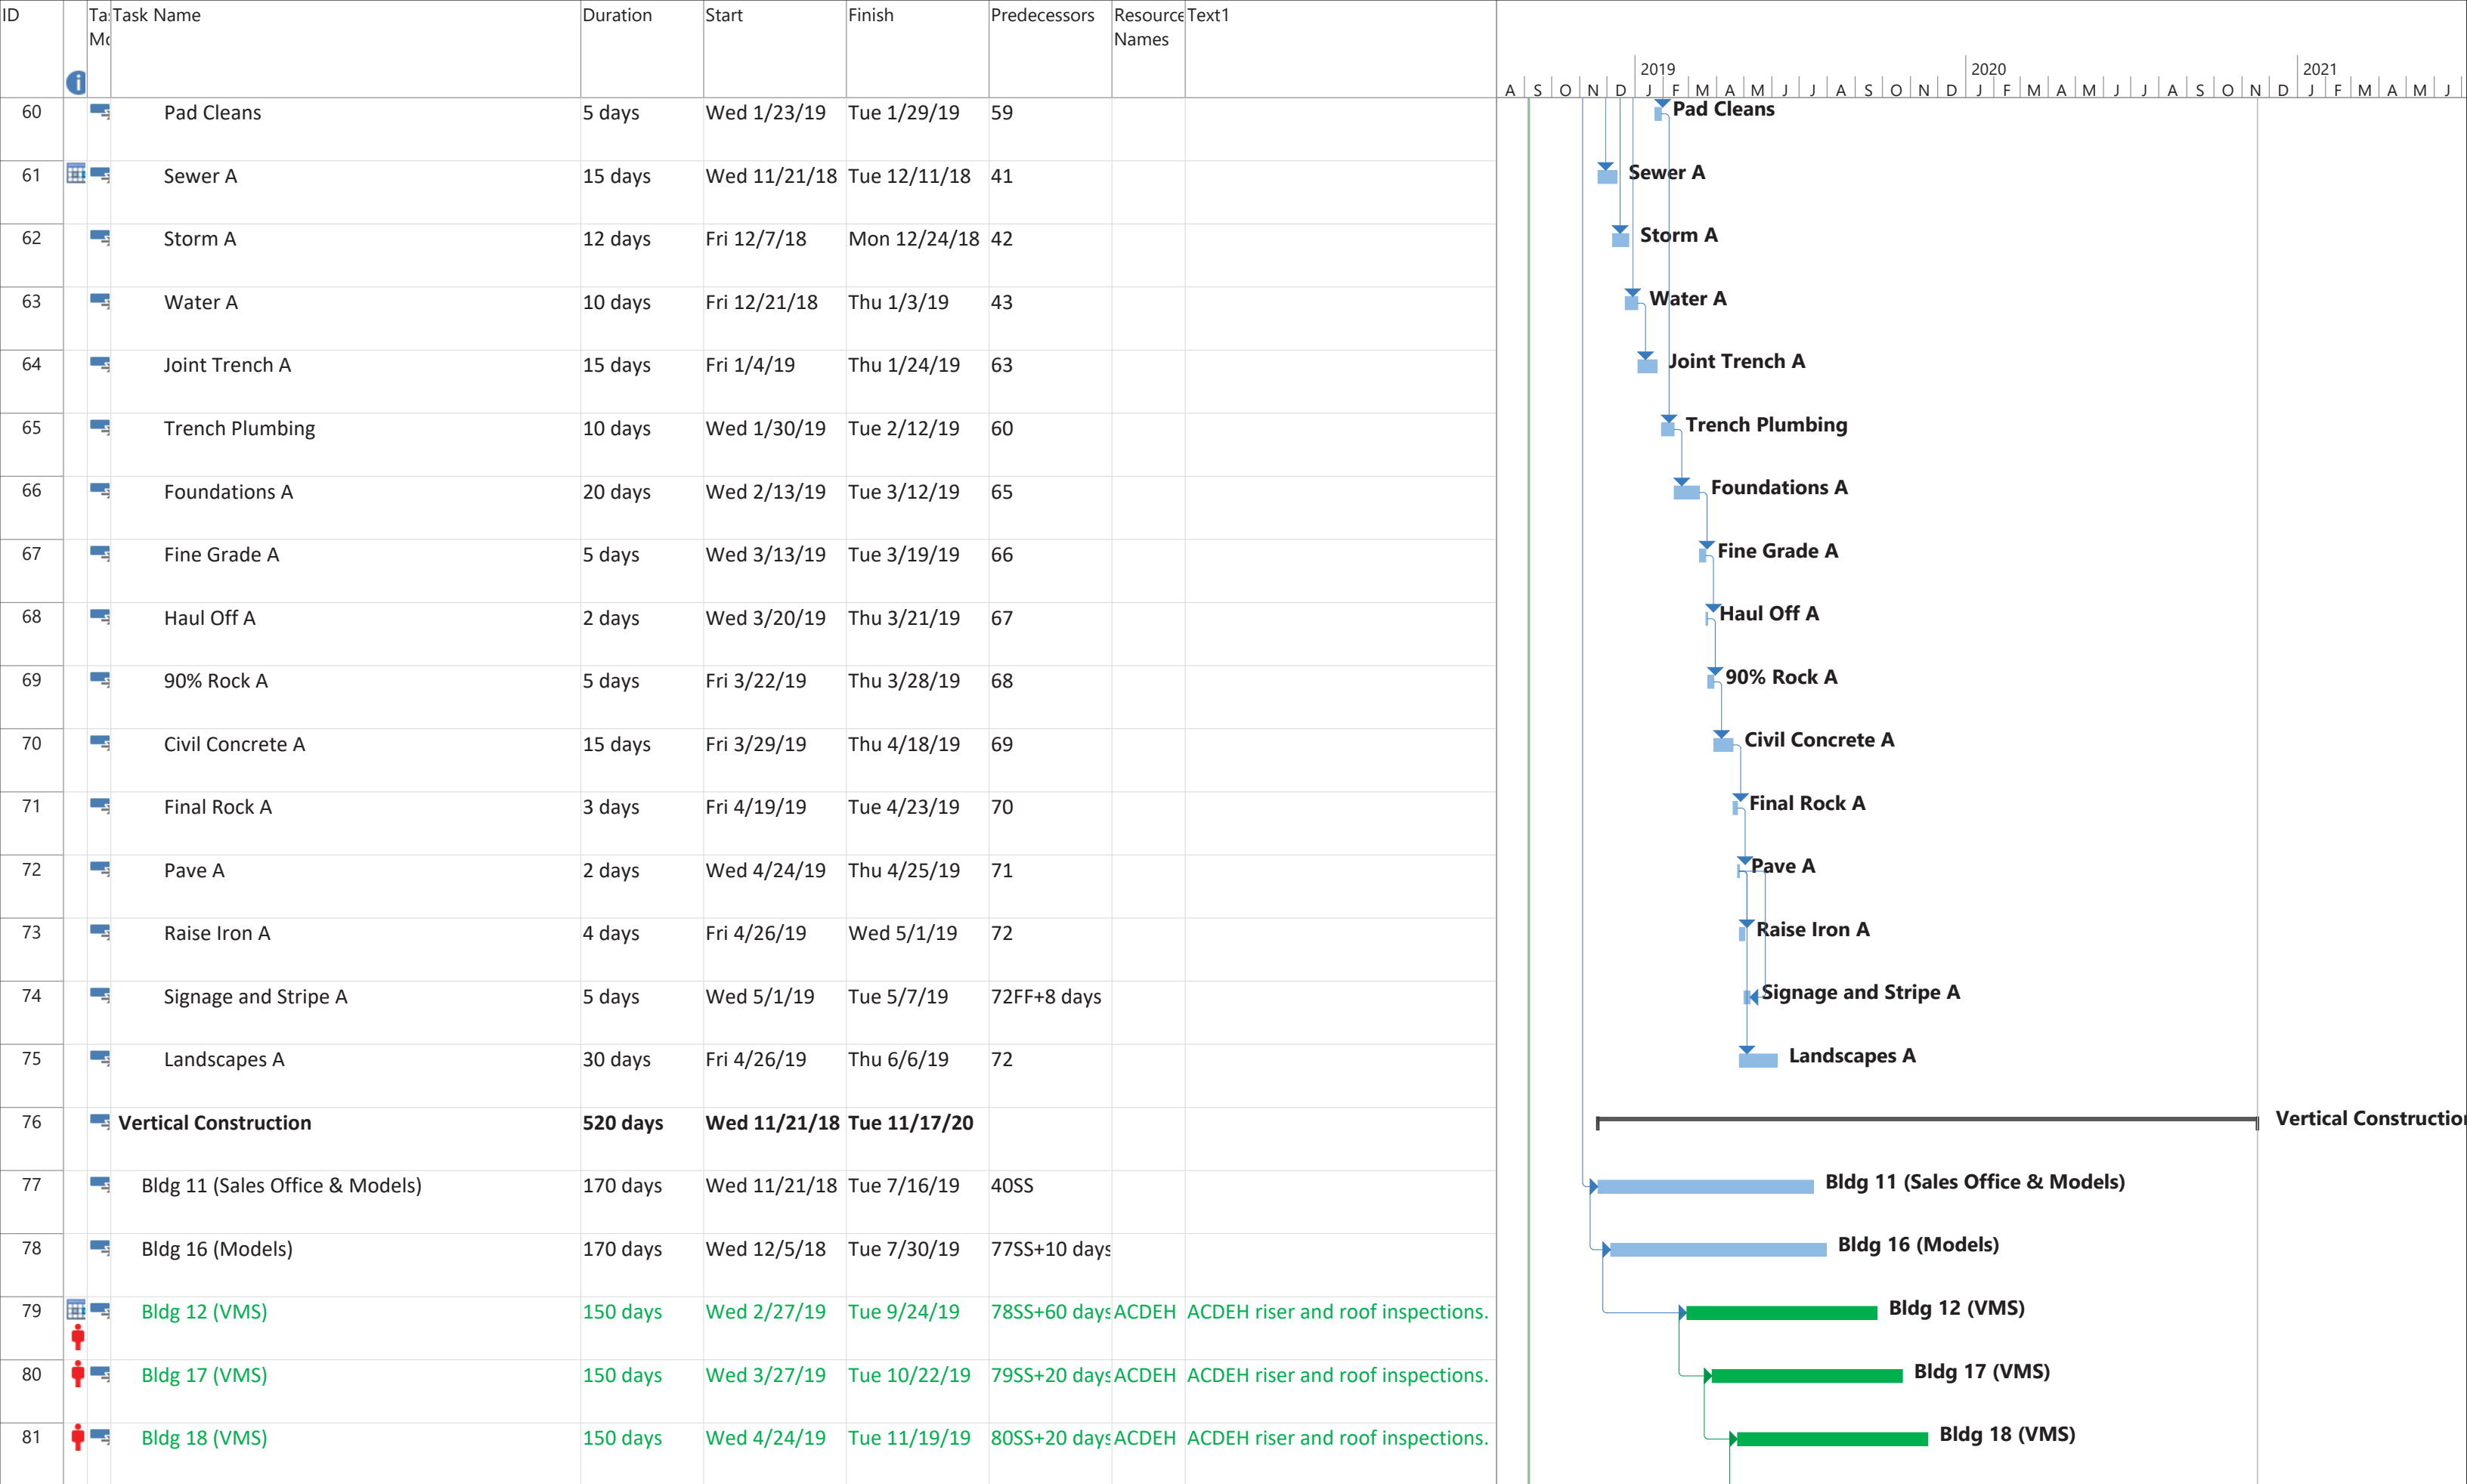

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Text1	Gantt Chart (2019-2021)																											
82	Bldg 13	150 days	Wed 5/22/19	Tue 12/17/19	81SS+20 days			[Gantt bar for Bldg 13: 5/22/19 to 12/17/19]																											
83	Bldg 14	150 days	Wed 6/19/19	Tue 1/14/20	82SS+20 days			[Gantt bar for Bldg 14: 6/19/19 to 1/14/20]																											
84	Bldg 15	150 days	Wed 7/17/19	Tue 2/11/20	83SS+20 days			[Gantt bar for Bldg 15: 7/17/19 to 2/11/20]																											
85	Bldg 10	150 days	Wed 8/14/19	Tue 3/10/20	84SS+20 days			[Gantt bar for Bldg 10: 8/14/19 to 3/10/20]																											
86	Bldg 1	150 days	Wed 9/11/19	Tue 4/7/20	85SS+20 days			[Gantt bar for Bldg 1: 9/11/19 to 4/7/20]																											
87	Bldg 6	150 days	Wed 10/9/19	Tue 5/5/20	86SS+20 days			[Gantt bar for Bldg 6: 10/9/19 to 5/5/20]																											
88	Bldg 2	150 days	Wed 11/6/19	Tue 6/2/20	87SS+20 days			[Gantt bar for Bldg 2: 11/6/19 to 6/2/20]																											
89	Bldg 7	150 days	Wed 12/4/19	Tue 6/30/20	88SS+20 days			[Gantt bar for Bldg 7: 12/4/19 to 6/30/20]																											
90	Bldg 8	150 days	Wed 1/1/20	Tue 7/28/20	89SS+20 days			[Gantt bar for Bldg 8: 1/1/20 to 7/28/20]																											
91	Bldg 9	150 days	Wed 1/29/20	Tue 8/25/20	90SS+20 days			[Gantt bar for Bldg 9: 1/29/20 to 8/25/20]																											
92	Bldg 3	150 days	Wed 2/26/20	Tue 9/22/20	91SS+20 days			[Gantt bar for Bldg 3: 2/26/20 to 9/22/20]																											
93	Bldg 4	150 days	Wed 3/25/20	Tue 10/20/20	92SS+20 days			[Gantt bar for Bldg 4: 3/25/20 to 10/20/20]																											
94	Bldg 5 (VMS?)	150 days	Wed 4/22/20	Tue 11/17/20	93SS+20 days	ACDEH	VMS requirement TBD.	[Gantt bar for Bldg 5 (VMS?): 4/22/20 to 11/17/20]																											
