5TID 1068

EXXON COMPANY, U.S.A. QUARTERLY SUMMARY REPORT

October - December 1992

Date: December 31, 1992

RAS # 7-0236 6630 East 14th Street Oakland, California Proj. No. 30-0491-01

WORK PERFORMED THIS QUARTER

1. Completed quarterly ground water monitoring and sampling October 13, 1992.

QUARTERLY GROUND WATER SAMPLING RESULTS (ug/L) (SAMPLED 10/13/92)

(6.11.1.2.2.2.2.2.2.2.2.2.2.2.2.2.2.2.2.2										
WELL ID	В	Т	Е	Х	TPH G	TPH D	TOG	HVOC	\$	
MW-1	<0.5	<0.5	<0.5	<0.5	<50	<50	< 5000	ND	-	
MW-2	97	2.6	97	53	3200	1900	< 5000	ND	\	
MW-3	5.5	< 0.5	4.6	1.1	1100	400		ND	1	
MW-4	<0.5	< 0.5	< 0.5	< 0.5	<50	< 80			-	
MW-5	<0.5	< 0.5	< 0.5	< 0.5	69	< 50			-	
MW-6	<0.5	< 0.5	< 0.5	< 0.5	< 50	< 50			-	
MW-7	0.8	<0.5	< 0.5	2.5	670	94			1	

- Recent historical trend
- Concentrations generally increased from recent historical trend
- Concentrations generally decreased from recent historical trend
- Concentrations generally unchanged from recent historical trend
- Not analyzed
- Not detected at or above various detection limits ND

FREE PHASE PRODUCT RECOVERY

Not Applicable

WORK TO BE PERFORMED NEXT QUARTER

Activity

Estimated Completion Date

1. Conduct quarterly fluid-level monitoring and ground water sampling.

March 1993

WORK TO BE PERFORMED NEXT 12 MONTHS

Activity

Estimated Completion Date

1. Submit a proposal for subsurface testing and generation of a feasibility study/remedial work plan.

March 1993

2. Continue quarterly fluid-level monitoring, and ground water sampling.

December 1993

FOR EXXON INTERNAL USE ONLY:

Date Report Submitted:

December 31, 1992

Quarter Ending:

December 1992

Exxon RAS #:

7-0236

Regulatory Agencies Involved:

Agency

Contact

Alameda County Hazardous Materials Division

Britt Johnson

Regional Water Quality Control Board

Eddy So

Contract and Budget Information:

Consultant: Alton Geoscience

Project Manager: John DeGeorge

Project Number: 30-0491-01

Project Phase: Supplemental Site Investigation

Project Start Date: 8/91

Original Budget Authorized:

\$17,050 (Preliminary Site Investigation)

Additional Budgets Approved:

\$20,300 (Supplemental Site Investigation)


\$12,700 (Quarterly Sampling Program)

Total Budget Authorized to Date:

\$50,050

Total Cost Spent to Date:

\$46,000 (approximate)

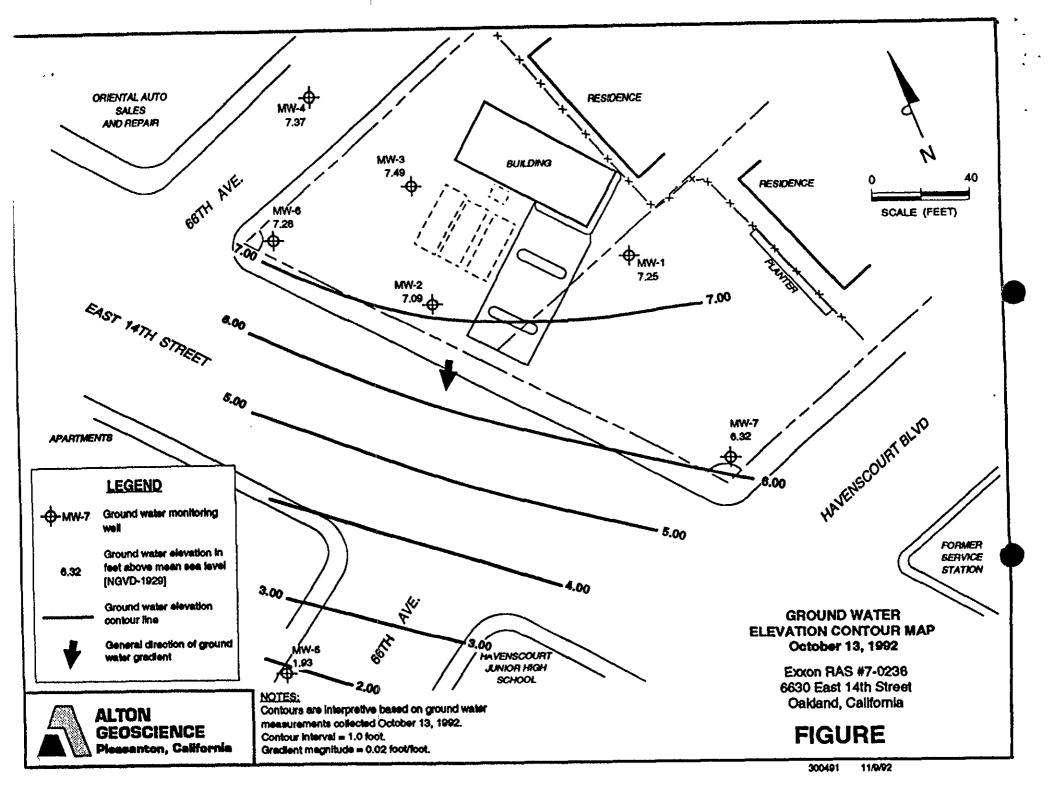

EXXON COMPANY, U.S.A. OUARTERLY SUMMARY REPORT

July - September 1992

Date: October 5, 1992

551068

RAS # 7-0236 6630 East 14th Street Oakland, California Proj. No. 30-0491-01

WORK PERFORMED THIS QUARTER

- 1. Completed quarterly ground water monitoring and sampling July 8, 1992.
- 2. Removed obstruction from monitoring well MW-5 on September 10, 1992.
- 3. Completed and mailed supplemental site investigation report June 17, 1992.

QUARTERLY GROUND WATER SAMPLING RESULTS (ug/L) (SAMPLED 07/08/92)

WELL ID	В	Т	E	X	TPH G	TPH D	TOG	HVOC	+
MW-1	<0.5	< 0.5	<0.5	<0.5	<50	<50	<5000	ND	-
MW-2	250	14	300	160	7000	2100	<5000	ND	1
MW-3	<0.5	2.6	12	3.7	2900	960	<5000	ND	†
MW-4	<0.5	< 0.5	< 0.5	< 0.5	<50	<50			-
MW-5									-
MW-6	<0.5	< 0.5	< 0.5	< 0.5	<50	<50	<5000	ND	-
MW-7	<0.5	<0.5	<0.5	<0.5	<50	< 50			

- Recent historical trend
- † Concentrations generally increased from recent historical trend
- ↓ Concentrations generally decreased from recent historical trend
- Concentrations generally unchanged from recent historical trend
- Not analyzed
- ND Not detected at or above various detection limits

TF

FREE PHASE PRODUCT RECOVERY

Not Applicable

WORK TO BE PERFORMED NEXT QUARTER

Activity

Estimated Completion Date

1. Conduct quarterly fluid-level monitoring and ground water sampling.

October 1992

WORK TO BE PERFORMED NEXT 12 MONTHS

Activity

Estimated Completion Date

1. Submit a proposal for subsurface testing and generation of a feasibility study/remedial work plan.

March 1993

2. Continue quarterly fluid-level monitoring, and ground water sampling.

March 1993
