

R096

Wickham, Jerry, Env. Health

From: Karel Detterman [KDetterman@clearwatergroup.com]
Sent: Friday, October 12, 2007 12:45 PM
To: Wickham, Jerry, Env. Health
Cc: Sandy Young; Hermy Tam; Gavin Fisco; Olivia Jacobs; Rob Nelson; Karel Detterman
Subject: RE: Fuel Leak Case # RO 0096, Eagle Gas, 4301 San Leandro Street, Oakland, CA, Clearwater Project # ZP046D

Hi Jerry:

I wanted to give you a brief update of the drilling events at and off-site from Eagle Gas and also let you that I am leaving the Clearwater Group and joining a firm that does work for the EPA.

Rob Nelson (Ext 237) will be taking over the project as of Monday, Oct. 15th.

Attached is the actual drilling schedule and a revised "Off-site Soil Boring Location" figure. As of today, all of the off-site soil borings are complete as are the installation of the six vapor monitoring wells, and the two deep groundwater monitoring wells, MW-1D & MW-7D. We ran CPT to a total depth of 60 feet bgs in CPT-1D and CPT-7D, located adjacent to new wells MW-1D & MW-7D. With the limited access direct push drilling equipment, we were able to reach a total depth of 34 feet bgs and obtain a groundwater sample at 34 feet in the Vulcan Lofts Courtyard soil boring, SB-12. We were able to reach a depth of 52 feet bgs in SB-13, SB-14, SB-15, and SB-17 and obtain water samples from the deeper water-bearing zone in all four soil borings.

Remediation Services, Inc. (RSI) is scheduled to perform the HVDPE pilot test Wednesday through Sunday, November 14 - 18, 2007.

Thank you for being responsive to Clearwater's questions and suggestions.

Sincerely,


Karel Detterman, P.G.
Clearwater Group
229 Tewksbury Avenue
Point Richmond, CA 94801
(510) 307-9943 Ext. 228
Fax (510) 232-2823

10/12/2007

Drilling Schedule
Sept - Oct, 2007
Eagle Gas Station, 4301 San Leandro St., Oakland


Day	Soil boring or drilling event
Wed 9/19	install VP-1 through VP-6 Eagle Gas Station
Thurs 9/20	SB-14 Creative Iron alley SB-17 YH Sheet Metal driveway start at 5 PM
Fri 9/21	SB-13 Vulcan Lofts alley
Tues 9/25	SB-15 Creative Iron alley
Wed 9/26	SB-12 Vulcan Lofts courtyard
Thurs 9/27	CPT -1D & CPT 7D on site
Thurs 10/4	MW-1D & MW-7D install on site

Note: SB-17, in YH Sheet Metal driveway will be started at 5 PM, when business closes for the day.

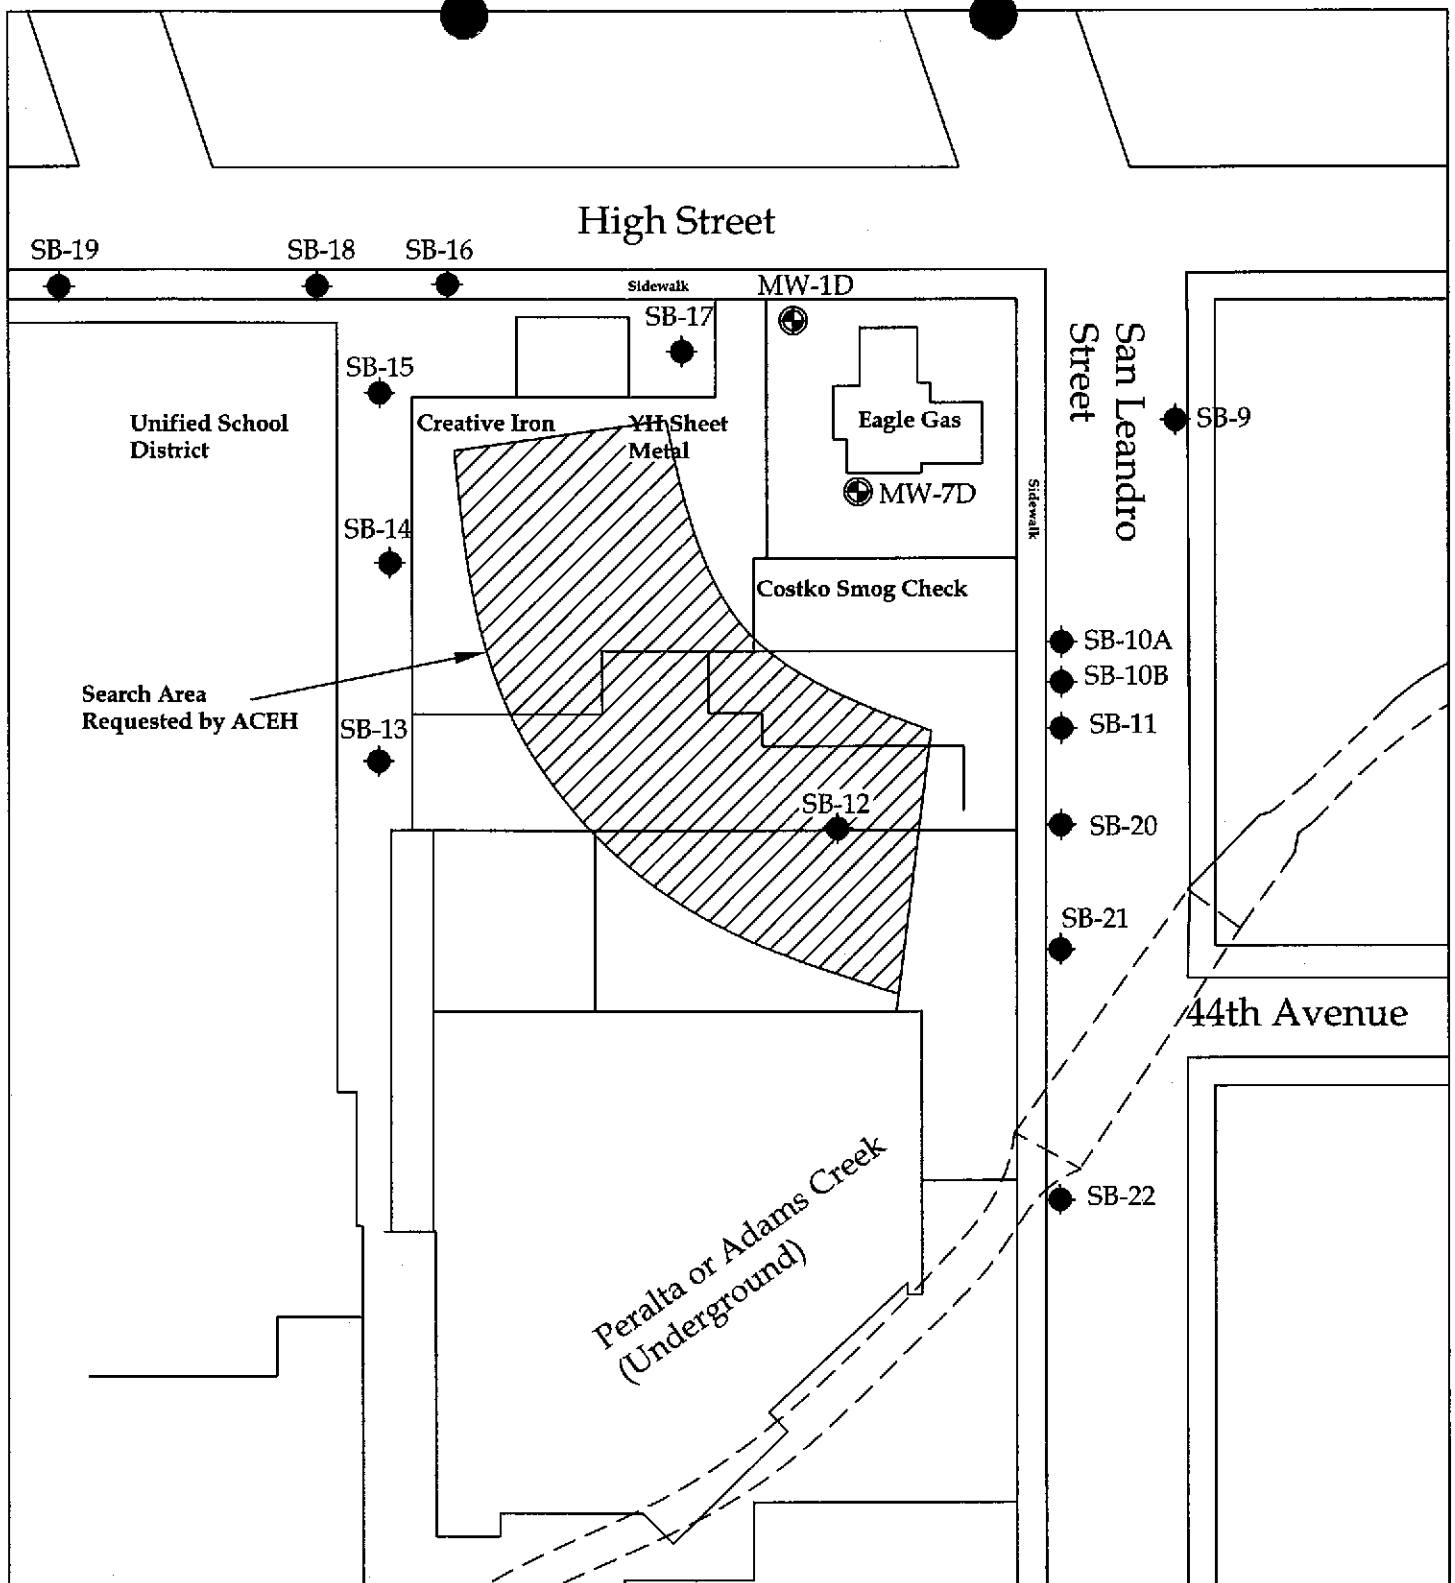

LEGEND

- Soil Boring Location
- ⊕ Deep Well Location



Off-site Soil Boring Locations

Eagle Gas
4301 San Leandro Street
Oakland, California

CLEARWATER GROUP

Project No.
ZP046

Figure Date
10/07

Figure
2b
