

3315 Almaden Expressway, Suite 34
San Jose, CA 95118
Phone: (408) 264-7723
FAX: (408) 264-2435

exxon1293

EXXON COMPANY, U.S.A.
QUARTERLY STATUS REPORT
October - December 1993
December 29, 1993
(Page 1 of 2)

RAS #7-3006
720 High Street
Oakland, California
Job No: 130006

Work Performed During This Quarter

October through December 1993

- o Performed monthly depth-to-water measurements on November 12 and December 20, 1993.
- o Submitted final report for third quarter 1993 Quarterly Monitoring on October 21, 1993.
- o Performed quarterly monitoring and sampling for fourth quarter 1993 on October 26 through 28, 1993.
- o Completed design and permitting of interim groundwater remediation system.
- o Submitted final report for fourth quarter 1993 Quarterly Monitoring to Exxon.
- o Initiated construction of interim groundwater remediation system on December 21, 1993.

Groundwater Sampling (sampled October 26 through 28, 1993) Results: (mg/L)

<u>Well</u>	<u>TPHg</u>	<u>B</u>	<u>T</u>	<u>E</u>	<u>X</u>	<u>TPHd</u>	<u>Trends</u>
MW-1	<0.05	<0.0005	<0.0005	<0.0005	<0.0005	<0.050	Unchanged
MW-2				Sheen			
MW-3				Sheen			
MW-4				Sheen			
MW-5				Well Destroyed			
MW-6				Sheen			
MW-7	2.500	0.090	0.0047	0.0066	0.015	1.0	Decreased
MW-8				Sheen			
MW-9	<0.050	<0.0005	<0.0005	<0.0005	<0.0005	<0.050	Unchanged
MW-10	<0.050	<0.0005	<0.0005	0.0005	<0.0005	<0.050	Decreased
MW-11	<0.050	<0.0005	<0.0005	<0.0005	<0.0005	0.08	Decreased
MW-12	68	11	8.3	3.4	13	17	Decreased
MW-13	46	5.2	3.2	2.5	11	15	Decreased
MW-14	0.260	<0.0005	<0.0005	<0.0005	0.0036	0.20	Increased
MW-15	3.4	0.079	<0.0025	0.115	0.032	0.97	Decreased

exxon1293

EXXON COMPANY, U.S.A.
QUARTERLY STATUS REPORT
October - December 1993
December 29, 1993
(Page 2 of 2)

RAS #7-3006
720 High Street
Oakland, California
Job No: 130006

Free Phase Product Recovery

- o No product was removed from the petrotraps.

Work to be Performed Next Quarter


Estimated Completion Date 03/31/94

- o Perform quarterly monitoring and sampling for the first quarter 1994 on February 2 and 3, 1994.
- o Perform monthly depth-to-water measurements on January 26 and March 16, 1994.
- o Submit final report for first quarter 1994 Quarterly Monitoring to Exxon.
- o Continue construction of interim groundwater remediation system.

Work to be Performed Next 12 Months

Estimated Completion Date 12/31/94

- o Continue quarterly groundwater monitoring and sampling program to evaluate the trends of gasoline and diesel hydrocarbons and groundwater gradient in first encountered groundwater below the site.
- o Begin start-up of interim groundwater remediation system.

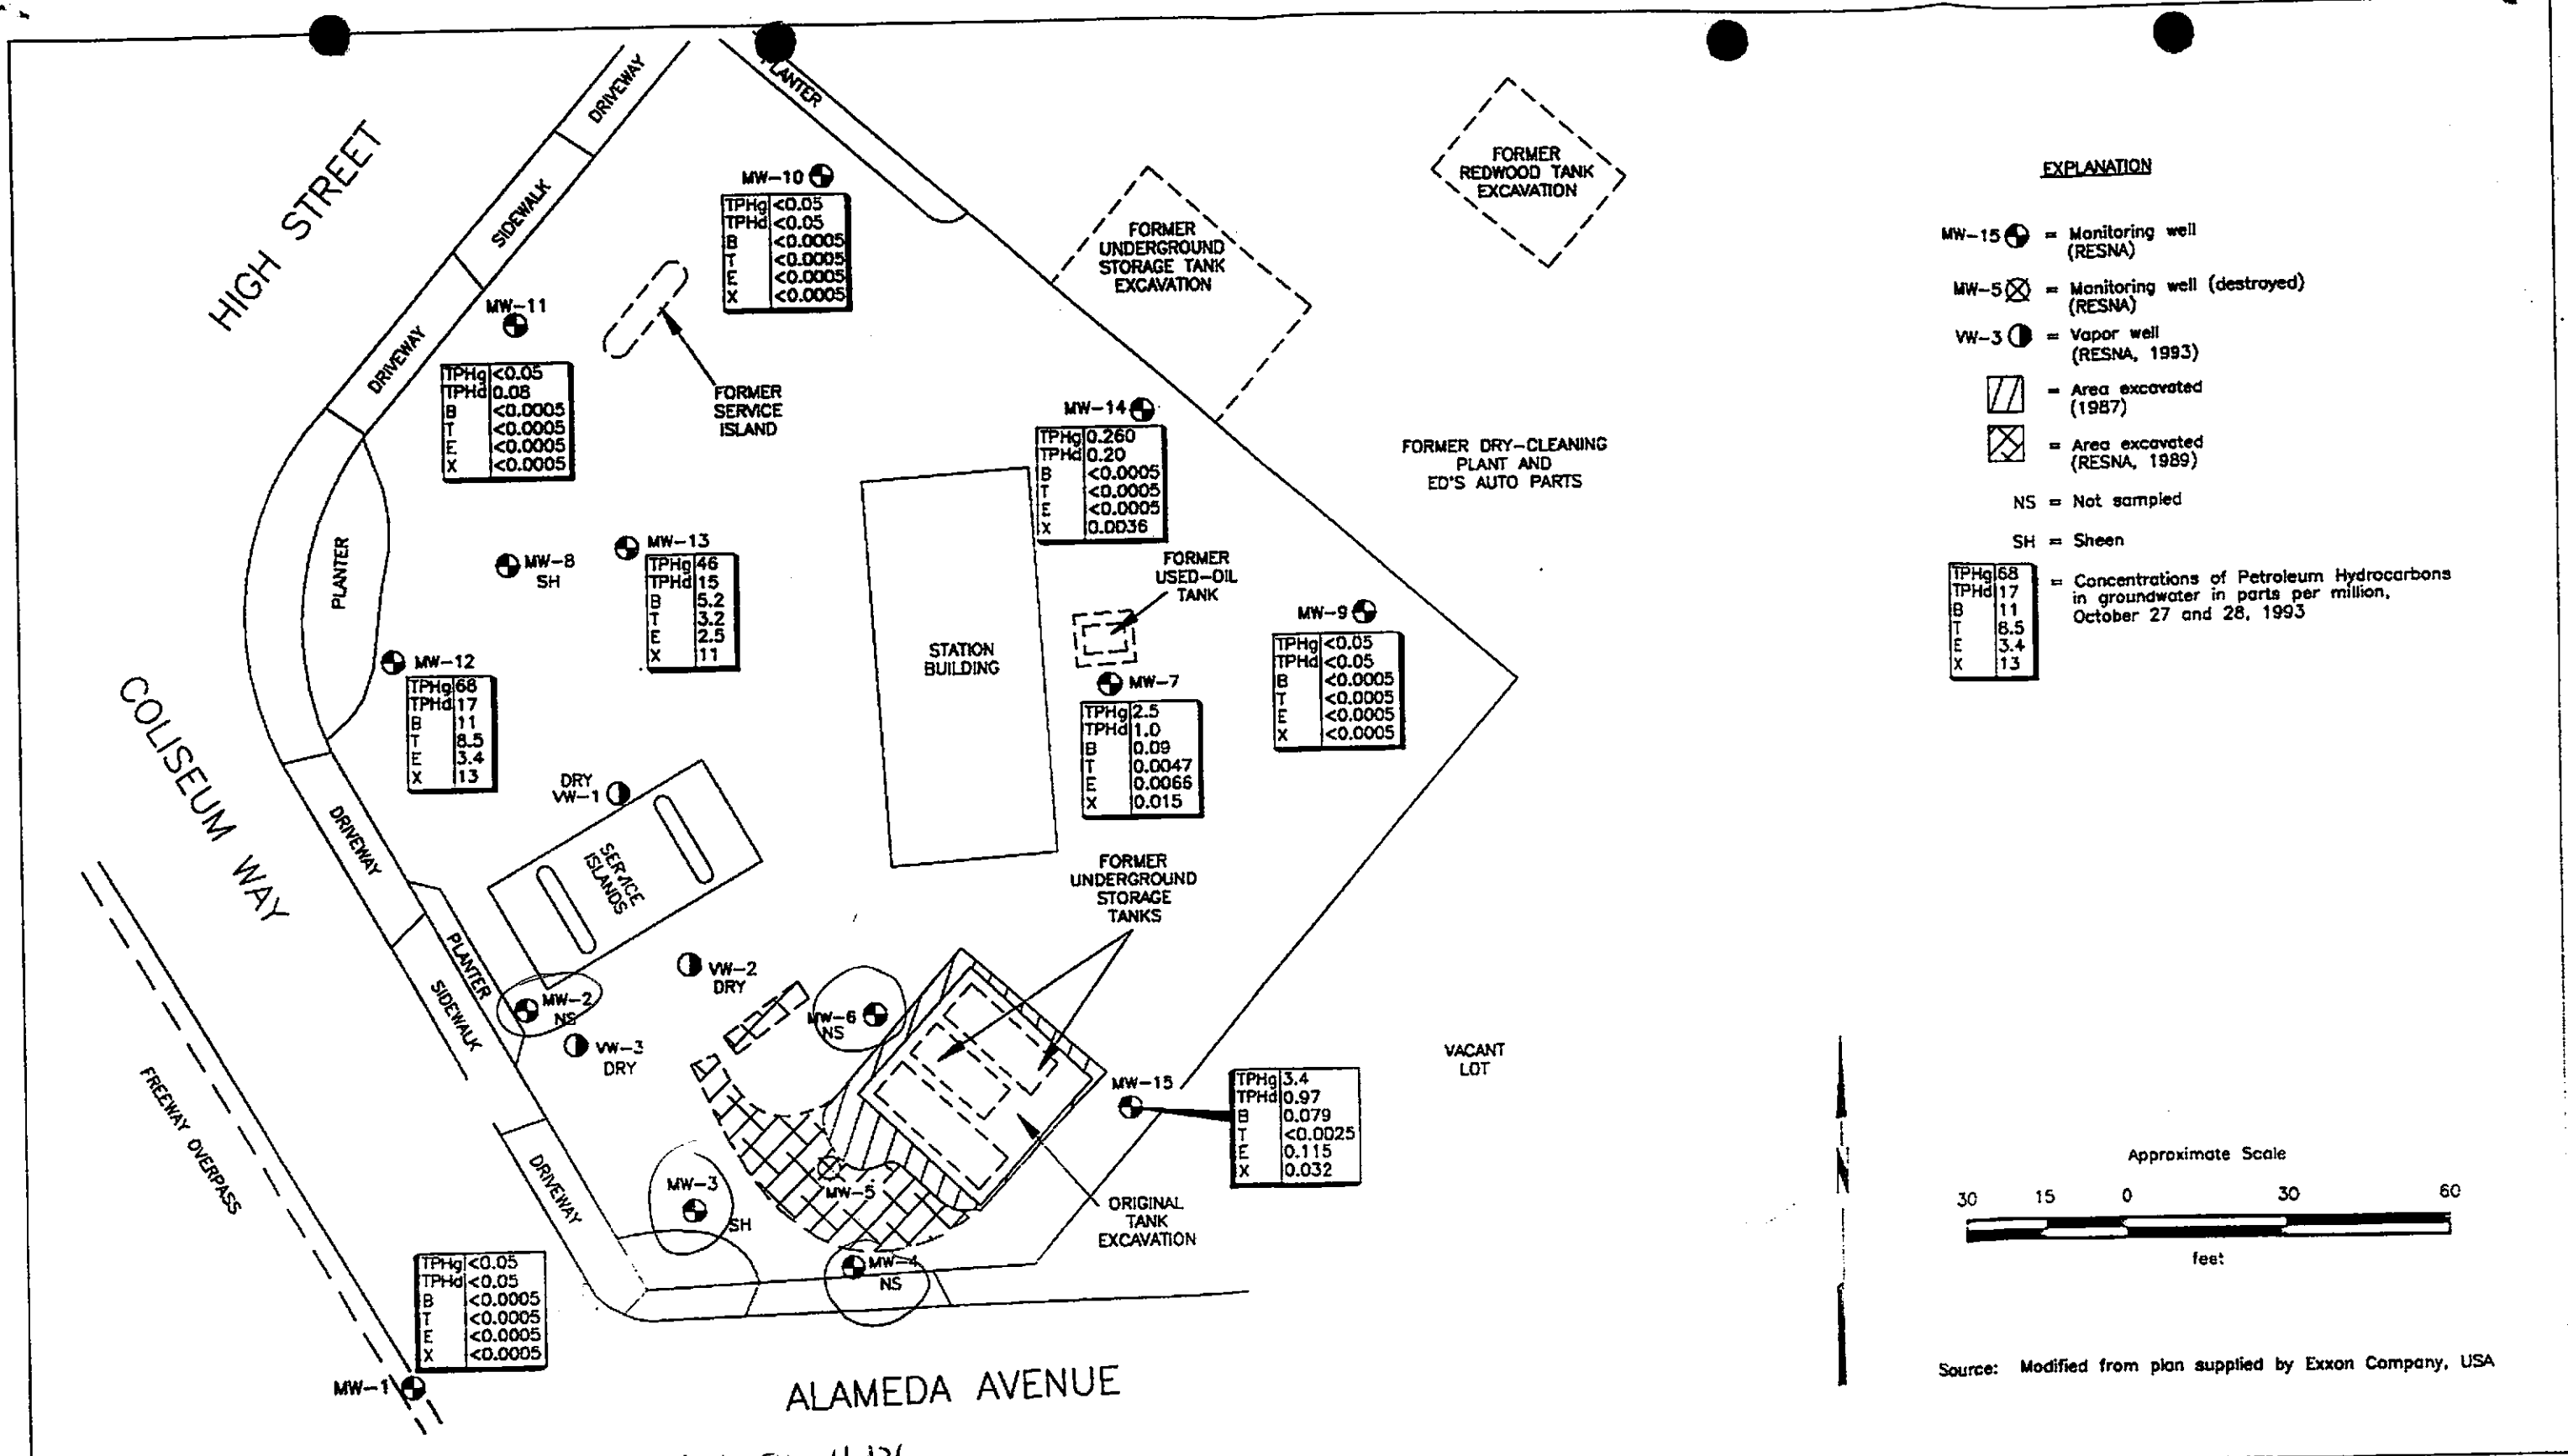

720 High St #136



PROJECT 130006.01

GENERALIZED SITE PLAN
Exxon Station 7-3006
720 High Street
Oakland, California

PLATE
1
