

STID 1062 TP

Exxon Company, U.S.A.
QUARTERLY STATUS REPORT
April - June 1995
Date: July 7, 1995

RAS # 7-0236
6630 East 14th Street
Oakland, California
ERI No. 2009

Work Performed During This Quarter

April through June 1995

- Performed Quarterly Groundwater Monitoring for second quarter 1995 on May 18, 1995 and submitted report to Exxon on June 15, 1995.

Quarterly Groundwater Sampling (05/18/95) Results ($\mu\text{g/L}$)

<u>Well No.</u>	<u>TEPHd</u>	<u>TPHg</u>	<u>B</u>	<u>T</u>	<u>E</u>	<u>X</u>	<u>Historical Trend</u>
MW1	<50	<50	<0.5	<0.5	<0.5	<0.5	Unchanged
MW2	2,000	6,000	180	9.9	220	55	Decreased
MW3	470	1,000	<0.5	<0.5	4.1	0.94	Decreased
MW4	<50	<50	<0.5	<0.5	<0.5	<0.5	Unchanged
MW5	<50	<50	<0.5	4.6	0.65	2.8	Increased
MW6	71	56	<0.5	<0.5	<0.5	<0.5	Unchanged
MW7	<50	<50	<0.5	<0.5	<0.5	<0.5	Decreased

Separate Phase Product Recovery

Not Applicable

Work to be Performed Next Quarter


Estimated Completion Date: 09/30/95

- Perform quarterly groundwater monitoring event for third quarter 1995 and submit report to Exxon.


Work to be Performed Next 12 Months

Estimated Completion Date: 06/30/96

- Continue quarterly groundwater monitoring and sampling program to evaluate the trends of gasoline hydrocarbons and groundwater flow direction and gradient.

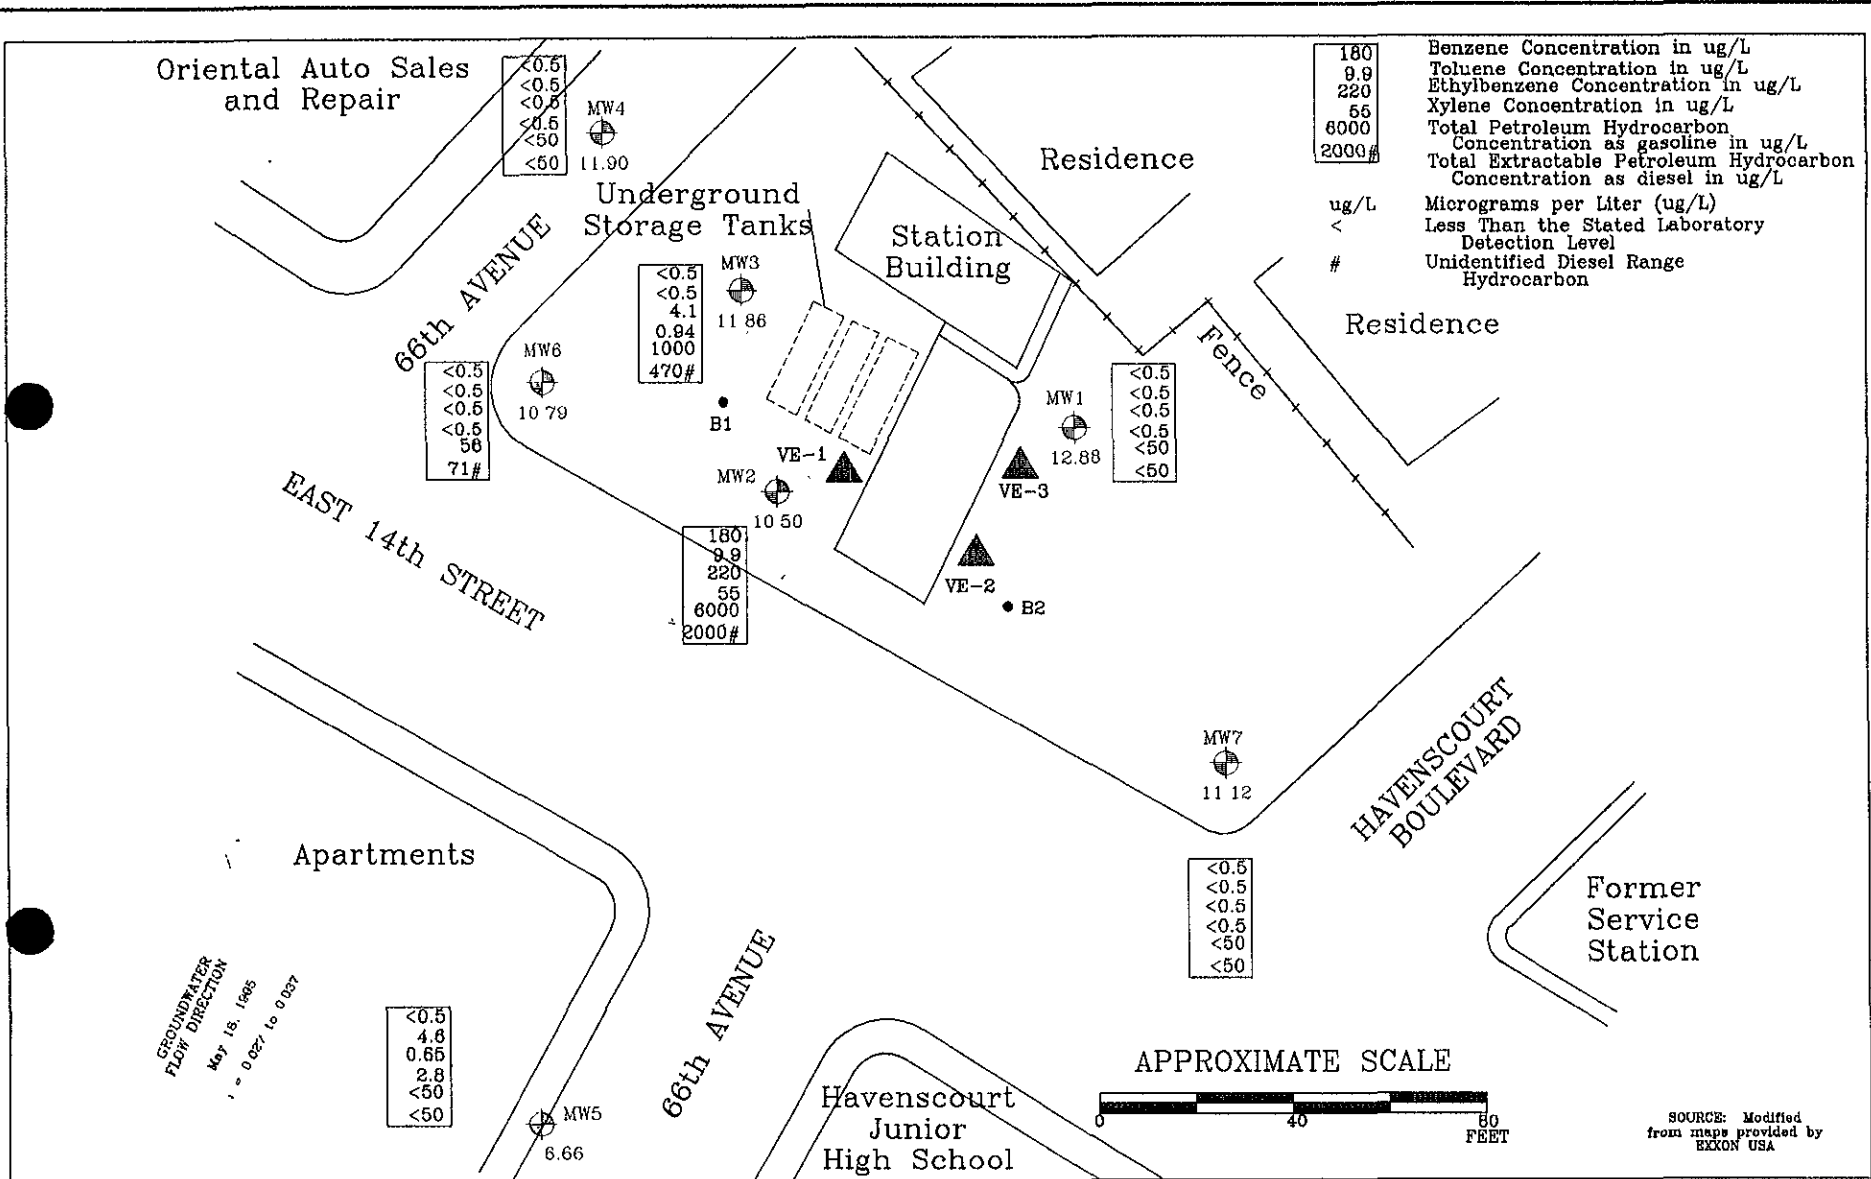


FN 20090002



GENERALIZED SITE PLAN
 EXXON SERVICE STATION 7-0236
 6630 E. 14th Street
 Oakland, California

EXPLANATION	
	Existing Monitoring Well and groundwater elevation
	Vapor Extraction Well
	Boring Location

PROJECT NO.	2009
PLATE	2
	06/01/95



Exxon Company, U.S.A.
QUARTERLY STATUS REPORT
January - March 1995
Date: March 30, 1995
(Page 1 of 2)

RAS # 7-0236
6630 East 14th Street
Oakland, California
ERI No. 2009

Work Performed During This Quarter

January through March 1995

- Submitted Quarterly Groundwater Monitoring report for fourth quarter 1994 to Exxon on January 6, 1995.
- Performed Quarterly Groundwater Monitoring for first quarter 1995 on March 27, 1995.

Quarterly Groundwater Sampling Results Pending

Separate Phase Product Recovery

Not Applicable

Work to be Performed Next Quarter

Estimated Completion Date: 06/30/95

- Submit Quarterly Groundwater Monitoring report for first quarter 1995 to Exxon.
- Perform quarterly groundwater monitoring event for second quarter 1995 and submit report to Exxon.

Work to be Performed Next 12 Months


Estimated Completion Date: 03/31/96

- Continue quarterly groundwater monitoring and sampling program to evaluate the trends of gasoline hydrocarbons and groundwater flow direction and gradient.

*Mark Briggs
(415) 387-9105*

*will be moving
factors as source
removal*

111

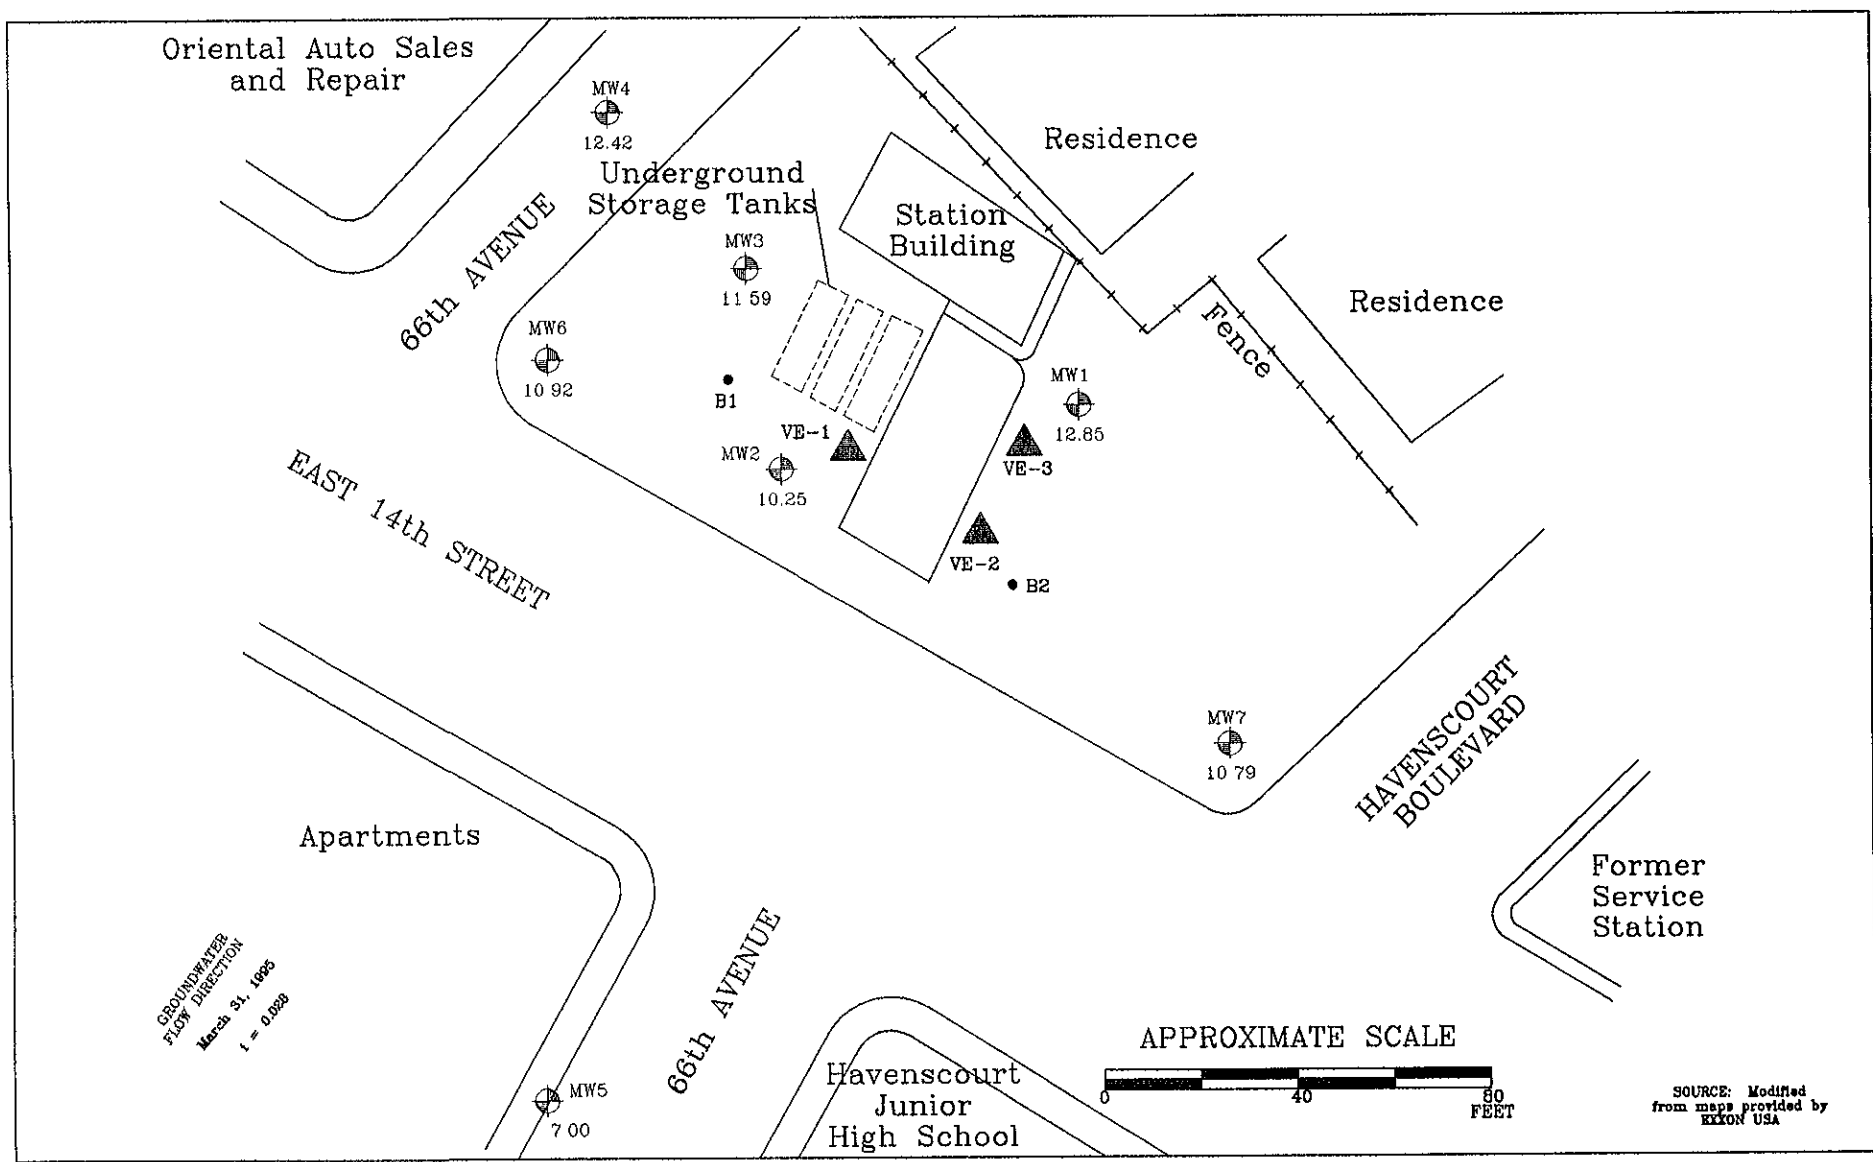





FN 20090002



GENERALIZED SITE PLAN

EXXON SERVICE STATION 7-0236
6630 E. 14th Street
Oakland, California

EXPLANATION

	Existing Monitoring Well and groundwater elevation
	Vapor Extraction Well
	Boring Location
	Sheen



PROJECT NO.	2009
PLATE	2
	01/03/95
