



July 12, 2000

Alameda County Health Care Services Agency
Attention Mr. Scott Seery
1131 Harbor Bay Parkway, Room 250
Alameda, CA 94502-6577

RE: Former BP Oil Site No. 11105
3159 Castro Valley Boulevard (at Redwood)
Castro Valley, CA


Dear Mr. Seery:

Enclosed find the 30 June 2000 and 24 May 2000 groundwater monitoring reports documenting groundwater monitoring data associated with 5 June 2000 and 9 March 2000.

It is noted that petroleum hydrocarbons were reported to be present in the soil and groundwater at this site at the time the property was sold during 1994. Concentrations detected since that time have increased and raise the concern that petroleum releases have occurred subsequent to BP's operation of the facility.

To illustrate the basis for BP's concern, water elevation data, together with MTBE and TPHg concentration data for well ESE-2 is depicted below.

ESE-2 TPHg, MTBE & Water Elevation

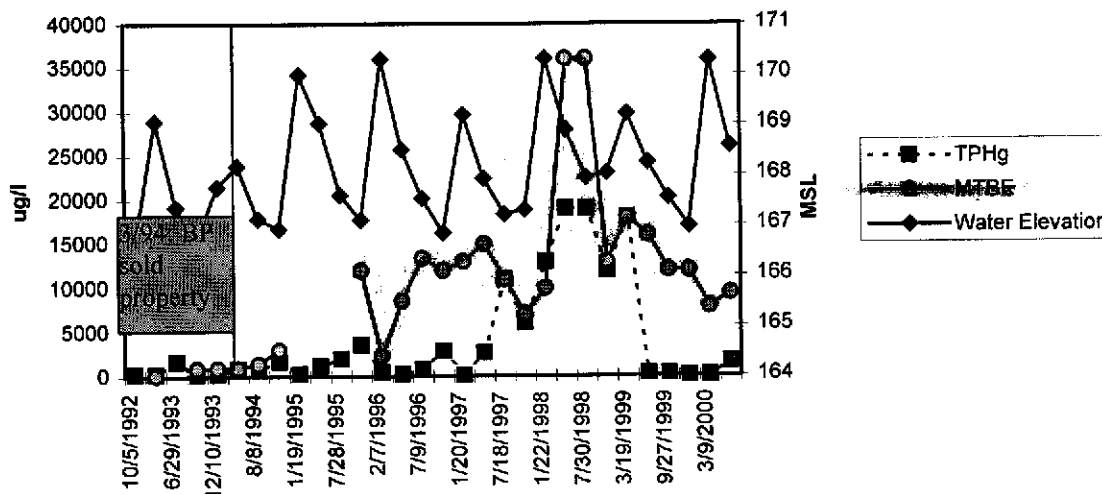

In contrast to the ESE-1 and ESE-2 data, well ESE-5 shows decreasing TPHg concentrations. Well ESE-5 is located south of a former dispenser island, and west of Redwood Road and the XTRA retail gasoline outlet.

Please contact me at (425) 251-0689 if you have any questions or concerns regarding this submittal.

Sincerely,



Scott Hooton

attachments (2)

cc: site file

A. Fagorala - RWQCB-SFBR

Mr. Azim Shakoori, Castro Valley Chevron, 3519 Castro Valley Boulevard, Castro Valley, CA 94546 (w/attachments)


BLAINE
TECH SERVICES, INC.

1680 ROGERS AVENUE
SAN JOSE, CA 95112-1105
(408) 573-7771 FAX
(408) 573-0555 PHONE
CONTRACTOR'S LICENSE #746684
www.blainetech.com



June 30, 2000

Scott Hooton
BP Oil Company
295 SW 41st Street, Bldg. 13, Suite N
Renton, WA 98055-4931



2nd Quarter 2000 Monitoring at 11105

Second Quarter 2000 Groundwater Monitoring at
BP Service Station Number 11105
3519 Castro Valley Blvd.
Castro Valley, CA

Monitoring Performed on June 5, 2000

Groundwater Sampling Report 000608-Y-4

This report covers the routine monitoring of groundwater wells at this BP facility. Blaine Tech Services, Inc.'s work at the site includes inspection, gauging, evacuation, purgewater containment, sample collection and sample handling in accordance with standard procedures that conform to Regional Water Quality Control Board requirements.

Routine field data collection includes depth to water, total well depth, thickness of any separate immiscible layer, water column volume, the appropriate calculated purge volume, elapsed evacuation time, total volume of water removed, and standard water parameter instrument readings. Sample material is collected, contained, stored, and transported to the laboratory in conformance with EPA standards. Purgewater is, likewise, collected and transported to Seaport Petroleum Corporation for disposal.


Basic field information is presented alongside analytical values excerpted from the laboratory report in the cumulative table of **WELL DATA AND ANALYTICAL RESULTS**. The full analytical report for the most recent samples is located in the **Analytical Appendix**. The table also contains new groundwater elevation calculations taken from the computer plotted gradient map, which is located in the **Professional Engineering Appendix**.

At a minimum, Blaine Tech Services, Inc. field personnel are certified upon completion of a forty-hour Hazardous Materials and Emergency Response training course per 29 CFR 1910.120. Field personnel are also enrolled in annual eight hour refresher courses.

Blaine Tech Services, Inc. conducts sampling and documentation assignments of this type as an independent third party. In order to avoid compromising the objectivity necessary for the proper and disinterested performance of this work, Blaine Tech Services, Inc. concentrates on objective data collection and does not participate in the interpretation of analytical results, the definition of geological or hydrological conditions, the formulation of recommendations, or the marketing of remedial systems.

Please call if you have any questions.

Yours truly,




A handwritten signature in black ink, appearing to read 'Francis Thie', written in a cursive style.

Francis Thie
Vice President

FPT/cm

attachments: Professional Engineering Appendix
Cumulative Table of Well Data and Analytical Results
Analytical Appendix
Field Data Sheets



Professional Engineering Appendix

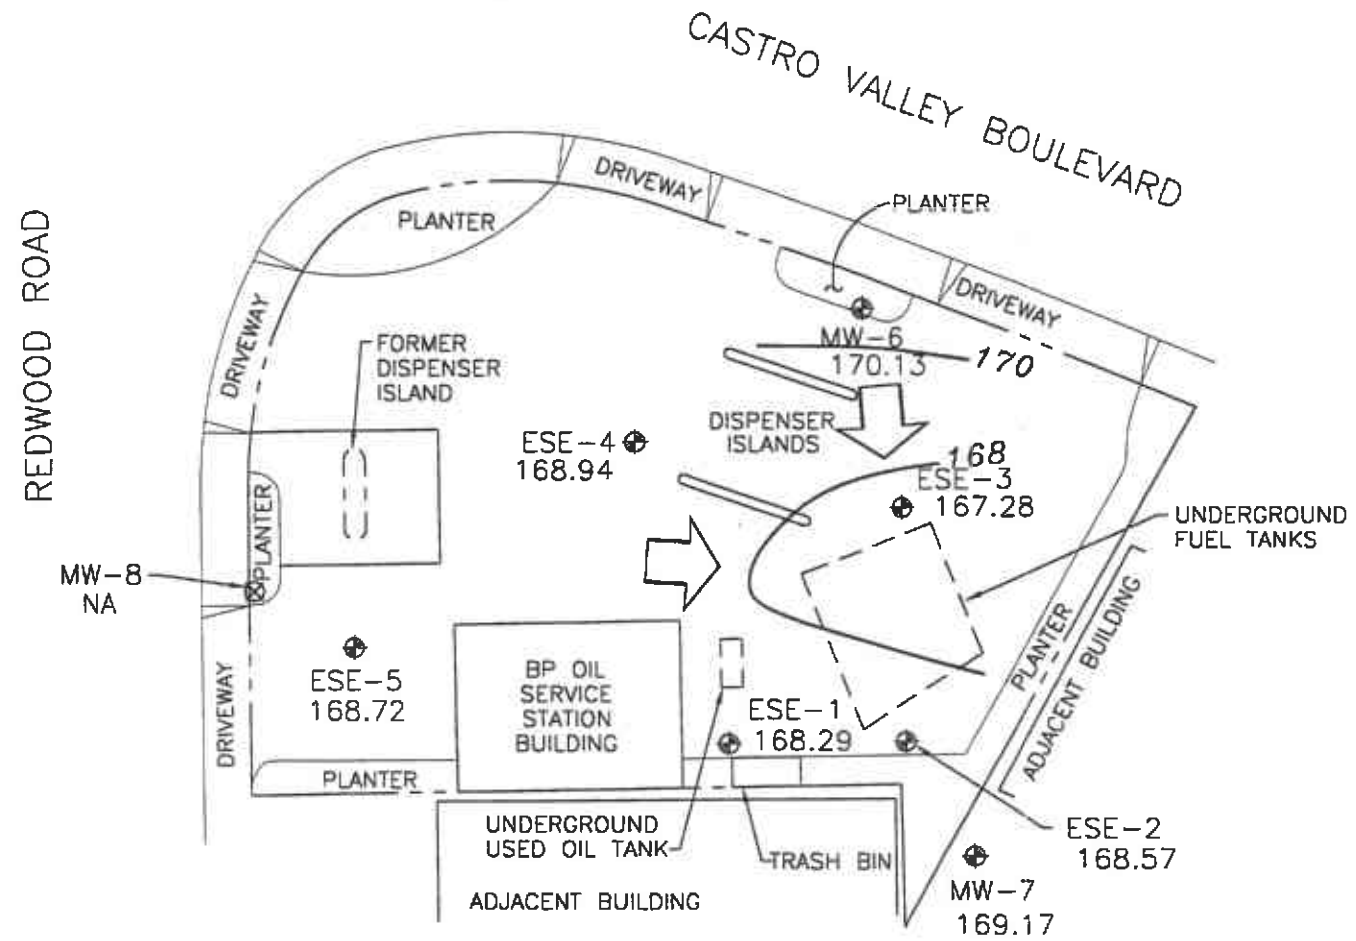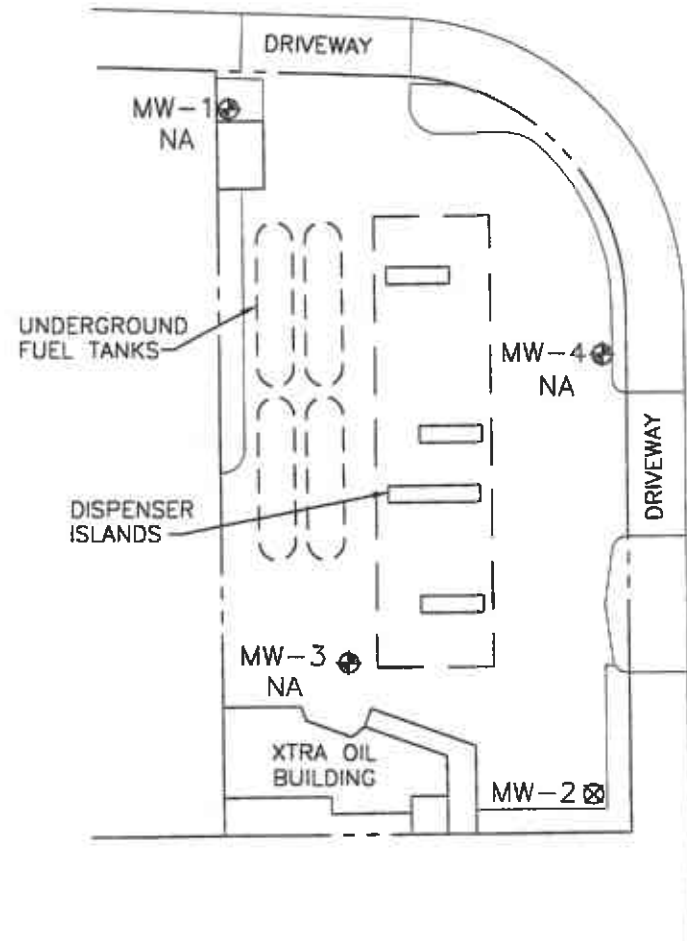

- EXPLANATION**
- ⊕ GROUNDWATER MONITORING WELL
 - ⊗ DESTROYED WELL
 - 169.17 GROUNDWATER ELEVATION (FT, MSL)
 - 170 — GROUNDWATER ELEVATION CONTOUR (FT, MSL)
 - NA DATA NOT AVAILABLE
 - ⇨ APPROXIMATE GROUNDWATER FLOW DIRECTION; APPROXIMATE GRADIENT = 0.07



PREPARED BY RRM engineering contracting firm	GROUNDWATER ELEVATION CONTOUR MAP, JUNE 8, 2000	FIGURE: 1 PROJECT: DAC04
	BP Oil Service Station No. 11105 3519 Castro Valley Boulevard Castro Valley, California	

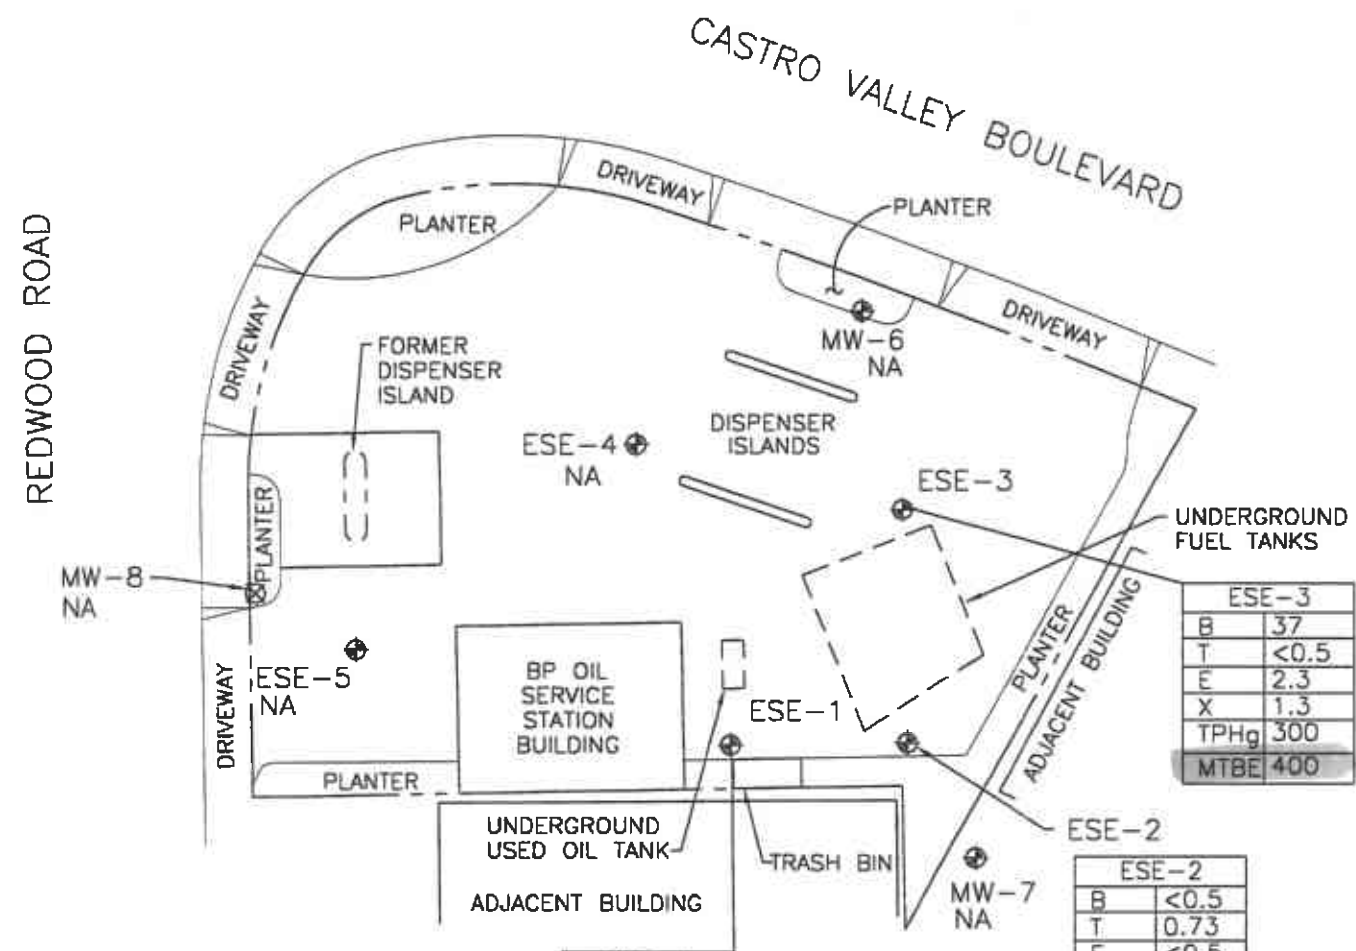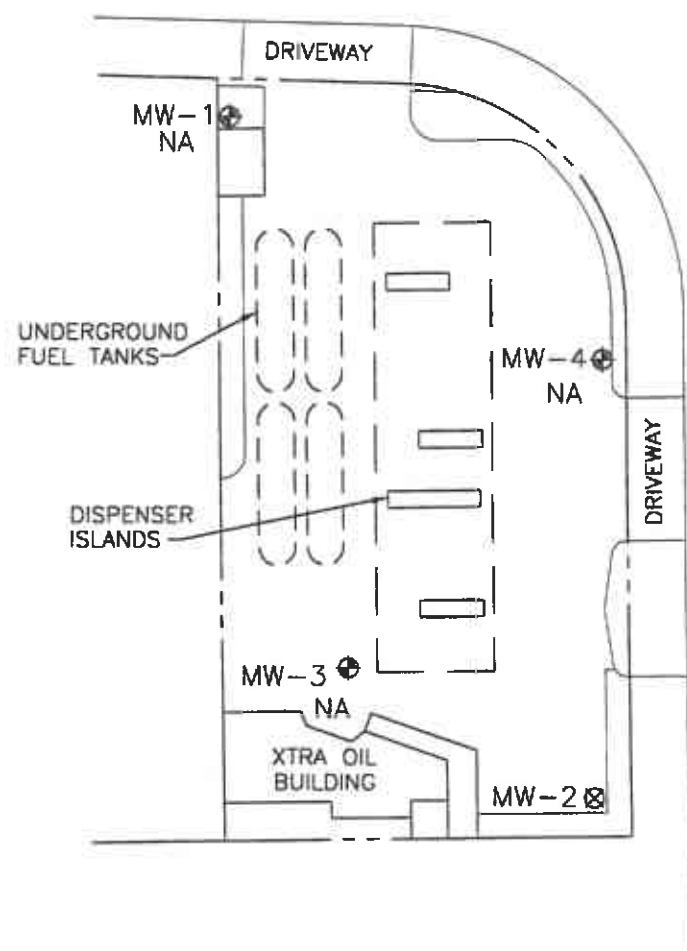

- EXPLANATION**
- ⊕ GROUNDWATER MONITORING WELL
 - ⊗ DESTROYED WELL
 - TPHg TOTAL PETROLEUM HYDROCARBON CALCULATED AS GASOLINE IN PARTS PER BILLION (ppb)
 - B BENZENE, ppb
 - T TOLUENE, ppb
 - E ETHYLBENZENE, ppb
 - X XYLENE, ppb
 - MTBE METHYL-TERT-BUTYL-ETHER, ppb
 - NA DATA NOT AVAILABLE

ESE-1	
B	540
T	9.7
E	20
X	17
TPHg	2900
MTBE	5200

ESE-2	
B	<0.5
T	0.73
E	<0.5
X	2.2
TPHg	1600
MTBE	9400

ESE-3	
B	37
T	<0.5
E	2.3
X	1.3
TPHg	300
MTBE	400

PREPARED BY engineering contracting firm	HYDROCARBON CONCENTRATION MAP, JUNE 8, 2000	FIGURE: 2 PROJECT: DAC04
	BP Oil Service Station No. 11105 3519 Castro Valley Boulevard Castro Valley, California	

Table of Well Data and Analytical Results

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (a) (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (b) (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
ESE-1 (c)	10/05/92	177.69	11.22	166.47	2100	370	150	17	110	---	---	---
ESE-1D (d)	10/05/92	---	---	---	2300	370	160	16	110	---	---	---
ESE-1	04/01/93	177.69	8.79	168.90	5900	1500	410	110	390	---	---	PACE
ESE-1	06/29/93	177.69	10.34	167.35	7600	2900	390	130	460	---	---	PACE
ESE-1	09/23/93	177.69	10.91	166.78	2000	490	40	20	56	600	(e) ---	PACE
QC-1 (d)	09/23/93	---	---	---	1500	420	39	19	56	550	(e) ---	PACE
ESE-1	12/10/93	177.69	9.93	167.76	1800	480	42	19	66	921	(e) 3.2	PACE
QC-1 (d)	12/10/93	---	---	---	1500	380	38	17	55	770	(e) ---	PACE
ESE-1	02/17/94	177.69	9.64	168.05	1900	380	48	24	80	590	(e) ---	PACE
QC-1 (d)	02/17/94	---	---	---	2200	430	42	19	65	680	(e) ---	PACE
ESE-1	08/08/94	177.69	11.72	165.97	2100	450	46	16	50	760	(e) 5.1	PACE
ESE-1	10/12/94	177.69	10.48	167.21	760	240	16	51	39	230	(e) 3.5	PACE
ESE-1	01/19/95	177.69	7.77	169.92	840	600	120	22	58	---	8.0	ATI
ESE-1	05/02/95	177.69	8.69	169.00	2000	640	67	24	98	---	8.5	ATI
ESE-1	07/28/95	177.69	10.12	167.57	190	ND<0.50	ND<0.50	ND<0.50	ND<1.0	---	7.9	ATI
ESE-1	11/17/95	177.69	10.57	167.12	200	3.4	ND<1.0	1	ND<2.0	600	7.7	ATI
ESE-1	02/07/96	177.69	7.41	170.28	750	370	23	21	64	680	2.5	SPL
ESE-1	04/23/96	177.69	9.12	168.57	310	100	ND<1	ND<1	ND<1	1500	6.3	SPL
ESE-1	07/09/96	177.69	10.12	167.57	730	230	74	13	63	750	2.9	SPL
ESE-1	10/10/96	177.69	10.80	166.89	420	26	1.6	7.3	12	430	7.4	SPL
ESE-1	01/20/97	177.69	8.52	169.17	660	290	4.2	13	36	450	5.9	SPL
ESE-1	04/25/97	177.69	9.77	167.92	410	ND<0.5	ND<1.0	ND<1.0	ND<1.0	580	5.3	SPL
ESE-1	07/18/97	177.69	10.55	167.14	420	ND<0.5	ND<1.0	ND<1.0	ND<1.0	370	5.0	SPL
ESE-1	10/27/97	177.69	10.36	167.33	300	56	ND<1.0	6.5	ND<1.0	220	4.8	SPL
ESE-1	01/22/98	177.69	7.52	170.17	4200	440	9	15	17.7	1300	4.2	SPL
ESE-1	04/23/98	177.69	8.80	168.89	15000	3400	190	910	900	4900	4.2	SPL
QC-1	04/23/98	---	---	---	15000	2800	140	730	730	4400	---	SPL
ESE-1	07/29/98	177.69	9.73	167.96	---	---	---	---	---	---	---	---
ESE-1	07/30/98	---	---	---	15000	ND<2.5	ND<5.0	ND<5.0	ND<5.0	15000	4.0	SPL
ESE-1	12/17/98	177.69	9.51	168.18	2400	73	1.0	2.8	4.6	2000/2500*	---	SPL
ESE-1	03/19/99	177.69	8.65	169.04	4700	58	ND<1.0	ND>1.0	ND<1.0	4700	---	SPL
ESE-1	06/23/99	177.69	10.51	167.18	600	170	ND<1.0	7.2	5.0	3900	---	SPL
ESE-1	09/27/99	177.69	10.32	167.37	920	200	ND<25	ND<25	ND<25	4900	---	SPL
ESE-1	12/09/99	177.69	10.24	167.45	460	130	1.2	5.2	1.5	5100	---	PACE
ESE-1	03/09/00	177.69	7.72	169.97	3000	(j) 1300	120	80	140	7300	---	PACE
ESE-1	06/08/00	177.69	9.40	168.29	2900	540	9.7	20	17	5200	---	PACE

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
ESE-2	10/05/92	178.23	11.68	166.55	300	5.4	16	3.9	45	---	---	---
ESE-2	04/01/93	178.23	9.17	169.06	240	27	ND<0.5	17	2.6	123	(e) ---	PACE
ESE-2	06/29/93	178.23	10.88	167.35	1700	260	24	110	23	---	---	PACE
QC-1 (d)	06/29/93	---	---	---	1300	240	17	110	25	---	---	PACE
ESE-2	09/23/93	178.23	11.56	166.67	240	3.1	0.5	0.6	2.5	900	(e) ---	PACE
ESE-2	12/10/93	178.23	10.48	167.75	250	2.4	2.4	1.5	11	940	(e) 2.6	PACE
ESE-2	02/17/94	178.23	10.06	168.17	900	ND<0.5	ND<0.5	ND<0.5	ND<0.5	930	(e) ---	PACE
ESE-2	08/08/94	178.23	11.11	167.12	750	ND<0.5	ND<0.5	ND<0.5	ND<0.5	1400	(e) 5.1	PACE
ESE-2	10/12/94	178.23	11.31	166.92	1700	ND<0.5	ND<0.5	ND<0.5	ND<0.5	3000	(e) 3.6	PACE
ESE-2	01/19/95	178.23	8.25	169.98	300	2	0.9	0.7	1	---	8.1	ATI
ESE-2	05/02/95	178.23	9.21	169.02	1200	4	ND<2.5	ND<2.5	ND<5.0	---	8.4	ATI
ESE-2	07/28/95	178.23	10.64	167.59	2000	ND<2.5	ND<2.5	ND<2.5	ND<5.0	---	7.7	ATI
ESE-2	11/17/95	178.23	11.13	167.10	3600	ND<25	ND<25	ND<25	ND<50	12000	7.4	ATI
QC-1 (d)	11/17/95	---	---	---	3400	ND<25	ND<25	ND<25	ND<50	12000	---	ATI
ESE-2	02/07/96	178.23	7.94	170.29	450	ND<0.5	ND<1	ND<1	ND<1	2300	1.8	SPL
ESE-2	04/23/96	178.23	9.73	168.50	260	0.9	ND<1	ND<1	ND<1	8600	7.2	SPL
ESE-2	07/09/96	178.23	10.70	167.53	780	ND<2.5	ND<5	ND<5	ND<5	13393	3.0	SPL
ESE-2	10/10/96	178.23	11.39	166.84	2900	ND<0.5	ND<1.0	ND<1.0	ND<1.0	12000	7.0	SPL
ESE-2	01/20/97	178.23	9.04	169.19	ND<250	ND<2.5	ND<5.0	ND<5.0	ND<5.0	13000	6.2	SPL
ESE-2	04/25/97	178.23	10.31	167.92	2700	ND<0.5	ND<1.0	ND<1.0	ND<1.0	15000	5.9	SPL
ESE-2	07/18/97	178.23	11.02	167.21	11000	ND<5	ND<10	ND<10	ND<10	11000	5.0	SPL
ESE-2	10/27/97	178.23	10.93	167.30	6100	ND<2.5	ND<5.0	ND<5.0	ND<5.0	7100	4.8	SPL
QC-1 (d)	10/27/97	---	---	---	6600	ND<2.5	ND<5.0	ND<5.0	ND<5.0	7400	---	SPL
ESE-2	01/22/98	178.23	7.93	170.30	13000	ND<0.5	ND<1.0	ND<1.0	ND<1.0	10000	4.6	SPL
QC-1 (d)	01/22/98	---	---	---	13000	ND<0.5	ND<1.0	ND<1.0	ND<1.0	10000	---	SPL
ESE-2	04/23/98	178.23	9.34	168.89	19000	ND<5	ND<10	ND<10	ND<10	36000	4.2	SPL
ESE-2	07/29/98	178.23	10.29	167.94	---	---	---	---	---	---	---	---
ESE-2	07/30/98	---	---	---	19000	ND<5	ND<10	ND<10	ND<10	36000	4.2	SPL
ESE-2	12/17/98	178.23	10.20	168.03	12000	ND<5.0	ND<5.0	ND<5.0	ND<5.0	13000/17000*	---	SPL
ESE-2	03/19/99	178.23	9.02	169.21	18000	160	ND<1.0	ND<1.0	ND<1.0	18000	---	SPL
ESE-2	06/23/99	178.23	9.99	168.24	280	ND<1.0	ND<1.0	ND<1.0	ND<1.0	16000	---	SPL
ESE-2	09/27/99	178.23	10.69	167.54	ND<500	ND<25	ND<25	ND<25	ND<25	12000	---	SPL
ESE-2	12/09/99	178.23	11.26	166.97	ND<50	ND<0.3	ND<0.3	ND<0.3	ND<0.6	12000	---	PACE
ESE-2	03/09/00	178.23	7.95	170.28	ND<50	1.6	ND<0.5	ND<0.5	ND<0.5	7900	---	PACE
ESE-2	06/08/00	178.23	9.66	168.57	1600	ND<0.5	0.73	ND<0.5	2.2	9400	---	PACE

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (a) (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (b) (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
ESE-3	10/05/92	178.20	10.58	167.62	430	57	31	3.6	34	---	---	---
ESE-3	04/01/93	178.20	8.14	170.06	2400	460	220	74	210	---	---	PACE
ESE-3	06/29/93	178.20	9.72	168.48	280	56	14	15	13	---	---	PACE
ESE-3	09/23/93	178.20	10.46	167.74	72	13	3.5	1.7	4.1	---	---	PACE
ESE-3	12/10/93	178.20	9.30	168.90	270	71	32	6.1	33	---	2.7	PACE
ESE-3	02/17/94	178.20	8.97	169.23	520	140	10	20	33	---	---	PACE
ESE-3	08/08/94	178.20	10.02	168.18	ND<50	8.8	1.6	1.6	2.3	---	6.2	PACE
ESE-3	10/12/94	178.20	10.32	167.88	470	190	6.4	15	18	---	3.5	PACE
ESE-3	01/19/95	178.20	7.40	170.80	330	260	27	21	20	---	6.7	ATI
ESE-3	05/02/95	178.20	8.26	169.94	530	180	30	23	44	---	8.6	ATI
ESE-3	07/28/95	178.20	9.54	168.66	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	---	8.8	ATI
ESE-3	11/17/95	178.20	10.04	168.16	ND<50	1.7	ND<0.50	ND<0.50	ND<1.0	ND<5.0	7.3	ATI
ESE-3	02/07/96	178.20	7.08	171.12	ND<50	8.6	ND<1	ND<1	ND<1	ND<10	3.9	SPL
ESE-3	04/23/96	178.20	8.79	169.41	ND<50	7.6	ND<1	ND<1	ND<1	65	6.9	SPL
ESE-3	07/09/96	178.20	10.09	168.11	ND<50	12	2.6	2	3.9	26	3.4	SPL
ESE-3	10/10/96	178.20	10.48	167.72	---	---	---	---	---	---	---	---
ESE-3	10/11/96	178.20	---	---	260	140	ND<1.0	ND<1.0	2.6	ND<10	7.2	SPL
ESE-3	01/20/97	178.20	8.65	169.55	ND<50	1.5	1.7	ND<1.0	ND<1.0	14	5.7	SPL
ESE-3	04/25/97	178.20	10.02	168.18	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	14	5.4	SPL
ESE-3	07/18/97	178.20	10.66	167.54	10000	1400	1400	300	1280	ND<250	5.2	SPL
ESE-3	10/27/97	178.20	9.83	168.37	ND<250	ND<2.5	ND<5.0	ND<5.0	36	ND<50	5.0	SPL
ESE-3	01/22/98	178.20	7.06	171.14	130	ND<0.5	ND<1.0	ND<1.0	ND<1.0	120	4.3	SPL
ESE-3	04/23/98	178.20	8.44	169.76	4800	560	ND<10	15	ND<10	4000	3.9	SPL
ESE-3	07/29/98	178.20	9.27	168.93	---	---	---	---	---	---	---	---
ESE-3	07/30/98	---	---	---	1800	6.2	ND<5.0	ND<5.0	ND<5.0	1700	4.1	SPL
ESE-3	12/17/98	178.20	9.15	169.05	600	54	ND<1.0	2.1	4.9	340/480*	---	SPL
ESE-3	03/19/99	178.20	8.14	170.06	2000	260	4.4	13	28	870	---	SPL
ESE-3	06/23/99	178.20	9.44	168.76	290	91	ND<1.0	8.3	16	240	---	SPL
ESE-3	09/27/99	178.20	9.69	168.51	130	35	ND<1.0	2.7	3.8	100	---	SPL
ESE-3	12/09/99	178.20	10.99	167.21	380	84	1.7	8.7	6.3	160	---	PACE
ESE-3	03/09/00	178.20	7.12	171.08	950	190	4.6	39	62	350	---	PACE
ESE-3	06/08/00	178.20	10.92	167.28	300	37	ND<0.5	2.3	1.3	400	---	PACE

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (b) (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
ESE-4	10/05/92	177.73	10.33	167.40	98	7.2	1.3	1.1	6.1	---	---	---
ESE-4	04/01/93	177.73	7.88	169.85	550	93	20	23	33	---	---	PACE
ESE-4	06/29/93	177.66	(f) 8.33	169.33	150	23	0.6	5.4	0.5	54	(e) ---	PACE
ESE-4	09/23/93	177.66	10.05	167.61	110	14	1.7	3.2	4.6	---	---	PACE
ESE-4	12/10/93	177.66	8.95	168.71	110	21	7.2	4.2	10	---	2.8	PACE
ESE-4	02/17/94	177.66	8.65	169.01	210	26	1.2	4.7	11	110	(e) ---	PACE
ESE-4	08/08/94	177.66	9.76	167.90	76	9.6	ND<0.5	2	ND<0.5	62	(e) 7.0	PACE
ESE-4	10/12/94	177.66	9.62	168.04	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	44	(e) 3.2	PACE
ESE-4	01/19/95	177.66	6.97	170.69	140	56	14	24	23	---	6.9	ATI
ESE-4	05/02/95	177.66	7.85	169.81	130	21	2.8	8.6	8.2	---	9.1	ATI
ESE-4	07/28/95	177.66	9.20	168.46	ND<50	ND<0.5	ND<0.50	ND<0.50	ND<1.0	---	8.1	ATI
ESE-4	11/17/95	177.66	9.68	167.98	ND<50	ND<0.5	0.6	ND<0.50	ND<1.0	18	5.7	ATI
ESE-4	02/07/96	177.66	6.59	171.07	100	2.6	ND<1	1.6	4.1	42	2.0	SPL
ESE-4	04/23/96	177.66	8.30	169.36	160	37	15	16	31	43	5.4	SPL
ESE-4	07/09/96	177.66	9.21	168.45	60	17	1.5	6.8	11.6	27	3.9	SPL
ESE-4	10/10/96	177.66	9.97	167.69	---	---	---	---	---	---	---	---
ESE-4	10/11/96	177.66	---	---	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	18	5.5	SPL
ESE-4	01/20/97	177.66	7.68	169.98	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	130	4.9	SPL
ESE-4	04/25/97	177.66	9.15	168.51	ND<250	ND<2.5	ND<5.0	ND<5.0	ND<5.0	ND<50	4.3	SPL
ESE-4	07/18/97	177.66	9.71	167.95	ND<50	15	ND<10	ND<10	ND<10	ND<100	4.5	SPL
ESE-4	10/27/97	177.66	9.38	168.28	ND<250	ND<2.5	ND<5.0	ND<5.0	ND<5.0	ND<50	4.9	SPL
ESE-4	01/22/97	177.66	6.59	171.07	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	4.3	SPL
ESE-4	04/23/98	177.66	7.90	169.76	ND<250	ND<2.5	ND<5.0	ND<5.0	ND<5.0	ND<50	4.0	SPL
ESE-4	07/29/98	177.66	8.96	168.70	---	---	---	---	---	---	---	---
ESE-4	07/30/98	---	---	---	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	4.2	SPL
ESE-4	12/17/98	177.66	8.32	169.34	---	---	---	---	---	---	---	---
ESE-4	03/19/99	177.66	7.71	169.95	---	---	---	---	---	---	---	---
ESE-4	06/23/99	177.66	8.78	168.88	---	---	---	---	---	---	---	---
ESE-4	09/27/99	177.66	9.27	168.39	---	---	---	---	---	---	---	---
ESE-4	12/09/99	177.66	9.21	168.45	---	---	---	---	---	---	---	---
ESE-4	03/09/00	177.66	6.82	170.84	---	---	---	---	---	---	---	---
ESE-4	06/08/00	177.66	8.72	168.94	---	---	---	---	---	---	---	---

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (a) (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (b) (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
ESE-5	10/05/92	176.08	9.22	166.86	1300	200	3.8	1.2	18	---	---	---
ESE-5	04/01/93	176.08	7.02	169.06	13000	2200	26	730	1000	---	---	PACE
QC-1 (d)	04/01/93	---	---	---	13000	2500	25	740	1100	---	---	PACE
ESE-5	06/29/93	176.08	10.21	165.87	7600	1500	9.3	170	100	---	---	PACE
ESE-5	09/23/93	176.08	10.64	165.44	560	19	1.2	0.9	1.8	---	---	PACE
ESE-5	12/10/93	176.08	9.42	166.66	1700	300	3	76	110	---	2.5	PACE
ESE-5	02/07/94	176.08	9.35	166.73	3500	640	7.8	90	130	---	---	PACE
ESE-5	08/08/94	176.08	8.76	167.32	2600	210	4.6	9.4	4.4	33	(e) 5.8	PACE
QC-1 (d)	08/08/94	---	---	---	2500	230	4.6	13	4.8	32	(e) ---	PACE
ESE-5	10/12/94	176.08	8.95	167.13	5600	560	9.5	75	21	---	3.6	PACE
QC-1 (d)	10/12/94	---	---	---	6000	550	10	78	22	77	(e) ---	PACE
ESE-5	01/19/95	176.08	5.40	170.68	1900	620	ND<5	95	15	---	7.6	ATI
QC-1 (d)	01/19/95	---	---	---	1600	620	ND<5	93	17	---	---	ATI
ESE-5	05/02/95	176.08	6.48	169.60	5700	1100	ND<10	180	58	---	8.2	ATI
QC-1 (d)	05/02/95	---	---	---	5300	1100	ND<10	180	58	---	---	ATI
ESE-5	07/28/95	176.08	7.97	168.11	520	15	ND<0.50	1.7	1.3	---	8.2	ATI
QC-1 (d)	07/28/95	---	---	---	460	7.2	ND<0.50	1.9	1.5	---	---	ATI
ESE-5	11/17/95	176.08	8.39	167.69	850	39	1.8	7.6	2.7	24	6.3	ATI
ESE-5	02/07/96	176.08	4.71	171.37	4100	670	6	190	140	ND<50	1.5	SPL
ESE-5	04/23/96	176.08	7.35	168.73	3000	570	ND<5	79	100	84	6.5	SPL
ESE-5	07/09/96	176.08	9.40	166.68	620	150	1.7	9.3	6.4	25	3.7	SPL
ESE-5	10/10/96	176.08	9.04	167.04	1100	29	ND<5.0	ND<5.0	ND<5.0	ND<50	6.3	SPL
QC-1 (d)	10/10/96	---	---	---	1100	31	ND<5.0	ND<5.0	ND<5.0	ND<50	---	SPL
ESE-5	01/20/97	176.08	5.82	170.26	2100	980	ND<25	280	80	ND<250	5.4	SPL
QC-1 (d)	01/20/97	---	---	---	2700	910	8.8	280	84	180	---	SPL
ESE-5	04/25/97	176.08	7.24	168.84	---	---	---	---	---	---	---	---
ESE-5	04/28/97	176.08	---	---	ND<250	7.9	ND<5.0	ND<5.0	ND<5.0	ND<50	4.9	SPL
ESE-5	07/18/97	176.08	7.86	168.22	1200	ND<5	ND<10	ND<10	ND<10	ND<100	5.0	SPL
QC-1 (d)	07/18/97	---	---	---	630	31	ND<5.0	ND<5.0	ND<5.0	130	---	SPL
ESE-5	10/27/97	176.08	7.91	168.17	ND<250	5.4	ND<5.0	ND<5.0	ND<5.0	ND<50	5.2	SPL
ESE-5	01/22/98	176.08	4.64	171.44	170	7.7	ND<1.0	ND<1.0	ND<1.0	130	4.6	SPL
ESE-5	04/23/98	176.08	6.31	169.77	720	79	ND<5.0	9.0	ND<5.0	180	4.6	SPL
ESE-5	07/29/98	176.08	7.43	168.65	---	---	---	---	---	---	---	---
ESE-5	07/30/98	---	---	---	840	9.8	ND<1.0	4.0	ND<1.0	710	4.3	SPL
ESE-5	12/17/98	176.08	7.05	169.03	---	---	---	---	---	---	---	---
ESE-5	03/19/99	176.08	5.00	171.08	ND<250	ND<5.0	ND<5.0	ND<5.0	ND<5.0	ND<5.0	---	SPL
ESE-5	06/23/99	176.08	7.77	168.31	---	---	---	---	---	---	---	SPL
ESE-5	09/27/99	176.08	8.11	167.97	450	10	ND<5.0	6.3	ND<5.0	220	---	SPL
ESE-5	12/09/99	176.08	7.66	168.42	---	---	---	---	---	---	---	---

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (a) (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (b) (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
ESE-5	03/09/00	176.08	5.08	171.00	1700	170	2.5	45	6.4	140	---	PACE
ESE-5	06/08/00	176.08	7.36	168.72	---	---	---	---	---	---	---	---

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (a) (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (b) (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
MW-6	07/28/95	179.24	10.00	169.24	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	---	8.1	ATI
MW-6	11/17/95	179.24	10.44	168.80	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	ND<5.0	6.8	ATI
MW-6	02/07/96	179.24	7.68	171.56	ND<50	ND<0.5	ND<1	ND<1	ND<1	ND<10	2.4	SPL
MW-6	04/23/96	179.24	9.33	169.91	ND<50	ND<0.5	ND<1	ND<1	ND<1	ND<10	6.6	SPL
MW-6	07/09/96	179.24	10.10	169.14	ND<50	ND<0.5	ND<1	ND<1	ND<1	ND<10	2.7	SPL
MW-6	10/10/96	179.24	11.00	168.24	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	6.9	SPL
MW-6	01/20/97	179.24	8.70	170.54	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	5.5	SPL
MW-6	04/25/97	179.24	10.16	169.08	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	5.1	SPL
MW-6	07/18/97	179.24	10.66	168.58	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	4.8	SPL
MW-6	10/27/97	179.24	10.25	168.99	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	4.8	SPL
MW-6	01/22/98	179.24	7.76	171.48	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	4.0	SPL
MW-6	04/23/98	179.24	9.10	170.14	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	4.2	SPL
MW-6	07/29/98	179.24	10.40	168.84	---	---	---	---	---	---	---	---
MW-6	07/30/98	---	---	---	ND<50	ND<0.5	ND<1.0	ND<1.0	ND<1.0	ND<10	3.8	SPL
MW-6	12/17/98	179.24	9.40	169.84	---	---	---	---	---	---	---	---
MW-6	03/19/99	179.24	9.10	170.14	---	---	---	---	---	---	---	---
MW-6	06/23/99	179.24	9.79	169.45	---	---	---	---	---	---	---	---
MW-6	09/27/99	179.24	10.10	169.14	---	---	---	---	---	---	---	---
MW-6	12/09/99	179.24	9.97	169.27	---	---	---	---	---	---	---	---
MW-6	03/09/00	179.24	8.56	170.68	---	---	---	---	---	---	---	---
MW-6	06/08/00	179.24	9.11	170.13	---	---	---	---	---	---	---	---

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (a) (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (b) (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
MW-7	07/28/95	176.55	9.25	167.30	ND<50	0.54 (g)	0.54	ND<0.50	ND<1.0	---	7.1	ATI
MW-7	11/17/95	176.55	9.73	166.82	1100	ND<10	ND<10	ND<10	ND<20	4000	6.3	ATI
MW-7	02/07/96	176.55	6.48	170.07	610	ND<0.5	ND<1	ND<1	ND<1	2500	4.1	SPL
QC-1 (d)	02/07/96	---	---	---	280	ND<0.5	ND<1	ND<1	ND<1	2600	---	SPL
MW-7	04/23/96	176.55	8.37	168.18	110	ND<0.5	ND<1	ND<1	ND<1	3500	6.4	SPL
QC-1 (d)	04/23/96	---	---	---	230	ND<0.5	ND<1	ND<1	ND<1	3500	---	SPL
MW-7	07/09/96	176.55	9.24	167.31	230	ND<0.5	ND<1	ND<1	ND<1	4296	3.1	SPL
QC-1 (d)	07/09/96	---	---	---	220	ND<0.5	ND<1	ND<1	ND<1	4400	---	SPL
MW-7	10/10/96	176.55	10.05	166.50	---	---	---	---	---	---	---	---
MW-7	10/11/96	176.55	---	---	1600	ND<0.5	ND<1.0	ND<1.0	ND<1.0	3000	6.9	SPL
MW-7	01/20/97	176.55	7.51	169.04	ND<50	0.63	1	ND<1.0	ND<1.0	2600	5.7	SPL
MW-7	04/25/97	176.55	8.79	167.76	---	---	---	---	---	---	---	---
MW-7	04/28/97	176.55	---	---	1500	ND<0.5	ND<1.0	ND<1.0	ND<1.0	3600	5.1	SPL
QC-1 (d)	04/28/97	---	---	---	7700	3500	ND<25	74	37	ND<250	---	SPL
MW-7	07/18/97	176.55	9.50	167.05	1400	ND<0.5	ND<1.0	ND<1.0	ND<1.0	2600	5.2	SPL
MW-7	10/27/97	176.55	9.19	167.36	420	ND<0.5	ND<1.0	ND<1.0	ND<1.0	560	4.9	SPL
MW-7	01/22/98	176.55	6.45	170.10	3100	ND<0.5	ND<1.0	ND<1.0	1.4	2300	4.2	SPL
MW-7	04/23/98	176.55	8.02	168.53	3800	ND<0.5	ND<1.0	ND<1.0	ND<1.0	3800	3.9	SPL
MW-7	07/29/98	176.55	8.88	167.67	---	---	---	---	---	---	---	---
MW-7	07/30/98	---	---	---	500	ND<2.5	ND<5.0	ND<5.0	ND<5.0	ND<50	4.1	SPL
QC-1 (d)	07/30/98	---	---	---	4700	ND<12	ND<25	ND<25	ND<25	4700	---	SPL
MW-7	12/17/98	176.55	8.62	167.93	---	---	---	---	---	---	---	---
MW-7	03/19/99	176.55	7.52	169.03	3800	ND<1.0	ND<1.0	ND<1.0	ND<1.0	3800	---	SPL
MW-7	06/23/99	176.55	9.63	166.92	---	---	---	---	---	---	---	---
MW-7	09/27/99	176.55	9.39	167.16	140	ND<10	ND<10	ND<10	ND<10	3800	---	SPL
MW-7	12/09/99	176.55	9.94	166.61	---	---	---	---	---	---	---	---
MW-7	03/09/00	176.55	6.72	169.83	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	1400	---	PACE
MW-7	06/08/00	176.55	7.38	169.17	---	---	---	---	---	---	---	---

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

WELL ID	DATE OF SAMPLING/ MONITORING	CASING ELEVATION (a) (Feet)	DEPTH TO WATER (Feet)	GROUNDWATER ELEVATION (b) (Feet)	TPH-G (ug/l)	B (ug/l)	T (ug/l)	E (ug/l)	X (ug/l)	MTBE (ug/l)	DO (ppm)	LAB
MW-8	07/28/95	176.34	7.80	168.54	1100	ND<2.5	ND<2.5	ND<2.5	ND<5.0	---	7.2	ATI
MW-8	11/17/95	176.34	8.29	168.05	8300	75	5.3	670	240	140	7.0	ATI
MW-8	02/07/96	176.34	4.99	171.35	2300	33	ND<10	190	216	ND<100	1.7	SPL
MW-8	04/23/96	176.34	6.09	170.25	2000	390	ND<20	150	26	ND<250	5.1	SPL
MW-8 (h)	07/09/96	---	---	---	---	---	---	---	---	---	---	---
QC-2 (i)	04/01/93	---	---	---	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	---	---	PACE
QC-2 (i)	06/29/93	---	---	---	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	---	---	PACE
QC-2 (i)	09/23/93	---	---	---	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	---	---	PACE
QC-2 (i)	12/10/93	---	---	---	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	---	---	PACE
QC-2 (i)	02/17/94	---	---	---	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	---	---	PACE
QC-2 (i)	08/08/94	---	---	---	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	---	---	PACE
QC-2 (i)	10/12/94	---	---	---	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<0.5	---	---	PACE
QC-2 (i)	01/19/95	---	---	---	ND<50	ND<0.5	ND<0.5	ND<0.5	ND<1	---	---	ATI
QC-2 (i)	05/02/95	---	---	---	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	---	---	ATI
QC-2 (i)	07/28/95	---	---	---	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	---	---	ATI
QC-2 (i)	11/17/95	---	---	---	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	ND<5.0	---	ATI
QC-2 (i)	02/07/96	---	---	---	ND<50	ND<0.5	ND<1	ND<1	ND<1	ND<10	---	SPL
QC-2 (i)	04/23/96	---	---	---	ND<50	ND<0.5	ND<1	ND<1	ND<1	ND<10	---	SPL
QC-2 (i)	07/09/96	---	---	---	ND<50	ND<0.5	ND<1	ND<1	ND<1	ND<10	---	SPL

TABLE 1 - SUMMARY OF RESULTS OF GROUNDWATER MONITORING

ABBREVIATIONS:

TPH-G	Total petroleum hydrocarbons as gasoline
B	Benzene
T	Toluene
E	Ethylbenzene
X	Total xylenes
MTBE	Methyl tert butyl ether
DO	Dissolved oxygen
ug/l	Micrograms per liter
ppm	Parts per million
ND	Not detected above reported detection limit
---	Not applicable/available/measured/analyzed
PACE	Pace, Inc.
ATI	Analytical Technologies, Inc.
SPL	Southern Petroleum Laboratories

NOTES:

- (a) Top of casing elevations surveyed relative to mean sea level.
- (b) Groundwater elevations in feet relative to mean sea level.
- (c) Additional analysis of the sample collected from ESE-1 on 10/5/92 detected 96 ug/l total petroleum hydrocarbons as diesel and 1.8 ug/l 1,2-dichloroethane.
- (d) Blind duplicate.
- (e) A copy of the documentation for this data is included in Appendix C of Alisto report 10-138-09-004.
- (f) Top of casing lowered by 0.07 foot after the monitoring event on 4/01/93.
- (g) Sample result may be falsely elevated due to matrix interference.
- (h) Well destroyed.
- (i) Travel blank.
- (j) Gasoline does not include MTBE.
- (*) MTBE by EPA 8020/8260

Analytical Appendix



Pace Analytical Services, Inc.
3970 Gilman Street
Long Beach, CA 90815
Phone: 562.498.9515
Fax: 562.597.0786

June 20, 2000

Mr. MORGAN HARGRAVE
BLAINE TECH SERVICES, INC.
1680 ROGERS AVE.
SAN JOSE, CA 95112

RE: Pace Project Number: 6042036
Client Project ID: BP 11105 Castro Valley

Dear Mr. HARGRAVE:

Enclosed are the results of analyses for sample(s) received by the laboratory on June 13, 2000. If you have any questions concerning this report, please feel free to contact me.

Sincerely,

A handwritten signature in cursive script that reads "Lily Bayati".

Lily Bayati
Project Manager

Enclosures

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc.



Pace Analytical Services, Inc.
 3970 Gilman Street
 Long Beach, CA 90815
 Phone: 562.498.9515
 Fax: 562.597.0786

DATE: 06/20/00
 PAGE: 1

BLAINE TECH SERVICES, INC.
 1680 ROGERS AVE.
 SAN JOSE, CA 95112

Pace Project Number: 6042036
 Client Project ID: BP 11105 Castro Valley

Attn: Mr. MORGAN HARGRAVE
 Phone: (408)573-0555 x218

Solid results are reported on a wet weight basis

Pace Sample No: 603563263 Date Collected: 06/08/00 Matrix: Water
 Client Sample ID: A Date Received: 06/13/00

Parameters	Results	Units	PRL	Analyzed	Analyst	CAS#	Footnotes
------------	---------	-------	-----	----------	---------	------	-----------

Long Beach Laboratory

GAS BTEX by 8015, Water	Method: EPA 8015 Mod/8020			Prep Method: EPA 8015 Mod/8020			
Gasoline	1600	ug/l	50	06/13/00	VN		1.2
Benzene	ND	ug/l	0.5	06/13/00	VN	71-43-2	
Toluene	0.73	ug/l	0.5	06/13/00	VN	108-88-3	
Ethylbenzene	ND	ug/l	0.5	06/13/00	VN	100-41-4	
Methyl tert-butyl Ether	9400	ug/l	150	06/13/00	VN	1634-04-4	
Xylene (Total)	2.2	ug/l	0.5	06/13/00	VN	1330-20-7	
a.a.a-Trifluorotoluene (S)	104	%		06/13/00	VN	2164-17-2	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
 without the written consent of Pace Analytical Services, Inc.



Pace Analytical Services, Inc.
 3970 Gilman Street
 Long Beach, CA 90815
 Phone: 562.498.9515
 Fax: 562.597.0786

DATE: 06/20/00
 PAGE: 2

Pace Project Number: 6042036
 Client Project ID: BP 11105 Castro Valley

Pace Sample No: 603563271 Date Collected: 06/08/00 Matrix: Water
 Client Sample ID: B Date Received: 06/13/00

Parameters Results Units PRL Analyzed Analyst CAS# Footnotes

Long Beach Laboratory

Parameters	Results	Units	PRL	Analyzed	Analyst	CAS#	Footnotes
GAS BTEX by 8015, Water							
Method: EPA 8015 Mod/8020							
Prep Method: EPA 8015 Mod/8020							
Gasoline	300	ug/l	50	06/13/00	VN		2
Benzene	37	ug/l	0.5	06/13/00	VN	71-43-2	
Toluene	ND	ug/l	0.5	06/13/00	VN	108-88-3	
Ethylbenzene	2.3	ug/l	0.5	06/13/00	VN	100-41-4	
Methyl-tert-butyl Ether	400	ug/l	38	06/13/00	VN	1634-04-4	
Xylene (Total)	1.3	ug/l	0.5	06/13/00	VN	1330-20-7	
a,a,a-Trifluorotoluene (S)	116	%		06/13/00	VN	2164-17-2	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
 without the written consent of Pace Analytical Services, Inc.



Pace Analytical Services, Inc.

3970 Gilman Street
Long Beach, CA 90815

Phone: 562.498.9515
Fax: 562.597.0786

DATE: 06/20/00

PAGE: 3

Pace Project Number: 6042036

Client Project ID: BP 11105 Castro Valley

Pace Sample No: 603563289 Date Collected: 06/08/00 Matrix: Water
Client Sample ID: C Date Received: 06/13/00

Parameters	Results	Units	PRL	Analyzed	Analyst	CAS#	Footnotes
------------	---------	-------	-----	----------	---------	------	-----------

Long Beach Laboratory

GAS BTEX by 8015, Water		Method: EPA 8015 Mod/8020		Prep Method: EPA 8015 Mod/8020			
Gasoline	2900	ug/l	50	06/13/00	VN		2
Benzene	540	ug/l	75	06/13/00	VN	71-43-2	
Toluene	9.7	ug/l	0.5	06/13/00	VN	108-88-3	
Ethylbenzene	20	ug/l	0.5	06/13/00	VN	100-41-4	
Methyl-tert-butyl Ether	5200	ug/l	75	06/13/00	VN	1634-04-4	
Xylene (Total)	17	ug/l	0.5	06/13/00	VN	1330-20-7	
a,a,a-Trifluorotoluene (S)	125	%		06/13/00	VN	2164-17-2	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc.



Pace Analytical Services, Inc.

3970 Gilman Street
Long Beach, CA 90815

Phone: 562.498.9515

Fax: 562.597.0786

DATE: 06/20/00

PAGE: 4

Pace Project Number: 6042036

Client Project ID: BP 11105 Castro Valley

PARAMETER FOOTNOTES

ND Not Detected
NC Not Calculable
PRL Pace Reporting Limit
(S) Surrogate
[1] Sample does not fit gasoline profile. Sample contain mainly MTBE.
[2] Concentration of MTBE in the calculation of TPHG is an estimate only.

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc.



Pace Analytical Services, Inc.
 3970 Gilman Street
 Long Beach, CA 90815
 Phone: 562.498.9515
 Fax: 562.597.0786

QUALITY CONTROL DATA

DATE: 06/20/00
 PAGE: 5

BLAINE TECH SERVICES, INC.
 1680 ROGERS AVE.
 SAN JOSE, CA 95112

Pace Project Number: 6042036
 Client Project ID: BP 11105 Castro Valley

Attn: Mr. MORGAN HARGRAVE
 Phone: (408)573-0555 x218

QC Batch ID: 85029 QC Batch Method: EPA 8015 Mod/8020
 Analysis Method: EPA 8015 Mod/8020 Analysis Description: GAS BTEX by 8015, Water
 Associated Pace Samples: 603563263 603563271 603563289

METHOD BLANK: 603564626
 Associated Pace Samples:

Parameter	Units	Method Blank		Footnotes
		603563263	603563271	
Gasoline	ug/l	ND	PRL	
Benzene	ug/l	ND	0.05	
Toluene	ug/l	ND	0.05	
Ethylbenzene	ug/l	ND	0.05	
Methyl-tert-butyl Ether	ug/l	ND	0.05	
Xylene (Total)	ug/l	ND	0.05	
a,a,a-Trifluorotoluene (S)	%	110		

MATRIX SPIKE & MATRIX SPIKE DUPLICATE: 603564634 603564642

Parameter	Units	Matrix Spike		Matrix Spike		Matrix Spike		RPD	Footnotes
		603563446	Conc.	Spike Result	% Rec	Sp. Dup. Result	% Rec		
Gasoline	ug/l	0	40	42.80	107	42.80	107	0	
Benzene	ug/l	0.5753	6.667	7.490	104	7.490	104	0	
Toluene	ug/l	0	6.667	7.410	111	7.410	111	0	
Ethylbenzene	ug/l	0	6.667	7.260	109	7.260	109	0	
Methyl-tert-butyl Ether	ug/l	0	6.667	7.040	106	7.040	106	0	
Xylene (Total)	ug/l	0.8446	20	22.19	107	22.19	107	0	
a,a,a-Trifluorotoluene (S)	%				109		109		

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
 without the written consent of Pace Analytical Services, Inc.



Pace Analytical Services, Inc.
3970 Gilman Street
Long Beach, CA 90815
Phone: 562.498.9515
Fax: 562.597.0786

DATE: 06/20/00

PAGE: 6

Pace Project Number: 6042036

Client Project ID: BP 11105 Castro Valley

QUALITY CONTROL DATA PARAMETER FOOTNOTES

Consistent with EPA guidelines unrounded concentrations are displayed and have been used to calculate % Rec and RPD values.

ND Not Detected
NC Not Calculable
PRL Pace Reporting Limit
RPD Relative Percent Difference
(S) Surrogate

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, Inc.



CHAIN OF CUSTODY

16592A
6042036

CONSULTANT'S NAME Blaine Tech Services, Inc.		CONSULTANT'S ADDRESS 1680 Rogers Ave., San Jose CA 95112	
BP SITE NUMBER 11105	BP SITE / FACILITY ADDRESS 3519 Castro Valley Blvd., Castro Valley		CONSULTANT PROJECT NUMBER 000608-44
CONSULTANT PROJECT MANAGER Morgan Hargrave		PHONE NUMBER (408) 573-0555 x 218	FAX NUMBER (408) 573-7771
BP CONTACT Scott Hooton		BP ADDRESS 295 SW 41st Street, Suite N, Renton WA	PHONE NUMBER (425) 251-0689
LAB CONTACT Pace - Lily Bayati		LABORATORY ADDRESS 3970 Gilman Street, Long Beach, CA	PHONE NUMBER (562) 498-9515
BP CONTACT REQUESTING RUSH TAT (Print BP Contact Name)	RUSH REQUESTED OF (Print Consultant Contact Name)	DATE/TIME	SHIPMENT DATE
			SHIPMENT METHOD AIRBORNE

TAT: 24 HOURS 48 HOURS 72 HOURS Standard 7 or 14 Days

ANALYSIS REQUIRED

AIRBILL NUMBER: 5301432555

SAMPLE DESCRIPTION	COLLECTION DATE	COLLECTION TIME	MATRIX SOIL/WATER	CONTAINERS		PRESERVATIVE	TPH-G + BTEX / MTBE (8015M)	TPH-O (8015M)	FUEL OXYGENATES (8250)	1,2 DCA + EDB (8010)									COMMENTS	
				NO.	TYPE (VOL)	LAB SAMPLE #														
A	6/8/00	1513	W	3	40 20	Hel	X													
B	↓	1532	↓	↓	↓	↓	X													
C	↓	1551	↓	↓	↓	↓	X													

SAMPLED BY (Please Print Name) LEON G.				SAMPLED BY (Signature) 				ADDITIONAL COMMENTS			
RELINQUISHED BY / AFFILIATION (Print Name / Signature)	DATE	TIME	ACCEPTED BY / AFFILIATION (Print Name / Signature)	DATE	TIME						
	6/12/00	13:15	NOEY TONG	6/13/00	09:45						

Field Data Sheets

WELL GAUGING DATA

Project # 000605-44 Date 6-8-00 Client BP

Site 3519 CASTRO VALLEY BWD CASTRO VALLEY

	Well ID	Well Size (in.)	Sheen / Odor	Depth to Immiscible Liquid (ft.)	Thickness of Immiscible Liquid (ft.)	Volume of Immiscibles Removed (ml)	Depth to water (ft.)	Depth to well bottom (ft.)	Survey Point: TOB or TOC	
7	ESE-1	2					9.40	29.27	TOC	C
4	ESE-2	2					9.66	29.90		A
5	ESE-3	2				10.92	29.60	B		
2	ESE-4	2				8.72	22.76			
6	ESE-5	2				7.36	23.65			
1	MW-6	2				9.11	29.93			
3	MW-7	2				7.38	29.64			

BP WELL MONITORING DATA SHEET

Project #: <u>000606-44</u>	Station # <u>11105</u>
Sampler: <u>LEON G.</u>	Date: <u>6-8-00</u>
Well I.D.: <u>ESE-1</u>	Well Diameter: <u>(2)</u> 3 4 6 8 _____
Total Well Depth: <u>29.27</u>	Depth to Water: <u>9.40</u>
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: <u>PVC</u> Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
1"	0.04	4"	0.65
2"	0.16	6"	1.47
3"	0.37	Other	radius ² * 0.163

Purge Method: <u>Bailer</u> Disposable Bailer <u>Middleburg</u> Electric Submersible Extraction Pump Other: _____	Sampling Method: <u>Bailer</u> <u>Disposable Bailer</u> Extraction Port Other: _____
--	---

<u>3.1</u>	X	<u>3</u>	=	<u>9.3</u>	Gals.
1 Case Volume (Gals.)		Specified Volumes		Calculated Volume	

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
1541	66.1	6.9	694	3	
1544	65.8	7.5	901	6	
1547	65.7	7.5	915	9.5	

Did well dewater? Yes <input type="checkbox"/> No <input checked="" type="checkbox"/>	Gallons actually evacuated: <u>9.5</u>
Sampling Time: <u>1551</u>	Sampling Date: <u>6-8-00</u>
Sample I.D. (Blind): <u>C</u>	Laboratory: <u>Pace</u> Other: _____
Analyzed for: <u>TPH-G</u> <u>BTEX</u> <u>MTBE</u> TPH-D Other: _____	
D.O. (if req'd): Pre-purge: _____ mg/L	Post-purge: _____ mg/L
O.R.P. (if req'd): Pre-purge: _____ mV	Post-purge: _____ mV

BP WELL MONITORING DATA SHEET

Project #: 000608-44	Station # 11105
Sampler: LEON G.	Date: 6-8-00
Well I.D.: ESE-2	Well Diameter: (2) 3 4 6 8 _____
Total Well Depth: 29.90	Depth to Water: 9.66
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: (PVC) Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
1"	0.04	4"	0.65
2"	0.16	6"	1.47
3"	0.37	Other	radius ² * 0.163

Purge Method: <input type="checkbox"/> Bailer <input type="checkbox"/> Disposable Bailer <input checked="" type="checkbox"/> Middleburg <input type="checkbox"/> Electric Submersible <input type="checkbox"/> Extraction Pump Other: _____	Sampling Method: <input type="checkbox"/> Bailer <input checked="" type="checkbox"/> Disposable Bailer <input type="checkbox"/> Extraction Port Other: _____
---	--

<u>3.2</u>	X	<u>3</u>	=	<u>9.6</u>	Gals.
1 Case Volume (Gals.)		Specified Volumes		Calculated Volume	

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
1502	65.6	7.4	1002	3	
1505	65.3	6.8	1005	7	
1504	65.1	6.7	994	10	

Did well dewater? Yes <input type="checkbox"/> (No)	Gallons actually evacuated: 10	
Sampling Time: 1513	Sampling Date: 6-8-00	
Sample I.D. (Blind): A	Laboratory: (Pace) Other: _____	
Analyzed for: (TPH-G) (BTEX) (MTBE) TPH-D Other: _____		
D.O. (if req'd):	Pre-purge: _____ mg/L	Post-purge: _____ mg/L
O.R.P. (if req'd):	Pre-purge: _____ mV	Post-purge: _____ mV

BP WELL MONITORING DATA SHEET

Project #: <u>000606-44</u>	Station # <u>11105</u>
Sampler: <u>LEON G.</u>	Date: <u>6-8-00</u>
Well I.D.: <u>ESE-3</u>	Well Diameter: <u>(2)</u> 3 4 6 8 _____
Total Well Depth: <u>29.60</u>	Depth to Water: <u>10.92</u>
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: <u>PVC</u> Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
1"	0.04	4"	0.65
2"	0.16	6"	1.47
3"	0.37	Other	radius ² * 0.163

Purge Method: <input type="checkbox"/> Bailer <input type="checkbox"/> Disposable Bailer <input checked="" type="checkbox"/> <u>Middleburg</u> <input type="checkbox"/> Electric Submersible <input type="checkbox"/> Extraction Pump Other: _____	Sampling Method: <input type="checkbox"/> Bailer <input checked="" type="checkbox"/> <u>Disposable Bailer</u> <input type="checkbox"/> Extraction Port Other: _____
---	--

<u>2.9</u>	X	<u>3</u>	=	<u>8.7</u>	Gals.
1 Case Volume (Gals.)		Specified Volumes		Calculated Volume	

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
<u>1521</u>	<u>67.6</u>	<u>6.6</u>	<u>1096</u>	<u>3</u>	
<u>1524</u>	<u>68.3</u>	<u>6.5</u>	<u>946</u>	<u>6</u>	
<u>1527</u>	<u>68.3</u>	<u>6.5</u>	<u>950</u>	<u>9</u>	

Did well dewater? Yes <input type="checkbox"/> No <input checked="" type="checkbox"/>	Gallons actually evacuated: <u>9</u>	
Sampling Time: <u>1532</u>	Sampling Date: <u>6-8-00</u>	
Sample I.D. (Blind): <u>B</u>	Laboratory: <u>Pace</u> Other: _____	
Analyzed for: <u>TPH-G</u> <u>BTEX</u> <u>MTBE</u> TPH-D Other: _____		
D.O. (if req'd):	Pre-purge: _____ mg/L	Post-purge: _____ mg/L
O.R.P. (if req'd):	Pre-purge: _____ mV	Post-purge: _____ mV
