EMCON
1921 Ringwood Avenue • San Jose, California 95131-1721 • **(408) 453-7300** • Fax (408) 437-9526

Date December 13, 1996
Project 20805-122.003

To:

Ms. Susan Hugo
Alameda County Health Care Services Agency
Department of Environmental Health
1131 Harborbay Parkway, Suite 250
Alameda, California 94502-6577

We are enclosing:

Copies	Description
1	Third quarter 1996 groundwater monitoring results and remediation system performance evaluation report for ARCO service station 771, Livermore, California

For your:	X	Use	Sent by:	X	Regular Mail
		Approval			Standard Air
		Review			Courier
		Information			Other:

Comments:

The enclosed groundwater monitoring report is being sent to you per the request of ARCO Products Company. Plaese call if you have questions or comments.

John C. Young
Project Manager

cc: Sum Arigala, RWQCB - SFBR
Danielle Stefani, LFD
Paul Supple, ARCO Products Company
File

ARCO Products Company

Date:
December 12, 1996

Re: ARCO Station #

771 • 899 Rincon Avenue • Livermore, CA
Third Quarter 1996 Groundwater Monitoring Results and
Remediation System Performance Evaluation Report

"I declare, that to the best of my knowledge at the present time, that the information and/or recommendations contained in the attached proposal or report are true and correct."

Submitted by:

Paul Supple
Environmental Engineer

EMCON
1921 Ringwood Avenue • San Jose, California 95131-1721 • (408) 453-7300 • Fax (408) 437-9526

December 12, 1996
Project 20805-122.003

Mr. Paul Supple
ARCO Products Company
P.O. Box 6549
Moraga, California 94570

Re: Third quarter 1996 groundwater monitoring program results and remediation system performance evaluation report, ARCO service station 771, Livermore, California

Dear Mr. Supple:

This letter presents the results of the third quarter 1996 groundwater monitoring program at ARCO Products Company (ARCO) service station 771, 899 Rincon Avenue, Livermore, California (Figure 1). Operation and performance data for the site's interim soil-vapor extraction (SVE) and air-bubbling systems are also presented. The quarterly monitoring program complies with Alameda County Health Care Services Agency (ACHCSA) requirements regarding underground tank investigations.

LIMITATIONS

No monitoring event is thorough enough to describe all geologic and hydrogeologic conditions of interest at a given site. If conditions have not been identified during the monitoring event, such a finding should not therefore be construed as a guarantee of the absence of such conditions at the site, but rather as the result of the scope, limitations, and cost of work performed during the monitoring event.

Please call if you have questions.

Sincerely,

EMCON

Krishnaveni M.
Krishnaveni Meka
Staff Engineer

John C. Young, R.G. 6407
Project Manager

REGISTERED GEOLOGIST
JOHN CHARLES YOUNG
7/98
NO. 6407
STATE OF CALIFORNIA

December 12, 1996

ARCO QUARTERLY REPORT

Station No.: 771	Address: 899 Rincon Avenue, Livermore, California
EMCON Project No.:	20805-122.003
ARCO Environmental Engineer/Phone No.:	Paul Supple /(510) 299-8891
EMCON Project Manager/Phone No.:	John C. Young /(408) 453-7300
Primary Agency/Regulatory ID No.:	ACHCSA /Susan Hugo
Reporting Period:	July 1, 1996 to October 1, 1996

WORK PERFORMED THIS QUARTER (Third- 1996):

1. Conducted quarterly groundwater monitoring and sampling for third quarter 1996.
2. Operated air-bubbling system.
3. Monitored dissolved oxygen in air-bubbling wells VW-1, MW-1, MW-2, MW-4, MW-5, MW-7, and RW-1.
4. Prepared and submitted quarterly report for second quarter 1996.

WORK PROPOSED FOR NEXT QUARTER (Fourth- 1996):

1. Perform quarterly groundwater monitoring and sampling for fourth quarter 1996.
2. Continue pulsing air-bubbling system hourly.
3. Continue monitoring dissolved oxygen in air bubbling wells.
4. Prepare and submit quarterly report for third quarter 1996.

QUARTERLY MONITORING:

Current Phase of Project:	Quarterly Groundwater Monitoring and Operation and Maintenance of Remediation Systems Soil Vapor Extraction (SVE) system was shut down on 10-10-95. Air bubbling system pulses hourly.
Frequency of Sampling:	Quarterly (groundwater)
Frequency of Monitoring:	Quarterly (groundwater), Monthly (air-bubbling system)
Is Floating Product (FP) Present On-site:	☐ Yes ☒ No
Cumulative FP Recovered to Date :	3.06 gallons, Wells MW-1, MW-2, and MW-5
FP Recovered This Quarter :	None (FP was last recovered in 1992.)
Bulk Soil Removed to Date :	1,700 cubic yards of TPH-impacted soil
Bulk Soil Removed This Quarter :	None
Water Wells or Surface Waters within 2000 ft., impacted by site:	None
Current Remediation Techniques:	Air-Bubbling
Approximate Depth to Groundwater:	24.44 feet
Groundwater Gradient (Average):	0.03 ft/ft toward north-northwest (consistent with past events)

SVE QUARTERLY OPERATION AND PERFORMANCE:

Equipment Inventory:	King Buck, 200 cfm, Model MMC-6A/E, Catalytic Oxidizer
Operating Mode:	Catalytic Oxidation
BAAQMD Permit #:	9051

TPH Conc. End of Period (lab):	NA (Not Available)
Benzene Conc. End of Period (lab):	NA
Flowrate End of Period:	NA
HC Destroyed This Period:	0.0 pounds
HC Destroyed to Date:	56.9 pounds
Utility Usage This Period	
Electric (KWH):	380
Gas (Therms):	NA
Operating Hours This Period:	0.0 hours
Percent Operational:	0.0%
Operating Hours to Date:	1737.5 hours
Unit Maintenance:	NA
Number of Auto Shut Downs:	NA
Destruction Efficiency Permit	
Requirement:	90%
Percent TPH Conversion:	NA
Stack Temperature:	NA
Source Flow:	NA
Process Flow:	NA
Source Vacuum:	NA

ATTACHED:

- Table 1 - Groundwater Monitoring Data, Third Quarter 1996
- Table 2 - Historical Groundwater Elevation and Analytical Data, Petroleum Hydrocarbons and Their Constituents
- Table 3 - Approximate Cumulative Floating Product Recovered (Wells MW-1, MW-2, and MW-5)
- Table 4 - Soil-Vapor Extraction System Operation and Performance Data
- Table 5 - Soil-Vapor Extraction Well Data
- Table 6 - Air-Bubbling System Operation and Performance Data
- Figure 1 - Site Location
- Figure 2 - Groundwater Data, Third Quarter 1996
- Figure 3 - Soil-Vapor Extraction and Treatment System, Historical System Influent TVHG and Benzene Concentrations
- Figure 4 - Soil-Vapor Extraction and Treatment System, Historical Hydrocarbon Removal Rates
- Appendix A - Field Data Sheets, Third Quarter 1996 Groundwater Monitoring Event
- Appendix B - Analytical Results and Chain of Custody Documentation, Third Quarter 1996 Groundwater Monitoring Event
- Appendix C - SVE System Monitoring Data Log Sheets
- Appendix D - Field Data Sheets, Operation and Maintenance Visits, Third Quarter 1996

cc: Susan Hugo, ACHCSA
Sum Arigala, RWQCB-SFBR
Danielle Stefani, LFD

Table 1
Groundwater Monitoring Data
Third Quarter 1996

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designation	Water Level Field Date	Top of Casing Elevation	Depth to Water	Groundwater Elevation	Floating Product Thickness	Groundwater Flow Direction	Hydraulic Gradient	Water Sample Field Date	**TPHG** LUFT Method	**Benzene** EPA 8020	**Toluene** EPA 8020	**Ethylbenzene** EPA 8020	**Total Xylenes** EPA 8020	**MTBE** EPA 8020	**MTBE** EPA 8240	**TPHD** LUFT Method	**TOG** SM 5520F	**TOG** SM 5520C	**TOG** EPA 413.2	**TRPH** EPA 418.1
		ft-MSL	feet	ft-MSL	feet	MWN	ft/ft		µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	mg/L	mg/L	mg/L	mg/L
MW-1	08-13-96	451.73	26.83	424.90	ND	NNW	0.03	08-13-96	19000	730	580	450	2500	<200^	--	--	--	--	--	--
MW-2	08-13-96	449.49	24.44	425.05	ND	NNW	0.03	08-13-96	19000	640	110	420	1200	<300^	--	--	--	--	--	--
MW-3	08-13-96	450.28	25.67	424.61	ND	NNW	0.03	08-13-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-4	08-13-96	451.09	26.20	424.89	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											
MW-5	08-13-96	451.40	26.48	424.92	ND	NNW	0.03	08-13-96	1700	150	16	24	35	47	--	--	--	--	--	--
MW-6	08-13-96	451.37	28.55	422.82	ND	NNW	0.03	08-13-96	3800	91	8.2	69	25	<20^	--	--	--	--	--	--
MW-7	08-13-96	450.33	25.52	424.81	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											
MW-8	08-13-96	449.43	30.20	419.23	ND	NNW	0.03	08-13-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-9	08-13-96	449.21	24.17	425.04	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											
MW-10	08-13-96	449.22	23.70	425.52	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											
MW-11	08-13-96	448.02	29.19	418.83	ND	NNW	0.03	08-13-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
RW-1	08-13-96	451.67	24.74	426.93	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											

ft-MSL: elevation in feet, relative to mean sea level
MWN: ground-water flow direction and gradient apply to the entire monitoring well network
ft/ft: foot per foot
TPHG: total petroleum hydrocarbons as gasoline, California DHS LUFT Method
µg/L: micrograms per liter
EPA: United Statest Environmental Protection Agency
MTBE: methyl-tert-butyl ether
TPHD: total petroleum hydrocarbons as diesel, California DHS LUFT Method
TOG: total oil and grease
SM: standard method
mg/L: milligrams per liter
TRPH: total recoverable petroleum hydrocarbons
ND: none detected
NNW: north-northwest
^: method reporting limit was raised due to: (1) high analyte concentration requiring sample dilution, or (2) matrix interference
- -: not analyzed or not applicable

esj/h:\0771\0771mdb.xls\Table 1:imi
20805-122.003

Table 2
Historical Groundwater Elevation and Analytical Data
Petroleum Hydrocarbons and Their Constituents
1994 - Present*

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designation	Water Level Field Date	Top of Casing Elevation	Depth to Water	Groundwater Elevation	Floating Product Thickness	Groundwater Flow Direction	Hydraulic Gradient	Water Sample Field Date	**TPHG** LUFT Method	**Benzene** EPA 8020	**Toluene** EPA 8020	**Ethylbenzene** EPA 8020	**Total Xylenes** EPA 8020	**MTBE** EPA 8020	**MTBE** EPA 8240	**TPHD** LUFT Method	**TOG** SM 5520F	**TOG** SM 5520C	**TOG** EPA 413.2	**TRPH** EPA 418.1
		ft-MSL	feet	ft-MSL	feet	MWN	ft/ft		µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	mg/L	mg/L	mg/L	mg/L
MW-1	03-26-94	451.73	28.22	423.51	ND	NR	NR	03-26-94	29000	1000	290	610	3300	--	--	--	--	--	--	--
MW-1	06-13-94	451.73	29.86	421.87	ND	NR	NR	06-13-94	25000	600	160	500	2500	--	--	--	--	--	--	--
MW-1	09-22-94	451.73	31.61	420.12	ND	NNE	0.056	09-22-94	51000	1400	280	570	2800	--	--	--	--	--	--	--
MW-1	11-25-94	451.73	29.76	421.97	ND	N	0.06	11-25-94	170000	990	1000	1700	9400	--	--	--	--	--	--	--
MW-1	03-20-95	451.73	24.50	427.23	ND	NW	0.03	03-20-95	90000	1800	1100	1000	5600	--	--	--	--	--	--	--
MW-1	06-02-95	451.73	25.60	426.13	ND	NNW	0.014	06-03-95	81000	2000	1400	990	4600	--	--	--	--	--	--	--
MW-1	08-23-95	451.73	29.04	422.69	ND	NNW	0.03	08-23-95	44000	2400	1900	670	3800	<300	--	--	--	--	--	--
MW-1	12-04-95	451.73	31.31	420.42	ND	NNW	0.03	12-04-95	22000	870	660	390	2200	--	100	--	--	--	--	--
MW-1	02-20-96	451.73	22.26	429.47	ND	NW	0.016	02-20-96	21000	1500	1200	650	3500	<300	--	--	--	--	--	--
MW-1	05-15-96	451.73	23.42	428.31	ND	NW	0.024	05-15-96	36000	3000	2500	960	5700	<250	--	--	--	--	--	--
MW-1	08-13-96	451.73	26.83	424.90	ND	NNW	0.03	08-13-96	19000	730	580	450	2500	<200^	--	--	--	--	--	--
MW-2	03-26-94	449.49	25.30	424.19	ND	NR	NR	03-26-94	22000	1100	1400	190	3700	--	--	--	--	--	--	--
MW-2	06-13-94	449.49	27.28	422.21	ND	NR	NR	06-13-94	71000	4100	4600	1700	9900	--	--	--	--	--	--	--
MW-2	09-22-94	449.49	29.54	419.95	ND	NNE	0.056	09-22-94	42000	1200	620	710	2000	--	--	--	--	--	--	--
MW-2	11-25-94	449.49	27.85	421.64	ND	N	0.06	11-25-94	60000	3900	4100	1400	7400	--	--	--	--	--	--	--
MW-2	03-20-95	449.49	20.27	429.22	ND	NW	0.03	03-20-95	54000	2600	1600	1200	7600	--	--	--	--	--	-	--
MW-2	06-02-95	449.49	22.32	427.17	ND	NNW	0.014	06-03-95	37000	2200	800	980	4800	--	--	--	--	--	--	--
MW-2	08-23-95	449.49	25.69	423.80	ND	NNW	0.03	08-23-95	65000	1100	310	840	3000	<500	--	--	--	--	--	--
MW-2	12-04-95	449.49	28.52	420.97	ND	NNW	0.03	12-04-95	19000	680	150	410	1600	--	--	--	--	--	--	--
MW-2	02-20-96	449.49	19.00	430.49	ND	NW	0.016	02-20-96	22000	1200	240	590	2200	<300	--	--	--	--	--	--
MW-2	05-15-96	449.49	20.03	429.46	ND	NW	0.024	05-15-96	25000	1200	240	610	2100	<300	--	--	--	--	--	--
MW-2	08-13-96	449.49	24.44	425.05	ND	NNW	0.03	08-13-96	19000	640	110	420	1200	<300^	--	--	--	--	--	--

Table 2
Historical Groundwater Elevation and Analytical Data
Petroleum Hydrocarbons and Their Constituents
1994 - Present*

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designation	Water Level Field Date	Top of Casing Elevation	Depth to Water	Groundwater Elevation	Floating Product Thickness	Groundwater Flow Direction	Hydraulic Gradient	Water Sample Field Date	**TPHG** LUFT Method	**Benzene** EPA 8020	**Toluene** EPA 8020	**Ethylbenzene** EPA 8020	**Total Xylenes** EPA 8020	**MTBE** EPA 8020	**MTBE** EPA 8240	**TPHD** LUFT Method	**TOG** SM 5520F	**TOG** SM 5520C	**TOG** EPA 413.2	**TRPH** EPA 418.1
		ft-MSL	feet	ft-MSL	feet	MWN	ft/ft		µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	mg/L	mg/L	mg/L	mg/L
MW-3	03-26-94	450.28	26.97	423.31	ND	NR	NR	03-26-94	54	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-3	06-13-94	450.28	28.71	421.57	ND	NR	NR	06-13-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-3	09-22-94	450.28	32.34	417.94	ND	NNE	0.056	09-22-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-3	11-25-94	450.28	30.76	419.52	ND	N	0.06	11-25-94	54	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-3	03-20-95	450.28	22.19	428.09	ND	NW	0.03	03-20-95	94	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-3	06-02-95	450.28	23.28	427.00	ND	NNW	0.014	06-02-95	72	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-3	08-23-95	450.28	26.55	423.73	ND	NNW	0.03	08-23-95	98	<0.5	<0.5	<0.6	0.5	<3	--	--	--	--	--	--
MW-3	12-04-95	450.28	29.52	420.76	ND	NNW	0.03	12-04-95	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-3	02-20-96	450.28	19.83	430.45	ND	NW	0.016	02-20-96	130	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-3	05-15-96	450.28	21.03	429.25	ND	NW	0.024	05-15-96	120	<0.5	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--
MW-3	08-13-96	450.28	25.67	424.61	ND	NNW	0.03	08-13-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-4	03-26-94	451.09	26.94	424.15	ND	NR	NR	03-26-94	27000	1800	830	1300	2900	--	--	--	--	--	--	--
MW-4	06-13-94	451.09	28.88	422.21	ND	NR	NR	06-13-94	17000	1300	620	670	1600	--	--	--	--	--	--	--
MW-4	09-22-94	451.09	30.98	420.11	ND	NNE	0.056	09-22-94	10000	700	61	420	570	--	--	--	--	--	--	--
MW-4	11-25-94	451.09	29.08	422.01	ND	N	0.06	11-25-94	13000	1400	250	490	1200	--	--	--	--	--	--	--
MW-4	03-20-95	451.09	22.68	428.41	ND	NW	0.03	03-20-95	12000	1000	100	450	700	--	--	--	--	--	--	--
MW-4	06-02-95	451.09	24.41	426.68	ND	NNW	0.014	06-02-95	9000	850	56	380	430	--	--	--	--	--	--	--
MW-4	08-23-95	451.09	27.72	423.37	ND	NNW	0.03	08-23-95	5300	400	25	240	170	<100	--	--	--	--	--	--
MW-4	12-04-95	451.09	29.85	421.24	ND	NNW	0.03	12-04-95	6700	100	<10	90	38	--	--	--	--	--	--	--
MW-4	02-20-96	451.09	21.16	429.93	ND	NW	0.016	02-20-96	7000	360	22	180	160	<70	--	--	--	--	--	--
MW-4	05-15-96	451.09	22.18	428.91	ND	NW	0.024	05-15-96	Not sampled: not scheduled for chemical analysis											
MW-4	08-13-96	451.09	26.20	424.89	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											

Table 2
Historical Groundwater Elevation and Analytical Data
Petroleum Hydrocarbons and Their Constituents
1994 - Present*

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designation	Water Level Field Date	Top of Casing Elevation	Depth to Water	Groundwater Elevation	Floating Product Thickness	Groundwater Flow Direction	Hydraulic Gradient	Water Sample Field Date	TPHG LUFT Method	Benzene EPA 8020	Toluene EPA 8020	Ethylbenzene EPA 8020	Total Xylenes EPA 8020	MTBE EPA 8020	MTBE EPA 8240	TPHD LUFT Method	TOG SM 5520F	TOG SM 5520C	TOG EPA 413.2	TRPH EPA 418.1
		ft-MSL	feet	ft-MSL	feet	MWN	ft/ft		µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	mg/L	mg/L	mg/L	mg/L
MW-5	03-26-94	451.40	27.41	423.99	ND	NR	NR	03-26-94	39000	4000	2300	1600	6200	--	--	--	--	--	--	--
MW-5	06-13-94	451.40	29.29	422.11	ND	NR	NR	06-13-94	28000	2500	1700	1100	3900	--	--	--	--	--	--	--
MW-5	09-22-94	451.40	Not surveyed: vehicle was parked on well					09-22-94	Not sampled: vehicle was parked on well											
MW-5	11-25-94	451.40	29.76	421.64	ND	N	0.06	11-25-94	31000	2400	1100	1100	4400	--	--	--	--	--	--	--
MW-5	03-20-95	451.40	23.20	428.20	ND	NW	0.03	03-20-95	26000	1300	180	890	2900	--	--	--	--	--	--	--
MW-5	06-02-95	451.40	24.80	426.60	ND	NNW	0.014	06-02-95	39000	940	160	740	1900	--	--	--	--	--	--	--
MW-5	08-23-95	451.40	28.10	423.30	ND	NNW	0.03	08-23-95	14000	490	74	250	890	<300	--	--	--	--	--	--
MW-5	12-04-95	451.40	29.83	421.57	ND	NNW	0.03	12-04-95	7600	230	13	61	80	--	--	--	--	--	--	--
MW-5	02-20-96	451.40	21.63	429.77	ND	NW	0.016	02-20-96	4300	220	12	45	130	<50	--	--	--	--	--	--
MW-5	05-15-96	451.40	22.87	428.53	ND	NW	0.024	05-15-96	2200	380	17	58	84	<40	--	--	--	--	--	--
MW-5	08-13-96	451.40	26.48	424.92	ND	NNW	0.03	08-13-96	1700	150	16	24	35	47	--	--	--	--	--	--
MW-6	03-26-94	451.37	28.24	423.13	ND	NR	NR	03-26-94	3100	350	99	130	340	--	--	880	--	--	--	1.5
MW-6	06-13-94	451.37	29.20	422.17	ND	NR	NR	06-13-94	2300	250	12	130	31	--	--	350*	--	--	--	0.8
MW-6	09-22-94	451.37	30.37	421.00	ND	NNE	0.056	09-22-94	73	2.6	<0.5	1.7	0.7	--	--	<50	<0.5	--	--	--
MW-6	11-25-94	451.37	29.88	421.49	ND	N	0.06	11-25-94	1100	78	<2.5	46	17	--	--	<50	--	--	--	<0.5
MW-6	03-20-95	451.37	25.19	426.18	ND	NW	0.03	03-20-95	2600	210	87	82	140	--	--	2000*	--	--	--	1.7
MW-6	06-02-95	451.37	25.75	425.62	ND	NNW	0.014	06-02-95	1600	55	7.9	40	26	--	--	1200*	--	--	--	1
MW-6	08-23-95	451.37	29.53	421.84	ND	NNW	0.03	08-23-95	1400	42	2.5	36	13	<20	--	530*	--	--	--	1.6
MW-6	12-04-95	451.37	32.28	419.09	ND	NNW	0.03	12-04-95	2500	52	5.8	59	13	--	--	1100*	--	--	--	1.5
MW-6	02-20-96	451.37	22.27	429.10	ND	NW	0.016	02-20-96	2500	120	16	73	12	<30	--	--	--	--	--	1.8
MW-6	05-15-96	451.37	23.86	427.51	ND	NW	0.024	05-15-96	2000	71	6.4	47	25	<15	--	--	--	--	--	--
MW-6	08-13-96	451.37	28.55	422.82	ND	NNW	0.03	08-13-96	3800	91	8.2	69	25	<20^	--	--	--	--	--	--

Table 2
Historical Groundwater Elevation and Analytical Data
Petroleum Hydrocarbons and Their Constituents
1994 - Present*

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designation	Water Level Field Date	Top of Casing Elevation	Depth to Water	Groundwater Elevation	Floating Product Thickness	Groundwater Flow Direction	Hydraulic Gradient	Water Sample Field Date	TPHG LUFT Method	Benzene EPA 8020	Toluene EPA 8020	Ethylbenzene EPA 8020	Total Xylenes EPA 8020	MTBE EPA 8020	MTBE EPA 8240	TPHD LUFT Method	TOG SM 5520F	TOG SM 5520C	TOG EPA 413.2	TRPH EPA 418.1
		ft-MSL	feet	ft-MSL	feet	MWN	ft/ft		µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	mg/L	mg/L	mg/L	mg/L
MW-7	03-26-94	450.33	26.03	424.30	ND	NR	NR	03-26-94	22000	2700	280	500	2600	--	--	--	--	--	--	--
MW-7	06-13-94	450.33	27.94	422.39	ND	NR	NR	06-13-94	21000	1500	180	360	1900	--	--	--	--	--	--	--
MW-7	09-22-94	450.33	30.46	419.87	ND	NNE	0.056	09-22-94	22000	1800	240	430	1900	--	--	--	--	--	--	--
MW-7	11-25-94	450.33	28.30	422.03	ND	N	0.06	11-25-94	29000	2600	380	640	3300	--	--	--	--	--	--	--
MW-7	03-20-95	450.33	22.07	428.26	ND	NW	0.03	03-20-95	31000	2300	400	620	2900	--	--	--	--	--	--	--
MW-7	06-02-95	450.33	23.42	426.91	ND	NNW	0.014	06-03-95	40000	1400	280	610	2400	--	--	--	--	--	--	--
MW-7	08-23-95	450.33	27.13	423.20	ND	NNW	0.03	08-23-95	25000	1400	200	600	1600	350	--	--	--	--	--	--
MW-7	12-04-95	450.33	29.45	420.88	ND	NNW	0.03	12-04-95	23000	1100	74	490	720	--	--	--	--	--	--	--
MW-7	02-20-96	450.33	20.25	430.08	ND	NW	0.016	02-20-96	39000	1200	140	640	1800	<400	--	--	--	--	--	--
MW-7	05-15-96	450.33	21.38	428.95	ND	NW	0.024	05-15-96	Not sampled: not scheduled for chemical analysis											
MW-7	08-13-96	450.33	25.52	424.81	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											
MW-8	03-26-94	449.43	31.40	418.03	ND	NR	NR	03-26-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-8	06-13-94	449.43	35.10	414.33	ND	NR	NR	06-13-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-8	09-22-94	449.43	38.77	410.66	ND	NNE	0.056	09-22-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-8	11-25-94	449.43	36.46	412.97	ND	N	0.06	11-25-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-8	03-20-95	449.43	24.75	424.68	ND	NW	0.03	03-20-95	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-8	06-02-95	449.43	24.95	424.48	ND	NNW	0.014	06-02-95	Not sampled: not scheduled for chemical analysis											
MW-8	08-23-95	449.43	30.94	418.49	ND	NNW	0.03	08-23-95	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-8	12-04-95	449.43	31.99	417.44	ND	NNW	0.03	12-04-95	Not sampled: not scheduled for chemical analysis											
MW-8	02-20-96	449.43	21.13	428.30	ND	NW	0.016	02-20-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-8	05-15-96	449.43	21.96	427.47	ND	NW	0.024	05-15-96	Not sampled: not scheduled for chemical analysis											
MW-8	08-13-96	449.43	30.20	419.23	ND	NNW	0.03	08-13-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--

Table 2
Historical Groundwater Elevation and Analytical Data
Petroleum Hydrocarbons and Their Constituents
1994 - Present*

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designation	Water Level Field Date	Top of Casing Elevation	Depth to Water	Groundwater Elevation	Floating Product Thickness	Groundwater Flow Direction	Hydraulic Gradient	Water Sample Field Date	**TPHG** LUFT Method	**Benzene** EPA 8020	**Toluene** EPA 8020	**Ethylbenzene** EPA 8020	**Total Xylenes** EPA 8020	**MTBE** EPA 8020	**MTBE** EPA 8240	**TPHD** LUFT Method	**TOG** SM 5520F	**TOG** SM 5520C	**TOG** EPA 413.2	**TRPH** EPA 418.1
		ft-MSL	feet	ft-MSL	feet	MWN	ft/ft		µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	mg/L	mg/L	mg/L	mg/L
MW-9	03-26-94	449.21	25.68	423.53	ND	NR	NR	03-26-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-9	06-13-94	449.21	27.69	421.52	ND	NR	NR	06-13-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-9	09-22-94	449.21	31.36	417.85	ND	NNE	0.056	09-22-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-9	11-25-94	449.21	29.84	419.37	ND	N	0.06	11-25-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-9	03-20-95	449.21	19.11	430.10	ND	NW	0.03	03-20-95	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-9	06-02-95	449.21	21.23	427.98	ND	NNW	0.014	06-02-95	Not sampled: not scheduled for chemical analysis											
MW-9	08-23-95	449.21	24.33	424.88	ND	NNW	0.03	08-23-95	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-9	12-04-95	449.21	27.90	421.31	ND	NNW	0.03	12-04-95	Not sampled: not scheduled for chemical analysis											
MW-9	02-20-96	449.21	17.86	431.35	ND	NW	0.016	02-20-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-9	05-15-96	449.21	18.69	430.52	ND	NW	0.024	05-15-96	Not sampled: not scheduled for chemical analysis											
MW-9	08-13-96	449.21	24.17	425.04	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											
MW-10	03-26-94	449.22	26.20	423.02	ND	NR	NR	03-26-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-10	06-13-94	449.22	28.23	420.99	ND	NR	NR	06-13-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-10	09-22-94	449.22	31.79	417.43	ND	NNE	0.056	09-22-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-10	11-25-94	449.22	30.30	418.92	ND	N	0.06	11-25-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-10	03-20-95	449.22	20.96	428.26	ND	NW	0.03	03-20-95	Not sampled: not scheduled for chemical analysis											
MW-10	06-02-95	449.22	22.15	427.07	ND	NNW	0.014	06-02-95	Not sampled: not scheduled for chemical analysis											
MW-10	08-23-95	449.22	24.47	424.75	ND	NNW	0.03	08-23-95	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-10	12-04-95	449.22	26.97	422.25	ND	NNW	0.03	12-04-95	Not sampled: not scheduled for chemical analysis											
MW-10	02-20-96	449.22	18.40	430.82	ND	NW	0.016	02-20-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-10	05-15-96	449.22	Not surveyed: vehicle was parked on well					05-15-96	Not sampled: not scheduled for chemical analysis											
MW-10	08-13-96	449.22	23.70	425.52	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											

Table 2
Historical Groundwater Elevation and Analytical Data
Petroleum Hydrocarbons and Their Constituents
1994 - Present*

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designation	Water Level Field Date	Top of Casing Elevation	Depth to Water	Groundwater Elevation	Floating Product Thickness	Groundwater Flow Direction	Hydraulic Gradient	Water Sample Field Date	**TPHG** LUFT Method	**Benzene** EPA 8020	**Toluene** EPA 8020	**Ethylbenzene** EPA 8020	**Total Xylenes** EPA 8020	**MTBE** EPA 8020	**MTBE** EPA 8240	**TPHD** LUFT Method	**TOG** SM 5520F	**TOG** SM 5520C	**TOG** EPA 413.2	**TRPH** EPA 418.1
		ft-MSL	feet	ft-MSL	feet	MWN	ft/ft		µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	mg/L	mg/L	mg/L	mg/L
MW-11	03-26-94	448.02	30.20	417.82	ND	NR	NR	03-26-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-11	06-13-94	448.02	33.39	414.63	ND	NR	NR	06-13-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-11	09-22-94	448.02	34.75	413.27	ND	NNE	0.056	09-22-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-11	11-25-94	448.02	33.84	414.18	ND	N	0.06	11-25-94	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-11	03-20-95	448.02	25.02	423.00	ND	NW	0.03	03-20-95	<50	<0.5	<0.5	<0.5	<0.5	--	--	--	--	--	--	--
MW-11	06-02-95	448.02	23.82	424.20	ND	NNW	0.014	06-02-95	Not sampled: not scheduled for chemical analysis											
MW-11	08-23-95	448.02	30.15	417.87	ND	NNW	0.03	08-23-95	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-11	12-04-95	448.02	31.63	416.39	ND	NNW	0.03	12-04-95	Not sampled: not scheduled for chemical analysis											
MW-11	02-20-96	448.02	20.94	427.08	ND	NW	0.016	02-20-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
MW-11	05-15-96	448.02	23.03	424.99	ND	NW	0.024	05-15-96	Not sampled: not scheduled for chemical analysis											
MW-11	08-13-96	448.02	29.19	418.83	ND	NNW	0.03	08-13-96	<50	<0.5	<0.5	<0.5	<0.5	<3	--	--	--	--	--	--
RW-1	03-26-94	451.67	27.78	423.89	ND	NR	NR	03-26-94	8100	780	100	360	340	--	--	--	--	--	--	--
RW-1	06-13-94	451.67	29.48	422.19	ND	NR	NR	06-13-94	4900	510	32	150	170	--	--	--	--	--	--	--
RW-1	09-22-94	451.67	30.52	421.15	ND	NNE	0.056	09-22-94	4900	390	30	190	210	--	--	--	--	--	--	--
RW-1	11-25-94	451.67	30.89	420.78	ND	N	0.06	11-25-94	4900	550	68	200	230	--	--	--	--	--	--	--
RW-1	03-20-95	451.67	23.76	427.91	ND	NW	0.03	03-20-95	15000	1000	140	310	950	--	--	--	--	--	--	--
RW-1	06-02-95	451.67	25.12	426.55	ND	NNW	0.014	06-02-95	12000	1300	280	420	1100	--	--	--	--	--	--	--
RW-1	08-23-95	451.67	28.80	422.87	ND	NNW	0.03	08-23-95	8200	520	190	240	610	<50	--	--	--	--	--	--
RW-1	12-04-95	451.67	31.15	420.52	ND	NNW	0.03	12-04-95	2600	140	59	83	210	--	--	--	--	--	--	--
RW-1	02-20-96	451.67	21.45	430.22	ND	NW	0.016	02-20-96	6300	410	160	180	650	<40	--	--	--	--	--	--
RW-1	05-15-96	451.67	22.97	428.70	ND	NW	0.024	05-15-96	Not sampled: not scheduled for chemical analysis											
RW-1	08-13-96	451.67	24.74	426.93	ND	NNW	0.03	08-13-96	Not sampled: not scheduled for chemical analysis											

Table 2
Historical Groundwater Elevation and Analytical Data
Petroleum Hydrocarbons and Their Constituents
1994 - Present*

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designation	Water Level Field Date	Top of Casing Elevation	Depth to Water	Groundwater Elevation	Floating Product Thickness	Groundwater Flow Direction	Hydraulic Gradient	Water Sample Field Date	**TPHG** LUFT Method	**Benzene** EPA 8020	**Toluene** EPA 8020	**Ethylbenzene** EPA 8020	**Total Xylenes** EPA 8020	**MTBE** EPA 8020	**MTBE** EPA 8240	**TPHD** LUFT Method	**TOG** SM 5520F	**TOG** SM 5520C	**TOG** EPA 413.2	**TRPH** EPA 418.1
		ft-MSL	feet	ft-MSL	feet	MWN	ft/ft		µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	µg/L	mg/L	mg/L	mg/L	mg/L

ft-MSL: elevation in feet, relative to mean sea level
MWN: ground-water flow direction and gradient apply to the entire monitoring well network
ft/ft: foot per foot
TPHG: total petroleum hydrocarbons as gasoline, California DHS LUFT Method
µg/L: micrograms per liter
EPA: United States Environmental Protection Agency
MTBE: Methyl-tert-butyl ether
TOG: total oil and grease
SM: standard method
mg/L: milligrams per liter
TRPH: total recoverable petroleum hydrocarbons
NR: not reported; data not available
ND: none detected
NNE: north-northeast
N: north
NW: northwest
NNW: north-northwest
^: method reporting limit was raised due to: (1) high analyte concentration requiring sample dilution, or (2) matrix interference
- -: not analyzed or not applicable
*: For previous historical groundwater elevation and analytical data please refer to *Fourth Quarter 1995 Groundwater Monitoring Program Results and Remediation System Performance Evaluation Report, ARCO Service Station 771, Livermore, California*, (EMCON, March 1, 1996).

Table 3
Approximate Cumulative Floating Product Recovered

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Well Designations	Date	Floating Product Recovered gallons
MW-1, MW-2, and MW-5	1991	2.77
MW-1, MW-2, and MW-5	1992	0.29
MW-1, MW-2, and MW-5	1993	0.00
MW-1, MW-2, and MW-5	1994	0.00
MW-1, MW-2, and MW-5	1995	0.00
MW-1, MW-2, and MW-5	1996	0.00
	1991 to 1996 Total:	3.06

esj/h:\0771\0771mdb.xls\Table 3:imi
20805-122.003

Table 4
Soil-Vapor Extraction System
Operation and Performance Data

Facility Number: 771
Location: 899 Rincon Avenue
Livermore, California

Consultant: EMCON
1921 Ringwood Avenue
San Jose, California

Vapor Treatment Unit: King Buck / 200 cfm
Model MMC-6A/E
catalytic oxidizer

Start-Up Date: 12-20-94
Operation and Performance Data From: 12-20-94
To: 10-01-96
System was shut down on 10-10-95.

Date Begin:		12-20-94	01-01-95	02-01-95	07-01-95	08-01-95
Date End:		01-01-95	02-01-95	07-01-95	08-01-95	09-01-95
Mode of Oxidation:		Catalytic	Catalytic	Catalytic	Catalytic	Catalytic
Days of Operation:		11	11	0	8	14
Days of Downtime:		1	20	150	23	17
Average Vapor Concentrations (1)						
Well Field Influent:	ppmv (2) as gasoline	100	<15	NA	54	33
	mg/m3 (3) as gasoline	300	<60	NA	218	120
	ppmv as benzene	<0.1	<0.1	NA	1.2	0.4
	mg/m3 as benzene	<0.5	<0.5	NA	3.6	1.2
System Influent:	ppmv as gasoline	<15	NA	NA	48	24
	mg/m3 as gasoline	<60	NA	NA	200	87
	ppmv as benzene	<0.1	NA	NA	1.2	0.3
	mg/m3 as benzene	<0.5	NA	NA	3.8	0.8
System Effluent:	ppmv as gasoline	<15	NA	NA	<15	<15
	mg/m3 as gasoline	<60	NA	NA	<60	<60
	ppmv as benzene	<0.1	NA	NA	<0.1	<0.1
	mg/m3 as benzene	<0.5	NA	NA	<0.5	<0.5
Average Well Field Flow Rate (4), scfm (5):		27.3	13.0	0.0	83.3	104.3
Average System Influent Flow Rate (4), scfm:		201.7	180.7	0.0	163.4	170.9
Average Destruction Efficiency (6), percent (7):		NA (13)	NA	NA	70.0 (14)	31.0 (14)
Average Emission Rates (8), pounds per day (9)						
Gasoline:		1.09	0.97	0.00	0.88	0.92
Benzene:		0.01	0.01	0.00	0.01	0.01
Operating Hours This Period:		275.50	269.23	0.00	195.40	342.12
Operating Hours To Date:		275.5	544.7	544.7	740.1	1082.3
Pounds/ Hour Removal Rate, as gasoline (10):		0.03	0.00	0.00	0.07	0.05
Pounds Removed This Period, as gasoline (11):		8.4	0.8	0.0	13.3	16.0
Pounds Removed To Date, as gasoline:		8.4	9.2	9.2	22.5	38.5
Gallons Removed This Period, as gasoline (12):		1.4	0.1	0.0	2.1	2.6
Gallons Removed To Date, as gasoline:		1.4	1.5	1.5	3.6	6.2

Table 4
Soil-Vapor Extraction System
Operation and Performance Data

Facility Number: 771
Location: 899 Rincon Avenue
Livermore, California

Consultant: EMCON
1921 Ringwood Avenue
San Jose, California

Vapor Treatment Unit: King Buck / 200 cfm
Model MMC-6A/E
catalytic oxidizer

Start-Up Date: 12-20-94
Operation and Performance Data From: 12-20-94
To: 10-01-96
System was shut down on 10-10-95.

Date Begin:		09-01-95	10-01-95	01-01-96	04-01-96	07-01-96
Date End:		10-01-95	01-01-96	04-01-96	07-01-96	10-01-96
Mode of Oxidation:		Catalytic	Catalytic	Catalytic	Catalytic	Catalytic
Days of Operation:		27	0	0	0	0
Days of Downtime:		3	92	91	91	92
Average Vapor Concentrations (1)						
Well Field Influent:	ppmv (2) as gasoline	20	NA	NA	NA	NA
	mg/m3 (3) as gasoline	89	NA	NA	NA	NA
	ppmv as benzene	<0.1	NA	NA	NA	NA
	mg/m3 as benzene	<0.5	NA	NA	NA	NA
System Influent:	ppmv as gasoline	18	NA	NA	NA	NA
	mg/m3 as gasoline	79	NA	NA	NA	NA
	ppmv as benzene	<0.1	NA	NA	NA	NA
	mg/m3 as benzene	<0.5	NA	NA	NA	NA
System Effluent:	ppmv as gasoline	<15	NA	NA	NA	NA
	mg/m3 as gasoline	<60	NA	NA	NA	NA
	ppmv as benzene	<0.1	NA	NA	NA	NA
	mg/m3 as benzene	<0.5	NA	NA	NA	NA
Average Well Field Flow Rate (4), scfm (5):		84.0	0.0	0.0	0.0	0.0
Average System Influent Flow Rate (4), scfm:		84.0	0.0	0.0	0.0	0.0
Average Destruction Efficiency (6), percent (7):		24.1 (14)	NA	NA	NA	NA
Average Emission Rates (8), pounds per day (9)						
Gasoline:		0.45	0.00	0.00	0.00	0.00
Benzene:		0.00	0.00	0.00	0.00	0.00
Operating Hours This Period:		654.88	0.00	0.40	0.00	0.00
Operating Hours To Date:		1737.1	1737.1	1737.5	1737.5	1737.5
Pounds/ Hour Removal Rate, as gasoline (10):		0.03	0.00	0.00	0.00	0.00
Pounds Removed This Period, as gasoline (11):		18.3	0.0	0.0	0.0	0.0
Pounds Removed To Date, as gasoline:		56.9	56.9	56.9	56.9	56.9
Gallons Removed This Period, as gasoline (12):		3.0	0.0	0.0	0.0	0.0
Gallons Removed To Date, as gasoline:		9.2	9.2	9.2	9.2	9.2

Table 4
Soil-Vapor Extraction System
Operation and Performance Data

Facility Number: 771	Vapor Treatment Unit: King Buck / 200 cfm
Location: 899 Rincon Avenue	Model MMC-6A/E
Livermore, California	catalytic oxidizer
Consultant: EMCON	Start-Up Date: 12-20-94
1921 Ringwood Avenue	Operation and Performance Data From: 12-20-94
San Jose, California	To: 10-01-96
	System was shut down on 10-10-95.

CURRENT REPORTING PERIOD:	07-01-96	to	10-01-96
DAYS / HOURS IN PERIOD:	92	2208.0	
DAYS / HOURS OF OPERATION:	0	0.0	
DAYS / HOURS OF DOWN TIME:	92	2208.0	
PERCENT OPERATIONAL:		0.0	%
PERIOD POUNDS REMOVED:	0.0		
PERIOD GALLONS REMOVED:	0.0		
AVERAGE SYSTEM INFLUENT FLOW RATE (scfm):		0.0	

1. Average concentrations are based on discrete sample results reported during the month; refer to Appendix C for discrete sample results.
2. ppmv: parts per million by volume
3. mg/m3: milligrams per cubic meter
4. Average flow rates (time weighted average) are based on instantaneous flow rates recorded during the month; refer to Appendix C for instantaneous flow data.
5. scfm: flow in standard cubic feet per minute at one atmosphere and 70 degrees Fahrenheit
6. Average destruction efficiencies are calculated using monthly average concentrations; refer to Appendix C for instantaneous destruction efficiency data.
7. destruction efficiency, percent = ([system influent concentration (as gasoline in mg/m3) - system effluent concentration (as gasoline in mg/m3)] / system influent concentration (as gasoline in mg/m3)) x 100 percent
8. Average emission rates are calculated using monthly average concentrations and flow rates; refer to Appendix C for instantaneous emission rate data.
9. emission rates (pounds per day) = system effluent concentration (as gasoline or benzene in mg/m3) x system influent flow rate (scfm) x 0.02832 m3/ft3 x 1440 minutes/day x 1 pound/454,000 mg
10. pounds/ hour removal rate (as gasoline) = well field influent concentration (as gasoline in mg/m3) x well field influent flow rate (scfm) x 0.02832 m3/ft3 x 60 minutes/hour x 1 pound/454,000 mg
11. pounds removed this period (as gasoline) = pounds/ hour removal rate x hours of operation
12. gallons removed this period (as gasoline) = pounds removed this period (as gasoline) x 0.1613 gallons/pound of gasoline
13. NA: not analyzed, not available, or not applicable
14. Although the destruction efficiency appeared to be less than 90 percent, laboratory analytical results collected during this period indicate the effluent TVHG and benzene concentrations in off-gas discharged to the atmosphere were below laboratory detection limits, indicating compliance with BAAQMD discharge requirements.

Table 5
Soil-Vapor Extraction Well Data

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Date	Well Identification											
	VW-1			MW-1			MW-2			MW-4		
	Valve Position	TVHG ppmv	Vacuum Response in-H2O	Valve Position	TVHG ppmv	Vacuum Response in-H2O	Valve Position	TVHG ppmv	Vacuum Response in-H2O	Valve Position	TVHG ppmv	Vacuum Response in-H2O
12-20-94	open	177 LAB	32.5	passive	NA	NA	passive	NA	NA	open	53 LAB	25.0
01-17-95	System shut down											
07-12-95	System was restarted											
07-12-95	open	NA	NA	open	NA	NA	open	NA	NA	open	NA	NA
08-01-95	open	NA	NA	open	NA	NA	open	NA	NA	open	NA	NA
08-29-95	open	NA	NA	open	NA	NA	open	NA	NA	open	NA	NA
09-18-95	open	44.8 PID	53.7	open	10.7 PID	56.9	open	12.0 PID	52.8	open	13.3 PID	54.7
09-18-95	open (b)	66.8 PID	56.0	open (b)	113 PID	58.2	open (b)	25.9 PID	55.1	open (b)	21.8 PID	56.9
10-10-95	open	NA	NA	open	NA	NA	open	NA	NA	open	NA	NA
10-10-95	System shut down											
12-19-95	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA
02-08-96	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA
02-14-96	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA
03-22-96	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA
04-09-96	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA
05-17-96	closed	NA	NA	closed	NA	NA	closed	NA	NA	closed	NA	NA
06-07-96	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA
06-25-96	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA
07-10-96	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA	closed (b)	NA	NA
08-05-96	closed	NA	NA	closed	NA	NA	closed	NA	NA	closed	NA	NA

TVHG: concentration of total volatile hydrocarbons as gasoline
ppmv: parts per million by volume
in-H2O: inches of water
open: open to the system
open (b): open to the system and bubbling air at 1 scfm per well
passive: open to the atmosphere
closed: closed to the system and atmosphere
closed (b): closed to the system and atmosphere, but bubbling air at 1 scfm per well
NA: not analyzed or not measured
FID: TVHG concentration was measured with a portable flame ionization detector
LAB: TVHG concentration was analyzed in the laboratory

Table 5
Soil-Vapor Extraction Well Data

ARCO Service Station 771
899 Rincon Avenue, Livermore, California

Date: 11-26-96

Date	Well Identification							
	MW-5			MW-7			Bubbler-Only Well	
	Valve Position	TVHG ppmv	Vacuum Response in-H2O	Valve Position	TVHG ppmv	Vacuum Response in-H2O	RW-1	
12-20-94	passive	NA	NA	passive	NA	NA		
01-17-95	System shut down							
07-12-95	System was restarted							
07-12-95	open	NA	NA	open	NA	NA		
08-01-95	open	NA	NA	open	NA	NA		
08-29-95	open	NA	NA	open	NA	NA		
09-18-95	open	11.2 PID	55.9	open	19.0 PID	53.9		
09-18-95	open (b)	117 PID	58.0	open (b)	20.0 PID	56.2		
10-10-95	open	NA	NA	open	NA	NA		
10-10-95	System shut down							
12-19-96	closed (b)	NA	NA	closed (b)	NA	NA		
02-08-96	closed (b)	NA	NA	closed (b)	NA	NA	bubbling	
02-14-96	closed (b)	NA	NA	closed (b)	NA	NA	bubbling	
03-22-96	closed (b)	NA	NA	closed (b)	NA	NA	bubbling	
04-09-96	closed (b)	NA	NA	closed (b)	NA	NA	bubbling	
05-17-96	closed	NA	NA	closed	NA	NA		
06-07-96	closed (b)	NA	NA	closed (b)	NA	NA	bubbling	
06-25-96	closed (b)	NA	NA	closed (b)	NA	NA	bubbling	
07-10-96	closed (b)	NA	NA	closed (b)	NA	NA	bubbling	
08-05-96	closed	NA	NA	closed	NA	NA		

TVHG: concentration of total volatile hydrocarbons as gasoline
ppmv: parts per million by volume
in-H2O: inches of water
open: open to the system
open (b): open to the system and bubbling air at 1 scfm per well
passive: open to the atmosphere
closed: closed to the system and atmosphere
closed (b): closed to the system and atmosphere, but bubbling air at 1 scfm per well
NA: not analyzed or not measured
FID: TVHG concentration was measured with a portable flame ionization detector
LAB: TVHG concentration was analyzed in the laboratory

Table 6
Air-Bubbling System
Operation and Performance Data

Facility Number: 771
Location: 899 Rincon Avenue
Livermore, California

Consultant: EMCON
1921 Ringwood Avenue
San Jose, California

Air-Bubbling Unit:
3-horsepower Conde blower

Start-Up Date: 07-12-96
Operation and Performance Data From: 07-12-96
To: 10-01-96

Air-Bubbling system was shut down on 8-5-96, for groundwater monitoring event.

Date:		Before start-up	07-12-95	08-29-95	09-18-95	09-18-95	10-10-95
Air-Bubbling Well Status:		See Table 6 for the status of the 7 air-bubbling wells.					
Air-Bubbling Pressure (psig) (1):		0.0	10.0	8.0	8.0	0.0	0.0
Air-Bubbling Flow Rate (scfm) (2):		- - (4)	- -	- -	- -	- -	- -
Dissolved Oxygen (ppm) (3):							
Air-Bubbling Wells:	VW-1	1.0	- -	- -	- -	- -	7.8
	MW-1	1.0	- -	- -	- -	- -	8.4
	MW-2	0.9	- -	- -	- -	- -	7.9
	MW-4	0.9	- -	- -	- -	- -	5.3
	MW-5	1.1	- -	- -	- -	- -	8.9
	MW-7	1.0	- -	- -	- -	- -	7.9
	RW-1	0.8	- -	- -	- -	- -	6.4

Table 6
Air-Bubbling System
Operation and Performance Data

Facility Number: 771
Location: 899 Rincon Avenue
Livermore, California

Consultant: EMCON
1921 Ringwood Avenue
San Jose, California

Air-Bubbling Unit:
3-horsepower Conde blower

Start-Up Date: 07-12-96
Operation and Performance Data From: 07-12-96
To: 10-01-96

Air-Bubbling system was shut down on 8-5-96, for groundwater monitoring event.

Date:		12-19-95	01-19-96	02-08-96 (5)	02-14-96	02-26-96	03-22-96
Air-Bubbling Well Status:		See Table 6 for the status of the 7 air-bubbling wells.					
Air-Bubbling Pressure (psig):		--	--	11.0	10.0	9.0	--
Air-Bubbling Flow Rate (scfm) (3):		--	--	--	--	--	--
Dissolved Oxygen (ppm) (4):							
Air-Bubbling Wells:	VW-1	0.2	0.8	--	8.9	--	9.2
	MW-1	0.4	0.9	--	8.8	--	9.0
	MW-2	0.4	0.9	--	9.3	--	8.8
	MW-4	0.4	0.9	--	8.9	--	8.6
	MW-5	0.9	1.8	--	9.1	--	8.4
	MW-7	0.3	1.0	--	9.0	--	8.2
	RW-1	--	--	--	--	--	--

Table 6
Air-Bubbling System
Operation and Performance Data

Facility Number: 771
Location: 899 Rincon Avenue
Livermore, California

Consultant: EMCON
1921 Ringwood Avenue
San Jose, California

Air-Bubbling Unit:
3-horsepower Conde blower

Start-Up Date: 07-12-96
Operation and Performance Data From: 07-12-96
To: 10-01-96

Air-Bubbling system was shut down on 8-5-96, for groundwater monitoring event.

Date:		04-09-96	05-15-96	05-17-96	06-07-96	07-10-96	08-05-96
Air-Bubbling Well Status:		See Table 6 for the status of the 7 air-bubbling wells.					
Air-Bubbling Pressure (psig):		--	--	8.0	8.0	8.0	8.0
Air-Bubbling Flow Rate (scfm) (3):		--	--	10.9	10.9	10.9	10.9
Dissolved Oxygen (ppm) (4):							
Air-Bubbling Wells:	VW-1	8.7	1.5	--	--	2.5	1.0
	MW-1	8.7	1.0	--	--	2.2	2.0
	MW-2	8.9	1.5	--	--	2.1	1.5
	MW-4	9.0	<1.0	--	--	2.0	1.5
	MW-5	9.2	<1.0	--	--	4.9	1.5
	MW-7	9.0	1.0	--	--	5.2	1.0
	RW-1	--	<1.0	--	--	4.8	1.0

Table 6
Air-Bubbling System
Operation and Performance Data

Facility Number: 771	Air-Bubbling Unit:
Location: 899 Rincon Avenue Livermore, California	3-horsepower Conde blower
Consultant: EMCON 1921 Ringwood Avenue San Jose, California	Start-Up Date: 07-12-96 Operation and Performance Data From: 07-12-96 To: 10-01-96

Air-Bubbling system was shut down on 8-5-96, for groundwater monitoring event.

CURRENT REPORTING PERIOD:	07-01-96	to	10-01-96
DAYS / HOURS IN PERIOD:	92		2208

1. psig: pounds per square inch gauge
2. scfm: standard cubic feet per minute at 14.7 psi and 70° F
3. ppm: parts per million
4. - - : not analyzed, not applicable, or not available
5. On February 8, 1996 a timer was installed on the air-bubbling system.
   Since February 8, 1996, the air bubbling system has been pulsed hourly.

152753

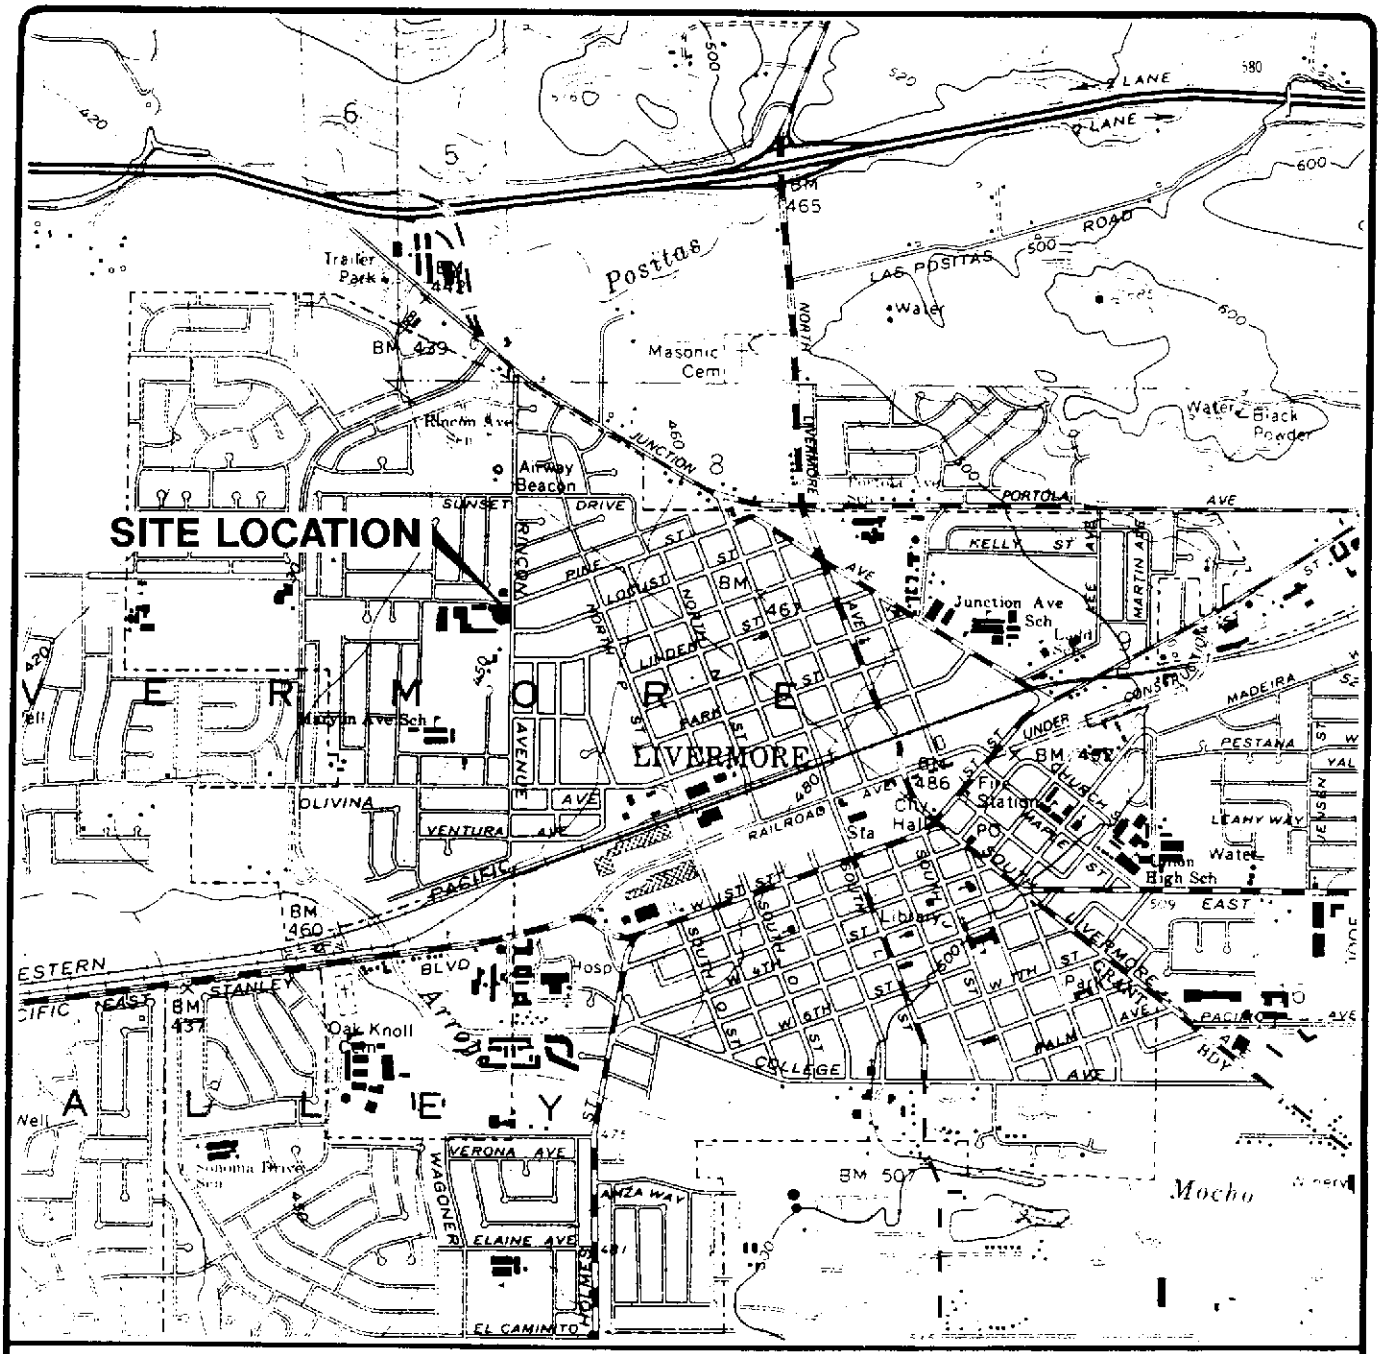

EMCON

ARCO PRODUCTS COMPANY
SERVICE STATION 771, 899 RINCON AVENUE
QUARTERLY GROUNDWATER MONITORING
LIVERMORE, CALIFORNIA

SITE LOCATION

FIGURE
1
PROJECT NO.
805-122.03

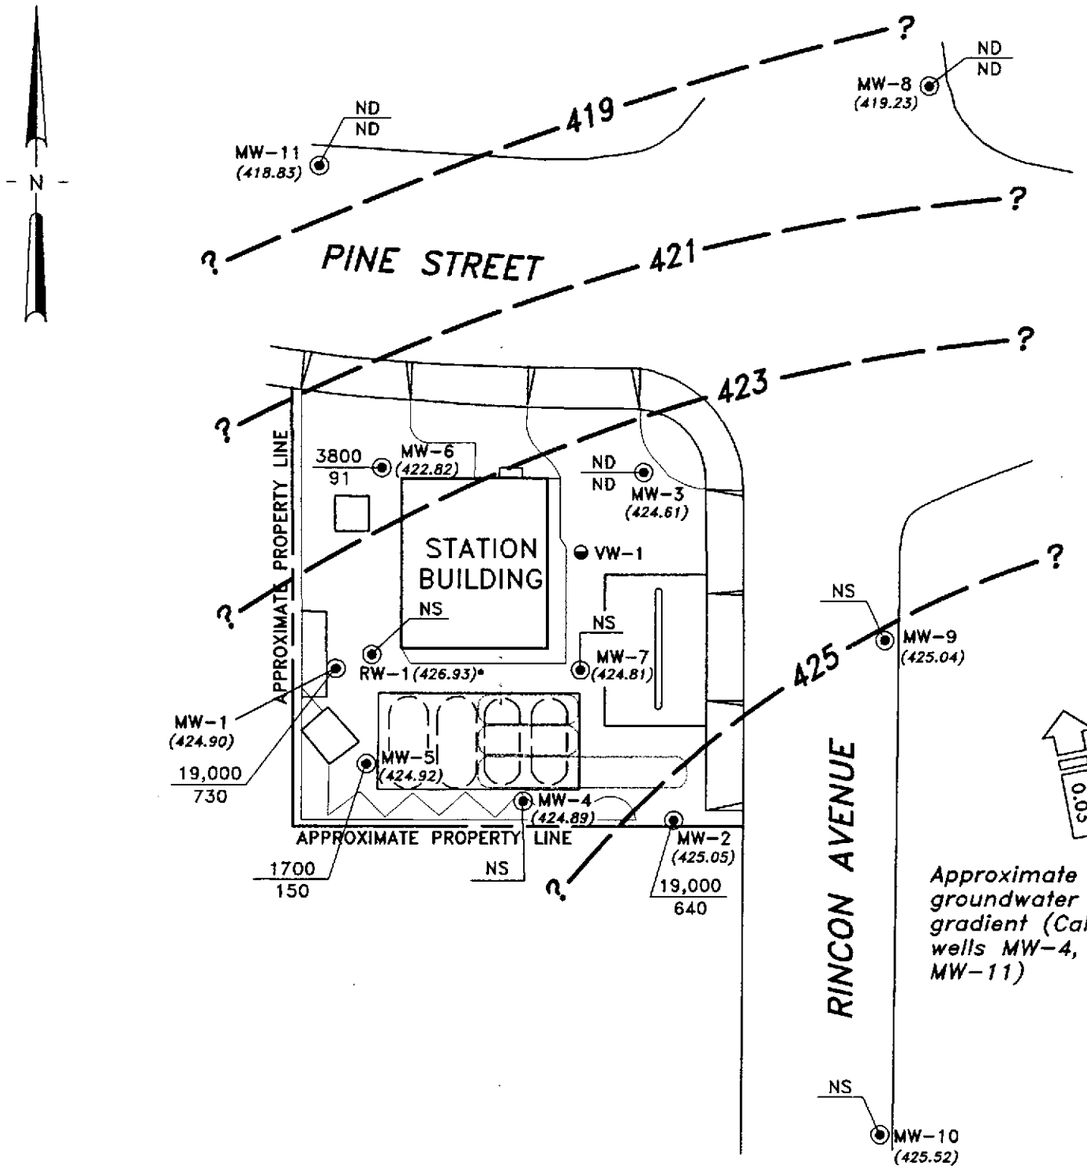

Approximate direction of groundwater flow showing gradient (Calculated using wells MW-4, MW-8, and MW-11)

EXPLANATION

- ⊙ Groundwater monitoring well
- ◒ Vapor extraction well
- Former underground gasoline storage tank
- Existing underground gasoline storage tank
- (424.90) Groundwater elevation (Ft.–MSL) measured 8/13/96
- ? Groundwater elevation contour (Ft.–MSL)
- 19,000 / 730 TPHG concentration in groundwater (ug/L); sampled 8/13/96
- Benzene concentration in groundwater (ug/L); sampled 8/13/96
- ND Not detected at or above the method reporting limit for TPHG (50 ug/L) and benzene (0.5 ug/L)
- NS Not sampled; not scheduled for chemical analysis
- * Groundwater elevation not used in contouring

EMCON

SCALE: 0 40 80 FEET
(Approximate)

ARCO PRODUCTS COMPANY
SERVICE STATION 771, 899 RINCON AVENUE
QUARTERLY GROUNDWATER MONITORING
LIVERMORE, CALIFORNIA

GROUNDWATER DATA
THIRD QUARTER 1996

FIGURE NO.
2

PROJECT NO.
805–122.003

G:\805-122\GOO REV 0 11/21/96 12:25:17 DD DJ

Figure 3

ARCO Service Station 771
Soil-Vapor Extraction and Treatment System
Historical Well Field Influent TVHG and Benzene Concentrations

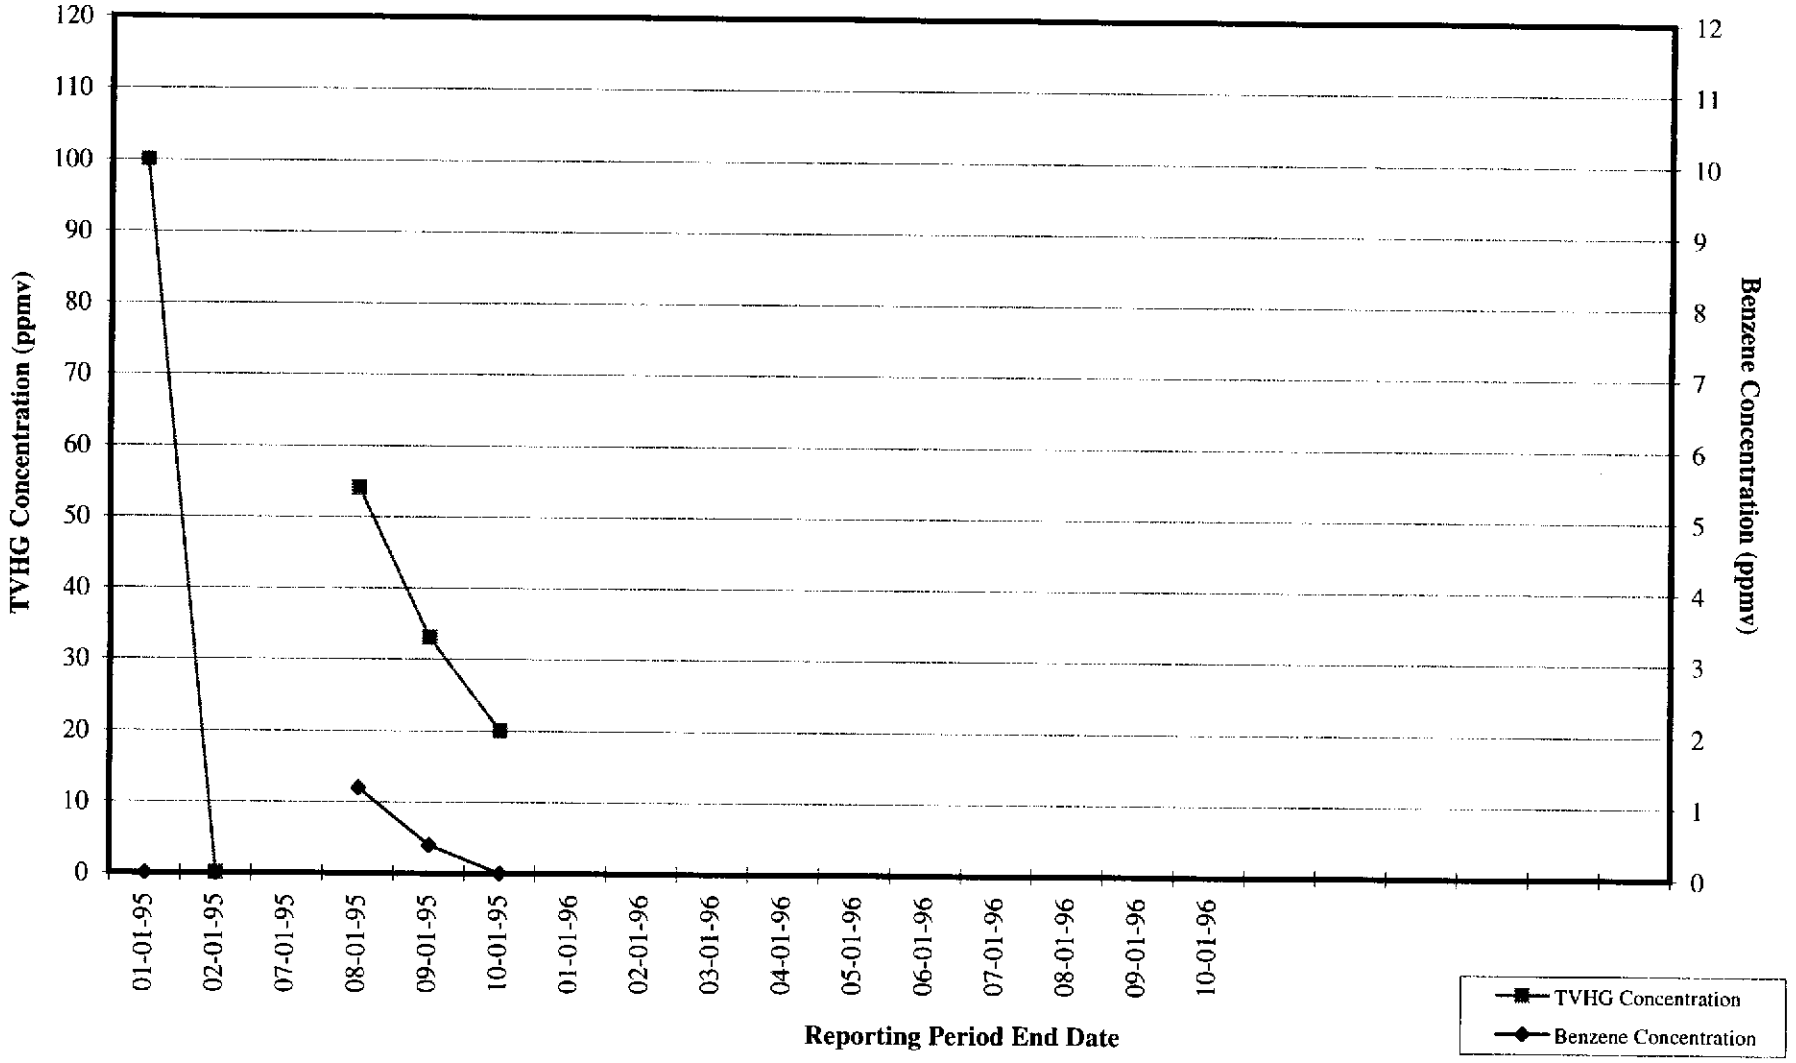

TVHG: total volatile hydrocarbons as gasoline
ppmv: parts per million by volume

esj/h:\0771\0771tdb.xls\SVE Model:imi
20805-122.003

Figure 4

ARCO Service Station 771
Soil-Vapor Extraction and Treatment System
Historical Hydrocarbon Removal Rates

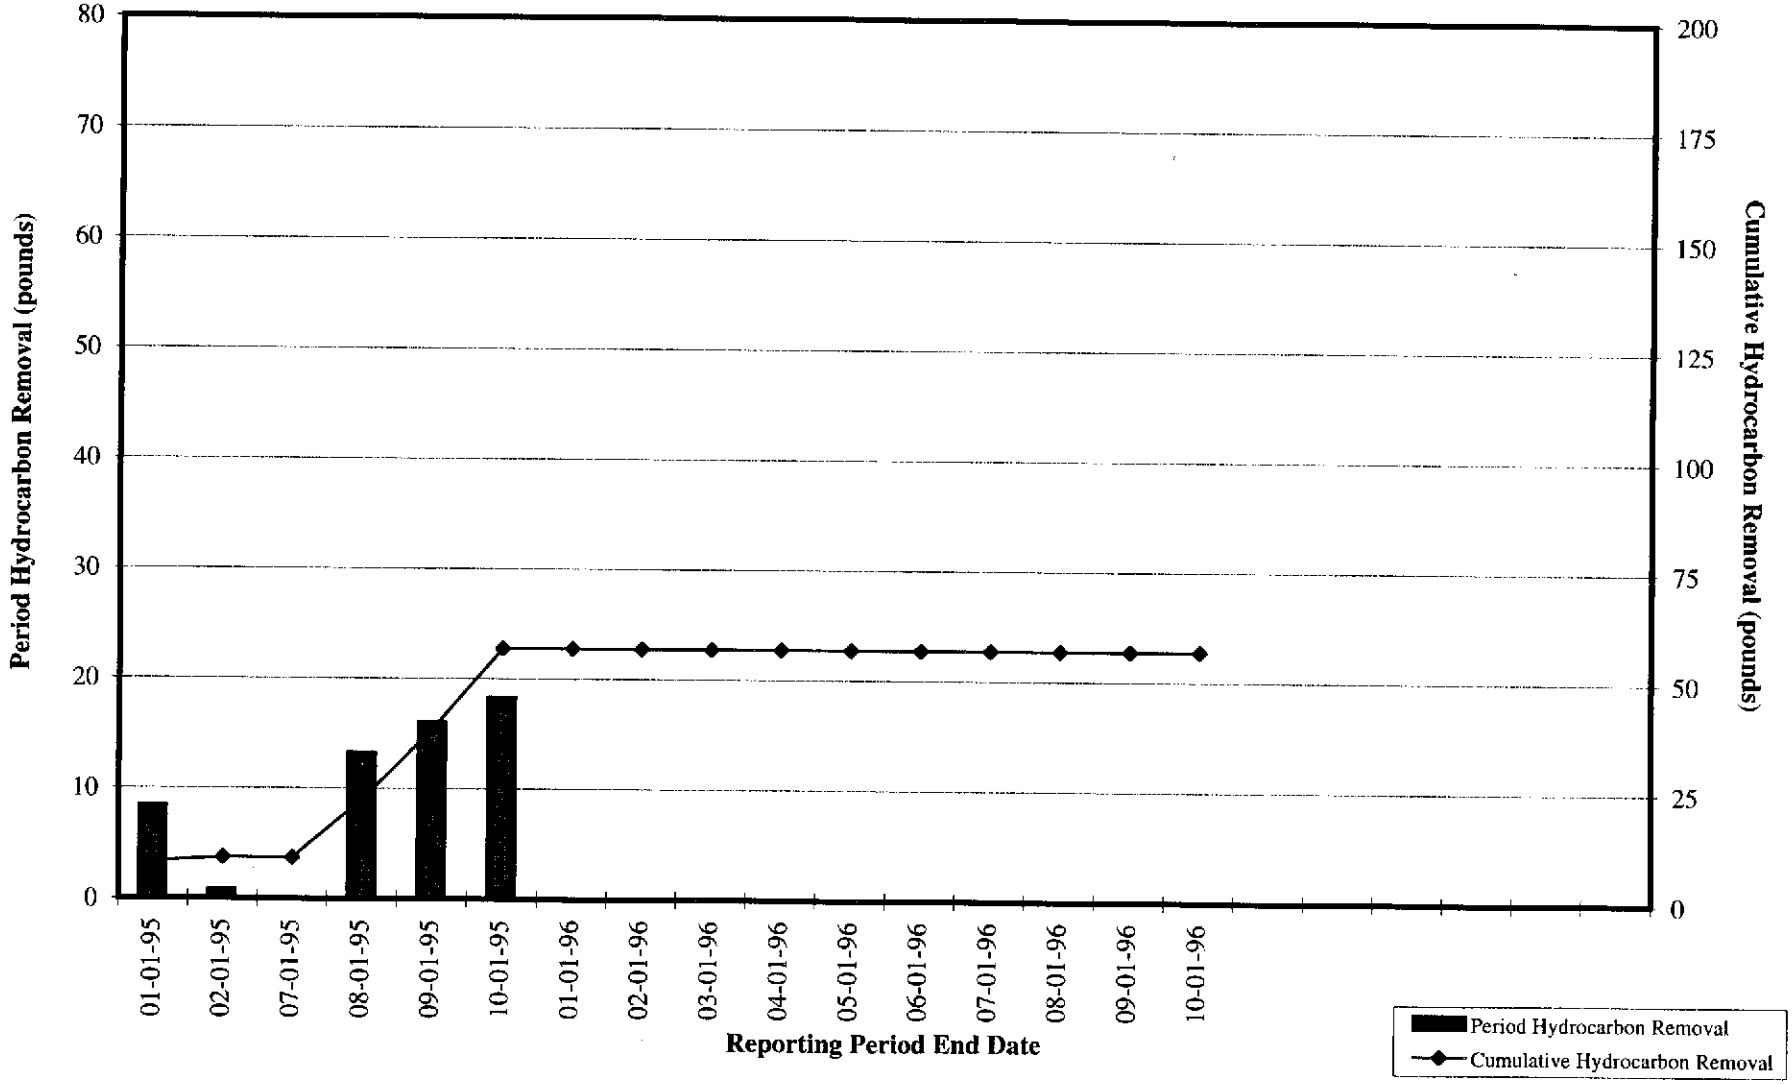

esj/h:\0771\0771tdb.xls\SVE Model:ini
20805-122.003

APPENDIX A

FIELD DATA SHEETS, THIRD QUARTER 1996 GROUNDWATER MONITORING EVENT

FIELD REPORT
DEPTH TO WATER / FLOATING PRODUCT SURVEY

PROJECT # : 21775-213.002 STATION ADDRESS : 899 Rincon Avenue, Livermore DATE : 7-13-96

ARCO STATION # : 771 FIELD TECHNICIAN : M. Ross DAY : Tuesday

DTW Order	WELL ID	Well Box Seal	Well Lid Secure	Gasket Present	Lock Number	Type Of Well Cap	FIRST DEPTH TO WATER (feet)	SECOND DEPTH TO WATER (feet)	DEPTH TO FLOATING PRODUCT (feet)	FLOATING PRODUCT THICKNESS (feet)	WELL TOTAL DEPTH (feet)	COMMENTS
1	MW-8	OK	Yes	Yes	3499	LW	30.20	30.20	NA	NA	41.6	
2	MW-9	OK	Yes	Yes	3499	LW	24.17	24.17	NA	NA	39.0	
3	MW-10	OK	Yes	Yes	3499	LW	23.70	23.70	NA	NA	35.9	
4	MW-11	OK	Yes	Yes	3499	LW	29.19	29.19	NA	NA	38.5	
5	MW-3	OK	Yes		3499	LW	25.67	25.67	NA	NA	39.5	No ARCO BOLT
6	MW-6	OK	Yes	Yes	3499	LW	28.55	28.55	NA	NA	43.2	
7	MW-5	OK	Yes	NO	NONE	SLOTTED CAP	26.48	26.48	NA	NA	40.0	D.O. reading- 2 NEED ARCO BOLT
8	RW-1	OK	NO	Yes	NONE	LW	24.74	24.74	NA	NA	39.9	D.O. reading- 2 WELL CAP WAS NOT SECURE
9	MW-4	OK	NO	NO	NONE	LW	26.20	26.20	NA	NA	41.1	D.O. reading- 1 NO LOCK
10	MW-2	OK	NO	NO	NONE	LW	24.44	24.44	NA	NA	37.7	D.O. reading- 1 NO BOLT
11	MW-1	OK	Yes	NO	NONE	SLOTTED CAP	26.83	26.83	NA	NA	36.5	D.O. reading- 1
12	MW-7	OK	NO	NO	NONE	SLOTTED CAP	25.52	25.52	NA	NA	39.7	D.O. reading- 1 NO BOLTS
13	VW-1	OK	NO	NO	NONE	LW	22.00	22.00	NA	NA	28.0	D.O. reading- 2 NO BOLTS

SURVEY POINTS ARE TOP OF WELL CASINGS

WELL LIDS AND ALL MISSING BOLTS

Rev. 3, 2/94

WATER SAMPLE FIELD DATA SHEET

EMCON ASSOCIATES

PROJECT NO: 21775-213-002 SAMPLE ID: MW-1 (36')

PURGED BY: M. Gallegos CLIENT NAME: ARCO #771

SAMPLED BY: ✓ LOCATION: Livermore, CA

TYPE: Ground Water X Surface Water ___ Treatment Effluent ___ Other ___

CASING DIAMETER (inches): 2 ___ 3 ___ 4 X 4.5 ___ 6 ___ Other ___

CASING ELEVATION (feet/MSL): N/R VOLUME IN CASING (gal.): 6.31

DEPTH TO WATER (feet): 26.83 CALCULATED PURGE (gal.): 18.95

DEPTH OF WELL (feet): 36.5 ACTUAL PURGE VOL. (gal.): 19.0

DATE PURGED: 8-13-96 Start (2400 Hr) 1228 End (2400 Hr) 1240

DATE SAMPLED: ✓ Start (2400 Hr) 1250 End (2400 Hr) ___

TIME (2400 Hr)	VOLUME (gal.)	pH (units)	E.C. (µmhos/cm @ 25° C)	TEMPERATURE (°F)	COLOR (visual)	TURBIDITY (visual)
1233	6.5	7.11	882	81.0	Clear	Clear
1236	13.0	6.97	900	77.0	↓	↓
1240	19.0	6.98	907	77.3	↓	↓

D. O. (ppm): ~~N/R~~ ODOR: moderate

COLOR (COBALT 0 - 500): N/R TURBIDITY (NTU 0 - 200 or 0 - 1000): N/R

Field QC samples collected at this well: N/R

Parameters field filtered at this well: N/R

PURGING EQUIPMENT

- ___ 2" Bladder Pump
- X Centrifugal Pump
- ___ Submersible Pump
- ___ Well Wizard™
- ___ Bailer (Teflon®)
- ___ Bailer (PVC)
- ___ Bailer (Stainless Steel)
- ___ Dedicated
- Other: ___

SAMPLING EQUIPMENT

- ___ 2" Bladder Pump
- ___ DDL Sampler
- ___ Dipper
- ___ Well Wizard™
- X Bailer (Teflon®)
- ___ Bailer (Stainless Steel)
- ___ Submersible Pump
- ___ Dedicated
- Other: ___

WELL INTEGRITY: Good LOCK #: ARCO-key

REMARKS: all samples to Kas

Meter Calibration: Date: 8-13-96 Time: ___ Meter Serial #: 9204 Temperature °F: ___

(EC 1000 ___ / ___) (DI ___) (pH 7 ___ / ___) (pH 10 ___ / ___) (pH 4 ___ / ___)

Location of previous calibration: MW-5

Signature: [signature] Reviewed By: [signature] Page 1 of 7

WATER SAMPLE FIELD DATA SHEET

Rev. 3, 2/94

EMCON ASSOCIATES

PROJECT NO: 21775-213-002 SAMPLE ID: MW-2(37')

PURGED BY: M. Collins CLIENT NAME: APCO # 771

SAMPLED BY: V LOCATION: Livermore, CA

TYPE: Ground Water X Surface Water ___ Treatment Effluent ___ Other ___

CASING DIAMETER (inches): 2 ___ 3 ___ 4 X 4.5 ___ 6 ___ Other ___

CASING ELEVATION (feet/MSL): NR VOLUME IN CASING (gal.): 8.66

DEPTH TO WATER (feet): 24.44 CALCULATED PURGE (gal.): 25.98

DEPTH OF WELL (feet): 32.7 ACTUAL PURGE VOL. (gal.): 26.0

DATE PURGED: 8-13-96 Start (2400 Hr) 1325 End (2400 Hr) 1345

DATE SAMPLED: V Start (2400 Hr) 1352 End (2400 Hr) —

TIME (2400 Hr)	VOLUME (gal.)	pH (units)	E.C. (µmhos/cm @ 25° C)	TEMPERATURE (°F)	COLOR (visual)	TURBIDITY (visual)
1331	8.5	7.40	1018	77.5	Clear	Light
1338	17.0	7.48	1160	80.1	Clear	Light
1345	26.0	7.49	1152	79.4	"	"

D. O. (ppm): NR ODOR: Strong

Field QC samples collected at this well: NR

Parameters field filtered at this well: NR

COLOR (COBALT 0 - 500): NR

TURBIDITY (visual) (NTU 0 - 200 or 0 - 1000): NR

PURGING EQUIPMENT

___ 2" Bladder Pump
X Centrifugal Pump
___ Submersible Pump
___ Well Wizard™
___ Bailer (Teflon®)
___ Bailer (PVC)
___ Bailer (Stainless Steel)
___ Dedicated
Other: ___

SAMPLING EQUIPMENT

___ 2" Bladder Pump
___ DDL Sampler
___ Dipper
___ Well Wizard™
X Bailer (Teflon®)
___ Bailer (Stainless Steel)
___ Submersible Pump
___ Dedicated
Other: ___

WELL INTEGRITY: Good LOCK #: Arrowkey

REMARKS: All Sample taken

Meter Calibration: Date: 8/13/96 Time: ___ Meter Serial #: 9204 Temperature °F: ___

(EC 1000 ___ / ___) (DI ___) (pH 7 ___ / ___) (pH 10 ___ / ___) (pH 4 ___ / ___)

Location of previous calibration: MW-5

Signature: [signature] Reviewed By: [signature] Page 2 of 7

Rev. 3, 2/94

WATER SAMPLE FIELD DATA SHEET

EMCON ASSOCIATES

PROJECT NO: 21775-215.002 SAMPLE ID: MW-3

PURGED BY: M. Ross CLIENT NAME: ARCO 771

SAMPLED BY: M. Ross LOCATION: Livermore, CA

TYPE: Ground Water ✓ Surface Water ___ Treatment Effluent ___ Other ___

CASING DIAMETER (inches): 2 ___ 3 ___ 4 ✓ T.94 4.5 ___ 6 ___ Other ___

CASING ELEVATION (feet/MSL):	NA	VOLUME IN CASING (gal.):	8.86
DEPTH TO WATER (feet):	21.03	CALCULATED PURGE (gal.):	26.59
DEPTH OF WELL (feet):	39.6	ACTUAL PURGE VOL. (gal.):	19.0

DATE PURGED: 2-13-96 Start (2400 Hr) 1240 End (2400 Hr) 1249

DATE SAMPLED: 2-13-96 Start (2400 Hr) 1300 End (2400 Hr) —

TIME (2400 Hr)	VOLUME (gal.)	pH (units)	E.C. (µmhos/cm @ 25° C)	TEMPERATURE (°F)	COLOR (visual)	TURBIDITY (visual)
1244	9.0	7.06	783	75.9	clr	clr
1247	13.0	7.02	807	73.2	clr	clr
1249	DRY	cut	19.0 GALLONS			
1256	START	→	33.59			
1300	Recharge	7.05	866	78.5	clr	clr

D. O. (ppm): NA ODOR: NONE

COLOR (visual)	TURBIDITY (visual)
NA	NA
(COBALT 0 - 500)	(NTU 0 - 200 or 0 - 1000)

Field QC samples collected at this well: NA

Parameters field filtered at this well: NA

PURGING EQUIPMENT

___ 2" Bladder Pump ___ Bailer (Teflon®)
___ Centrifugal Pump ___ Bailer (PVC)
✓ Submersible Pump ___ Bailer (Stainless Steel)
___ Well Wizard™ ___ Dedicated
Other: ___

SAMPLING EQUIPMENT

___ 2" Bladder Pump ✓ Bailer (Teflon®)
___ DDL Sampler ___ Bailer (Stainless Steel)
___ Dipper ___ Submersible Pump
___ Well Wizard™ ___ Dedicated
Other: ___

WELL INTEGRITY: Good LOCK #: 3499

REMARKS: WELL PURGED at 19.0 GALLONS

Meter Calibration: Date: 2-13-96 Time: 1115 Meter Serial #: 9210 Temperature °F: ___

(EC 1000 ___ / ___) (DI ___) (pH 7 ___ / ___) (pH 10 ___ / ___) (pH 4 ___ / ___)

Location of previous calibration: MW-8

Signature: [signature] Reviewed By: [signature] Page 3 of 7

Rev. 3, 2/94

WATER SAMPLE FIELD DATA SHEET

EMCON ASSOCIATES

PROJECT NO: 2175-212-002 SAMPLE ID: MW-5 (40')

PURGED BY: M. Gill-605 CLIENT NAME: ARCO #771

SAMPLED BY: ↓ LOCATION: Livermore, CA

TYPE: Ground Water Y Surface Water ___ Treatment Effluent ___ Other ___

CASING DIAMETER (inches): 2 ___ 3 ___ 4 X 4.5 ___ 6 ___ Other ___

CASING ELEVATION (feet/MSL): N/R VOLUME IN CASING (gal.): 8.83

DEPTH TO WATER (feet): 26.48 CALCULATED PURGE (gal.): 26.49

DEPTH OF WELL (feet): 40.0 ACTUAL PURGE VOL. (gal.): 26.5

DATE PURGED: 8-13-96 Start (2400 Hr) 1145 End (2400 Hr) 1159

DATE SAMPLED: ↓ Start (2400 Hr) 1205 End (2400 Hr) ___

TIME (2400 Hr)	VOLUME (gal.)	pH (units)	E.C. (µmhos/cm @ 25° C)	TEMPERATURE (°F)	COLOR (visual)	TURBIDITY (visual)
1151	9.0	6.87	1067	77.4	Clear	Clear
1155	18.0	7.28	1138	79.2	↓	↓
1159	26.5	7.30	1130	78.9	↓	↓

D. O. (ppm): NL ODOR: moderate

COLOR (COBALT 0 - 500): N/R

TURBIDITY (NTU 0 - 200 or 0 - 1000): N/R

Field QC samples collected at this well: NL

Parameters field filtered at this well: NL

PURGING EQUIPMENT

- ___ 2" Bladder Pump
- X Centrifugal Pump
- ___ Submersible Pump
- ___ Well Wizard™
- ___ Bailer (Teflon®)
- ___ Bailer (PVC)
- ___ Bailer (Stainless Steel)
- ___ Dedicated

Other: ___

SAMPLING EQUIPMENT

- ___ 2" Bladder Pump
- ___ DDL Sampler
- ___ Dipper
- ___ Well Wizard™
- X Bailer (Teflon®)
- ___ Bailer (Stainless Steel)
- ___ Submersible Pump
- ___ Dedicated

Other: ___

WELL INTEGRITY: Good LOCK #: ARCO-Key

REMARKS: All Samples taken.

Meter Calibration: Date: 8-13-96 Time: 1140 Meter Serial #: 9204 Temperature °F: 85.5

(EC 1000 995 / 1000) (DI ___) (pH 7 702 / 700) (pH 10 9.8 / 10.0) (pH 4 399 / ___)

Location of previous calibration: ___

Signature: [signature] Reviewed By: [signature] Page 4 of 7

Rev. 3, 2/94

WATER SAMPLE FIELD DATA SHEET

EMCON ASSOCIATES

PROJECT NO: 21775-213.002 SAMPLE ID: MW-6

PURGED BY: M. ROSS CLIENT NAME: ARCO 771

SAMPLED BY: M. ROSS LOCATION: Livermore, CA

TYPE: Ground Water ✓ Surface Water ___ Treatment Effluent ___ Other ___

CASING DIAMETER (inches): 2 ___ 3 ___ 4 ✓ 4.5 ___ 6 ___ Other ___

CASING ELEVATION (feet/MSL):	NA	VOLUME IN CASING (gal.):	9.59
DEPTH TO WATER (feet):	28.52	CALCULATED PURGE (gal.):	28.77
DEPTH OF WELL (feet):	43.2	ACTUAL PURGE VOL. (gal.):	28.0

DATE PURGED: 8-13-96 Start (2400 Hr) 1324 End (2400 Hr) 1349

DATE SAMPLED: 8-13-96 Start (2400 Hr) 1355 End (2400 Hr) —

TIME (2400 Hr)	VOLUME (gal.)	pH (units)	E.C. (µmhos/cm @ 25° C)	TEMPERATURE (°F)	COLOR (visual)	TURBIDITY (visual)
1330	10.0	6.34	809	77.8	clr	clr
1336	19.5	6.83	853	74.7	clr	clr
1340	~~20.0~~	DRY at	26.0	GALLONS		
1347	DTW	→	39.13			
1355	Recharge	6.91	936	77.9	clr	clr

D. O. (ppm): NA ODOR: NONE

COLOR (visual): NA (COBALT 0 - 500)

TURBIDITY (visual): NA (NTU 0 - 200 or 0 - 1000)

Field QC samples collected at this well: NA

Parameters field filtered at this well: NA

PURGING EQUIPMENT

___ 2" Bladder Pump ___ Bailer (Teflon®)
___ Centrifugal Pump ___ Bailer (PVC)
✓ Submersible Pump ___ Bailer (Stainless Steel)
___ Well Wizard™ ___ Dedicated
Other: ___

SAMPLING EQUIPMENT

___ 2" Bladder Pump ✓ Bailer (Teflon®)
___ DDL Sampler ___ Bailer (Stainless Steel)
___ Dipper ___ Submersible Pump
___ Well Wizard™ ___ Dedicated
Other: ___

WELL INTEGRITY: GOOD LOCK #: 3499

REMARKS: NEEDS NEW WELL CAP

DRY at 26.0 GALLONS

Meter Calibration: Date: 8-13-96 Time: 1115 Meter Serial #: 9210 Temperature °F: ___

(EC 1000 ___ / ___) (DI ___) (pH 7 ___ / ___) (pH 10 ___ / ___) (pH 4 ___ / ___)

Location of previous calibration: MW-8

Signature: [signature] Reviewed By: [signature] Page 5 of 7

Rev. 3, 2/94

WATER SAMPLE FIELD DATA SHEET

EMCON ASSOCIATES

PROJECT NO: 21775-213.002 SAMPLE ID: MW-8

PURGED BY: M. Ross CLIENT NAME: ARCO 771

SAMPLED BY: M. Ross LOCATION: Livermore, CA

TYPE: Ground Water ✓ Surface Water ___ Treatment Effluent ___ Other ___

CASING DIAMETER (inches): 2 ✓ 3 ___ 4 ___ 4.5 ___ 6 ___ Other ___

CASING ELEVATION (feet/MSL):	NA	VOLUME IN CASING (gal.):	1.85
DEPTH TO WATER (feet):	30.08	CALCULATED PURGE (gal.):	5.64
DEPTH OF WELL (feet):	41.6	ACTUAL PURGE VOL. (gal.):	6.0

DATE PURGED: 8-13-96 Start (2400 Hr) 1134 End (2400 Hr) 11.09

DATE SAMPLED: 8-17-96 Start (2400 Hr) 1155 End (2400 Hr) —

TIME (2400 Hr)	VOLUME (gal.)	pH (units)	E.C. (µmhos/cm @ 25° C)	TEMPERATURE (°F)	COLOR (visual)	TURBIDITY (visual)
1137	2.0	6.99	899	77.0	BRN	HEAVY
1143	4.0	6.96	810	77.4	BRN	HEAVY
1149	6.0	7.03	785	77.5	BRN	HEAVY

D. O. (ppm): NA ODOR: NONE

COLOR (visual): NA (COBALT 0 - 500)

TURBIDITY (visual): NA (NTU 0 - 200 or 0 - 1000)

Field QC samples collected at this well: NA

Parameters field filtered at this well: NA

PURGING EQUIPMENT		SAMPLING EQUIPMENT	
___ 2" Bladder Pump	✓ Bailer (Teflon®)	___ 2" Bladder Pump	✓ Bailer (Teflon®)
___ Centrifugal Pump	___ Bailer (PVC)	___ DDL Sampler	___ Bailer (Stainless Steel)
___ Submersible Pump	___ Bailer (Stainless Steel)	___ Dipper	___ Submersible Pump
___ Well Wizard™	___ Dedicated	___ Well Wizard™	___ Dedicated
Other: ___		Other: ___	

WELL INTEGRITY: Good LOCK #: 3499

REMARKS: ___

Meter Calibration: Date: 8-13-96 Time: 1115 Meter Serial #: 9210 Temperature °F: 79.6

(EC 1000 1084 / 1500) (DI —) (pH 7 7.00 / 7.00) (pH 10 10.03 / 10.00) (pH 4 3.96 / —)

Location of previous calibration: —

Signature: Mike Ross Reviewed By: SK Page 6 of 7

Rev. 3, 2/94

WATER SAMPLE FIELD DATA SHEET

EMCON ASSOCIATES

PROJECT NO: 21775-213.002 SAMPLE ID: MW-11

PURGED BY: M. Ross CLIENT NAME: ARCO 771

SAMPLED BY: M. Ross LOCATION: Livermore, CA

TYPE: Ground Water ✓ Surface Water ___ Treatment Effluent ___ Other ___

CASING DIAMETER (inches): 2 ✓ 3 ___ 4 ___ 4.5 ___ 6 ___ Other ___

CASING ELEVATION (feet/MSL): NA VOLUME IN CASING (gal.): 1.52

DEPTH TO WATER (feet): 29.16 CALCULATED PURGE (gal.): 4.57

DEPTH OF WELL (feet): 38.5 ACTUAL PURGE VOL. (gal.): 5.0

DATE PURGED: 8-13-96 Start (2400 Hr) 1210 End (2400 Hr) 1221

DATE SAMPLED: 8-13-96 Start (2400 Hr) 1230 End (2400 Hr) —

TIME (2400 Hr)	VOLUME (gal.)	pH (units)	E.C. (µmhos/cm @ 25° C)	TEMPERATURE (°F)	COLOR (visual)	TURBIDITY (visual)
1214	2.0	7.02	785	77.6	BRN	Heavy
1217	3.5	6.99	750	74.6	BRN	Heavy
1221	5.0	6.93	741	74.6	BRN	Heavy

D. O. (ppm): NA ODOR: None

COLOR (COBALT 0 - 500): NA

TURBIDITY (NTU 0 - 200 or 0 - 1000): NA

Field QC samples collected at this well: NA

Parameters field filtered at this well: NA

PURGING EQUIPMENT

- ___ 2" Bladder Pump
- ✓ Bailer (Teflon®)
- ___ Centrifugal Pump
- ___ Bailer (PVC)
- ___ Submersible Pump
- ___ Bailer (Stainless Steel)
- ___ Well Wizard™
- ___ Dedicated

Other: ___

SAMPLING EQUIPMENT

- ___ 2" Bladder Pump
- ✓ Bailer (Teflon®)
- ___ ODL Sampler
- ___ Bailer (Stainless Steel)
- ___ Dipper
- ___ Submersible Pump
- ___ Well Wizard™
- ___ Dedicated

Other: ___

WELL INTEGRITY: Good LOCK #: 3499

REMARKS: ___

Meter Calibration: Date: 8-13-96 Time: 1115 Meter Serial #: 9210 Temperature °F: ___

(EC 1000 ___ / ___) (DI ___) (pH 7 ___ / ___) (pH 10 ___ / ___) (pH 4 ___ / ___)

Location of previous calibration: MW-8

Signature: Mike Ross Reviewed By: ___ Page 7 of 7

APPENDIX B

ANALYTICAL RESULTS AND CHAIN OF CUSTODY DOCUMENTATION, THIRD QUARTER 1996 GROUNDWATER MONITORING EVENT

Columbia Analytical Services, Inc.

August 26, 1996 Service Request No.: S9601330

Mr. John Young
EMCON
1921 Ringwood Avenue
San Jose, CA 95131

RE: 771 LIVERMORE/20805-122.003/TO#19350.00

Dear Mr. Young:

Attached are the results of the samples submitted to our lab on August 13, 1996. For you reference, our service request number for this work is S9601330.

Analytical results were produced by procedures consistent with Columbia Analytical Services' (CAS) Quality Assurance Manual (with any deviations noted). Signature of this CAS Analytical Report below confirms that pages 2 through 9, following, have been thoroughly reviewed and approved for release in accord with CAS Standard Operating Procedure ADM-DatRev3.

If you have questions or further needs, please call me at (408) 428-1283.

Sincerely,

Steven L. Green
Project Chemist

SG/sh

COLUMBIA ANALYTICAL SERVICES, Inc.

Acronyms

A2LA	American Association for Laboratory Accreditation
ASTM	American Society for Testing and Materials
BOD	Biochemical Oxygen Demand
BTEX	Benzene, Toluene, Ethylbenzene, Xylenes
CAM	California Assessment Metals
CARB	California Air Resources Board
CAS Number	Chemical Abstract Service registry Number
CFC	Chlorofluorocarbon
CFU	Colony-Forming Unit
COD	Chemical Oxygen Demand
DEC	Department of Environmental Conservation
DEQ	Department of Environmental Quality
DHS	Department of Health Services
DLCS	Duplicate Laboratory Control Sample
DMS	Duplicate Matrix Spike
DOE	Department of Ecology
DOH	Department of Health
EPA	U. S. Environmental Protection Agency
ELAP	Environmental Laboratory Accreditation Program
GC	Gas Chromatography
GC/MS	Gas Chromatography/Mass Spectrometry
IC	Ion Chromatography
ICB	Initial Calibration Blank sample
ICP	Inductively Coupled Plasma atomic emission spectrometry
ICV	Initial Calibration Verification sample
J	Estimated concentration. The value is less than the MRL, but greater than or equal to the MDL. If the value is equal to the MRL, the result is actually <MRL before rounding.
LCS	Laboratory Control Sample
LUFT	Leaking Underground Fuel Tank
M	Modified
MBAS	Methylene Blue Active Substances
MCL	Maximum Contaminant Level. The highest permissible concentration of a substance allowed in drinking water as established by the U. S. EPA.
MDL	Method Detection Limit
MPN	Most Probable Number
MRL	Method Reporting Limit
MS	Matrix Spike
MTBE	Methyl tert-Butyl Ether
NA	Not Applicable
NAN	Not Analyzed
NC	Not Calculated
NCASI	National Council of the paper industry for Air and Stream Improvement
ND	Not Detected at or above the method reporting/detection limit (MRL/MDL)
NIOSH	National Institute for Occupational Safety and Health
NTU	Nephelometric Turbidity Units
ppb	Parts Per Billion
ppm	Parts Per Million
PQL	Practical Quantitation Limit
QA/QC	Quality Assurance/Quality Control
RCRA	Resource Conservation and Recovery Act
RPD	Relative Percent Difference
SIM	Selected Ion Monitoring
SM	Standard Methods for the Examination of Water and Wastewater, 18th Ed., 1992
STLC	Solubility Threshold Limit Concentration
SW	Test Methods for Evaluating Solid Waste, Physical/Chemical Methods, SW-846, 3rd Ed., 1986 and as amended by Updates I, II, IIA, and IIB.
TCLP	Toxicity Characteristic Leaching Procedure
TDS	Total Dissolved Solids
TPH	Total Petroleum Hydrocarbons
tr	Trace level. The concentration of an analyte that is less than the PQL but greater than or equal to the MDL. If the value is equal to the PQL, the result is actually <PQL before rounding.
TRPH	Total Recoverable Petroleum Hydrocarbons
TSS	Total Suspended Solids
TTLC	Total Threshold Limit Concentration
VOA	Volatile Organic Analyte(s)

COLUMBIA ANALYTICAL SERVICES, INC.

Analytical Report

Client:	ARCO Products Company	**Service Request:**	S9601330
Project:	771 LIVERMORE/20805-122.003/TO#19350.00	**Date Collected:**	8/13/96
Sample Matrix:	Water	**Date Received:**	8/13/96
		Date Extracted:	NA

BTEX, MTBE and TPH as Gasoline
EPA Methods 5030/8020/California DHS LUFT Method
Units: ug/L (ppb)

Sample Name:	**MW-8 (41)**	**MW-11 (38)**	**MW-3 (39)**
Lab Code:	S9601330-001	S9601330-002	S9601330-003
Date Analyzed:	8/14/96	8/14/96	8/14/96

Analyte	**MRL**			
TPH as Gasoline	50	ND	ND	ND
Benzene	0.5	ND	ND	ND
Toluene	0.5	ND	ND	ND
Ethylbenzene	0.5	ND	ND	ND
Total Xylenes	0.5	ND	ND	ND
Methyl *tert*-Butyl Ether	3	ND	ND	ND

3S22/060194

COLUMBIA ANALYTICAL SERVICES, INC.

Analytical Report

Client:	ARCO Products Company	**Service Request:**	S9601330
Project:	771 LIVERMORE/20805-122.003/TO#19350.00	**Date Collected:**	8/13/96
Sample Matrix:	Water	**Date Received:**	8/13/96
		Date Extracted:	NA

BTEX, MTBE and TPH as Gasoline
EPA Methods 5030/8020/California DHS LUFT Method
Units: ug/L (ppb)

		Sample Name:	**MW-6 (43)**	**MW-5 (40)**	**MW-1 (36)**
		Lab Code:	S9601330-004	S9601330-005	S9601330-006
		Date Analyzed:	8/14/96	8/15/96	8/15/96
Analyte	**MRL**				
TPH as Gasoline	50		3,800	1,700	19,000
Benzene	0.5		91	150	730
Toluene	0.5		8.2	16	580
Ethylbenzene	0.5		69	24	450
Total Xylenes	0.5		25	35	2,500
Methyl *tert*-Butyl Ether	3		<20*	47	<200*

* Raised MRL due to matrix interference.

3S22/060194

COLUMBIA ANALYTICAL SERVICES, INC.

Analytical Report

Client:	ARCO Products Company	**Service Request:**	S9601330
Project:	771 LIVERMORE/20805-122.003/TO#19350.00	**Date Collected:**	8/13/96
Sample Matrix:	Water	**Date Received:**	8/13/96
		Date Extracted:	NA

BTEX, MTBE and TPH as Gasoline
EPA Methods 5030/8020/California DHS LUFT Method
Units: ug/L (ppb)

		Sample Name:	**MW-2 (37)**	**Method Blank**	**Method Blank**
		Lab Code:	S9601330-007	S960814-WB1	S960815-WB1
		Date Analyzed:	8/14/96	8/14/96	8/15/96
Analyte	**MRL**				
TPH as Gasoline	50		19,000	ND	ND
Benzene	0.5		640	ND	ND
Toluene	0.5		110	ND	ND
Ethylbenzene	0.5		420	ND	ND
Total Xylenes	0.5		1,200	ND	ND
Methyl *tert*-Butyl Ether	3		<300*	ND	ND

* Raised MRL due to matrix interference.

3S22/060194

COLUMBIA ANALYTICAL SERVICES, INC.

QA/QC Report

Client: ARCO Products Company
Project: 771 LIVERMORE/20805-122.003/TO#19350.00
Sample Matrix: Water

Service Request: S9601330
Date Collected: 8/13/96
Date Received: 8/13/96
Date Extracted: NA
Date Analyzed: 8/14-15/96

Surrogate Recovery Summary
BTEX, MTBE and TPH as Gasoline
EPA Methods 5030/8020/California DHS LUFT Method

Sample Name	Lab Code	PID Detector Percent Recovery 4-Bromofluorobenzene	FID Detector Percent Recovery α,α,α–Trifluorotoluene
MW-8 (41)	S9601330-001	99	102
MW-11 (38)	S9601330-002	100	102
MW-3 (39)	S9601330-003	103	102
MW-6 (43)	S9601330-004	85	109*
MW-5 (40)	S9601330-005	98	106
MW-1 (36)	S9601330-006	97	104
MW-2 (37)	S9601330-007	101	101
MW-11(38) (MS)	S9601330-002MS	97	109
MW-11(38) (DMS)	S9601330-002DMS	97	111
Method Blank	S960814-WB1	99	99
Method Blank	S960815-WB1	102	91
CAS Acceptance Limits:		69-116	69-116

* The surrogate used for this sample was 4-Bromofluorobenzene.

SUR2/060194

COLUMBIA ANALYTICAL SERVICES, INC.

QA/QC Report

Client:	ARCO Products Company	**Service Request:**	S9601330
Project:	771 LIVERMORE/20805-122.003/TO#19350.00	**Date Collected:**	8/13/96
Sample Matrix:	Water	**Date Received:**	8/13/96
		Date Extracted:	NA
		Date Analyzed:	8/14/96

Matrix Spike/Duplicate Matrix Spike Summary
TPH as Gasoline
EPA Methods 5030/California DHS LUFT Method
Units: ug/L (ppb)

Sample Name: MW-11(38)
Lab Code: S9601330-002

	Spike Level		Sample	Spike Result		Percent Recovery		CAS Acceptance	Relative Percent
Analyte	MS	DMS	**Result**	MS	DMS	MS	DMS	Limits	**Difference**
Gasoline	250	250	ND	240	240	96	96	67-121	<1

DMS1S/060194

COLUMBIA ANALYTICAL SERVICES, INC.

QA/QC Report

Client:	ARCO Products Company	**Service Request:**	S9601330
Project:	771 LIVERMORE/20805-122.003/TO#19350.00	**Date Analyzed:**	8/14/96

Initial Calibration Verification (ICV) Summary
BTEX, MTBE and TPH as Gasoline
EPA Methods 5030/8020/California DHS LUFT Method
Units: ppb

Analyte	True Value	Result	Percent Recovery	CAS Percent Recovery Acceptance Limits
Benzene	25	23.9	96	85-115
Toluene	25	24.7	99	85-115
Ethylbenzene	25	23.8	95	85-115
Xylenes, Total	75	73.0	97	85-115
Gasoline	250	245	98	90-110
Methyl *tert*-Butyl Ether	50	47	94	85-115

ARCO Products Company
Division of AtlanticRichfieldCompany

Task Order No. 9350.00

Chain of Custody

ARCO Facility no. 771	City (Facility) Livermore	Project manager (Consultant) John Young	Laboratory name CAS
ARCO engineer Mike Whelan	Telephone no. (ARCO)	Telephone no. (Consultant) (408) 453-7300	Fax no. (Consultant) (408) 453 0452
Consultant name EMCON	Address (Consultant) 1921 Ringwood Ave San Jose, CA 95131		Contract number

	Sample I.D.	Lab no.	Container no.	Matrix: Soil	Matrix: Water	Matrix: Other	Preservation: Ice	Preservation: Acid	Sampling date	Sampling time	BTEX 602/EPA 8020	BTEX/TPH EPA M602/8020/8015	TPH Modified 8015 Gas ☐ Diesel ☐	Oil and Grease 413.1 ☐ 413.2 ☐	TPH EPA 418.1/SM503E	EPA 601/8010	EPA 624/8240	EPA 625/8270	TCLP Metals ☐ Semi VOA ☐ VOA ☐	CAM Metals EPA 6010/7000 TTLC ☐ STLC ☐	Lead Org./DHS ☐ Lead EPA 7420/7421 ☐
1	MW-8(41)		2		X		X	HCl	8-13-96	1155		X									
2	MW-11(38)		2		X		X	HCl		1230		X									
3	MW-3(39)		2		X		X	HCl		1300		X									
4	MW-6(43)		2		X		X	HCl		1355		X									
5	MW-5(40)		2		X		X	HCl		1205		X									
6	MW-1(36)		2		X		X	HCl		1250		X									
7	MW-2(37)		2		X		X	HCl	↓	1352		X									

Method of shipment: Sampler will deliver

Special detection Limit/reporting: Lowest Possible

Special QA/QC: As Normal

Remarks: 2-40ml HCl VOAs

#20805-122 003

Lab number: 5960330

Turnaround time

- Priority Rush 1 Business Day ☐
- Rush 2 Business Days ☐
- Expedited 5 Business Days ☐
- Standard 10 Business Days ☒

Condition of sample: ok		Temperature received: cool	
Relinquished by sampler	Date 8-13-96	Time 1530	Received by
Relinquished by	Date	Time	Received by
Relinquished by	Date	Time	Received by laboratory — Date 8/13/96 — Time 1530

Distribution: White copy — Laboratory; Canary copy — ARCO Environmental Engineering; Pink copy — Consultant
APPC-3292 (2-91)

RB

APPENDIX C

SVE SYSTEM MONITORING DATA LOG SHEETS

ARCO 771
SVE SYSTEM
MONITORING DATA

Reporting Period:
07/01/96 00:00
08/01/96 00:00

Hours in Period: 744.00
Days in Period: 31.00

Operation + Down Hours: 744.00
Operation + Down Days: 31.00

	Field Monitoring Data						Laboratory Monitoring Data															
	Flow Rates		FID or PID Results				Well Field Influent		System Influent		System Effluent											
Reading Date & Time	Well Field Flow Rate	System Influent Flow Rate	Well Field	System Influent	System Effluent	Destruction Efficiency	Laboratory Sample Time	Gasoline	Benzene	Gasoline	Benzene	Gasoline	Benzene	Destruction Efficiency	Gasoline Emission Rate	Benzene Emission Rate	Period Hours	Meter Hours	Hours of Operation	Days of Operation	Down Hours	Down Days
	scfm	scfm	ppm	ppm	ppm	%		ppmv mg/m3	ppmv mg/m3	ppmv mg/m3	ppmv mg/m3	ppmv mg/m3	ppmv mg/m3	%	lb/day	lb/day						
07/01/96 00:00																		1461.20				
08/01/96 00:00	0.0	0.0															744.00	1461.20	0.00	0.00	744.00	31.00
Period Totals:																	744.00		0.00	0.00	744.00	31.00
Period Averages:	0.0	0.0																				

ARCO 771
SVE SYSTEM
MONITORING DATA

Reporting Period:
09/01/96 00:00
10/01/96 00:00

Hours in Period: 720.00
Days in Period: 30.00

Operation + Down Hours: 720.00
Operation + Down Days: 30.00

	Field Monitoring Data						Laboratory Monitoring Data														
	Flow Rates		FID or PID Results				Well Field Influent		System Influent		System Effluent										
Reading Date & Time	Well Field Flow Rate	System Influent Flow Rate	Well Field	System Influent	System Effluent	Destruction Efficiency	Laboratory Sample Time	Gasoline	Benzene	Gasoline	Benzene	Gasoline	Benzene	Destruction Efficiency	Gasoline Emission Rate	Benzene Emission Rate	Period Hours	Meter Hours	Hours of Operation	Days of Operation	Down Hours	Down Days
	scfm	scfm	ppm	ppm	ppm	%		ppmv mg/m3	ppmv mg/m3	ppmv mg/m3	ppmv mg/m3	ppmv mg/m3	ppmv mg/m3	%	lb/day	lb/day						
09/01/96 00:00																						
10/01/96 00:00	0.0	0.0																1461.20				
																	720.00	1461.20	0.00	0.00	720.00	30.00
Period Totals:																	720.00		0.00	0.00	720.00	30.00
Period Averages:	0.0	0.0																				

APPENDIX D

FIELD DATA SHEETS, OPERATION AND MAINTENANCE VISITS, THIRD QUARTER 1996

Remarks: Arrived on site at 1136 HRS SVE OFF upon arrival per V. Voruganti
AIR Bubble System Running upon arrival Rotate Blower Approx 6 min.

Go to ARCO 6113 Per V. Voruganti

Check WL in MW-6 WL = 14.82
TD = 67.6 Soft Bottom

Unscheduled site visit ☐ Scheduled site visit ☑

SYSTEM PARAMETERS (King Buck Electric Catalytic Oxidizer MMC-6A/E SN 9231)

Arrival Time (24:00 hour)	1136
System Status (on or off) Bubbler	on
Shutdown Time (24:00 hour)	1140
Restart Time (24:00 hour)	1258
Reading Time (24:00 hour)	1137
Well Field I-1 (2.5")	OFF
Vacuum (in. of H_2O)	
Velocity (ft/min)	
Temperature (°F)	
After Blower I-2 (2.5") (after dilution)	OFF
Total Pressure (in. of H_2O)	
Total Flow (in. of H_2O)	
Temperature (°F)	
Dilution Air open/closed	open
Alarm Trip ? yes/no	NO
Total Vapor Condensate on site (gal)	0

SYSTEM

Operating Set Point (°F)	OFF
High Temperature Set Point (°F)	
Fire Box Temperature (°F)	
Catalyst Temperature (°F)	
E-1 Effluent Stack Temperature (°F)	
Total Flow from Chart Recorder (cfm)	
Electric Meter (kwh)	27175
TOTAL HOURS	01461.2

AIR MONITORING

FID (ppm)	Amb	I-1	I-2	E-1
Date: (WITHOUT CARBON FILTER)				
(WITH CARBON FILTER)				
PID (ppm)	CAL GAS:			
Date:				

Lab samples taken for analysis at:

WELL FIELD

SVE WELL ID	Well Diameter (feet)	Screen Interval	DTW (feet)	TD (feet)	Valve Position (% open)	Vacuum (In. of H_2O)	Bubbler On/Off	PID (ppm)	DO (mg/l)	Remarks
VW-1	4"	18.5'-28.5'	23.31	NR			on		2.5	
MW-1	4"	32'-41'	25.90				on		2.2	
MW-2	4"	30'-38'	22.94				on		2.1	
MW-4	4"	26'-42'	24.94				on		2.0	
MW-5	4"	31.5'-41'	25.38				on		4.9	
MW-7	4"	30'-40'	24.11				on		5.2	
RW-1 (Bubbler Only)	6"	25'-40'	24.46		NA	NA	on	NA	4.8	

Temp = 85°F

Total Bubbler Data

Total Hours=	Total Pressure (psi)= 8.0	Total Flow (in H_2O)=	Timer Setting- 1HR on 1HR OFF

Special Instructions:

Use only ARCO chain-of-custody forms. Please include all analytical method numbers as requested on the chain-of-custody form. Request all TPHG,BTEX, and Benzene results in mg/m³. Report O_2 and CO_2 in % by volume.

Project # 20805-122.003 **Work Authorization # 19285**

Operator: L. RATH Date: 7-10-96

ARCO 771 Soil Vapor Extraction System

Remarks: Arrived on site at 1252 HRS. Scheduled to turn OFF Bubbler For upcoming Sampling event. Blower (Bubbler) unit Found OFF upon arrival. Belt on Blower unit Found Broken. Wires Found charred - Burnt inside Blower electric Box. Turn OFF Power to unit. Tree limb growing over Fence and touching Blower housing.

Clean G113 ARCO Site - NO electric in compound.

Unscheduled site visit [] Scheduled site visit [x]

SYSTEM PARAMETERS (King Buck Electric Catalytic Oxidizer MMC-6A/E SN 9231)

Arrival Time (24:00 hour)	1252
System Status (on or off)	OFF
Shutdown Time (24:00 hour)	NA
Restart Time (24:00 hour) OFF	NA
Reading Time (24:00 hour)	1252
Well Field I-1 (2.5")	NR
Vacuum (in. of H_2O)	
Velocity (ft/min)	
Temperature (°F)	
After Blower I-2 (2.5") (after dilution)	
Total Pressure (in. of H_2O)	
Total Flow (in. of H_2O)	
Temperature (°F)	
Dilution Air open/closed	
Alarm Trip ? yes/no	✓
Total Vapor Condensate on site (gal)	0

SYSTEM

Operating Set Point (°F)	NR
High Temperature Set Point (°F)	
Fire Box Temperature (°F)	
Catalyst Temperature (°F)	
E-1 Effluent Stack Temperature (°F)	
Total Flow from Chart Recorder (cfm)	
Electric Meter (kwh)	✓
TOTAL HOURS	SAme

AIR MONITORING

FID (ppm)	Amb	I-1	I-2	E-1
Date: (WITHOUT CARBON FILTER)				
(WITH CARBON FILTER)				
PID (ppm) CAL GAS:				
Date:				

Lab samples taken for analysis at:

WELL FIELD

SVE WELL ID	Well Diameter (feet)	Screen Interval	DTW (feet)	TD (feet)	Valve Position (% open)	Vacuum (in. of H_2O)	Bubbler On/Off	PID (ppm)	DO (mg/l)	Remarks
VW-1	4"	18.5'-28.5'	22.35						1.0	ABOVE
MW-1	4"	32'-41'	27.00						2.0	GROUND
MW-2	4"	30'-38'	24.25						1.5	D.O.
MW-4	4"	26'-42'	26.06		NR				1.5	Readings
MW-5	4"	31.5'-41'	26.51						1.5	
MW-7	4"	30'-40'	25.12						1.0	
RW-1 (Bubbler Only)	6"	25'-40'	25.02		NA	NA		NA	1.0	

Total Bubbler Data

Total Hours=	Total Pressure (psi)=	Total Flow (in H_2O)=	Timer Setting-

Special Instructions:

Use only ARCO chain-of-custody forms. Please include all analytical method numbers as requested on the chain-of-custody form. Request all TPHG,BTEX, and Benzene results in mg/m³. Report O_2 and CO_2 in % by volume.

Project # 20805-122.003 Work Authorization # 19285

Operator: L. RATH Date: 8-5-96

ARCO 771 Soil Vapor Extraction System
