Atlantic Richfield Company

Chuck Carmel
Remediation Management Project Manager

PO Box 1257
San Ramon, CA 94583
Phone: (925) 275-3804
Fax: (925) 275-3815
E-Mail: chuck.carmel@bp.com

October 29, 2013

Re: Third Quarter 2013 Monitoring Report
Atlantic Richfield Company Station #374
6407 Telegraph Avenue, Oakland, California
ACEH Case #RO0000078

"I declare, that to the best of my knowledge at the present time, that the information and/or recommendations contained in the attached document are true and correct.

Submitted by,

Chuck Carmel
Remediation Management Project Manager

Attachment

BROADBENT
875 Cotting Ln., Suite G, Vacaville, CA 95688
[T] 707-455-7290 [F] 707-455-7295
broadbentinc.com

Creating Solutions, Building Trust.

October 29, 2013 Project No. 06-88-602

Atlantic Richfield Company
P.O. Box 1257
San Ramon, CA 94583
Submitted via ENFOS

Attn.: Mr. Chuck Carmel

Re: Third Quarter 2013 Monitoring Report, Atlantic Richfield Company Station No. 374,
6407 Telegraph Avenue, Oakland, Alameda County, California
ACEH Case #RO0000078

Dear Mr. Carmel:

Provided herein is the *Third Quarter 2013 Monitoring Report* for Atlantic Richfield Company (a BP affiliated company) Station No. 374 located at 6407 Telegraph Avenue in Oakland, California (Site). This report presents a status update and the results of groundwater monitoring conducted at the Site during the Third Quarter 2013.

Should you have questions regarding the work performed or results obtained, please do not hesitate to contact us at (707) 455-7290.

Sincerely,
BROADBENT & ASSOCIATES, INC.

Alex Hernandez for

Alejandra Hernandez
Project Geologist



Kristene Tidwell, P.G., C.HG.
Senior Geologist

enclosures

cc: Ms. Dilan Roe, Alameda County Environmental Health (Submitted via ACEH ftp site)
Electronic copy uploaded to GeoTracker

THIRD QUARTER 2013
MONITORING REPORT
ATLANTIC RICHFIELD COMPANY STATION No. 374
OAKLAND, CALIFORNIA

Broadbent & Associates, Inc. (Broadbent) is pleased to present this *Third Quarter 2013 Monitoring Report* on behalf of Atlantic Richfield Company (ARC; a BP affiliated company) for Station No. 374 located at 6407 Telegraph Avenue in Oakland, Alameda County, California (Site; Drawing 1). Monitoring activities at the Site were performed in accordance with an agency directive issued by the Alameda County Environmental Health (ACEH). Details of work performed, discussion of results, and recommendations are provided below.

Facility Name / Address:	Station No. 374 / 6407 Telegraph Avenue, Oakland, California
Client Project Manager / Title:	Mr. Chuck Carmel / Remediation Management Project Manager
Broadbent Contact:	Ms. Kristene Tidwell, P.G., C.HG.
Broadbent Project No.:	06-88-602
Primary Regulatory Agency / ID No.:	ACEH / Case #RO0000078
Current phase of project:	Monitoring
List of Acronyms / Abbreviations:	See end of report text for list of acronyms/abbreviations used in report.

WORK PERFORMED THIS QUARTER (Third Quarter 2013):

1. Submitted *Second Quarter 2013 Status Report* on July 9, 2013.
2. Broadbent conducted Third Quarter 2013 groundwater monitoring and sampling event on August 22, 2013.

WORK SCHEDULED FOR NEXT QUARTER (Fourth Quarter 2013):

1. Submit *Third Quarter 2013 Monitoring Report* (contained herein).
2. Carry out proposed scope of work outlined in the *Conceptual Site Model and Revised Soil Vapor Investigation Work Plan* submitted on June 19, 2013.

QUARTERLY MONITORING PLAN SUMMARY:

Groundwater level gauging:	MW-1 through MW-9	(Semi-Annually, 1Q & 3Q)
Groundwater sample collection:	MW-1, MW-2, MW-4, MW-7, MW8, and MW-9	(Semi-Annually, 1Q & 3Q)
	MW-3, MW-5, and MW-6	(Annually, 3Q)

QUARTERLY RESULTS SUMMARY:

LNAPL

LNAPL observed this quarter:	No	(yes\no)
LNAPL recovered this quarter:	None	(gal)
Cumulative LNAPL recovered:	None	(gal)

Groundwater Elevation and Gradient:

Depth to groundwater:	7.15 (MW-3) to 8.34 (MW-5)	(ft below TOC)
Gradient direction:	Southwest	(compass direction)
Gradient magnitude:	0.03	(ft/ft)
Average change in elevation:	- 1.79	(ft since last measurement)

Laboratory Analytical Data Summary:

Analytical results are as follows:

- GRO was detected in three wells with a maximum concentration of 6,900 µg/L in well MW-4.
- Benzene was detected in three wells with a maximum concentration of 1,600 µg/L in well MW-4.
- Toluene was detected in well MW-4 at a concentration of 100 µg/L.
- Ethylbenzene was detected in two wells with a maximum concentration of 120 µg/L in well MW-4.
- Total Xylenes were detected in two wells with a maximum concentration of 330 µg/L in well MW-4.
- MTBE was detected in six wells with a maximum concentration of 180 µg/L in well MW-8.
- TBA was detected in well MW-8 at a concentration of 39 µg/L.
- TAME was detected in three wells with a maximum concentration of 2.8 µg/L in well MW-8.
- The remaining petroleum hydrocarbon constituents were below laboratory detection limits.

ACTIVITIES CONDUCTED & RESULTS:

Third Quarter 2013 groundwater monitoring was conducted on August 22, 2013 in accordance with the monitoring plan summary presented above. No irregularities were noted during water level gauging with the exception of well MW-6 was not able to be gauged due to a car being parked over it. Collected depth to groundwater measurements ranged from 7.15 ft in well MW-3 to 8.34 ft in well MW-5. Resulting groundwater surface elevations ranged from 148.56 ft in well MW-5 to 157.41 ft in well MW-7. Groundwater elevations and analytical data are summarized in Table 1. A summary of fuel additives are summarized in Table 2. Water level elevations yielded a potentiometric groundwater gradient to the southwest at approximately 0.03 ft/ft. Historical groundwater gradient direction and magnitude data are summarized in Table 3. Field methods used during groundwater monitoring are provided in Appendix A. Field data sheets are included in Appendix B.

Groundwater samples collected from MW-1 through MW-5 and MW-7 through MW-9 were submitted to Test America Laboratories, Inc. (Test America) of Irvine, California for analysis of GRO, by EPA Method 8015B; BTEX, MTBE, ETBE, TAME, DIPE, TBA, EDB, 1,2-DCA, and Ethanol by EPA Method 8260B. No significant irregularities were encountered during analysis of the samples. Laboratory analytical report and chain of custody record are provided in Appendix C. Groundwater monitoring data (GEO-WELL) and laboratory analytical results (EDF) were uploaded to the GeoTracker AB2886 database. Upload confirmation receipts are provided in Appendix D.

Results of this sampling event are included in the laboratory analytical data summary presented above. The Third Quarter 2013 analytical summary map is presented as Drawing 2. These results indicate that the highest overall petroleum concentrations are present in well MW-4. The analytes detected this quarter are within historical concentration ranges. Further discussion of these results is presented below.

DISCUSSION:

Review of historical groundwater gradient data indicates that the gradient measured during Third Quarter 2013 monitoring is consistent with predominant measurements observed historically at the Site. During Third Quarter 2013, groundwater elevations decreased an average of 1.79 feet across the Site relative to measurements collected during First Quarter 2013, which is consistent with seasonal conditions.

Review of historical groundwater results indicate that well MW-4 contains the highest residual concentrations of petroleum compounds. Petroleum hydrocarbon concentrations from the Third Quarter 2013 monitoring event were within historical ranges. Historical analytical data indicates decreasing trends for all Site wells, with the exception of wells MW-4, MW-8, and MW-9 which have a stable or increasing trend.

Groundwater levels in many Site wells are currently above the top of their respective screen intervals. Ideally, groundwater samples would not be collected from wells with submerged screens. In general, wells with submerged screens are older wells, where water levels over time may have risen. Additionally, these wells only periodically have flooded screens. For example, well MW-4 is one of the oldest Site wells, and has elevated residual petroleum concentrations.

Concentrations have been consistent over time, indicating the submerged screen conditions as not generally influencing concentrations. Additionally, data from wells with lower hydrocarbon concentrations is comparable to site wells without submerged screens. For these reasons, the data reported herein appears valid despite the occurrence of flooded screens at the Site.

RECOMMENDATIONS:

Due to the elevated petroleum hydrocarbon concentrations in well MW-4, located near a potential offsite receptor of the adjacent apartment building, the *Soil Vapor Investigation Work Plan* dated November 20, 2012 was generated. This Work Plan was rejected by the ACEH. The *Conceptual Site Model and Revised Soil Vapor Investigation Work Plan* (CSM and Revised Work Plan) was submitted on June 19, 2013 to the ACEH. In the CSM and Revised Work Plan, soil vapor samples near the property line were recommended in order to assess potential vapor intrusion impacts to the offsite building. The ACEH recently approved this scope of work and it will be carried out during the Fourth Quarter 2013.

LIMITATIONS:

The findings presented in this report are based upon observations of field personnel, points investigated, results of laboratory tests performed by Test America and our understanding of ACEH guidelines. Our services were performed in accordance with the generally accepted standard of practice at the time this report was written. No other warranty, expressed or implied was made. This report has been prepared for the exclusive use of Atlantic Richfield Company (a BP affiliated company). It is possible that variations in soil or groundwater conditions could exist beyond points explored in this investigation. Also, changes in site conditions could occur due to variations in rainfall, temperature, regional water usage, or other factors.

ATTACHMENTS:

Drawing 1:	Site Location Map
Drawing 2:	Groundwater Elevation Contour and Analytical Summary Map August 22, 2013
Table 1:	Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses
Table 2:	Summary of Fuel Additives Analytical Data
Table 3:	Historical Groundwater Gradient - Direction and Magnitude
Appendix A:	Field Methods
Appendix B:	Field Data Sheets
Appendix C:	Laboratory Report and Chain-of-Custody Documentation
Appendix D:	GeoTracker Upload Confirmation Receipts

LIST OF COMMONLY USED ACCRONYMS/ABBREVIATIONS:

ACEH	Alameda County Environmental Health	gal:	gallons
ARC:	Atlantic Richfield Company	GRO:	Gasoline Range Organics (C6-12)
BP:	British Petroleum	LNAPL:	Light Non-Aqueous Phase Liquid
Broadbent:	Broadbent & Associates, Inc.	MTBE:	Methyl Tertiary Butyl Ether
BTEX:	Benzene, Toluene, Ethylbenzene, Total Xylenes	TAME:	Tert-Amyl Methyl Ether
1,2-DCA:	1,2-Dichloroethane	TBA:	Tert-Butyl Alcohol
DIPE:	Di-Isopropyl Ether	TOC:	top of casing
EDB:	1,2-Dibromomethane	UST:	Underground Storage Tank
EPA:	Environmental Protection Agency	µg/L:	micrograms per liter
ETBE:	Ethyl tert-butyl ether	1Q:	First Quarter
ft:	foot	3Q:	Third Quarter
ft/ft:	foot per foot		

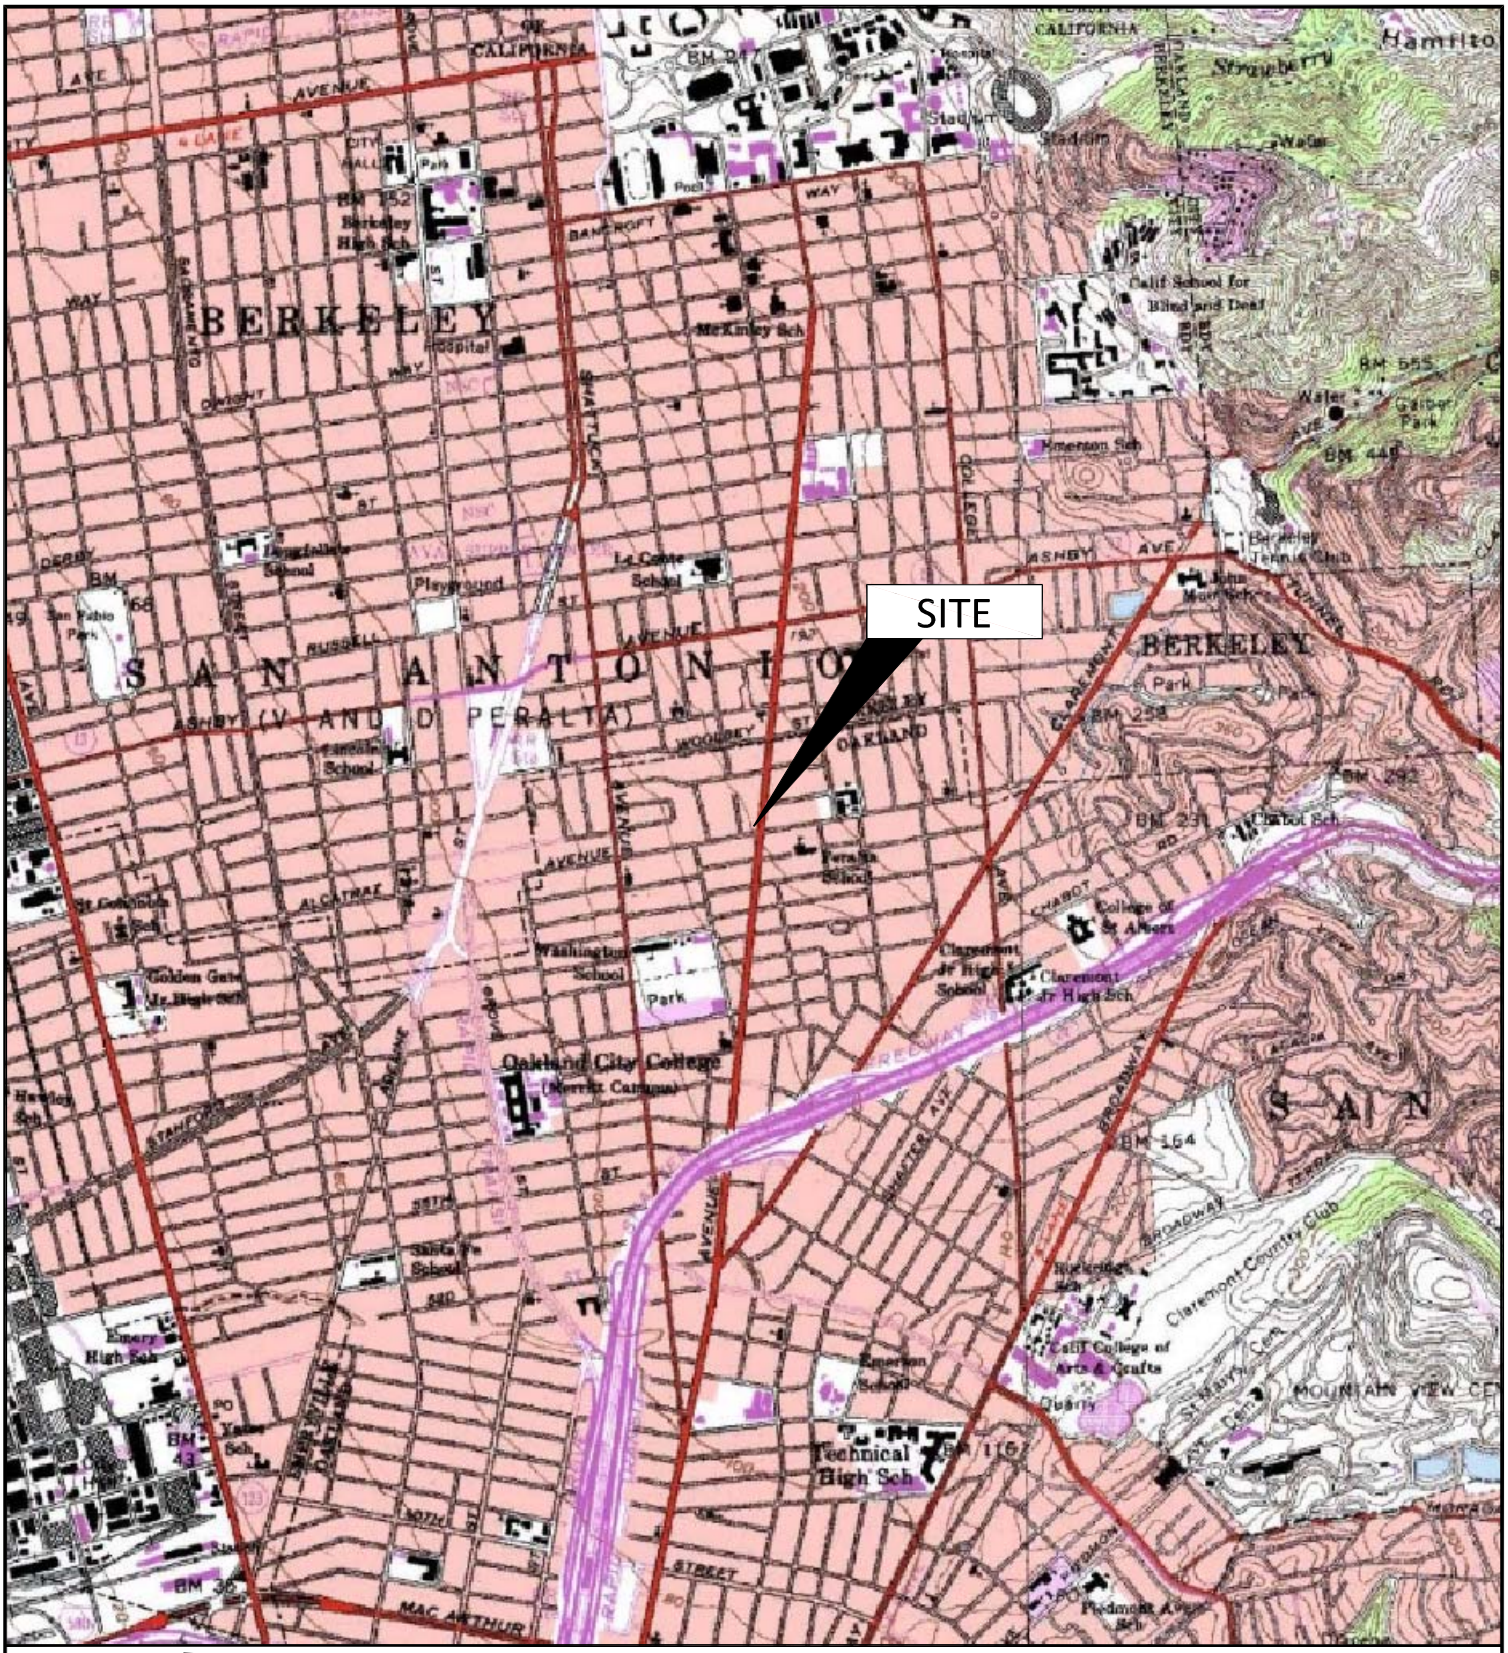

IMAGE SOURCE: USGS

BROADBENT 875 Cotting Lane, Suite G Vacaville, California 95688 Project No.: 06-88-602 Date: 8/22/2013	Station #374 6407 Telegraph Ave. Oakland, California	Site Location Map	Drawing 1

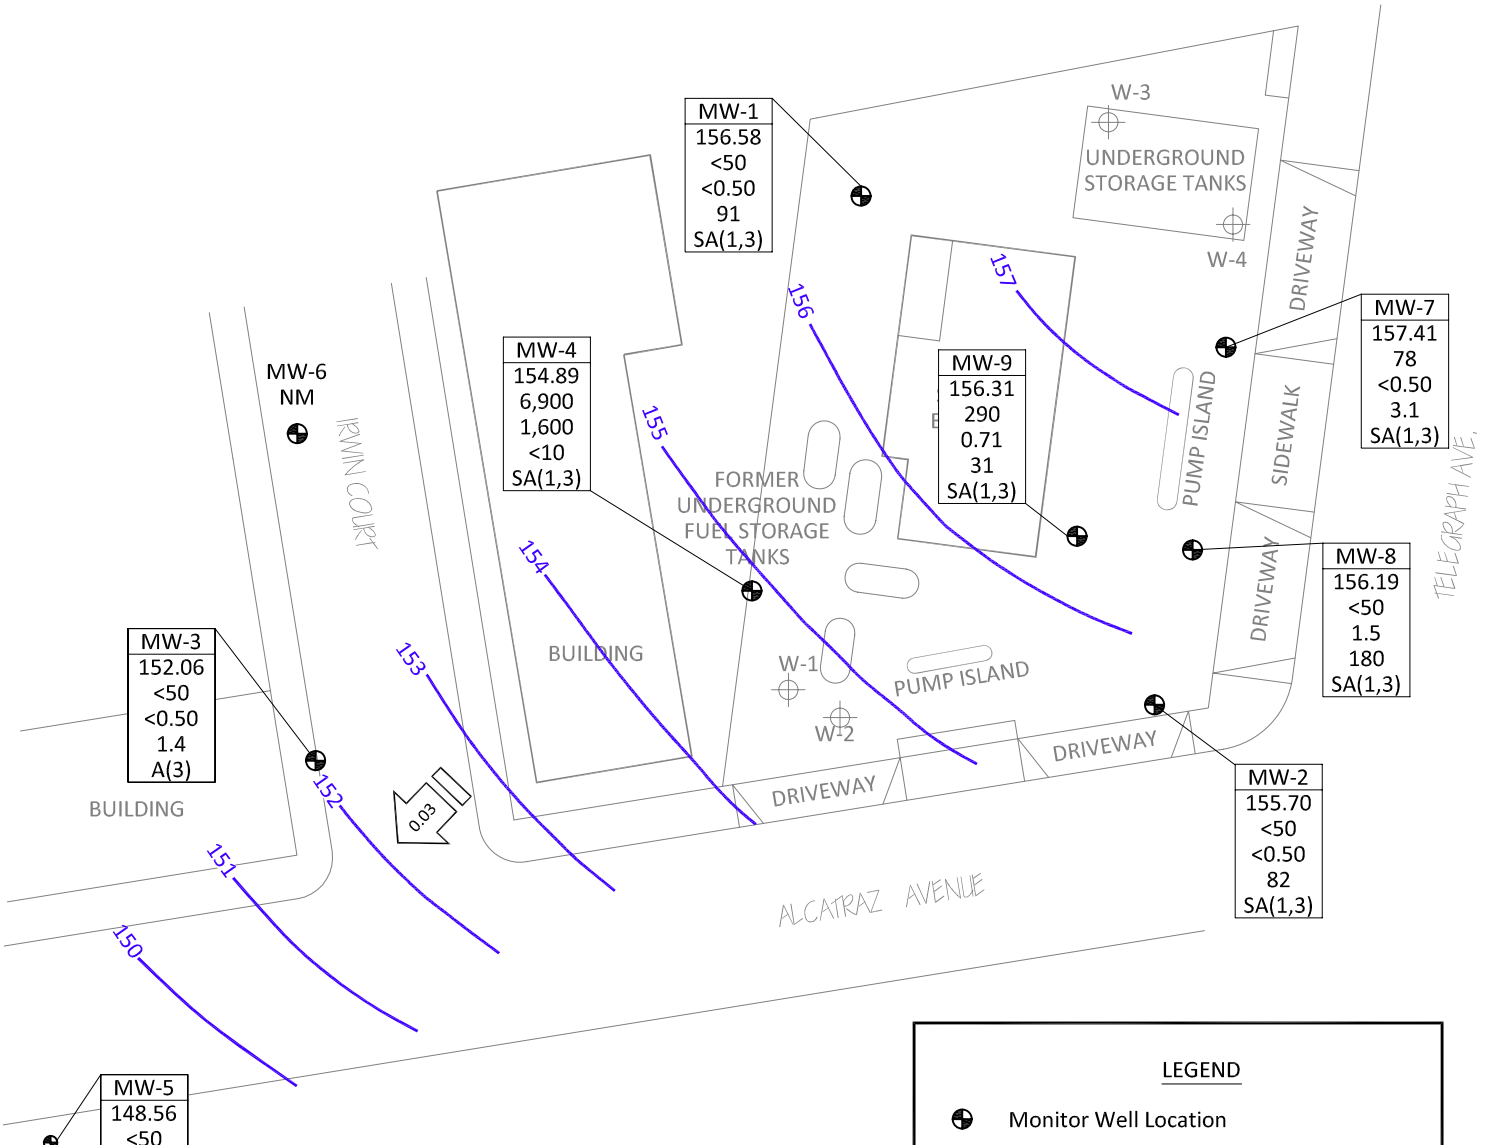

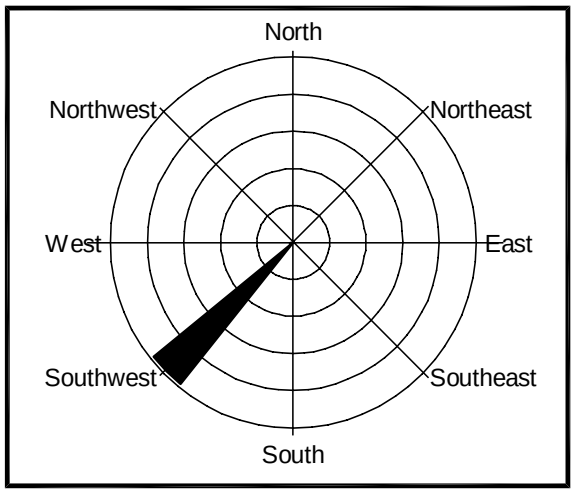

LEGEND

- Monitor Well Location
- Tank Pit Monitor Well Location
- Groundwater Elevation Contour (Feet Above Site Datum)
- 0.03 — Groundwater Gradient (ft/ft)
- A(3) — Sampled Annually - Third Quarter
- SA(1,3) — Sampled Semi-Annually - First and Third Quarter

WELL	Well Designation
ELEV	Groundwater Elevation (ft)
GRO, BZ, MTBE	GRO, Benzene, and MTBE Concentrations (µg/L)
A/SA/Q	Sampling Frequency

NM — Not Monitored

N

0 40 80

SCALE (ft)

NOTE: SITE MAP ADAPTED FROM IT CORPORATION FIGURES.
SITE DIMENSIONS AND FACILITY LOCATIONS NOT VERIFIED.

BROADBENT
875 Cotting Lane, Suite G
Vacaville, California 95688
Project No.: 06-88-602 Date: 3/8/2013

Station #374
6407 Telegraph Ave.
Oakland, California

Groundwater Elevation Contours and Analytical Summary Map
August 22, 2013

Drawing
2

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-1															
6/20/2000	--	158.91	7.00	27.00	6.86	152.05	--	--	--	--	--	--	--	--	
9/28/2000	--		7.00	27.00	7.50	151.41	--	--	--	--	--	--	--	--	
12/17/2000	--		7.00	27.00	7.49	151.42	--	--	--	--	--	--	--	--	
3/23/2001	--		7.00	27.00	5.90	153.01	<50	<0.5	<0.5	<0.5	<0.5	***2,710***	--	--	
6/21/2001	--		7.00	27.00	7.45	151.46	--	--	--	--	--	--	--	--	
9/23/2001	--		7.00	27.00	8.46	150.45	--	--	--	--	--	--	--	--	
12/31/2001	--		7.00	27.00	5.50	153.41	--	--	--	--	--	--	--	--	
3/21/2002	--		7.00	27.00	4.71	154.20	***<5,000***	***<50***	*<50*	***<50***	*<50*	***2,000***	--	--	
4/17/2002	--		7.00	27.00	5.54	153.37	--	--	--	--	--	--	--	--	
8/12/2002	--		7.00	27.00	7.77	151.14	--	--	--	--	--	--	--	--	
12/6/2002	--		7.00	27.00	7.65	151.26	--	--	--	--	--	--	--	--	
1/29/2003	--		7.00	27.00	5.88	153.03	--	--	--	--	--	--	--	--	b
5/23/2003	--		7.00	27.00	5.62	153.29	***<10,000***	***<100***	*<100*	***<100***	*<100*	*1,600*	1.3	7.1	
9/4/2003	--		7.00	27.00	7.85	151.06	--	--	--	--	--	--	--	--	
11/20/2003	P		7.00	27.00	8.17	150.74	***1,600***	*<10*	<10	<10	<10	*1,500*	1.7	6.7	
2/2/2004	P	164.57	7.00	27.00	6.71	157.86	--	--	--	--	--	--	1.0	--	f
5/14/2004	P		7.00	27.00	7.08	157.49	***<2,500***	*<25*	<25	<25	*<25*	*1,200*	1.4	6.6	
9/2/2004	P		7.00	27.00	8.12	156.45	***580***	*<5.0*	<5.0	<5.0	<5.0	*660*	3.8	6.7	
11/4/2004	P		7.00	27.00	7.38	157.19	***1,700***	*<10*	<10	<10	<10	*580*	6.0	6.5	
2/8/2005	P		7.00	27.00	6.60	157.97	***<1,000***	*<10*	<10	<10	<10	*610*	0.71	6.5	
5/9/2005	P		7.00	27.00	6.84	157.73	***540***	*<5.0*	<5.0	<5.0	5.5	*620*	3.12	6.6	e
8/11/2005	P		7.00	27.00	7.36	157.21	***540***	*<2.5*	<2.5	<2.5	4.0	*390*	0.8	6.6	
11/18/2005	P		7.00	27.00	8.02	156.55	***350***	*<2.5*	<2.5	<2.5	<2.5	*340*	2.6	6.7	e
2/16/2006	P		7.00	27.00	6.44	158.13	***350***	*<2.5*	<2.5	<2.5	<2.5	*340*	1.6	6.7	e
5/30/2006	P		7.00	27.00	6.87	157.70	***270***	*<2.5*	<2.5	<2.5	<2.5	*420*	4.73	6.4	
8/24/2006	P		7.00	27.00	7.75	156.82	95	*<5.0*	<5.0	<5.0	<5.0	*180*	0.65	6.9	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-1 Cont.															
11/1/2006	P	164.57	7.00	27.00	8.28	156.29	*120*	*<5.0*	<5.0	<5.0	<5.0	*220*	1.65	7.07	
2/7/2007	NP		7.00	27.00	7.40	157.17	*120*	*<5.0*	<5.0	<5.0	<5.0	*190*	1.88	7.45	e
5/8/2007	P		7.00	27.00	6.50	158.07	***<500***	*<5.0*	<5.0	<5.0	<5.0	*420*	1.21	6.94	
8/8/2007	NP		7.00	27.00	8.17	156.40	82	<0.50	<0.50	<0.50	<0.50	*110*	1.16	7.00	e
11/14/2007	NP		7.00	27.00	8.01	156.56	*170*	*<2.5*	<2.5	<2.5	<2.5	*210*	1.92	6.49	
2/22/2008	P		7.00	27.00	6.00	158.57	<50	<0.50	<0.50	<0.50	<0.50	*250*	2.57	6.65	
5/24/2008	NP		7.00	27.00	7.58	156.99	<50	*<5.0*	<5.0	<5.0	<5.0	*380*	2.28	6.81	
8/21/2008	NP		7.00	27.00	8.60	155.97	<50	*<2.5*	<2.5	<2.5	<2.5	*170*	2.16	6.98	
11/19/2008	NP		7.00	27.00	8.88	155.69	<50	<0.50	<0.50	<0.50	<0.50	*30*	2.12	7.27	
2/23/2009	P		7.00	27.00	6.40	158.17	78	*<2.5*	<2.5	<2.5	<2.5	*240*	2.19	6.03	
5/14/2009	P		7.00	27.00	6.67	157.90	53	<0.50	<0.50	<0.50	<0.50	*200*	1.75	6.69	
8/20/2009	NP		7.00	27.00	8.25	156.32	*150*	*<2.0*	<2.0	<2.0	<2.0	*170*	2.14	6.25	i (GRO)
2/19/2010	P		7.00	27.00	6.07	158.50	<50	<0.50	<0.50	<0.50	<0.50	*170*	0.92	6.66	
8/10/2010	NP		7.00	27.00	7.58	156.99	<50	*<2.5*	<2.5	<2.5	<2.5	*230*	3.86	7.1	
12/16/2010	P	164.45	7.00	27.00	6.64	157.81	<50	*<2.0*	<2.0	<2.0	<2.0	*140*	1.20	6.86	j
2/14/2011	NP		7.00	27.00	7.10	157.35	<50	*<2.5*	<2.5	<2.5	<2.5	*170*	1.18	6.7	
5/20/2011	--		7.00	27.00	6.38	158.07	--	--	--	--	--	--	--	--	
8/15/2011	NP		7.00	27.00	7.24	157.21	<50	*<2.5*	<2.5	<2.5	<2.5	*130*	2.54	6.9	
2/2/2012	P		7.00	27.00	7.32	157.13	<50	<1.0	<1.0	<1.0	<1.0	*66*	1.01	7.1	
8/9/2012	P		7.00	27.00	6.69	157.76	<50	<0.50	<0.50	<0.50	<1.0	*170*	1.65	6.99	
2/14/2013	P		7.00	27.00	5.97	158.48	<50	<0.50	<0.50	<0.50	<1.0	*140*	1.74	7.20	
8/22/2013	P		7.00	27.00	7.87	156.58	<50	<0.50	<0.50	<0.50	<1.0	*91*	5.69	7.21	
MW-2															
6/20/2000	--	157.92	7.00	27.00	7.67	150.25	--	--	--	--	--	--	--	--	
9/28/2000	--		7.00	27.00	8.51	149.41	--	--	--	--	--	--	--	--	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-2 Cont.															
12/17/2000	--	157.92	7.00	27.00	8.14	149.78	--	--	--	--	--	--	--	--	
3/23/2001	--		7.00	27.00	7.21	150.71	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
6/21/2001	--		7.00	27.00	7.99	149.93	--	--	--	--	--	--	--	--	
9/23/2001	--		7.00	27.00	8.52	149.40	--	--	--	--	--	--	--	--	
12/31/2001	--		7.00	27.00	6.01	151.91	--	--	--	--	--	--	--	--	
3/21/2002	--		7.00	27.00	5.95	151.97	<50	<0.5	<0.5	<0.5	<0.5	*45*	--	--	
4/17/2002	--		7.00	27.00	6.45	151.47	--	--	--	--	--	--	--	--	
8/12/2002	--		7.00	27.00	8.08	149.84	--	--	--	--	--	--	--	--	
12/6/2002	--		7.00	27.00	8.29	149.63	--	--	--	--	--	--	--	--	
1/29/2003	--		7.00	27.00	7.22	150.70	--	--	--	--	--	--	--	--	b
5/23/2003	--		7.00	27.00	6.85	151.07	<50	<0.50	<0.50	<0.50	<0.50	*55*	1.4	7.2	
9/4/2003	--		7.00	27.00	7.94	149.98	--	--	--	--	--	--	--	--	
11/20/2003	--		7.00	27.00	8.05	149.87	--	--	--	--	--	--	--	--	
2/2/2004	P	163.46	7.00	27.00	7.00	156.46	74	<0.50	<0.50	<0.50	<0.50	*37*	1.1	8.9	f
5/14/2004	--		7.00	27.00	7.97	155.49	--	--	--	--	--	--	--	--	
9/2/2004	P		7.00	27.00	8.19	155.27	***<250***	*<2.5*	<2.5	<2.5	<2.5	*67*	2.7	6.9	
11/4/2004	--		7.00	27.00	7.54	155.92	--	--	--	--	--	--	--	--	
2/8/2005	P		7.00	27.00	6.72	156.74	<50	<0.50	<0.50	<0.50	<0.50	*30*	0.86	6.7	
5/9/2005	--		7.00	27.00	7.16	156.30	--	--	--	--	--	--	--	--	
8/11/2005	P		7.00	27.00	7.85	155.61	<50	<0.50	<0.50	<0.50	<0.50	*35*	1.0	6.6	
11/18/2005	--		7.00	27.00	8.23	155.23	--	--	--	--	--	--	--	--	
2/16/2006	P		7.00	27.00	6.82	156.64	<50	<0.50	<0.50	<0.50	<0.50	*39*	1.3	7.0	
5/30/2006	--		7.00	27.00	7.23	156.23	--	--	--	--	--	--	--	--	
8/24/2006	P		7.00	27.00	8.00	155.46	60	<0.50	<0.50	<0.50	<0.50	*25*	0.90	6.8	
11/1/2006	--		7.00	27.00	8.38	155.08	--	--	--	--	--	--	--	--	
2/7/2007	NP		7.00	27.00	7.88	155.58	<50	0.50	<0.50	<0.50	<0.50	*7.2*	0.94	7.39	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-2 Cont.															
5/8/2007	--	163.46	7.00	27.00	7.28	156.18	--	--	--	--	--	--	--	--	
8/8/2007	NP		7.00	27.00	8.38	155.08	88	*3.2*	<0.50	<0.50	<0.50	*7.2*	0.94	7.75	
11/14/2007	--		7.00	27.00	8.10	155.36	--	--	--	--	--	--	--	--	
2/22/2008	P		7.00	27.00	6.75	156.71	<50	<0.50	<0.50	<0.50	<0.50	*24*	2.18	7.02	
5/24/2008	--		7.00	27.00	7.98	155.48	--	--	--	--	--	--	--	--	
8/21/2008	NP		7.00	27.00	8.58	154.88	<50	*2.6*	<0.50	<0.50	<0.50	4.9	2.20	7.11	
11/19/2008	--		7.00	27.00	8.66	154.80	--	--	--	--	--	--	--	--	
2/23/2009	P		7.00	27.00	6.67	156.79	74	1.0	<0.50	<0.50	<0.50	*24*	2.25	6.16	
5/14/2009	--		7.00	27.00	7.02	156.44	--	--	--	--	--	--	--	--	
8/20/2009	NP		7.00	27.00	8.41	155.05	82	*2.4*	<0.50	<0.50	<0.50	*8.4*	2.19	6.37	
2/19/2010	NP		7.00	27.00	7.36	156.10	<50	<0.50	<0.50	<0.50	<0.50	*22*	0.81	6.90	
8/10/2010	NP		7.00	27.00	7.69	155.77	<50	<0.50	<0.50	<0.50	<0.50	*23*	2.40	7.67	
12/16/2010	P	163.49	7.00	27.00	7.12	156.37	<50	<0.50	<0.50	<0.50	<0.50	*17*	0.69	7.06	j
2/14/2011	NP		7.00	27.00	7.35	156.14	<50	<0.50	<0.50	<0.50	<0.50	*11*	0.87	7.0	
5/20/2011	--		7.00	27.00	7.02	156.47	--	--	--	--	--	--	--	--	
8/15/2011	NP		7.00	27.00	7.62	155.87	<50	<0.50	<0.50	<0.50	<0.50	1.7	1.45	7.1	
2/2/2012	P		7.00	27.00	7.56	155.93	<50	<0.50	<0.50	<0.50	<0.50	1.8	0.85	7.3	
8/9/2012	P		7.00	27.00	6.31	157.18	<50	<0.50	<0.50	<0.50	<1.0	*73*	1.28	7.15	
2/14/2013	P		7.00	27.00	6.03	157.46	<50	<0.50	<0.50	<0.50	<1.0	*46*	1.71	7.48	
8/22/2013	P		7.00	27.00	7.79	155.70	<50	<0.50	<0.50	<0.50	<1.0	*82*	4.16	7.23	
MW-3															
6/20/2000	--	153.64	7.00	27.00	6.42	147.22	<50	<0.5	<0.5	<0.5	<1.0	*<10*	--	--	
9/28/2000	--		7.00	27.00	7.31	146.33	--	--	--	--	--	--	--	--	
12/17/2000	--		7.00	27.00	6.45	147.19	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
3/23/2001	--		7.00	27.00	6.01	147.63	--	--	--	--	--	--	--	--	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-3 Cont.															
6/21/2001	--	153.64	7.00	27.00	6.80	146.84	*110*	*5.5*	<0.5	5.4	4.1	2.5	--	--	
9/23/2001	--		7.00	27.00	7.32	146.32	--	--	--	--	--	--	--	--	
12/31/2001	--		7.00	27.00	4.48	149.16	<50	<0.5	<0.5	<0.5	<0.5	4.9	--	--	
3/21/2002	--		7.00	27.00	4.36	149.28	--	--	--	--	--	--	--	--	
4/17/2002	--		7.00	27.00	5.31	148.33	<50	<0.5	<0.5	<0.5	<0.5	*8.7*	--	--	
8/12/2002	--		7.00	27.00	7.00	146.64	--	--	--	--	--	--	--	--	
12/6/2002	--		7.00	27.00	7.32	146.32	<50	<0.5	<0.5	<0.5	<0.5	*6.2*	1.4	6.7	
1/29/2003	--		7.00	27.00	6.07	147.57	--	--	--	--	--	--	--	--	b
5/23/2003	--		7.00	27.00	6.45	147.19	<50	<0.50	<0.50	<0.50	<0.50	1.6	0.9	7.7	
9/4/2003	--		7.00	27.00	6.93	146.71	--	--	--	--	--	--	--	--	c
11/20/2003	--		7.00	27.00	7.04	146.60	--	--	--	--	--	--	--	--	c
2/2/2004	--	159.21	7.00	27.00	5.92	153.29	--	--	--	--	--	--	--	--	f
5/14/2004	--		7.00	27.00	7.52	151.69	--	--	--	--	--	--	--	--	
9/2/2004	P		7.00	27.00	7.19	152.02	<50	<0.50	<0.50	<0.50	<0.50	*6.5*	9.3	8.9	
11/4/2004	--		7.00	27.00	6.40	152.81	--	--	--	--	--	--	--	--	
2/8/2005	--		7.00	27.00	6.01	153.20	--	--	--	--	--	--	--	--	
5/9/2005	--		7.00	27.00	6.74	152.47	--	--	--	--	--	--	--	--	
8/11/2005	P		7.00	27.00	6.77	152.44	<50	<0.50	<0.50	<0.50	<0.50	*11*	1.9	6.5	
11/18/2005	--		7.00	27.00	7.83	151.38	--	--	--	--	--	--	--	--	
2/16/2006	--		7.00	27.00	7.26	151.95	--	--	--	--	--	--	--	--	
5/30/2006	--		7.00	27.00	5.82	153.39	--	--	--	--	--	--	--	--	
8/24/2006	P		7.00	27.00	7.00	152.21	<50	<0.50	<0.50	<0.50	<0.50	*7.6*	1.15	6.4	
11/1/2006	--		7.00	27.00	7.50	151.71	--	--	--	--	--	--	--	--	
2/7/2007	--		7.00	27.00	6.90	152.31	--	--	--	--	--	--	--	--	
5/8/2007	--		7.00	27.00	5.95	153.26	--	--	--	--	--	--	--	--	
8/8/2007	NP		7.00	27.00	7.47	151.74	<50	<0.50	<0.50	<0.50	<0.50	1.2	1.21	6.93	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-3 Cont.															
11/14/2007	--	159.21	7.00	27.00	7.05	152.16	--	--	--	--	--	--	--	--	
2/22/2008	--		7.00	27.00	5.50	153.71	--	--	--	--	--	--	--	--	
5/24/2008	--		7.00	27.00	7.03	152.18	--	--	--	--	--	--	--	--	
8/21/2008	NP		7.00	27.00	7.80	151.41	<50	<0.50	<0.50	<0.50	<0.50	3.1	2.11	6.84	
11/19/2008	--		7.00	27.00	7.69	151.52	--	--	--	--	--	--	--	--	
2/23/2009	--		7.00	27.00	7.28	151.93	--	--	--	--	--	--	--	--	
5/14/2009	--		7.00	27.00	6.17	153.04	--	--	--	--	--	--	--	--	
8/20/2009	NP		7.00	27.00	7.38	151.83	<50	<0.50	<0.50	<0.50	<0.50	2.2	2.05	7.01	
2/19/2010	--		7.00	27.00	5.31	153.90	--	--	--	--	--	--	--	--	
8/10/2010	NP		7.00	27.00	7.12	152.09	<50	<0.50	<0.50	<0.50	<0.50	1.6	1.27	7.33	
12/16/2010	--		7.00	27.00	5.65	153.56	--	--	--	--	--	--	--	--	j
2/14/2011	--		7.00	27.00	6.20	153.01	--	--	--	--	--	--	--	--	
5/20/2011	--		7.00	27.00	5.77	153.44	--	--	--	--	--	--	--	--	
8/15/2011	P		7.00	27.00	6.41	152.80	<50	<0.50	<0.50	<0.50	<0.50	1.2	1.04	7.0	
2/2/2012	--		7.00	27.00	6.34	152.87	--	--	--	--	--	--	--	--	
8/9/2012	P		7.00	27.00	6.62	152.59	<50	<0.50	<0.50	<0.50	<1.0	2.0	1.16	6.71	
2/14/2013	--		7.00	27.00	6.09	153.12	--	--	--	--	--	--	--	--	
8/22/2013	P		7.00	27.00	7.15	152.06	<50	<0.50	<0.50	<0.50	<1.0	1.4	4.35	6.72	
MW-4															
6/20/2000	--	156.53	7.00	27.00	7.50	149.03	***20,000***	***5,100***	***440***	***1,000***	***1,700***	*<250*	--	--	c
9/28/2000	--		7.00	27.00	8.20	148.33	--	--	--	--	--	--	--	--	
12/17/2000	--		7.00	27.00	8.11	148.42	***4,320***	***1,240***	<20	27.2	***249***	*<100*	--	--	
3/23/2001	--		7.00	27.00	6.69	149.84	--	--	--	--	--	--	--	--	
6/21/2001	--		7.00	27.00	8.01	148.52	***2,800***	***470***	16	19	***160***	*130*	--	--	
9/23/2001	--		7.00	27.00	8.91	147.62	--	--	--	--	--	--	--	--	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-4 Cont.															
12/31/2001	--	156.53	7.00	27.00	4.42	152.11	***4,600***	***1,500***	*100*	***160***	***210***	*160*	--	--	
3/21/2002	--		7.00	27.00	4.98	151.55	--	--	--	--	--	--	--	--	
4/17/2002	--		7.00	27.00	6.23	150.30	***7,100***	***2,200***	*110*	***290***	***450***	*<250*	--	--	
8/12/2002	--		7.00	27.00	8.24	148.29	--	--	--	--	--	--	--	--	
12/6/2002	--		7.00	27.00	8.42	148.11	***1,500***	***410***	6.8	20	*29*	*43*	1.1	6.7	a
1/29/2003	--		7.00	27.00	7.20	149.33	--	--	--	--	--	--	--	--	b
5/23/2003	--		7.00	27.00	7.18	149.35	***<5,000***	***1,300***	*89*	***210***	***260***	*<50*	1.4	6.9	
9/4/2003	--		7.00	27.00	8.15	148.38	--	--	--	--	--	--	--	--	c
11/20/2003	--		7.00	27.00	8.73	147.80	--	--	--	--	--	--	--	--	c
2/2/2004	P	163.25	7.00	27.00	6.25	157.00	***980***	***280***	21	29	*38*	*29*	1.4	10.6	c, f, g
5/14/2004	--		7.00	27.00	8.38	154.87	--	--	--	--	--	--	--	--	g
9/2/2004	P		7.00	27.00	8.36	154.89	***260***	*11*	<1.0	5.5	14	*28*	2.4	7.4	g
11/4/2004	--		7.00	27.00	7.71	155.54	--	--	--	--	--	--	--	--	c, g
2/8/2005	P		7.00	27.00	6.27	156.98	***7,500***	***1,700***	***320***	***480***	***920***	*45*	0.65	6.5	g
5/9/2005	--		7.00	27.00	5.90	157.35	--	--	--	--	--	--	--	--	g
8/11/2005	P		7.00	27.00	7.96	155.29	***3,100***	***1,100***	*41*	***160***	***110***	*32*	0.6	6.5	g
11/18/2005	--		7.00	27.00	8.57	154.68	--	--	--	--	--	--	--	--	g
2/16/2006	P		7.00	27.00	6.28	156.97	***9,400***	***1,800***	*130*	***600***	***420***	*35*	0.5	6.8	g
5/30/2006	--	162.47	7.00	27.00	7.02	155.45	--	--	--	--	--	--	--	--	g
8/24/2006	P		7.00	27.00	8.26	154.21	***3,600***	***1,400***	21	***110***	*70*	*39*	1.00	6.8	
11/1/2006	--		7.00	27.00	8.67	153.80	--	--	--	--	--	--	--	--	
2/7/2007	NP		7.00	27.00	8.02	154.45	***3,100***	***570***	17	***170***	***110***	*67*	0.95	7.07	
5/8/2007	--		7.00	27.00	7.03	155.44	--	--	--	--	--	--	--	--	
8/8/2007	NP		7.00	27.00	8.60	153.87	***2,900***	***630***	22	***67***	*57*	*72*	0.93	6.79	
11/14/2007	--		7.00	27.00	8.53	153.94	--	--	--	--	--	--	--	--	
2/22/2008	P		7.00	27.00	6.25	156.22	***3,900***	***880***	39	***180***	*92*	*70*	2.31	6.87	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-4 Cont.															
5/24/2008	--	162.47	7.00	27.00	--	--	--	--	--	--	--	--	--	--	d
8/21/2008	NP		7.00	27.00	8.96	153.51	***3,700***	***1,100***	26	***85***	***130***	*53*	2.26	6.80	
11/19/2008	--		7.00	27.00	9.20	153.27	--	--	--	--	--	--	--	--	
2/23/2009	P		7.00	27.00	6.35	156.12	***3,000***	***220***	9.1	23	19	*39*	2.21	6.51	
5/14/2009	--		7.00	27.00	7.00	155.47	--	--	--	--	--	--	--	--	
8/20/2009	NP		7.00	27.00	8.05	154.42	***5,700***	***1,100***	35	***110***	*100*	*23*	2.17	6.81	
2/19/2010	P		7.00	27.00	5.71	156.76	***12,000***	***1,200***	*120*	***230***	***390***	<5.0	0.81	6.70	i
8/10/2010	NP		7.00	27.00	7.59	154.88	***9,700***	***1,500***	*120*	***400***	***400***	*<20*	3.81	6.8	
12/16/2010	P	162.48	7.00	27.00	6.83	155.65	***15,000***	***1,800***	*82*	***270***	***210***	*<25*	0.49	6.81	j
2/14/2011	NP		7.00	27.00	7.33	155.15	***260***	<0.50	<0.50	2.7	11	*13*	0.80	7.10	
5/20/2011	--		7.00	27.00	6.89	155.59	--	--	--	--	--	--	--	--	
8/15/2011	P		7.00	27.00	7.59	154.89	***8,600***	***2,100***	*86*	***250***	***210***	*<12*	1.02	7.0	l
2/2/2012	P		7.00	27.00	7.71	154.77	***4,600***	***1,000***	34	23	*33*	*<12*	0.60	7.2	
8/9/2012	P		7.00	27.00	6.57	155.91	***3,200***	***660***	*44*	***53***	*57*	<5.0	1.09	7.05	
2/14/2013	P		7.00	27.00	6.26	156.22	***7,200***	***1,400***	***150***	***390***	***700***	*<10*	1.20	7.51	
8/22/2013	P		7.00	27.00	7.59	154.89	***6,900***	***1,600***	*100*	***120***	***330***	*<10*	4.50	6.98	
MW-5															
6/20/2000	--	151.33	10.00	23.00	7.84	143.49	<50	<0.5	<0.5	<0.5	<1.0	*<10*	--	--	
9/28/2000	--		10.00	23.00	8.37	142.96	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
12/17/2000	--		10.00	23.00	8.36	142.97	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
3/23/2001	--		10.00	23.00	7.55	143.78	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
6/21/2001	--		10.00	23.00	8.20	143.13	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
9/23/2001	--		10.00	23.00	8.68	142.65	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
12/31/2001	--		10.00	23.00	7.57	143.76	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
3/21/2002	--		10.00	23.00	6.12	145.21	<50	<0.5	<0.5	<0.5	<0.5	3.2	--	--	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-5 Cont.															
4/17/2002	--	151.33	10.00	23.00	6.61	144.72	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
8/12/2002	--		10.00	23.00	8.14	143.19	<50	<0.5	<0.5	<0.5	<0.5	<2.5	4.1	7.6	
12/6/2002	--		10.00	23.00	8.65	142.68	<50	<0.5	<0.5	<0.5	<0.5	<2.5	1.1	6.8	
1/29/2003	--		10.00	23.00	7.22	144.11	<50	<0.5	<0.5	<0.5	<0.5	<0.50	1	6.6	b
5/23/2003	--		10.00	23.00	7.31	144.02	<50	<0.50	<0.50	<0.50	<0.50	<0.50	1.1	6.6	
9/4/2003	--		10.00	23.00	9.50	141.83	<50	<0.50	<0.50	<0.50	<0.50	<0.50	3.2	6.7	
11/20/2003	--		10.00	23.00	8.31	143.02	--	--	--	--	--	--	--	--	
2/2/2004	--		10.00	23.00	6.92	144.41	--	--	--	--	--	--	--	--	c, f, h
5/14/2004	--		10.00	23.00	8.56	142.77	--	--	--	--	--	--	--	--	h
9/2/2004	P		10.00	23.00	8.79	142.54	<50	<0.50	<0.50	<0.50	<0.50	<0.50	3.5	6.8	h
11/4/2004	--		10.00	23.00	8.33	143.00	--	--	--	--	--	--	--	--	c, h
2/8/2005	--		10.00	23.00	7.28	144.05	--	--	--	--	--	--	--	--	h
5/9/2005	--		10.00	23.00	8.19	143.14	--	--	--	--	--	--	--	--	h
8/11/2005	P		10.00	23.00	8.39	142.94	<50	<0.50	<0.50	<0.50	<0.50	<0.50	1.2	6.6	h
11/18/2005	--		10.00	23.00	11.25	140.08	--	--	--	--	--	--	--	--	h
2/16/2006	--		10.00	23.00	9.22	142.11	--	--	--	--	--	--	--	--	h
5/30/2006	--		10.00	23.00	7.52	143.81	--	--	--	--	--	--	--	--	h
8/24/2006	P		10.00	23.00	7.95	143.38	<50	<0.50	<0.50	<0.50	<0.50	<0.50	2.60	6.6	
11/1/2006	--		10.00	23.00	8.32	143.01	--	--	--	--	--	--	--	--	
2/7/2007	--		10.00	23.00	8.25	143.08	--	--	--	--	--	--	--	--	
5/8/2007	--		10.00	23.00	7.60	143.73	--	--	--	--	--	--	--	--	
8/8/2007	P		10.00	23.00	8.12	143.21	<50	<0.50	<0.50	<0.50	<0.50	<0.50	3.26	7.31	
11/14/2007	--		10.00	23.00	9.10	142.23	--	--	--	--	--	--	--	--	
2/22/2008	--		10.00	23.00	7.48	143.85	--	--	--	--	--	--	--	--	
5/24/2008	--		10.00	23.00	8.12	143.21	--	--	--	--	--	--	--	--	
8/21/2008	P		10.00	23.00	8.65	142.68	<50	<0.50	<0.50	<0.50	<0.50	<0.50	2.14	6.54	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-5 Cont.															
11/19/2008	--	151.33	10.00	23.00	11.86	139.47	--	--	--	--	--	--	--	--	
2/23/2009	--		10.00	23.00	10.20	141.13	--	--	--	--	--	--	--	--	
5/14/2009	--		10.00	23.00	9.63	141.70	--	--	--	--	--	--	--	--	
8/20/2009	P		10.00	23.00	8.52	142.81	<50	<0.50	<0.50	<0.50	<0.50	<0.50	2.01	6.47	
2/19/2010	--		10.00	23.00	--	--	--	--	--	--	--	--	--	--	d
8/10/2010	P		10.00	23.00	8.05	143.28	<50	<0.50	<0.50	<0.50	<0.50	<0.50	1.15	7.1	
12/16/2010	--	156.90	10.00	23.00	8.10	148.80	--	--	--	--	--	--	--	--	j
2/14/2011	--		10.00	23.00	--	--	--	--	--	--	--	--	--	--	d
5/20/2011	--		10.00	23.00	--	--	--	--	--	--	--	--	--	--	d
8/15/2011	P		10.00	23.00	7.91	148.99	<50	<0.50	<0.50	<0.50	<0.50	<0.50	2.46	7.4	
2/2/2012	--		10.00	23.00	8.08	148.82	--	--	--	--	--	--	--	--	
8/9/2012	P		10.00	23.00	8.02	148.88	<50	<0.50	<0.50	<0.50	<1.0	<0.50	1.25	6.99	
2/14/2013	--		10.00	23.00	7.54	149.36	--	--	--	--	--	--	--	--	
8/22/2013	P		10.00	23.00	8.34	148.56	<50	<0.50	<0.50	<0.50	<1.0	<0.50	4.33	6.95	
MW-6															
6/20/2000	--	153.84	5.00	15.00	4.79	149.05	--	--	--	--	--	--	--	--	
9/28/2000	--		5.00	15.00	5.39	148.45	--	--	--	--	--	--	--	--	
12/17/2000	--		5.00	15.00	4.71	149.13	--	--	--	--	--	--	--	--	
3/23/2001	--		5.00	15.00	4.69	149.15	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--	
6/21/2001	--		5.00	15.00	5.22	148.62	--	--	--	--	--	--	--	--	
9/23/2001	--		5.00	15.00	5.40	148.44	--	--	--	--	--	--	--	--	
12/31/2001	--		5.00	15.00	3.95	149.89	--	--	--	--	--	--	--	--	
3/21/2002	--		5.00	15.00	2.94	150.90	<50	<0.5	<0.5	<0.5	<0.5	*5.2*	--	--	
4/17/2002	--		5.00	15.00	5.11	148.73	--	--	--	--	--	--	--	--	
8/12/2002	--		5.00	15.00	5.23	148.61	--	--	--	--	--	--	--	--	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-6 Cont.															
12/6/2002	--	153.84	5.00	15.00	5.29	148.55	--	--	--	--	--	--	--	--	
1/29/2003	--		5.00	15.00	4.79	149.05	--	--	--	--	--	--	--	--	b
5/23/2003	--		5.00	15.00	4.31	149.53	<50	<0.50	<0.50	<0.50	<0.50	*9.4*	1	6.7	
9/4/2003	--		5.00	15.00	--	--	--	--	--	--	--	--	--	--	d
11/20/2003	--		5.00	15.00	6.31	147.53	--	--	--	--	--	--	--	--	
2/2/2004	--	159.41	5.00	15.00	4.78	154.63	--	--	--	--	--	--	--	--	f
5/14/2004	--		5.00	15.00	6.29	153.12	--	--	--	--	--	--	--	--	
9/2/2004	--		5.00	15.00	5.79	153.62	--	--	--	--	--	--	--	--	d
11/4/2004	--		5.00	15.00	--	--	--	--	--	--	--	--	--	--	d
2/8/2005	--		5.00	15.00	5.13	154.28	--	--	--	--	--	--	--	--	
5/9/2005	--		5.00	15.00	4.52	154.89	--	--	--	--	--	--	--	--	
8/11/2005	P		5.00	15.00	5.02	154.39	<50	<0.50	<0.50	<0.50	<0.50	*7.9*	2.1	6.6	
11/18/2005	--		5.00	15.00	6.31	153.10	--	--	--	--	--	--	--	--	
2/16/2006	--		5.00	15.00	4.24	155.17	--	--	--	--	--	--	--	--	
5/30/2006	--		5.00	15.00	4.45	154.96	--	--	--	--	--	--	--	--	
8/24/2006	P		5.00	15.00	5.18	154.23	<50	<0.50	<0.50	<0.50	<0.50	*12*	3.4	6.8	
11/1/2006	--		5.00	15.00	6.05	153.36	--	--	--	--	--	--	--	--	
2/7/2007	--		5.00	15.00	5.00	154.41	--	--	--	--	--	--	--	--	
5/8/2007	--		5.00	15.00	4.30	155.11	--	--	--	--	--	--	--	--	
8/8/2007	NP		5.00	15.00	5.51	153.90	<50	<0.50	<0.50	<0.50	<0.50	0.57	2.94	6.87	
11/14/2007	--		5.00	15.00	5.38	154.03	--	--	--	--	--	--	--	--	
2/22/2008	--		5.00	15.00	4.70	154.71	--	--	--	--	--	--	--	--	
5/24/2008	--		5.00	15.00	5.25	154.16	--	--	--	--	--	--	--	--	
8/21/2008	NP		5.00	15.00	6.14	153.27	<50	<0.50	<0.50	<0.50	<0.50	1.9	1.99	7.13	
11/19/2008	--		5.00	15.00	5.94	153.47	--	--	--	--	--	--	--	--	
2/23/2009	--		5.00	15.00	5.00	154.41	--	--	--	--	--	--	--	--	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-6 Cont.															
5/14/2009	--	159.41	5.00	15.00	4.60	154.81	--	--	--	--	--	--	--	--	
8/20/2009	NP		5.00	15.00	5.65	153.76	<50	<0.50	<0.50	<0.50	<0.50	2.0	1.98	6.81	
2/19/2010	--		5.00	15.00	7.28	152.13	--	--	--	--	--	--	--	--	
8/10/2010	NP		5.00	15.00	5.02	154.39	<50	<0.50	<0.50	<0.50	<0.50	4.3	1.99	6.93	
12/16/2010	--		5.00	15.00	4.50	154.91	--	--	--	--	--	--	--	--	j
2/14/2011	--		5.00	15.00	4.80	154.61	--	--	--	--	--	--	--	--	
5/20/2011	--		5.00	15.00	4.29	155.12	--	--	--	--	--	--	--	--	
8/15/2011	P		5.00	15.00	4.52	154.89	<50	<0.50	<0.50	<0.50	<0.50	2.2	1.55	7.1	
2/2/2012	--		5.00	15.00	--	--	--	--	--	--	--	--	--	--	d
8/9/2012	P		5.00	15.00	4.65	154.76	<50	<0.50	<0.50	<0.50	<1.0	3.6	1.14	6.89	
2/14/2013	--		5.00	15.00	--	--	--	--	--	--	--	--	--	--	d
8/22/2013	--		5.00	15.00	--	--	--	--	--	--	--	--	--	--	d
MW-7															
12/16/2010	P	164.80	5.00	20.00	6.52	158.28	***700***	<0.50	<0.50	15	*32*	*62*	--	7.08	j
2/14/2011	NP		5.00	20.00	6.77	158.03	***7,100***	***1,700***	*98*	***260***	***210***	*<20*	1.02	6.8	
5/20/2011	NP		5.00	20.00	5.84	158.96	***570***	<0.50	<0.50	*37*	*25*	4.6	1.66	6.7	l (GRO)
8/15/2011	P		5.00	20.00	6.96	157.84	***420***	<1.0	<1.0	***49***	6.7	*14*	0.58	6.9	
2/2/2012	P		5.00	20.00	7.15	157.65	<50	<0.50	<0.50	<0.50	<0.50	*6.2*	0.45	7.5	
8/9/2012	P		5.00	20.00	5.05	159.75	85	<0.50	<0.50	5.8	1.1	*7.0*	1.04	7.25	
2/14/2013	P		5.00	20.00	4.38	160.42	***310***	*1.2*	<0.50	1.6	6.3	*5.1*	1.31	7.64	
8/22/2013	P		5.00	20.00	7.39	157.41	78	<0.50	<0.50	3.9	<1.0	3.1	4.01	7.00	
MW-8															
12/16/2010	P	164.14	5.00	20.00	6.85	157.29	***520***	*43*	<0.50	4.1	*21*	*150*	0.46	7.12	j
2/14/2011	NP		5.00	20.00	7.30	156.84	<50	*<2.0*	<2.0	<2.0	<2.0	*110*	1.07	6.7	
5/20/2011	NP		5.00	20.00	6.88	157.26	<50	*<2.0*	<2.0	<2.0	<2.0	*88*	1.35	6.5	

Table 1. Summary of Groundwater Monitoring Data: Relative Water Elevations and Laboratory Analyses

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	P/NP	TOC (feet)	Top of Screen (ft bgs)	Bottom of Screen (ft bgs)	DTW (feet)	Water Level Elevation (feet)	Concentrations in µg/L						DO (mg/L)	pH	Footnote
							GRO/ TPHg	Benzene	Toluene	Ethyl-Benzene	Total Xylenes	MTBE			
ESL - DW							100	1.0	40	30	20	5.0			
ESL - NDW							210	46	130	43	100	1,800			
MW-8 Cont.															
8/15/2011	P	164.14	5.00	20.00	6.00	158.14	<50	*5.2*	<1.0	9.7	<1.0	*57*	0.51	6.7	
2/2/2012	P		5.00	20.00	7.57	156.57	<50	<0.50	<0.50	<0.50	<0.50	3.9	0.68	7.1	
8/9/2012	P		5.00	20.00	6.08	158.06	*110*	***67***	<0.50	<0.50	<1.0	*150*	1.16	6.98	
2/14/2013	P		5.00	20.00	5.70	158.44	***720***	***350***	<2.0	<2.0	<4.0	*240*	1.23	7.40	
8/22/2013	P		5.00	20.00	7.95	156.19	<50	*1.5*	<0.50	<0.50	<1.0	*180*	3.96	6.88	
MW-9															
12/16/2010	P	163.77	5.00	20.00	6.63	157.14	***330***	*18*	<0.50	11	*38*	*390*	0.57	6.97	j
2/14/2011	NP		5.00	20.00	6.85	156.92	<50	*<4.0*	<4.0	<4.0	<4.0	*270*	0.98	6.9	
5/20/2011	NP		5.00	20.00	6.39	157.38	66	*<4.0*	<4.0	<4.0	<4.0	*280*	1.64	6.7	l (GRO)
8/15/2011	NP		5.00	20.00	7.09	156.68	<50	*<2.0*	<2.0	<2.0	<2.0	*120*	0.88	7.1	
2/2/2012	P		5.00	20.00	7.18	156.59	<50	<0.50	<0.50	<0.50	<0.50	*34*	0.65	7.2	
8/9/2012	P		5.00	20.00	5.68	158.09	82	*1.9*	<0.50	<0.50	<1.0	*19*	1.61	7.13	
2/14/2013	P		5.00	20.00	5.27	158.50	***250***	*5.2*	<0.50	<0.50	1.4	*25*	1.23	7.51	
8/22/2013	P		5.00	20.00	7.46	156.31	***290***	0.71	<0.50	<0.50	1.4	*31*	4.71	7.07	

Symbols & Abbreviations:
-- = Not analyzed/applicable/measured/available
< = Not detected at or above laboratory reporting limit
DO = Dissolved oxygen
DTW = Depth to water in ft below TOC
ft bgs = Feet below ground surface
GRO = Gasoline range organics
GWE = Groundwater elevation measured in ft
mg/L = Milligrams per liter
MTBE = Methyl tert-butyl ether
NP = Well was not purged prior to sampling
P = Well was purged prior to sampling
TOC = Top of casing measured in ft
TPH-g = Total petroleum hydrocarbons as gasoline
µg/L = Micrograms per liter
BTEX = Benzene, toluene, ethylbenzene and xylenes

ESL - DW = Environmental Screning Levels (ESLs), shallow soils (<3 meters bgs), groundwater is a current or potential source of drinking water, for residential land use. Ref. California Regional Water Quality Control Board, San Francisco Bay Region (CRWQCB-SFBR), Screening for Environmental Concerns at Sites with Contaminated Soil & Groundwater, Interim Final-November 2007 (Revised May 2008).

ESL - NDW = Environmental Screning Levels (ESLs), shallow soils (<3 meters bgs), groundwater is NOT a current or potential source of drinking water, for residential land use. Ref. California Regional Water Quality Control Board, San Francisco Bay Region (CRWQCB-SFBR), Screening for Environmental Concerns at Sites with Contaminated Soil & Groundwater, Interim Final-November 2007 (Revised May 2008).

NE = ESL not established

Footnotes:
a = Chromatogram pattern: Gasoline C6-C10 for GRO/TPH-g
b = Beginning this quarter, groundwater samples were analyzed by EPA method 8260B for TPH-g, BTEX, and fuel oxygenates
c = Wells gauged with ORC sock in well
d = Well inaccessible
e = The hydrocarbon result for GRO was partly due to individual peaks in the quantitative range
f = Well resurveyed on 1/27/2004 to NAVD88
g = Upon review of survey data (1/27/2004), TOC elevation for MW-4 is actually 162.47 ft.
h = Upon review of survey data (1/27/2004), MW-5 was not surveyed from the TOC. MW-5 was surveyed from the pavement due to inaccessibility to the TOC. Therefore, survey data for MW-5 from the TOC is unavailable. Historic data prior to 5/30/2006 (change in consultant) not modified
i = Quantitation of unknown hydrocarbon(s) in sample based on gasoline
j = Surveyed 12/9/2010
k = Grab groundwater sample
l = Quantitated against gasoline

Notes:
Beginning in the fourth quarter 2003, the laboratory modified the reported analyte list. TPH-g was changed to GRO. The resulting data may be impacted by the potential of non-TPH-g analytes within the requested fuel range resulting in a higher concentration being reported

Beginning in the second quarter 2004, the carbon range for GRO was changed from C6-C10 to C4-C12

Values for DO and pH were obtained through field measurements

The DTW's and TOC's for wells MW-5 and MW-6 were taken from Delta Environmental sampling sheets because the well logs were not available

GRO analysis was completed by EPA method 8260B (C4-C12) for samples collected from the time period April 2006 through February 4, 2008. The analysis for GRO was changed to EPA method 8015B (C6-C12) for samples collected from the time period February 5, 2008 through the present

The data within this table collected prior to April 2006 was provided to Broadbent & Associates, Inc. by Atlantic Richfield Company and their previous consultants. Broadbent & Associates, Inc. has not verified the accuracy of this information

Table 2. Summary of Fuel Additives Analytical Data

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	Concentrations in µg/L								Footnote
	Ethanol	TBA	MTBE	DIPE	ETBE	TAME	1,2-DCA	EDB	
ESL - DW	NE	12	5.0	NE	NE	NE	0.5	0.05	
ESL - NDW	NE	18,000	1,800	NE	NE	NE	200	150	
MW-1									
3/23/2001	--	--	***2,710***	--	--	--	--	--	
3/21/2002	--	--	***2,000***	--	--	--	--	--	
5/23/2003	<20,000	*<4,000*	*1,600*	<100	<100	<100	--	--	
11/20/2003	<2,000	*<400*	*1,500*	<10	<10	<10	--	--	a
5/14/2004	<5,000	*<1,000*	*1,200*	<25	<25	<25	*<25*	*<25*	
9/2/2004	<1,000	*<200*	*660*	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	
11/4/2004	<2,000	*<400*	*580*	<10	<10	<10	*<10*	*<10*	
2/8/2005	<2,000	*<400*	*610*	<10	<10	<10	*<10*	*<10*	
5/9/2005	<1,000	*<200*	*620*	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	a
8/11/2005	<500	*250*	*390*	<2.5	<2.5	2.6	*<2.5*	*<2.5*	a
11/18/2005	<500	*<100*	*340*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	a
2/16/2006	<1,500	*<100*	*340*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
5/30/2006	<1,500	*<100*	*420*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	a
8/24/2006	<3,000	*<200*	*180*	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	
11/1/2006	<3,000	*<200*	*220*	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	a
2/7/2007	<3,000	*<200*	*190*	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	
5/8/2007	<3,000	*<200*	*420*	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	
8/8/2007	<300	*<20*	*110*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
11/14/2007	<1,500	*<100*	*210*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
2/22/2008	<300	<10	*250*	<0.50	<0.50	1.5	<0.50	*<0.50*	
5/24/2008	<3,000	*<100*	*380*	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	
8/21/2008	<1,500	*<50*	*170*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
11/19/2008	<300	<10	*30*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/23/2009	<1,500	*<50*	*240*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
5/14/2009	<300	<10	*200*	<0.50	<0.50	1.3	<0.50	*<0.50*	
8/20/2009	<1,200	*<40*	*170*	<2.0	<2.0	<2.0	*<2.0*	*<2.0*	
2/19/2010	<300	<10	*170*	<0.50	<0.50	1.2	<0.50	*<0.50*	
8/10/2010	<1,500	*<50*	*230*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
12/16/2010	<1,200	*<40*	*140*	<2.0	<2.0	<2.0	*<2.0*	*<2.0*	

Table 2. Summary of Fuel Additives Analytical Data

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	Concentrations in µg/L								Footnote
	Ethanol	TBA	MTBE	DIPE	ETBE	TAME	1,2-DCA	EDB	
ESL - DW	NE	12	5.0	NE	NE	NE	0.5	0.05	
ESL - NDW	NE	18,000	1,800	NE	NE	NE	200	150	
MW-1 Cont.									
2/14/2011	<1,500	*<50*	*170*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
8/15/2011	<1,500	*<50*	*130*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
2/2/2012	<600	*<20*	*66*	<1.0	<1.0	<1.0	*<1.0*	*<1.0*	
8/9/2012	<150	<10	*170*	<0.50	<0.50	0.78	<0.50	*<0.50*	
2/14/2013	<150	<10	*140*	<0.50	<0.50	0.58	<0.50	*<0.50*	
8/22/2013	<150	<10	*91*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
MW-2									
3/23/2001	--	--	<2.5	--	--	--	--	--	
3/21/2002	--	--	*45*	--	--	--	--	--	
5/23/2003	<100	*<20*	*55*	<0.50	<0.50	0.53	--	--	
2/2/2004	<100	*<20*	*37*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
9/2/2004	<500	*<100*	*67*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
2/8/2005	<100	*<20*	*30*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/11/2005	<100	*<20*	*35*	<0.50	<0.50	<0.50	<0.50	*<0.50*	a
2/16/2006	<300	*<20*	*39*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/24/2006	<300	*<20*	*25*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/7/2007	<300	*<20*	*7.2*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/8/2007	<300	*<20*	*7.2*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/22/2008	<300	<10	*24*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/21/2008	<300	<10	4.9	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/23/2009	<300	<10	*24*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/20/2009	<300	<10	*8.4*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/19/2010	<300	<10	*22*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/10/2010	<300	<10	*23*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
12/16/2010	<300	<10	*17*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/14/2011	<300	<10	*11*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/15/2011	<300	<10	1.7	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/2/2012	<300	<10	1.8	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/9/2012	<150	<10	*73*	<0.50	<0.50	0.61	<0.50	*<0.50*	

Table 2. Summary of Fuel Additives Analytical Data

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	Concentrations in µg/L								Footnote
	Ethanol	TBA	MTBE	DIPE	ETBE	TAME	1,2-DCA	EDB	
ESL - DW	NE	12	5.0	NE	NE	NE	0.5	0.05	
ESL - NDW	NE	18,000	1,800	NE	NE	NE	200	150	
MW-2 Cont.									
2/14/2013	<150	<10	*46*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/22/2013	<150	<10	*82*	<0.50	<0.50	1.1	<0.50	*<0.50*	
MW-3									
6/20/2000	--	--	*<10*	--	--	--	--	--	
12/17/2000	--	--	<2.5	--	--	--	--	--	
6/21/2001	--	--	2.5	--	--	--	--	--	
12/31/2001	--	--	4.9	--	--	--	--	--	
4/17/2002	--	--	*8.7*	--	--	--	--	--	
12/6/2002	--	--	*6.2*	--	--	--	--	--	
5/23/2003	<100	*<20*	1.6	<0.50	<0.50	<0.50	--	--	
9/2/2004	<100	*<20*	*6.5*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/11/2005	<100	*<20*	*11*	<0.50	<0.50	<0.50	<0.50	*<0.50*	a
8/24/2006	<300	*<20*	*7.6*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/8/2007	<300	*<20*	1.2	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/21/2008	<300	<10	3.1	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/20/2009	<300	<10	2.2	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/10/2010	<300	<10	1.6	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/15/2011	<300	<10	1.2	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/9/2012	<150	<10	2.0	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/22/2013	<150	<10	1.4	<0.50	<0.50	<0.50	<0.50	*<0.50*	
MW-4									
6/20/2000	--	--	*<250*	--	--	--	--	--	
12/17/2000	--	--	*<100*	--	--	--	--	--	
6/21/2001	--	--	*130*	--	--	--	--	--	
12/31/2001	--	--	*160*	--	--	--	--	--	
4/17/2002	--	--	*<250*	--	--	--	--	--	
12/6/2002	--	--	*43*	--	--	--	--	--	
5/23/2003	<10,000	*<2,000*	*<50*	<50	<50	<50	--	--	

Table 2. Summary of Fuel Additives Analytical Data

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	Concentrations in µg/L								Footnote
	Ethanol	TBA	MTBE	DIPE	ETBE	TAME	1,2-DCA	EDB	
ESL - DW	NE	12	5.0	NE	NE	NE	0.5	0.05	
ESL - NDW	NE	18,000	1,800	NE	NE	NE	200	150	
MW-4 Cont.									
2/2/2004	<500	*<100*	*29*	<2.5	<2.5	2.6	*<2.5*	*<2.5*	
9/2/2004	<200	*<40*	*28*	<1.0	<1.0	<1.0	*<1.0*	*<1.0*	
2/8/2005	<5,000	*<1,000*	*45*	<25	<25	<25	*<25*	*<25*	
8/11/2005	<2,000	*<400*	*32*	<10	<10	<10	*<10*	*<10*	
2/16/2006	<6,000	*<400*	*35*	<10	<10	<10	*<10*	*<10*	
8/24/2006	<1,500	*<100*	*39*	<2.5	<2.5	<2.5	*<2.5*	*<2.5*	
2/7/2007	<6,000	*<400*	*67*	<10	<10	<10	*<10*	*<10*	
8/8/2007	<6,000	*<400*	*72*	<10	<10	<10	*<10*	*<10*	
2/22/2008	<6,000	*<200*	*70*	<10	<10	<10	*<10*	*<10*	
8/21/2008	<12,000	*<400*	*53*	<20	<20	<20	*<20*	*<20*	
2/23/2009	<3,000	*<100*	*39*	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	
8/20/2009	<12,000	*<400*	*23*	<20	<20	<20	*<20*	*<20*	
2/19/2010	<3,000	*<100*	<5.0	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	
8/10/2010	<12,000	*<400*	*<20*	<20	<20	<20	*<20*	*<20*	
12/16/2010	<15,000	*<500*	*<25*	<25	<25	<25	*<25*	*<25*	
2/14/2011	<300	<10	*13*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/15/2011	<7,500	*<250*	*<12*	<12	<12	<12	*<12*	*<12*	
2/2/2012	<7,500	*<250*	*<12*	<12	<12	<12	*<12*	*<12*	
8/9/2012	<1,500	*<100*	<5.0	<5.0	<5.0	<5.0	*<5.0*	*<5.0*	
2/14/2013	<3,000	*<200*	*<10*	<10	<10	<10	*<10*	*<10*	
8/22/2013	<3,000	*<200*	*<10*	<10	<10	<10	*<10*	*<10*	
MW-5									
6/20/2000	--	--	*<10*	--	--	--	--	--	
9/28/2000	--	--	<2.5	--	--	--	--	--	
12/17/2000	--	--	<2.5	--	--	--	--	--	
3/23/2001	--	--	<2.5	--	--	--	--	--	
6/21/2001	--	--	<2.5	--	--	--	--	--	
9/23/2001	--	--	<2.5	--	--	--	--	--	
12/31/2001	--	--	<2.5	--	--	--	--	--	

Table 2. Summary of Fuel Additives Analytical Data

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	Concentrations in µg/L								Footnote
	Ethanol	TBA	MTBE	DIPE	ETBE	TAME	1,2-DCA	EDB	
ESL - DW	NE	12	5.0	NE	NE	NE	0.5	0.05	
ESL - NDW	NE	18,000	1,800	NE	NE	NE	200	150	
MW-5 Cont.									
3/21/2002	--	--	3.2	--	--	--	--	--	
4/17/2002	--	--	<2.5	--	--	--	--	--	
8/12/2002	--	--	<2.5	--	--	--	--	--	
12/6/2002	--	--	<2.5	--	--	--	--	--	
1/29/2003	<40	*<20*	<0.50	<0.50	<0.50	<0.50	--	--	
5/23/2003	<100	*<20*	<0.50	<0.50	<0.50	<0.50	--	--	
9/4/2003	<100	*<20*	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
9/2/2004	<100	*<20*	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/11/2005	<100	*<20*	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/24/2006	<300	*<20*	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/8/2007	<300	*<20*	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/21/2008	<300	<10	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/20/2009	<300	<10	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/10/2010	<300	<10	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/15/2011	<300	<10	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/9/2012	<150	<10	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/22/2013	<150	<10	<0.50	<0.50	<0.50	<0.50	<0.50	*<0.50*	
MW-6									
3/23/2001	--	--	<2.5	--	--	--	--	--	
3/21/2002	--	--	*5.2*	--	--	--	--	--	
5/23/2003	<100	*<20*	*9.4*	<0.50	<0.50	<0.50	--	--	
8/11/2005	<100	*<20*	*7.9*	<0.50	<0.50	<0.50	<0.50	*<0.50*	a
8/24/2006	<300	*<20*	*12*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/8/2007	<300	*<20*	0.57	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/21/2008	<300	<10	1.9	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/20/2009	<300	<10	2.0	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/10/2010	<300	<10	4.3	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/15/2011	<300	<10	2.2	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/9/2012	<150	<10	3.6	<0.50	<0.50	<0.50	<0.50	*<0.50*	

Table 2. Summary of Fuel Additives Analytical Data

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Well ID and Date Monitored	Concentrations in µg/L								Footnote
	Ethanol	TBA	MTBE	DIPE	ETBE	TAME	1,2-DCA	EDB	
ESL - DW	NE	12	5.0	NE	NE	NE	0.5	0.05	
ESL - NDW	NE	18,000	1,800	NE	NE	NE	200	150	
MW-7									
12/16/2010	<300	<10	*62*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/14/2011	<1,2000	*<400*	*<20*	<20	<20	<20	*<20*	*<20*	
5/20/2011	<300	<10	4.6	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/15/2011	<600	*<20*	*14*	<1.0	<1.0	<1.0	*<1.0*	*<1.0*	
2/2/2012	<300	<10	*6.2*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/9/2012	<150	<10	*7.0*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/14/2013	<150	<10	*5.1*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/22/2013	<150	<10	3.1	<0.50	<0.50	<0.50	<0.50	*<0.50*	
MW-8									
12/16/2010	<300	<10	*150*	<0.50	<0.50	1.7	<0.50	*<0.50*	
2/14/2011	<1,200	*<40*	*110*	<2.0	<2.0	<2.0	*<2.0*	*<2.0*	
5/20/2011	<1,200	*<40*	*88*	<2.0	<2.0	<2.0	*<2.0*	*<2.0*	
8/15/2011	<600	*<20*	*57*	<1.0	<1.0	<1.0	*<1.0*	*<1.0*	
2/2/2012	<300	<10	3.9	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/9/2012	<150	*31*	*150*	<0.50	<0.50	2.0	<0.50	*<0.50*	
2/14/2013	<600	*150*	*240*	<2.0	<2.0	5.2	*<2.0*	*<2.0*	
8/22/2013	<150	*39*	*180*	<0.50	<0.50	2.8	<0.50	*<0.50*	
MW-9									
12/16/2010	<300	*40*	*390*	<0.50	<0.50	4.1	<0.50	*<0.50*	
2/14/2011	<2,400	*<80*	*270*	<4.0	<4.0	<4.0	*<4.0*	*<4.0*	
5/20/2011	<2,400	*<80*	*280*	<4.0	<4.0	<4.0	*<4.0*	*<4.0*	
8/15/2011	<1,200	*<40*	*120*	<2.0	<2.0	<2.0	*<2.0*	*<2.0*	
2/2/2012	<300	<10	*34*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/9/2012	<150	<10	*19*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
2/14/2013	<150	<10	*25*	<0.50	<0.50	<0.50	<0.50	*<0.50*	
8/22/2013	<150	<10	*31*	<0.50	<0.50	0.55	<0.50	*<0.50*	

Symbols & Abbreviations:
-- = Not analyzed/applicable/measured/available
< = Not detected at or above the laboratory reporting limi
1,2-DCA = 1,2-Dichloroethane
ether
EDB = 1,2-Dibromoethane
ETBE = Ethyl tert-butyl ether
MTBE = Methyl tert-butyl ether
TAME = tert-Amyl methyl ether
TBA = tert-Butyl alcohol
µg/L = Micrograms per Liter

ESL - DW = Environmental Screning Levels (ESLs), shallow soils (<3 meters bgs), groundwater is a current or potential source of drinking water, for residential land use. Ref. California Regional Water Quality Control Board, San Francisco Bay Region (CRWQCB-SFBR), Screening for Environmental Concerns at Sites with Contaminated Soil & Groundwater, Interim Final-November 2007 (Revised May 2008).

ESL - NDW = Environmental Screning Levels (ESLs), shallow soils (<3 meters bgs), groundwater is NOT a current or potential source of drinking water, for residential land use. Ref. California Regional Water Quality Control Board, San Francisco Bay Region (CRWQCB-SFBR), Screening for Environmental Concerns at Sites with Contaminated Soil & Groundwater, Interim Final-November 2007 (Revised May 2008).

NE = ESL not established

Footnotes:
a = The continuing calibration verification for ethanol was outside of client contractual limits, however, it was within method acceptance limits. The data should still be useful for its intended purpose

Notes:
All volatile organic compounds analyzed using EPA Method 8260B

The data within this table collected prior to April 2006 was provided to Broadbent & Associates, Inc. by Atlantic Richfield Company and their previous consultants. Broadbent & Associates, Inc. has not verified the accuracy of this information

Table 3. Historical Groundwater Gradient - Direction and Magnitude

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Date Measured	Approximate Gradient Direction	Approximate Gradient Magnitude (ft/ft)
1/31/1996	Southwest	0.04
4/10/1996	Southwest	0.04
7/16/1996	Southwest	0.03
10/14/1996	Southwest	0.03
3/27/1997	Southwest	0.04
5/27/1997	Southwest	0.03
8/12/1997	Southwest	0.04
11/17/1997	Southwest	0.03
3/16/1998	Southwest	0.03
5/12/1998	Southwest	0.04
7/27/1998	Southwest	0.04
10/15/1998	Southwest	0.02
2/18/1999	Southwest	0.05
5/24/1999	Southwest	0.03
8/27/1999	Southwest	0.03
10/26/1999	Southwest	0.03
2/3/2000	Southwest	0.047
6/20/2000	Southwest	0.035
9/28/2000	Southwest	0.034
12/17/2000	Southwest	0.032
3/23/2001	Southwest	0.034
6/21/2001	Southwest	0.032
9/23/2001	Southwest	0.029
12/31/2001	Southwest	0.043
3/21/2002	Southwest	0.038
4/17/2002	Southwest	0.031
8/12/2002	Southwest	0.032
12/6/2002	Southwest	0.020
1/29/2003	Southwest	0.027
5/23/2003	Southwest	0.039
9/4/2003	Southwest	0.033
11/20/2003	Southwest	0.029
2/2/2004	Southwest	0.043 (a)
5/14/2004	Southwest	0.037 (a)
9/2/2004	Southwest	0.027 (a)
11/4/2004	Southwest	0.034 (a)
2/8/2005	Southwest	0.061 (a)
5/9/2005	Southwest	0.08 (a)
8/11/2005	Southwest	0.06 (a)
11/18/2005	Southwest	0.07 (a)
2/16/2006	Southwest	0.09 (a)
5/30/2006	Southwest	0.06 (a)
8/24/2006	Southwest	0.03
11/1/2006	Southwest	0.02
2/7/2007	Southwest	0.03

Table 3. Historical Groundwater Gradient - Direction and Magnitude

ARCO Service Station #0374, 6407 Telegraph Ave., Oakland, CA

Date Measured	Approximate Gradient Direction	Approximate Gradient Magnitude (ft/ft)
5/8/2007	Southwest	0.03
8/8/2007	Southwest	0.03
11/14/2007	Southwest	0.03
2/22/2008	Southwest	0.03
5/24/2008	Southwest	0.03
8/21/2008	Southwest	0.03
11/19/2008	Southwest	0.03
2/23/2009	Southwest	0.04
5/14/2009	Southwest	0.03
8/20/2009	Southwest	0.03
2/19/2010	West-Southwest	0.05
8/10/2010	Southwest	0.03
12/16/2010	Southwest	0.03
2/14/2011	Southwest	0.03
5/20/2011	Southwest	0.03
8/15/2011	Southwest	0.03
2/2/2012	Southwest	0.03
8/9/2012	Southwest	0.03
2/14/2013	Southwest	0.04
8/22/2013	**Southwest**	**0.03**

Footnotes:
a = Gradients potentially suspect due to error in MW-4 and MW-5 TOC measuring point elevations discovered third quarter 2006

Notes:
The data within this table collected prior to April 2006 was provided to Broadbent & Associates, Inc. by Atlantic Richfield Company and their previous consultants. Broadbent & Associates, Inc. has not verified the accuracy of this information

APPENDIX A

FIELD METHODS

QUALITY ASSURANCE/QUALITY CONTROL
FIELD METHODS

Field methods discussed herein were implemented to provide for accuracy and reliability of field activities, data collection, sample collection, and handling. Discussion of these methods is provided below.

1.0 Equipment Calibration

Equipment calibration was performed per equipment manufacturer specifications before use.

2.0 Depth to Groundwater and Light Non-Aqueous Phase Liquid Measurement

Depth to groundwater was measured in wells identified for gauging in the scope of work using a decontaminated water level indicator. The depth to water measurement was taken from a cut notch or permanent mark at the top of the well casing to which the well head elevation was originally surveyed.

Once depth to water was measured, an oil/water interface meter or a new disposable bailer was utilized to evaluate the presence and, if present, to measure the "apparent" thickness of light non-aqueous phase liquid (LNAPL) in the well. If LNAPL was present in the well, groundwater purging and sampling were not performed, unless sampling procedures in the scope of work specified collection of samples in the presence of LNAPL. Otherwise, time allowing, LNAPL was bailed from the well using either a new disposable bailer, or the disposal bailer previously used for initial LNAPL assessment. Bailing of LNAPL continued until the thickness of LNAPL (or volume) stabilized in each bailer pulled from the well, or LNAPL was no longer present. After LNAPL thickness either stabilized or was eliminated, periodic depth to water and depth to LNAPL measurements were collected as product came back into the well to evaluate product recovery rate and to aid in further assessment of LNAPL in the subsurface. LNAPL thickness measurements were recorded as "apparent." If a bailer was used for LNAPL thickness measurement, the field sampler noted the bailer entry diameter and chamber diameter to enable correction of thickness measurements. Recovered LNAPL was stored on-site in a labeled steel drum(s) or other appropriate container(s) prior to disposal.

3.0 Well Purging and Groundwater Sample Collection

Well purging and groundwater sampling were performed in wells specified in the scope of work after measuring depth to groundwater and evaluating the presence of LNAPL. Purging and sampling were performed using one of the methods detailed below. The method used was noted in the field records. Purge water was stored on-site in labeled steel drum(s) or other appropriate container(s) prior to disposal or on-site treatment (in cases where treatment using an on-site system is authorized).

3.1 Purging a Predetermined Well Volume

Purging a predetermined well volume is performed per ASTM International (ASTM) D4448-01. This purging method has the objective of removing a predetermined volume of stagnant water from the well prior to sampling. The volume of stagnant water is defined as either the volume of water contained within the well casing, or the volume within the well casing and sand/gravel in the annulus if natural flow through these is deemed insufficient to keep them flushed out.

This purging method involves removal of a minimum of three stagnant water volumes from the well using a decontaminated pump with new disposable plastic discharge or suction tubing, dedicated well tubing, or using a new disposable or decontaminated reusable bailer. If a new disposable bailer was used for assessment of LNAPL, that bailer may be used for purging. The withdrawal rate used is one that minimizes drawdown while satisfying time constraints.

To evaluate when purging is complete, one or more groundwater stabilization parameters are monitored and recorded during purging activities until stabilization is achieved. Most commonly, stabilization parameters include temperature, conductivity, and pH, but field procedures detailed in the scope of work may also include monitoring of dissolved oxygen concentrations, oxidation reduction potential, and/or turbidity[1]. Parameters are considered stable when two (2) consecutive readings recorded three (3) minutes apart fall within ranges provided below in Table 1. In the event that the parameters have not stabilized and five (5) well casing volumes have been removed, purging activities will cease and be considered complete. Once the well is purged, a groundwater sample(s) is collected from the well using a new disposable bailer. If a new disposable bailer was used for purging, that bailer may be used to collect the sample(s). A sample is not collected if the well is inadvertently purged dry.

Table 1. Criteria for Defining Stabilization of Water-Quality Indicator Parameters

Parameter	Stabilization Criterion
Temperature	± 0.2ºC (± 0.36ºF)
pH	± 0.1 standard units
Conductivity	± 3%
Dissolved oxygen	± 10%
Oxidation reduction potential	± 10 mV
Turbidity[1]	± 10% or 1.0 NTU (whichever is greater)

3.2 Low-Flow Purging and Sampling

“Low-Flow”, “Minimal Drawdown”, or "Low-Stress” purging is performed per ASTM D6771-02. It is a method of groundwater removal from within a well’s screened interval that is intended to minimize drawdown and mixing of the water column in the well casing. This is accomplished by pumping the well using a decontaminated pump with new disposable plastic discharge or

[1] As stated in ASTM D6771-02, turbidity is not a chemical parameter and not indicative of when formation-quality water is being purged; however, turbidity may be helpful in evaluating stress on the formation during purging. Turbidity measurements are taken at the same time that stabilization parameter measurements are made, or, at a minimum, once when purging is initiated and again just prior to sample collection, after stabilization parameters have stabilized. To avoid artifacts in sample analysis, turbidity should be as low as possible when samples are collected. If turbidity values are persistently high, the withdrawal rate is lowered until turbidity decreases. If high turbidity persists even after lowering the withdrawal rate, the purging is stopped for a period of time until turbidity settles, and the purging process is then restarted. If this fails to solve the problem, the purging/sampling process for the well is ceased, and well maintenance or redevelopment is considered.

suction tubing or dedicated well tubing at a low flow rate while evaluating the groundwater elevation during pumping.

The low flow pumping rate is well specific and is generally established at a volume that is less than or equal to the natural recovery rate of the well. A pump with adjustable flow rate control is positioned with the intake at or near the mid-point of the submerged well screen. The pumping rate used during low-flow purging is low enough to minimize mobilization of particulate matter and drawdown (stress) of the water column. Low-flow purging rates will vary based on the individual well characteristics; however, the purge rate should not exceed 1.0 Liter per minute (L/min) or 0.25 gallon per minute (gal/min). Low-flow purging should begin at a rate of approximately 0.1 L/min (0.03 gal/min)[2], or the lowest rate possible, and be adjusted based on an evaluation of drawdown. Water level measurements should be recorded at approximate one (1) to two (2) minute intervals until the low-flow rate has been established, and drawdown is minimized. As a general rule, drawdown should not exceed 25% of the distance between the top of the water column and the pump in-take.

To evaluate when purging is complete, one or more groundwater stabilization parameters are monitored and recorded during purging activities until stabilization is achieved. Most commonly, stabilization parameters include temperature, conductivity, and pH, but field procedures detailed in the scope of work may also include monitoring of dissolved oxygen concentrations, oxidation reduction potential, and/or turbidity[1]. The frequency between measurements will be at an interval of one (1) to three (3) minutes; however, if a flow cell is used, the frequency will be determined based on the time required to evacuate one cell volume. Stabilization is defined as three (3) consecutive readings recorded several minutes apart falling within ranges provided in Table 1. Samples will be collected by filling appropriate containers from the pump discharge tubing at a rate not to exceed the established pumping rate.

3.3 Minimal Purge, Discrete Depth, and Passive Sampling

Per ASTM D4448-01, sampling techniques that do not rely on purging, or require only minimal purging, may be used if a particular zone within a screened interval is to be sampled or if a well is not capable of yielding sufficient groundwater for purging. To properly use these sampling techniques, a water sample is collected within the screened interval with little or no mixing of the water column within the casing. These techniques include minimal purge sampling which uses a dedicated sampling pump capable of pumping rates of less than 0.1 L/min (0.03 gal/min)[2], discrete depth sampling using a bailer that allows groundwater entry at a controlled depth (e.g. differential pressure bailer), or passive (diffusion) sampling. These techniques are based on certain studies referenced in ASTM D4448-01 that indicate that under certain conditions, natural groundwater flow is laminar and horizontal with little or no mixing within the well screen.

---

[2] According to ASTM D4448-01, studies have indicated that at flow rates of 0.1 L/min, low-density polyethylene (LDPE) and plasticized polypropylene tubing materials are prone to sorption. Therefore, TFE-fluorocarbon or other appropriate tubing material is used, particularly when tubing lengths of 50 feet or longer are used.

4.0 Decontamination

Reusable groundwater sampling equipment were cleaned using a solution of Alconox or other acceptable detergent, rinsed with tap water, and finally rinsed with distilled water prior to use in each well. Decontamination water was stored on-site in labeled steel drum(s) or other appropriate container(s) prior to disposal.

5.0 Sample Containers, Labeling, and Storage

Samples were collected in laboratory prepared containers with appropriate preservative (if preservative was required). Samples were properly labeled (site name, sample I.D., sampler initials, date, and time of collection) and stored chilled (refrigerator or ice chest with ice) until delivery to a certified laboratory, under chain of custody procedures.

6.0 Chain of Custody Record and Procedure

The field sampler was personally responsible for care and custody of the samples collected until they were properly transferred to another party. To document custody and transfer of samples, a Chain of Custody Record was prepared. The Chain of Custody Record provided identification of the samples corresponding to sample labels and specified analyses to be performed by the laboratory. The original Chain of Custody Record accompanied the shipment, and a copy of the record was stored in the project file. When the samples were transferred, the individuals relinquishing and receiving them signed, dated, and noted the time of transfer on the record.

7.0 Field Records

Daily Report and data forms were completed by staff personnel to provide daily record of significant events, observations, and measurements. Field records were signed, dated, and stored in the project file.

APPENDIX B

FIELD DATA SHEETS

BROADBENT

DAILY REPORT

Page 1 of 1

Project: BP 374 Project No.: 06-82-640

Field Representative(s): A. Martinez / A. Hernandez Day: Thursday Date: 8/22/13

Time Onsite: From: 0700 To: 1200 ; From: _____ To: _____; From: _____ To: _____

✓ Signed HASP ✓ Safety Glasses ✓ Hard Hat ✓ Steel Toe Boots ✓ Safety Vest

✓ UST Emergency System Shut-off Switches Located ✓ Proper Gloves

✓ Proper Level of Barricading ___ Other PPE (describe) _____

Weather: Overcast

Equipment In Use: Peri pump, water level meter, water quality meter.

Visitors: Kristene Tidwell

TIME:	WORK DESCRIPTION:
0700	Arrived onsite conducted tailgate. Property manager requested recent report.
0745	Set up @ MW-1.
0825	Set up @ MW-2
0850	Set up @ MW-9
0920	Set up @ MW-8
0950	Set up @ MW-7
1020	Set up @ MW-3
	* MW-6 covered by car.
1045	Set up @ MW-5
1115	Set up @ MW-4
	MW-4 vault measurements:
	Vault 40.5" x 38.5" x 21" Vault Lid: 35.5"
	Well vault in good shape, latches into place when opened
	and properly secured with functioning bolts.
1200	Completed fieldwork & offsite.

Signature: _____

Revision: 1/24/2012

BROADBENT

GROUNDWATER MONITORING SITE SHEET

Project: BP 374 Project No.: 06-88-602 Date: 8/22/13

Field Representative: AH & AM Elevation: _____

Formation recharge rate is historically: (High) Low *(circle one)*

W. L. Indicator ID #: _____ Oil/Water Interface ID #: _____ *(List #s of all equip used.)*

WELL ID RECORD					WELL GAUGING RECORD					NOTES
Well ID	Well Sampling Order	As-Built Well Diameter (inches)	As-Built Well Screen Interval (ft)	Previous Depth to Water (ft)	Time (24:00)	Depth to LNAPL (ft)	Apparent LNAPL Thickness (ft)*	Depth to Water (ft)	Well Total Depth (ft)	
MW-1					0757	—	—	7.87	26.77	
MW-2					0826	—	—	7.79	26.35	
MW-3					1025	—	—	7.15	26.80	
MW-4					1117	—	—	7.59	26.97	
MW-5					1051	—	—	8.34	23.10	
MW-6					Car parked over well				14.65	
MW-7					0955	—	—	7.39	19.80	
MW-8					0927			7.95	19.40	
MW-9					0857	—	—	7.46	19.35	

* Device used to measure LNAPL thickness: Bailer Oil/Water Interface Meter *(circle one)*

If bailer used, note bailer dimensions (inches): Entry Diameter _____ Chamber Diameter _____

Signature: _____

BROADBENT

GROUNDWATER SAMPLING DATA SHEET

Project: BP No. 374 Project No.: 06-88-602 Date: 8/22/13

Field Representative: AH & AM

Well ID: MW-1 Start Time: 0800 End Time: 0820 Total Time (minutes): 20

PURGE EQUIPMENT ___ Disp. Bailer ___ 120V Pump ___ Flow Cell ___ Disp. Tubing ___ 12V Pump X Peristaltic Pump Other/ID#:

WELL HEAD INTEGRITY (cap, lock, vault, etc.) Comments:

(Good) Improvement Needed *(circle one)*

PURGING/SAMPLING METHOD Predetermined Well Volume (Low-Flow) Other: *(circle one)*

PREDETERMINED WELL VOLUME

Casing Diameter | Unit Volume (gal/ft) *(circle one)*

1" | (0.04) 1.25" | (0.08) 2" | (0.17) 3" | (0.38) Other:

4" | (0.66) 6" | (1.50) 8" | (2.60) 12" | (5.81) ___" | (___)

Total Well Depth (a): ___(ft)

Initial Depth to Water (b): ___(ft)

Water Column Height (WCH) = (a - b): ___(ft)

Water Column Volume (WCV) = WCH x Unit Volume: ___(gal)

Three Casing Volumes = WCV x 3: ___(gal)

Five Casing Volumes = WCV x 5: ___(gal)

Pump Depth (if pump used): ___(ft)



LOW-FLOW

Previous Low-Flow Purge Rate: ___(lpm)

Total Well Depth (a): 26.77 (ft)

Initial Depth to Water (b): 7.87 (ft)

Pump In-take Depth = b + (a-b)/2: 17.32 (ft)

Maximum Allowable Drawdown = (a-b)/8: 2.36 (ft)

Low-Flow Purge Rate: 0.25 (Lpm)*

Comments:

**Low-flow purge rate should be within range of instruments used but should not exceed 0.25 gpm. Drawdown should not exceed Maximum Allowable Drawdown.*

GROUNDWATER STABILIZATION PARAMETER RECORD

Time (24:00)	Cumulative Volume (L)	Temperature °C	pH	Conductivity µS or mS	DO mg/L	ORP mV	Turbidity NTU	NOTES Odor, color, sheen or other
0803	0.0	23.58	8.73	0.453	6.11	32	310	NONE
0806	0.5	22.97	7.72	0.456	5.55	67	312	"
0809	1.0	22.34	7.40	0.461	5.54	86	315	"
0812	1.5	21.43	7.21	0.469	5.69	102	314	"
Previous Stabilized Parameters								

PURGE COMPLETION RECORD X Low Flow & Parameters Stable ___ 3 Casing Volumes & Parameters Stable ___ 5 Casing Volumes ___ Other:

SAMPLE COLLECTION RECORD

Depth to Water at Sampling: 8.18 (ft)

Sample Collected Via: ___ Disp. Bailer ___ Dedicated Pump Tubing X Disp. Pump Tubing Other:

Sample ID: MW-1 Sample Collection Time: 0815 (24:00)

Containers (#): X VOA (X preserved or ___ unpreserved) ___ Liter Amber

___ Other: ___ Other:

___ Other: ___ Other:

GEOCHEMICAL PARAMETERS

Parameter	Time	Measurement
DO (mg/L)		
Ferrous Iron (mg/L)		
Redox Potential (mV)		
Alkalinity (mg/L)		
Other:		
Other:		

Signature:

BROADBENT

GROUNDWATER SAMPLING DATA SHEET

Project: BP No. 374 Project No.: 06-88602 Date: 8/22/12

Field Representative: AH & AM

Well ID: MW-2 Start Time: 0825 End Time: 0850 Total Time (minutes): 25

PURGE EQUIPMENT ___ Disp. Bailer ___ 120V Pump ___ Flow Cell
X Disp. Tubing ___ 12V Pump ___ Peristaltic Pump Other/ID#:

WELL HEAD INTEGRITY (cap, lock, vault, etc.) Comments:
(Good) Improvement Needed *(circle one)*

PURGING/SAMPLING METHOD Predetermined Well Volume (Low-Flow) Other: *(circle one)*

PREDETERMINED WELL VOLUME

Casing Diameter | Unit Volume (gal/ft) *(circle one)*

1" | (0.04) 1.25" | (0.08) 2" | (0.17) 3" | (0.38) Other:
4" | (0.66) 6" | (1.50) 8" | (2.60) 12" | (5.81) ___" | (___)

Total Well Depth (a): ___(ft)
Initial Depth to Water (b): ___(ft)
Water Column Height (WCH) = (a - b): ___(ft)
Water Column Volume (WCV) = WCH x Unit Volume: ___(gal)
Three Casing Volumes = WCV x 3: ___(gal)
Five Casing Volumes = WCV x 5: ___(gal)
Pump Depth (if pump used): ___(ft)



LOW-FLOW

Previous Low-Flow Purge Rate: ___(lpm)
Total Well Depth (a): 26.35 (ft)
Initial Depth to Water (b): 7.79 (ft)
Pump In-take Depth = b + (a-b)/2: 17.07 (ft)
Maximum Allowable Drawdown = (a-b)/8: 2.32 (ft)
Low-Flow Purge Rate: 0.25 (Lpm)*
Comments:

**Low-flow purge rate should be within range of instruments used but should not exceed 0.25 gpm. Drawdown should not exceed Maximum Allowable Drawdown.*

GROUNDWATER STABILIZATION PARAMETER RECORD

Time (24:00)	Cumulative Volume (L)	Temperature °C	pH	Conductivity µS or mS	DO mg/L	ORP mV	Turbidity NTU	NOTES Odor, color, sheen or other
0831	0.0	22.44	7.50	0.398	6.55	121	501	NONE
0834	0.5	22.76	7.30	0.395	5.60	132	530	"
0836	1.0	22.86	7.26	0.395	4.99	134	521	"
0839	1.5	22.98	7.23	0.393	4.16	137	481	"
Previous Stabilized Parameters								

PURGE COMPLETION RECORD X Low Flow & Parameters Stable ___ 3 Casing Volumes & Parameters Stable ___ 5 Casing Volumes
___ Other:

SAMPLE COLLECTION RECORD

Depth to Water at Sampling: 8.05 (ft)
Sample Collected Via: ___ Disp. Bailer ___ Dedicated Pump Tubing
X Disp. Pump Tubing Other:
Sample ID: MW-2 Sample Collection Time: 0840 (24:00)
Containers (#): X VOA (X preserved or ___ unpreserved) ___ Liter Amber
___ Other: ___ Other:
___ Other: ___ Other:

GEOCHEMICAL PARAMETERS

Parameter	Time	Measurement
DO (mg/L)		
Ferrous Iron (mg/L)		
Redox Potential (mV)		
Alkalinity (mg/L)		
Other:		
Other:		

Signature:

BROADBENT

GROUNDWATER SAMPLING DATA SHEET

Project: BP No. 374 Project No.: 06-89-602 Date: 8/22/13

Field Representative: AH & AM

Well ID: MW-3 Start Time: 1025 End Time: 1045 Total Time (minutes): 20

PURGE EQUIPMENT

X Disp. Tubing ___ Disp. Bailer ___ 12V Pump ___ 120V Pump ___ Peristaltic Pump ___ Flow Cell Other/ID#:

WELL HEAD INTEGRITY (cap, lock, vault, etc.)

Good (Improvement Needed) *(circle one)* Comments: missing bolts

PURGING/SAMPLING METHOD Predetermined Well Volume (Low-Flow) Other: *(circle one)*

PREDETERMINED WELL VOLUME

Casing Diameter | Unit Volume (gal/ft) *(circle one)*

1" | (0.04) 1.25" | (0.08) 2" | (0.17) 3" | (0.38) Other: ___" | (___)

4" | (0.66) 6" | (1.50) 8" | (2.60) 12" | (5.81)

Total Well Depth (a): _____ (ft)

Initial Depth to Water (b): _____ (ft)

Water Column Height (WCH) = (a - b): _____ (ft)

Water Column Volume (WCV) = WCH x Unit Volume: _____ (gal)

Three Casing Volumes = WCV x 3: _____ (gal)

Five Casing Volumes = WCV x 5: _____ (gal)

Pump Depth (if pump used): _____ (ft)



LOW-FLOW

Previous Low-Flow Purge Rate: _____ (lpm)

Total Well Depth (a): 26.80 (ft)

Initial Depth to Water (b): 7.15 (ft)

Pump In-take Depth = b + (a-b)/2: 16.98 (ft)

Maximum Allowable Drawdown = (a-b)/8: 2.46 (ft)

Low-Flow Purge Rate: 0.25 (Lpm)*

Comments:

**Low-flow purge rate should be within range of instruments used but should not exceed 0.25 gpm. Drawdown should not exceed Maximum Allowable Drawdown.*

GROUNDWATER STABILIZATION PARAMETER RECORD

Time (24:00)	Cumulative Vol. gal or L	Temperature °C	pH	Conductivity µS or (mS)	DO mg/L	ORP mV	Turbidity NTU	NOTES Odor, color, sheen or other
1031	0.0	21.94	7.40	0.422	5.03	112	342	NONE
1033	0.5	21.90	6.95	0.422	4.53	123	330	"
1035	1.0	21.48	6.77	0.425	4.40	113	329	"
1037	1.5	21.32	6.72	0.426	4.35	103	329	"
Previous Stabilized Parameters								

PURGE COMPLETION RECORD X Low Flow & Parameters Stable ___ 3 Casing Volumes & Parameters Stable ___ 5 Casing Volumes ___ Other:

SAMPLE COLLECTION RECORD

Depth to Water at Sampling: 7.37 (ft)

Sample Collected Via: ___ Disp. Bailer ___ Dedicated Pump Tubing X Disp. Pump Tubing Other:

Sample ID: MW-3 Sample Collection Time: 1040 (24:00)

Containers (#): X VOA (X preserved or ___ unpreserved) ___ Liter Amber

___ Other: ___ ___ Other: ___

___ Other: ___ ___ Other: ___

GEOCHEMICAL PARAMETERS

Parameter	Time	Measurement
DO (mg/L)		
Ferrous Iron (mg/L)		
Redox Potential (mV)		
Alkalinity (mg/L)		
Other:		
Other:		

Signature: _____

BROADBENT

GROUNDWATER SAMPLING DATA SHEET

Project: BP No. 374 Project No.: 06-88-602 Date: 8/22/13

Field Representative: AH & AM

Well ID: MW-4 Start Time: 1115 End Time: 1140 Total Time (minutes): 25

PURGE EQUIPMENT

X Disp. Tubing ___ Disp. Bailer ___ 12V Pump ___ 120V Pump ___ Peristaltic Pump ___ Flow Cell Other/ID#:

WELL HEAD INTEGRITY (cap, lock, vault, etc.) Comments:

(Good) Improvement Needed *(circle one)*

PURGING/SAMPLING METHOD Predetermined Well Volume (Low-Flow) Other: *(circle one)*

PREDETERMINED WELL VOLUME

Casing Diameter | Unit Volume (gal/ft) *(circle one)*

1" | (0.04) 1.25" | (0.08) 2" | (0.17) 3" | (0.38) Other: ___" | (___)

4" | (0.66) 6" | (1.50) 8" | (2.60) 12" | (5.81)

Total Well Depth (a): ___ (ft)

Initial Depth to Water (b): ___ (ft)

Water Column Height (WCH) = (a - b): ___ (ft)

Water Column Volume (WCV) = WCH x Unit Volume: ___ (gal)

Three Casing Volumes = WCV x 3: ___ (gal)

Five Casing Volumes = WCV x 5: ___ (gal)

Pump Depth (if pump used): ___ (ft)



LOW-FLOW

Previous Low-Flow Purge Rate: ___ (lpm)

Total Well Depth (a): 26.97 (ft)

Initial Depth to Water (b): 7.59 (ft)

Pump In-take Depth = b + (a-b)/2: 17.28 (ft)

Maximum Allowable Drawdown = (a-b)/8: 2.42 (ft)

Low-Flow Purge Rate: 0.25 (Lpm)*

Comments:

**Low-flow purge rate should be within range of instruments used but should not exceed 0.25 gpm. Drawdown should not exceed Maximum Allowable Drawdown.*

GROUNDWATER STABILIZATION PARAMETER RECORD

Time (24:00)	Cumulative Vol. gal or L	Temperature °C	pH	Conductivity µS or mS	DO mg/L	ORP mV	Turbidity NTU	NOTES Odor, color, sheen or other
1123	0.0	20.60	7.11	0.519	5.04	111	321	NONE
1125	0.5	20.42	7.02	0.521	4.76	65	322	MODERATE HC ODOR
1127	1.0	20.38	7.00	0.521	4.60	0	321	"
1129	1.5	20.36	6.98	0.521	4.50	-28	320	"
Previous Stabilized Parameters								

PURGE COMPLETION RECORD X Low Flow & Parameters Stable ___ 3 Casing Volumes & Parameters Stable ___ 5 Casing Volumes ___ Other:

SAMPLE COLLECTION RECORD

Depth to Water at Sampling: 7.92 (ft)

Sample Collected Via: ___ Disp. Bailer ___ Dedicated Pump Tubing X Disp. Pump Tubing Other:

Sample ID: MW-4 Sample Collection Time: 1135 (24:00)

Containers (#): X VOA (X preserved or ___ unpreserved) ___ Liter Amber

___ Other: ___ ___ Other: ___

___ Other: ___ ___ Other: ___

GEOCHEMICAL PARAMETERS

Parameter	Time	Measurement
DO (mg/L)		
Ferrous Iron (mg/L)		
Redox Potential (mV)		
Alkalinity (mg/L)		
Other:		
Other:		

Signature:

BROADBENT

GROUNDWATER SAMPLING DATA SHEET

Project: BP No. 374 Project No.: 06-88-602 Date: 8/22/13

Field Representative: AH&AM

Well ID: MW-5 Start Time: 1050 End Time: 1110 Total Time (minutes): 20

PURGE EQUIPMENT ___ Disp. Bailer ___ 120V Pump ___ Flow Cell
X Disp. Tubing ___ 12V Pump ___ Peristaltic Pump Other/ID#:

WELL HEAD INTEGRITY (cap, lock, vault, etc.) Comments:
(Good) Improvement Needed *(circle one)*

PURGING/SAMPLING METHOD Predetermined Well Volume (Low-Flow) Other: *(circle one)*

PREDETERMINED WELL VOLUME

Casing Diameter | Unit Volume (gal/ft) *(circle one)*

1" | (0.04) 1.25" | (0.08) 2" | (0.17) 3" | (0.38) Other:
4" | (0.66) 6" | (1.50) 8" | (2.60) 12" | (5.81) ___" | (___)

Total Well Depth (a): ___(ft)
Initial Depth to Water (b): ___(ft)
Water Column Height (WCH) = (a - b): ___(ft)
Water Column Volume (WCV) = WCH x Unit Volume: ___(gal)
Three Casing Volumes = WCV x 3: ___(gal)
Five Casing Volumes = WCV x 5: ___(gal)
Pump Depth (if pump used): ___(ft)



LOW-FLOW

Previous Low-Flow Purge Rate: ___(lpm)
Total Well Depth (a): 23.10 (ft)
Initial Depth to Water (b): 8.34 (ft)
Pump In-take Depth = b + (a-b)/2: 15.72 (ft)
Maximum Allowable Drawdown = (a-b)/8: 1.85 (ft)
Low-Flow Purge Rate: 0.25 (Lpm)*
Comments:

**Low-flow purge rate should be within range of instruments used but should not exceed 0.25 gpm. Drawdown should not exceed Maximum Allowable Drawdown.*

GROUNDWATER STABILIZATION PARAMETER RECORD

Time (24:00)	Cumulative Vol. gal or L	Temperature °C	pH	Conductivity µS or (mS)	DO mg/L	ORP mV	Turbidity NTU	NOTES Odor, color, sheen or other
1056	0.0	22.22	7.10	0.374	5.25	94	337	NONE
1058	0.5	22.37	7.02	0.372	4.72	98	342	"
1100	1.0	22.43	6.98	0.372	4.48	96	324	"
1102	1.5	22.48	6.95	0.372	4.33	93	312	"
Previous Stabilized Parameters								

PURGE COMPLETION RECORD X Low Flow & Parameters Stable ___ 3 Casing Volumes & Parameters Stable ___ 5 Casing Volumes
___ Other:

SAMPLE COLLECTION RECORD

Depth to Water at Sampling: 8.78 (ft)
Sample Collected Via: ___ Disp. Bailer ___ Dedicated Pump Tubing
X Disp. Pump Tubing Other:
Sample ID: MW-5 Sample Collection Time: 1105 (24:00)
Containers (#): X VOA (X preserved or ___ unpreserved) ___ Liter Amber
___ Other: ___ Other:
___ Other: ___ Other:

GEOCHEMICAL PARAMETERS

Parameter	Time	Measurement
DO (mg/L)		
Ferrous Iron (mg/L)		
Redox Potential (mV)		
Alkalinity (mg/L)		
Other:		
Other:		

Signature:

Revision: 3/15/2013

BROADBENT

GROUNDWATER SAMPLING DATA SHEET

Project: BP No. 374 Project No.: 06-88-602 Date: 8/22/13

Field Representative: AH & AM

Well ID: MW-7 Start Time: 0955 End Time: 1015 Total Time (minutes): 20

PURGE EQUIPMENT

X Disp. Tubing ___ Disp. Bailer ___ 12V Pump ___ 120V Pump ___ Peristaltic Pump ___ Flow Cell Other/ID#:

WELL HEAD INTEGRITY (cap, lock, vault, etc.) Comments:

(Good) Improvement Needed *(circle one)*

PURGING/SAMPLING METHOD Predetermined Well Volume (Low-Flow) Other: *(circle one)*

PREDETERMINED WELL VOLUME

Casing Diameter | Unit Volume (gal/ft) *(circle one)*

1" | (0.04) 1.25" | (0.08) 2" | (0.17) 3" | (0.38) Other: ___" | (___)

4" | (0.66) 6" | (1.50) 8" | (2.60) 12" | (5.81)

Total Well Depth (a): ___(ft)

Initial Depth to Water (b): ___(ft)

Water Column Height (WCH) = (a - b): ___(ft)

Water Column Volume (WCV) = WCH x Unit Volume: ___(gal)

Three Casing Volumes = WCV x 3: ___(gal)

Five Casing Volumes = WCV x 5: ___(gal)

Pump Depth (if pump used): ___(ft)



LOW-FLOW

Previous Low-Flow Purge Rate: ___(lpm)

Total Well Depth (a): 19.80 (ft)

Initial Depth to Water (b): 7.39 (ft)

Pump In-take Depth = b + (a-b)/2: 13.60 (ft)

Maximum Allowable Drawdown = (a-b)/8: 1.55 (ft)

Low-Flow Purge Rate: 0.25 (Lpm)*

Comments:

**Low-flow purge rate should be within range of instruments used but should not exceed 0.25 gpm. Drawdown should not exceed Maximum Allowable Drawdown.*

GROUNDWATER STABILIZATION PARAMETER RECORD

Time (24:00)	Cumulative Vol. gal or L	Temperature °C	pH	Conductivity µS or mS	DO mg/L	ORP mV	Turbidity NTU	NOTES Odor, color, sheen or other
1000	0.0	22.77	7.11	0.662	5.32	127	310	None
1002	0.5	23.09	7.01	0.660	4.27	118	311	"
1005	1.0	23.16	7.00	0.659	4.14	109	311	"
1007	1.5	23.22	7.00	0.659	4.01	97	312	"
Previous Stabilized Parameters								

PURGE COMPLETION RECORD X Low Flow & Parameters Stable ___ 3 Casing Volumes & Parameters Stable ___ 5 Casing Volumes ___ Other:

SAMPLE COLLECTION RECORD

Depth to Water at Sampling: 7.78 (ft)

Sample Collected Via: ___ Disp. Bailer ___ Dedicated Pump Tubing X Disp. Pump Tubing Other:

Sample ID: MW-7 Sample Collection Time: 1010 (24:00)

Containers (#): X VOA (X preserved or ___ unpreserved) ___ Liter Amber

___ Other: ___ Other:

___ Other: ___ Other:

GEOCHEMICAL PARAMETERS

Parameter	Time	Measurement
DO (mg/L)		
Ferrous Iron (mg/L)		
Redox Potential (mV)		
Alkalinity (mg/L)		
Other:		
Other:		

Signature:

BROADBENT

GROUNDWATER SAMPLING DATA SHEET

Project: BP No. 374 Project No.: 06-88-602 Date: 8/22/13

Field Representative: AH & AM

Well ID: MW-8 Start Time: 0925 End Time: 0950 Total Time (minutes): 25

PURGE EQUIPMENT

___ Disp. Bailer ___ 120V Pump ___ Flow Cell

X Disp. Tubing ___ 12V Pump ___ Peristaltic Pump Other/ID#:

WELL HEAD INTEGRITY (cap, lock, vault, etc.) Comments:

(Good) Improvement Needed *(circle one)*

PURGING/SAMPLING METHOD Predetermined Well Volume (Low-Flow) Other: *(circle one)*

PREDETERMINED WELL VOLUME

Casing Diameter | Unit Volume (gal/ft) *(circle one)*

1" | (0.04) 1.25" | (0.08) 2" | (0.17) 3" | (0.38) Other:

4" | (0.66) 6" | (1.50) 8" | (2.60) 12" | (5.81) ____" | (____)

Total Well Depth (a): _____(ft)

Initial Depth to Water (b): _____(ft)

Water Column Height (WCH) = (a - b): _____(ft)

Water Column Volume (WCV) = WCH x Unit Volume: _____(gal)

Three Casing Volumes = WCV x 3: _____(gal)

Five Casing Volumes = WCV x 5: _____(gal)

Pump Depth (if pump used): _____(ft)



LOW-FLOW

Previous Low-Flow Purge Rate: _____(lpm)

Total Well Depth (a): 19.40 (ft)

Initial Depth to Water (b): 7.95 (ft)

Pump In-take Depth = b + (a-b)/2: 13.68 (ft)

Maximum Allowable Drawdown = (a-b)/8: 1.43 (ft)

Low-Flow Purge Rate: 0.25 (Lpm)*

Comments:

**Low-flow purge rate should be within range of instruments used but should not exceed 0.25 gpm. Drawdown should not exceed Maximum Allowable Drawdown.*

GROUNDWATER STABILIZATION PARAMETER RECORD

Time (24:00)	Cumulative Vol. gal or L	Temperature °C	pH	Conductivity µS or mS	DO mg/L	ORP mV	Turbidity NTU	NOTES Odor, color, sheen or other
0933	0.0	22.52	7.27	0.472	5.20	101	396	NONE
0935	0.5	23.06	6.96	0.467	4.33	107	401	"
0938	1.0	23.21	6.90	0.465	4.09	105	356	"
0940	1.5	23.33	6.88	0.464	3.96	103	324	"
Previous Stabilized Parameters								

PURGE COMPLETION RECORD X Low Flow & Parameters Stable ___ 3 Casing Volumes & Parameters Stable ___ 5 Casing Volumes

___ Other:

SAMPLE COLLECTION RECORD

Depth to Water at Sampling: 8.14 (ft)

Sample Collected Via: ___ Disp. Bailer ___ Dedicated Pump Tubing

X Disp. Pump Tubing Other:

Sample ID: MW-8 Sample Collection Time: 0945 (24:00)

Containers (#): X VOA (X preserved or ___ unpreserved) ___ Liter Amber

___ Other: ___ Other:

___ Other: ___ Other:

GEOCHEMICAL PARAMETERS

Parameter	Time	Measurement
DO (mg/L)		
Ferrous Iron (mg/L)		
Redox Potential (mV)		
Alkalinity (mg/L)		
Other:		
Other:		

Signature: _____

Revision: 3/15/2013

BROADBENT

GROUNDWATER SAMPLING DATA SHEET

Project: BP No. 374 Project No.: 06-88-602 Date: 8/22/13

Field Representative: AH & AM

Well ID: MW-9 Start Time: 0855 End Time: 0920 Total Time (minutes): 25

PURGE EQUIPMENT

X Disp. Tubing ___ Disp. Bailer ___ 12V Pump ___ 120V Pump ___ Peristaltic Pump ___ Flow Cell Other/ID#:

WELL HEAD INTEGRITY (cap, lock, vault, etc.) Comments:

Good / Improvement Needed *(circle one)*

PURGING/SAMPLING METHOD Predetermined Well Volume / Low-Flow / Other: *(circle one)*

PREDETERMINED WELL VOLUME

Casing Diameter | Unit Volume (gal/ft) *(circle one)*

1" | (0.04) 1.25" | (0.08) 2" | (0.17) 3" | (0.38) Other: ___" | (___)

4" | (0.66) 6" | (1.50) 8" | (2.60) 12" | (5.81)

Total Well Depth (a): ___ (ft)

Initial Depth to Water (b): ___ (ft)

Water Column Height (WCH) = (a - b): ___ (ft)

Water Column Volume (WCV) = WCH x Unit Volume: ___ (gal)

Three Casing Volumes = WCV x 3: ___ (gal)

Five Casing Volumes = WCV x 5: ___ (gal)

Pump Depth (if pump used): ___ (ft)



LOW-FLOW

Previous Low-Flow Purge Rate: ___ (lpm)

Total Well Depth (a): 19.35 (ft)

Initial Depth to Water (b): 7.46 (ft)

Pump In-take Depth = b + (a-b)/2: 13.41 (ft)

Maximum Allowable Drawdown = (a-b)/8: 1.47 (ft)

Low-Flow Purge Rate: 0.25 (Lpm)*

Comments:

**Low-flow purge rate should be within range of instruments used but should not exceed 0.25 gpm. Drawdown should not exceed Maximum Allowable Drawdown.*

GROUNDWATER STABILIZATION PARAMETER RECORD

Time (24:00)	Cumulative Vol. gal or L	Temperature °C	pH	Conductivity µS or mS	DO mg/L	ORP mV	Turbidity NTU	NOTES Odor, color, sheen or other
0902	0.0	22.10	7.31	0.583	5.81	146	311	NONE
0904	0.5	22.17	7.14	0.583	5.30	124	311	"
0907	1.0	22.18	7.10	0.584	4.98	64	311	"
0909	1.5	22.22	7.08	0.584	4.89	51	311	"
0912	2.0	22.23	7.07	0.584	4.71	7	311	"
Previous Stabilized Parameters								

PURGE COMPLETION RECORD X Low Flow & Parameters Stable ___ 3 Casing Volumes & Parameters Stable ___ 5 Casing Volumes ___ Other:

SAMPLE COLLECTION RECORD

Depth to Water at Sampling: 7.65 (ft)

Sample Collected Via: ___ Disp. Bailer ___ Dedicated Pump Tubing ___ Disp. Pump Tubing Other:

Sample ID: MW-9 Sample Collection Time: 0915 (24:00)

Containers (#): X VOA (X preserved or ___ unpreserved) ___ Liter Amber

___ Other: ___ Other:

___ Other: ___ Other:

GEOCHEMICAL PARAMETERS

Parameter	Time	Measurement
DO (mg/L)		
Ferrous Iron (mg/L)		
Redox Potential (mV)		
Alkalinity (mg/L)		
Other:		
Other:		

Signature:

APPENDIX C

LABORATORY REPORT
AND CHAIN-OF-CUSTODY DOCUMENTATION

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.
TestAmerica Irvine
17461 Derian Ave
Suite 100
Irvine, CA 92614-5817
Tel: (949)261-1022

TestAmerica Job ID: 440-55267-1
Client Project/Site: ARCO 0374, Oakland

For:
Broadbent & Associates, Inc.
875 Cotting Lane
Suite G
Vacaville, California 95688

Attn: Kristene Tidwell

Authorized for release by:
9/6/2013 10:55:35 AM
Lena Davidkova, Project Manager I
lena.davidkova@testamericainc.com

Designee for

Kathleen Robb, Project Manager II
kathleen.robb@testamericainc.com

Table of Contents

Sample Summary

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
440-55267-1	MW-1	Water	08/22/13 08:15	08/23/13 09:50
440-55267-2	MW-2	Water	08/22/13 08:40	08/23/13 09:50
440-55267-3	MW-3	Water	08/22/13 10:40	08/23/13 09:50
440-55267-4	MW-4	Water	08/22/13 11:35	08/23/13 09:50
440-55267-5	MW-5	Water	08/22/13 11:05	08/23/13 09:50
440-55267-6	MW-7	Water	08/22/13 10:10	08/23/13 09:50
440-55267-7	MW-8	Water	08/22/13 09:45	08/23/13 09:50
440-55267-8	MW-9	Water	08/22/13 09:15	08/23/13 09:50

Job ID: 440-55267-1

Laboratory: TestAmerica Irvine

Narrative

Job Narrative
440-55267-1

Comments
No additional comments.

Receipt
The samples were received on 8/23/2013 9:50 AM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperature of the cooler at receipt was 2.2º C.

GC/MS VOA
No analytical or quality issues were noted.

GC VOA
Method(s) 8015B: Surrogate recovery was outside control limits for the following sample: (CCV 440-127516/51), (CCV 440-127516/63). The GRO standard coeluted with the 4-bromofluorobenzene surrogate. Data not impacted.

Method(s) 8015B: Surrogate recovery was outside control limits for the following sample: (CCVRT 440-127516/1). The GRO standard coeluted with the 4-bromofluorobenzene surrogate. Data not impacted.

Method(s) 8015B: Surrogate recovery for the following sample(s) was outside control limits: MW-9 (440-55267-8). Evidence of matrix interference is present; therefore, re-extraction and/or re-analysis was not performed.

Method(s) 8015B: Surrogate recovery was outside control limits for the following sample: (CCV 440-128029/11), (CCV 440-128029/23), (CCVRT 440-128029/1), (LCS 440-128029/2). The GRO standard coeluted with the 4-bromofluorobenzene surrogate. Data not impacted.

Method(s) 8015B: Surrogate recovery for the following sample(s) was outside control limits: (440-55409-6 MS), (440-55409-6 MSD), MW-24 (440-55409-6). Evidence of matrix interference is present; therefore, re-extraction and/or re-analysis was not performed.

Method(s) 8015B: Surrogate recovery for the following sample(s) was outside control limits: MW-4 (440-55267-4). Evidence of matrix interference is present; therefore, re-extraction and/or re-analysis was not performed.

No other analytical or quality issues were noted.

VOA Prep
No analytical or quality issues were noted.

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-1
Date Collected: 08/22/13 08:15
Date Received: 08/23/13 09:50

Lab Sample ID: 440-55267-1
Matrix: Water

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		0.50		ug/L			08/30/13 19:12	1
1,2-Dichloroethane	ND		0.50		ug/L			08/30/13 19:12	1
Benzene	ND		0.50		ug/L			08/30/13 19:12	1
Ethanol	ND		150		ug/L			08/30/13 19:12	1
Ethylbenzene	ND		0.50		ug/L			08/30/13 19:12	1
Ethyl-t-butyl ether (ETBE)	ND		0.50		ug/L			08/30/13 19:12	1
Isopropyl Ether (DIPE)	ND		0.50		ug/L			08/30/13 19:12	1
m,p-Xylene	ND		1.0		ug/L			08/30/13 19:12	1
Methyl-t-Butyl Ether (MTBE)	**91**		0.50		ug/L			08/30/13 19:12	1
o-Xylene	ND		0.50		ug/L			08/30/13 19:12	1
Tert-amyl-methyl ether (TAME)	ND		0.50		ug/L			08/30/13 19:12	1
tert-Butyl alcohol (TBA)	ND		10		ug/L			08/30/13 19:12	1
Toluene	ND		0.50		ug/L			08/30/13 19:12	1
Xylenes, Total	ND		1.0		ug/L			08/30/13 19:12	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*106*		*80 - 120*		*08/30/13 19:12*	*1*
Dibromofluoromethane (Surr)	*89*		*80 - 120*		*08/30/13 19:12*	*1*
Toluene-d8 (Surr)	*108*		*80 - 120*		*08/30/13 19:12*	*1*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	ND		50		ug/L			08/28/13 13:26	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*89*		*65 - 140*		*08/28/13 13:26*	*1*

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-2
Date Collected: 08/22/13 08:40
Date Received: 08/23/13 09:50

Lab Sample ID: 440-55267-2
Matrix: Water

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		0.50		ug/L			08/30/13 20:33	1
1,2-Dichloroethane	ND		0.50		ug/L			08/30/13 20:33	1
Benzene	ND		0.50		ug/L			08/30/13 20:33	1
Ethanol	ND		150		ug/L			08/30/13 20:33	1
Ethylbenzene	ND		0.50		ug/L			08/30/13 20:33	1
Ethyl-t-butyl ether (ETBE)	ND		0.50		ug/L			08/30/13 20:33	1
Isopropyl Ether (DIPE)	ND		0.50		ug/L			08/30/13 20:33	1
m,p-Xylene	ND		1.0		ug/L			08/30/13 20:33	1
Methyl-t-Butyl Ether (MTBE)	**82**		0.50		ug/L			08/30/13 20:33	1
o-Xylene	ND		0.50		ug/L			08/30/13 20:33	1
Tert-amyl-methyl ether (TAME)	**1.1**		0.50		ug/L			08/30/13 20:33	1
tert-Butyl alcohol (TBA)	ND		10		ug/L			08/30/13 20:33	1
Toluene	ND		0.50		ug/L			08/30/13 20:33	1
Xylenes, Total	ND		1.0		ug/L			08/30/13 20:33	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*108*		*80 - 120*		*08/30/13 20:33*	*1*
Dibromofluoromethane (Surr)	*93*		*80 - 120*		*08/30/13 20:33*	*1*
Toluene-d8 (Surr)	*108*		*80 - 120*		*08/30/13 20:33*	*1*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	ND		50		ug/L			08/28/13 13:53	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*86*		*65 - 140*		*08/28/13 13:53*	*1*

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-3
Date Collected: 08/22/13 10:40
Date Received: 08/23/13 09:50

Lab Sample ID: 440-55267-3
Matrix: Water

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		0.50		ug/L			08/30/13 21:00	1
1,2-Dichloroethane	ND		0.50		ug/L			08/30/13 21:00	1
Benzene	ND		0.50		ug/L			08/30/13 21:00	1
Ethanol	ND		150		ug/L			08/30/13 21:00	1
Ethylbenzene	ND		0.50		ug/L			08/30/13 21:00	1
Ethyl-t-butyl ether (ETBE)	ND		0.50		ug/L			08/30/13 21:00	1
Isopropyl Ether (DIPE)	ND		0.50		ug/L			08/30/13 21:00	1
m,p-Xylene	ND		1.0		ug/L			08/30/13 21:00	1
Methyl-t-Butyl Ether (MTBE)	**1.4**		0.50		ug/L			08/30/13 21:00	1
o-Xylene	ND		0.50		ug/L			08/30/13 21:00	1
Tert-amyl-methyl ether (TAME)	ND		0.50		ug/L			08/30/13 21:00	1
tert-Butyl alcohol (TBA)	ND		10		ug/L			08/30/13 21:00	1
Toluene	ND		0.50		ug/L			08/30/13 21:00	1
Xylenes, Total	ND		1.0		ug/L			08/30/13 21:00	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*107*		*80 - 120*		*08/30/13 21:00*	*1*
Dibromofluoromethane (Surr)	*92*		*80 - 120*		*08/30/13 21:00*	*1*
Toluene-d8 (Surr)	*106*		*80 - 120*		*08/30/13 21:00*	*1*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	ND		50		ug/L			08/28/13 14:21	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*82*		*65 - 140*		*08/28/13 14:21*	*1*

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-4
Date Collected: 08/22/13 11:35
Date Received: 08/23/13 09:50

Lab Sample ID: 440-55267-4
Matrix: Water

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		10		ug/L			08/30/13 21:27	20
1,2-Dichloroethane	ND		10		ug/L			08/30/13 21:27	20
Benzene	**1600**		10		ug/L			08/30/13 21:27	20
Ethanol	ND		3000		ug/L			08/30/13 21:27	20
Ethylbenzene	**120**		10		ug/L			08/30/13 21:27	20
Ethyl-t-butyl ether (ETBE)	ND		10		ug/L			08/30/13 21:27	20
Isopropyl Ether (DIPE)	ND		10		ug/L			08/30/13 21:27	20
m,p-Xylene	**320**		20		ug/L			08/30/13 21:27	20
Methyl-t-Butyl Ether (MTBE)	ND		10		ug/L			08/30/13 21:27	20
o-Xylene	**10**		10		ug/L			08/30/13 21:27	20
Tert-amyl-methyl ether (TAME)	ND		10		ug/L			08/30/13 21:27	20
tert-Butyl alcohol (TBA)	ND		200		ug/L			08/30/13 21:27	20
Toluene	**100**		10		ug/L			08/30/13 21:27	20
Xylenes, Total	**330**		20		ug/L			08/30/13 21:27	20

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*111*		*80 - 120*		*08/30/13 21:27*	*20*
Dibromofluoromethane (Surr)	*90*		*80 - 120*		*08/30/13 21:27*	*20*
Toluene-d8 (Surr)	*111*		*80 - 120*		*08/30/13 21:27*	*20*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	**6900**		2500		ug/L			08/30/13 00:24	50

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*151*	*LH*	*65 - 140*		*08/30/13 00:24*	*50*

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-5
Date Collected: 08/22/13 11:05
Date Received: 08/23/13 09:50

Lab Sample ID: 440-55267-5
Matrix: Water

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		0.50		ug/L			08/30/13 21:54	1
1,2-Dichloroethane	ND		0.50		ug/L			08/30/13 21:54	1
Benzene	ND		0.50		ug/L			08/30/13 21:54	1
Ethanol	ND		150		ug/L			08/30/13 21:54	1
Ethylbenzene	ND		0.50		ug/L			08/30/13 21:54	1
Ethyl-t-butyl ether (ETBE)	ND		0.50		ug/L			08/30/13 21:54	1
Isopropyl Ether (DIPE)	ND		0.50		ug/L			08/30/13 21:54	1
m,p-Xylene	ND		1.0		ug/L			08/30/13 21:54	1
Methyl-t-Butyl Ether (MTBE)	ND		0.50		ug/L			08/30/13 21:54	1
o-Xylene	ND		0.50		ug/L			08/30/13 21:54	1
Tert-amyl-methyl ether (TAME)	ND		0.50		ug/L			08/30/13 21:54	1
tert-Butyl alcohol (TBA)	ND		10		ug/L			08/30/13 21:54	1
Toluene	ND		0.50		ug/L			08/30/13 21:54	1
Xylenes, Total	ND		1.0		ug/L			08/30/13 21:54	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*107*		*80 - 120*		*08/30/13 21:54*	*1*
Dibromofluoromethane (Surr)	*91*		*80 - 120*		*08/30/13 21:54*	*1*
Toluene-d8 (Surr)	*109*		*80 - 120*		*08/30/13 21:54*	*1*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	ND		50		ug/L			08/30/13 00:49	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*114*		*65 - 140*		*08/30/13 00:49*	*1*

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-7
Date Collected: 08/22/13 10:10
Date Received: 08/23/13 09:50

Lab Sample ID: 440-55267-6
Matrix: Water

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		0.50		ug/L			08/30/13 22:21	1
1,2-Dichloroethane	ND		0.50		ug/L			08/30/13 22:21	1
Benzene	ND		0.50		ug/L			08/30/13 22:21	1
Ethanol	ND		150		ug/L			08/30/13 22:21	1
Ethylbenzene	**3.9**		0.50		ug/L			08/30/13 22:21	1
Ethyl-t-butyl ether (ETBE)	ND		0.50		ug/L			08/30/13 22:21	1
Isopropyl Ether (DIPE)	ND		0.50		ug/L			08/30/13 22:21	1
m,p-Xylene	ND		1.0		ug/L			08/30/13 22:21	1
Methyl-t-Butyl Ether (MTBE)	**3.1**		0.50		ug/L			08/30/13 22:21	1
o-Xylene	ND		0.50		ug/L			08/30/13 22:21	1
Tert-amyl-methyl ether (TAME)	ND		0.50		ug/L			08/30/13 22:21	1
tert-Butyl alcohol (TBA)	ND		10		ug/L			08/30/13 22:21	1
Toluene	ND		0.50		ug/L			08/30/13 22:21	1
Xylenes, Total	ND		1.0		ug/L			08/30/13 22:21	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*110*		*80 - 120*		*08/30/13 22:21*	*1*
Dibromofluoromethane (Surr)	*92*		*80 - 120*		*08/30/13 22:21*	*1*
Toluene-d8 (Surr)	*109*		*80 - 120*		*08/30/13 22:21*	*1*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	**78**		50		ug/L			08/28/13 15:44	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*106*		*65 - 140*		*08/28/13 15:44*	*1*

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-8
Date Collected: 08/22/13 09:45
Date Received: 08/23/13 09:50

Lab Sample ID: 440-55267-7
Matrix: Water

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		0.50		ug/L			08/30/13 22:49	1
1,2-Dichloroethane	ND		0.50		ug/L			08/30/13 22:49	1
Benzene	**1.5**		0.50		ug/L			08/30/13 22:49	1
Ethanol	ND		150		ug/L			08/30/13 22:49	1
Ethylbenzene	ND		0.50		ug/L			08/30/13 22:49	1
Ethyl-t-butyl ether (ETBE)	ND		0.50		ug/L			08/30/13 22:49	1
Isopropyl Ether (DIPE)	ND		0.50		ug/L			08/30/13 22:49	1
m,p-Xylene	ND		1.0		ug/L			08/30/13 22:49	1
Methyl-t-Butyl Ether (MTBE)	**180**		0.50		ug/L			08/30/13 22:49	1
o-Xylene	ND		0.50		ug/L			08/30/13 22:49	1
Tert-amyl-methyl ether (TAME)	**2.8**		0.50		ug/L			08/30/13 22:49	1
tert-Butyl alcohol (TBA)	**39**		10		ug/L			08/30/13 22:49	1
Toluene	ND		0.50		ug/L			08/30/13 22:49	1
Xylenes, Total	ND		1.0		ug/L			08/30/13 22:49	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*108*		*80 - 120*		*08/30/13 22:49*	*1*
Dibromofluoromethane (Surr)	*93*		*80 - 120*		*08/30/13 22:49*	*1*
Toluene-d8 (Surr)	*110*		*80 - 120*		*08/30/13 22:49*	*1*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Analyte	Result	Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	ND		50		ug/L			08/28/13 16:12	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*79*		*65 - 140*		*08/28/13 16:12*	*1*

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-9
Date Collected: 08/22/13 09:15
Date Received: 08/23/13 09:50

Lab Sample ID: 440-55267-8
Matrix: Water

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Analyte	Result	Qualifier	RL	Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		0.50	ug/L			08/30/13 23:16	1
1,2-Dichloroethane	ND		0.50	ug/L			08/30/13 23:16	1
Benzene	**0.71**		0.50	ug/L			08/30/13 23:16	1
Ethanol	ND		150	ug/L			08/30/13 23:16	1
Ethylbenzene	ND		0.50	ug/L			08/30/13 23:16	1
Ethyl-t-butyl ether (ETBE)	ND		0.50	ug/L			08/30/13 23:16	1
Isopropyl Ether (DIPE)	ND		0.50	ug/L			08/30/13 23:16	1
m,p-Xylene	**1.4**		1.0	ug/L			08/30/13 23:16	1
Methyl-t-Butyl Ether (MTBE)	**31**		0.50	ug/L			08/30/13 23:16	1
o-Xylene	ND		0.50	ug/L			08/30/13 23:16	1
Tert-amyl-methyl ether (TAME)	**0.55**		0.50	ug/L			08/30/13 23:16	1
tert-Butyl alcohol (TBA)	ND		10	ug/L			08/30/13 23:16	1
Toluene	ND		0.50	ug/L			08/30/13 23:16	1
Xylenes, Total	**1.4**		1.0	ug/L			08/30/13 23:16	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*111*		*80 - 120*		*08/30/13 23:16*	*1*
Dibromofluoromethane (Surr)	*95*		*80 - 120*		*08/30/13 23:16*	*1*
Toluene-d8 (Surr)	*107*		*80 - 120*		*08/30/13 23:16*	*1*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Analyte	Result	Qualifier	RL	Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	**290**		50	ug/L			08/28/13 16:40	1

Surrogate	*%Recovery*	*Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*142*	*LH*	*65 - 140*		*08/28/13 16:40*	*1*

Method Summary

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Method	Method Description	Protocol	Laboratory
8260B/5030B	Volatile Organic Compounds (GC/MS)	SW846	TAL IRV
8015B/5030B	Gasoline Range Organics (GC)	SW846	TAL IRV

Protocol References:

SW846 = "Test Methods For Evaluating Solid Waste, Physical/Chemical Methods", Third Edition, November 1986 And Its Updates.

Laboratory References:

TAL IRV = TestAmerica Irvine, 17461 Derian Ave, Suite 100, Irvine, CA 92614-5817, TEL (949)261-1022

Lab Chronicle

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-1

Lab Sample ID: 440-55267-1

Date Collected: 08/22/13 08:15

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8260B/5030B		1	10 mL	10 mL	128403	08/30/13 19:12	AA	TAL IRV
Total/NA	Analysis	8015B/5030B		1	10 mL	10 mL	127516	08/28/13 13:26	SC	TAL IRV

Client Sample ID: MW-2

Lab Sample ID: 440-55267-2

Date Collected: 08/22/13 08:40

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8260B/5030B		1	10 mL	10 mL	128403	08/30/13 20:33	AA	TAL IRV
Total/NA	Analysis	8015B/5030B		1	10 mL	10 mL	127516	08/28/13 13:53	SC	TAL IRV

Client Sample ID: MW-3

Lab Sample ID: 440-55267-3

Date Collected: 08/22/13 10:40

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8260B/5030B		1	10 mL	10 mL	128403	08/30/13 21:00	AA	TAL IRV
Total/NA	Analysis	8015B/5030B		1	10 mL	10 mL	127516	08/28/13 14:21	SC	TAL IRV

Client Sample ID: MW-4

Lab Sample ID: 440-55267-4

Date Collected: 08/22/13 11:35

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8260B/5030B		20	10 mL	10 mL	128403	08/30/13 21:27	AA	TAL IRV
Total/NA	Analysis	8015B/5030B		50	10 mL	10 mL	128029	08/30/13 00:24	AK	TAL IRV

Client Sample ID: MW-5

Lab Sample ID: 440-55267-5

Date Collected: 08/22/13 11:05

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8260B/5030B		1	10 mL	10 mL	128403	08/30/13 21:54	AA	TAL IRV
Total/NA	Analysis	8015B/5030B		1	10 mL	10 mL	128029	08/30/13 00:49	AK	TAL IRV

Client Sample ID: MW-7

Lab Sample ID: 440-55267-6

Date Collected: 08/22/13 10:10

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8260B/5030B		1	10 mL	10 mL	128403	08/30/13 22:21	AA	TAL IRV

Lab Chronicle

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Client Sample ID: MW-7

Lab Sample ID: 440-55267-6

Date Collected: 08/22/13 10:10

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8015B/5030B		1	10 mL	10 mL	127516	08/28/13 15:44	SC	TAL IRV

Client Sample ID: MW-8

Lab Sample ID: 440-55267-7

Date Collected: 08/22/13 09:45

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8260B/5030B		1	10 mL	10 mL	128403	08/30/13 22:49	AA	TAL IRV
Total/NA	Analysis	8015B/5030B		1	10 mL	10 mL	127516	08/28/13 16:12	SC	TAL IRV

Client Sample ID: MW-9

Lab Sample ID: 440-55267-8

Date Collected: 08/22/13 09:15

Matrix: Water

Date Received: 08/23/13 09:50

Prep Type	Batch Type	Batch Method	Run	Dil Factor	Initial Amount	Final Amount	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	8260B/5030B		1	10 mL	10 mL	128403	08/30/13 23:16	AA	TAL IRV
Total/NA	Analysis	8015B/5030B		1	10 mL	10 mL	127516	08/28/13 16:40	SC	TAL IRV

Laboratory References:

TAL IRV = TestAmerica Irvine, 17461 Derian Ave, Suite 100, Irvine, CA 92614-5817, TEL (949)261-1022

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS)

Lab Sample ID: MB 440-128403/3
Matrix: Water
Analysis Batch: 128403

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
1,2-Dibromoethane (EDB)	ND		0.50		ug/L			08/30/13 18:14	1
1,2-Dichloroethane	ND		0.50		ug/L			08/30/13 18:14	1
Benzene	ND		0.50		ug/L			08/30/13 18:14	1
Ethanol	ND		150		ug/L			08/30/13 18:14	1
Ethylbenzene	ND		0.50		ug/L			08/30/13 18:14	1
Ethyl-t-butyl ether (ETBE)	ND		0.50		ug/L			08/30/13 18:14	1
Isopropyl Ether (DIPE)	ND		0.50		ug/L			08/30/13 18:14	1
m,p-Xylene	ND		1.0		ug/L			08/30/13 18:14	1
Methyl-t-Butyl Ether (MTBE)	ND		0.50		ug/L			08/30/13 18:14	1
o-Xylene	ND		0.50		ug/L			08/30/13 18:14	1
Tert-amyl-methyl ether (TAME)	ND		0.50		ug/L			08/30/13 18:14	1
tert-Butyl alcohol (TBA)	ND		10		ug/L			08/30/13 18:14	1
Toluene	ND		0.50		ug/L			08/30/13 18:14	1
Xylenes, Total	ND		1.0		ug/L			08/30/13 18:14	1

Surrogate	*MB %Recovery*	*MB Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*108*		*80 - 120*		*08/30/13 18:14*	*1*
Dibromofluoromethane (Surr)	*90*		*80 - 120*		*08/30/13 18:14*	*1*
Toluene-d8 (Surr)	*108*		*80 - 120*		*08/30/13 18:14*	*1*

Lab Sample ID: LCS 440-128403/4
Matrix: Water
Analysis Batch: 128403

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte			Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits		
1,2-Dibromoethane (EDB)			25.0	28.2		ug/L		113	70 - 130		
1,2-Dichloroethane			25.0	25.8		ug/L		103	57 - 138		
Benzene			25.0	25.5		ug/L		102	68 - 130		
Ethanol			250	221		ug/L		88	50 - 149		
Ethylbenzene			25.0	29.3		ug/L		117	70 - 130		
Ethyl-t-butyl ether (ETBE)			25.0	24.4		ug/L		98	60 - 136		
Isopropyl Ether (DIPE)			25.0	24.5		ug/L		98	58 - 139		
m,p-Xylene			50.0	56.2		ug/L		112	70 - 130		
Methyl-t-Butyl Ether (MTBE)			25.0	24.0		ug/L		96	63 - 131		
o-Xylene			25.0	27.5		ug/L		110	70 - 130		
Tert-amyl-methyl ether (TAME)			25.0	24.7		ug/L		99	57 - 139		
tert-Butyl alcohol (TBA)			125	117		ug/L		93	70 - 130		
Toluene			25.0	27.3		ug/L		109	70 - 130		

Surrogate	*LCS %Recovery*	*LCS Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*108*		*80 - 120*
Dibromofluoromethane (Surr)	*92*		*80 - 120*
Toluene-d8 (Surr)	*110*		*80 - 120*

Method: 8260B/5030B - Volatile Organic Compounds (GC/MS) (Continued)

Lab Sample ID: 440-55267-1 MS
Matrix: Water
Analysis Batch: 128403

Client Sample ID: MW-1
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
1,2-Dibromoethane (EDB)	ND		25.0	25.6		ug/L		102	70 - 131
1,2-Dichloroethane	ND		25.0	25.1		ug/L		100	56 - 146
Benzene	ND		25.0	24.5		ug/L		98	66 - 130
Ethanol	ND		250	229		ug/L		92	54 - 150
Ethylbenzene	ND		25.0	26.0		ug/L		104	70 - 130
Ethyl-t-butyl ether (ETBE)	ND		25.0	25.0		ug/L		100	70 - 130
Isopropyl Ether (DIPE)	ND		25.0	25.2		ug/L		101	64 - 138
m,p-Xylene	ND		50.0	50.6		ug/L		101	70 - 133
Methyl-t-Butyl Ether (MTBE)	91		25.0	121		ug/L		119	70 - 130
o-Xylene	ND		25.0	25.3		ug/L		101	70 - 133
Tert-amyl-methyl ether (TAME)	ND		25.0	26.3		ug/L		105	68 - 133
tert-Butyl alcohol (TBA)	ND		125	130		ug/L		104	70 - 130
Toluene	ND		25.0	25.9		ug/L		104	70 - 130

Surrogate	*MS %Recovery*	*MS Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*99*		*80 - 120*
Dibromofluoromethane (Surr)	*95*		*80 - 120*
Toluene-d8 (Surr)	*107*		*80 - 120*

Lab Sample ID: 440-55267-1 MSD
Matrix: Water
Analysis Batch: 128403

Client Sample ID: MW-1
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
1,2-Dibromoethane (EDB)	ND		25.0	26.9		ug/L		107	70 - 131	5	25
1,2-Dichloroethane	ND		25.0	25.0		ug/L		100	56 - 146	0	20
Benzene	ND		25.0	24.5		ug/L		98	66 - 130	0	20
Ethanol	ND		250	222		ug/L		89	54 - 150	3	30
Ethylbenzene	ND		25.0	27.9		ug/L		112	70 - 130	7	20
Ethyl-t-butyl ether (ETBE)	ND		25.0	25.0		ug/L		100	70 - 130	0	25
Isopropyl Ether (DIPE)	ND		25.0	25.3		ug/L		101	64 - 138	0	25
m,p-Xylene	ND		50.0	53.2		ug/L		106	70 - 133	5	25
Methyl-t-Butyl Ether (MTBE)	91		25.0	123		ug/L		128	70 - 130	2	25
o-Xylene	ND		25.0	26.6		ug/L		106	70 - 133	5	20
Tert-amyl-methyl ether (TAME)	ND		25.0	26.3		ug/L		105	68 - 133	0	30
tert-Butyl alcohol (TBA)	ND		125	125		ug/L		100	70 - 130	3	25
Toluene	ND		25.0	26.0		ug/L		104	70 - 130	0	20

Surrogate	*MSD %Recovery*	*MSD Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*108*		*80 - 120*
Dibromofluoromethane (Surr)	*96*		*80 - 120*
Toluene-d8 (Surr)	*108*		*80 - 120*

Method: 8015B/5030B - Gasoline Range Organics (GC)

Lab Sample ID: MB 440-127516/40
Matrix: Water
Analysis Batch: 127516

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	ND		50		ug/L			08/28/13 07:01	1

Surrogate	*MB %Recovery*	*MB Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*101*		*65 - 140*		*08/28/13 07:01*	*1*

Lab Sample ID: LCS 440-127516/39
Matrix: Water
Analysis Batch: 127516

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte			Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits		
GRO (C4-C12)			800	678		ug/L		85	80 - 120		

Surrogate	*LCS %Recovery*	*LCS Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*129*		*65 - 140*

Lab Sample ID: 440-55411-A-1 MS
Matrix: Water
Analysis Batch: 127516

Client Sample ID: Matrix Spike
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits		
GRO (C4-C12)	ND		800	529		ug/L		66	65 - 140		

Surrogate	*MS %Recovery*	*MS Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*127*		*65 - 140*

Lab Sample ID: 440-55411-A-1 MSD
Matrix: Water
Analysis Batch: 127516

Client Sample ID: Matrix Spike Duplicate
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
GRO (C4-C12)	ND		800	527		ug/L		66	65 - 140	0	20

Surrogate	*MSD %Recovery*	*MSD Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*129*		*65 - 140*

Lab Sample ID: MB 440-128029/3
Matrix: Water
Analysis Batch: 128029

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	RL		Unit	D	Prepared	Analyzed	Dil Fac
GRO (C6-C12)	ND		50		ug/L			08/29/13 16:00	1

Surrogate	*MB %Recovery*	*MB Qualifier*	*Limits*	*Prepared*	*Analyzed*	*Dil Fac*
4-Bromofluorobenzene (Surr)	*118*		*65 - 140*		*08/29/13 16:00*	*1*

Method: 8015B/5030B - Gasoline Range Organics (GC) (Continued)

Lab Sample ID: LCS 440-128029/2
Matrix: Water
Analysis Batch: 128029

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte			Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits		
GRO (C4-C12)			800	794		ug/L		99	80 - 120		

Surrogate	*LCS %Recovery*	*LCS Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*206*	*LH*	*65 - 140*

Lab Sample ID: 440-55409-B-6 MS
Matrix: Water
Analysis Batch: 128029

Client Sample ID: Matrix Spike
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits		
GRO (C4-C12)	700		800	1400		ug/L		87	65 - 140		

Surrogate	*MS %Recovery*	*MS Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*354*	*LH*	*65 - 140*

Lab Sample ID: 440-55409-B-6 MSD
Matrix: Water
Analysis Batch: 128029

Client Sample ID: Matrix Spike Duplicate
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
GRO (C4-C12)	700		800	1380		ug/L		85	65 - 140	1	20

Surrogate	*MSD %Recovery*	*MSD Qualifier*	*Limits*
4-Bromofluorobenzene (Surr)	*355*	*LH*	*65 - 140*

GC/MS VOA

Analysis Batch: 128403

Lab Sample ID	Client Sample ID	Prep Type	Matrix	Method	Prep Batch
440-55267-1	MW-1	Total/NA	Water	8260B/5030B	
440-55267-1 MS	MW-1	Total/NA	Water	8260B/5030B	
440-55267-1 MSD	MW-1	Total/NA	Water	8260B/5030B	
440-55267-2	MW-2	Total/NA	Water	8260B/5030B	
440-55267-3	MW-3	Total/NA	Water	8260B/5030B	
440-55267-4	MW-4	Total/NA	Water	8260B/5030B	
440-55267-5	MW-5	Total/NA	Water	8260B/5030B	
440-55267-6	MW-7	Total/NA	Water	8260B/5030B	
440-55267-7	MW-8	Total/NA	Water	8260B/5030B	
440-55267-8	MW-9	Total/NA	Water	8260B/5030B	
LCS 440-128403/4	Lab Control Sample	Total/NA	Water	8260B/5030B	
MB 440-128403/3	Method Blank	Total/NA	Water	8260B/5030B	

GC VOA

Analysis Batch: 127516

Lab Sample ID	Client Sample ID	Prep Type	Matrix	Method	Prep Batch
440-55267-1	MW-1	Total/NA	Water	8015B/5030B	
440-55267-2	MW-2	Total/NA	Water	8015B/5030B	
440-55267-3	MW-3	Total/NA	Water	8015B/5030B	
440-55267-6	MW-7	Total/NA	Water	8015B/5030B	
440-55267-7	MW-8	Total/NA	Water	8015B/5030B	
440-55267-8	MW-9	Total/NA	Water	8015B/5030B	
440-55411-A-1 MS	Matrix Spike	Total/NA	Water	8015B/5030B	
440-55411-A-1 MSD	Matrix Spike Duplicate	Total/NA	Water	8015B/5030B	
LCS 440-127516/39	Lab Control Sample	Total/NA	Water	8015B/5030B	
MB 440-127516/40	Method Blank	Total/NA	Water	8015B/5030B	

Analysis Batch: 128029

Lab Sample ID	Client Sample ID	Prep Type	Matrix	Method	Prep Batch
440-55267-4	MW-4	Total/NA	Water	8015B/5030B	
440-55267-5	MW-5	Total/NA	Water	8015B/5030B	
440-55409-B-6 MS	Matrix Spike	Total/NA	Water	8015B/5030B	
440-55409-B-6 MSD	Matrix Spike Duplicate	Total/NA	Water	8015B/5030B	
LCS 440-128029/2	Lab Control Sample	Total/NA	Water	8015B/5030B	
MB 440-128029/3	Method Blank	Total/NA	Water	8015B/5030B	

Qualifiers

GC VOA

Qualifier	Qualifier Description
LH	Surrogate Recoveries were higher than QC limits

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
¤	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Certification Summary

Client: Broadbent & Associates, Inc.
Project/Site: ARCO 0374, Oakland

TestAmerica Job ID: 440-55267-1

Laboratory: TestAmerica Irvine

All certifications held by this laboratory are listed. Not all certifications are applicable to this report.

Authority	Program	EPA Region	Certification ID	Expiration Date
Alaska	State Program	10	CA01531	06-30-14
Arizona	State Program	9	AZ0671	10-13-13
California	LA Cty Sanitation Districts	9	10256	01-31-14
California	NELAP	9	1108CA	01-31-14
California	State Program	9	2706	06-30-14
Guam	State Program	9	Cert. No. 12.002r	01-28-14 *
Hawaii	State Program	9	N/A	01-31-14
Nevada	State Program	9	CA015312007A	07-31-14
New Mexico	State Program	6	N/A	01-31-14
Northern Mariana Islands	State Program	9	MP0002	01-31-14
Oregon	NELAP	10	4005	09-12-13
USDA	Federal		P330-09-00080	06-06-14
USEPA UCMR	Federal	1	CA01531	01-31-15

* Expired certification is currently pending renewal and is considered valid.

bp rm — *Laboratory Management Program LaMP* Chain of Custody Record

BP Site Node Path: 06-88-602 | Req Due Date (mm/dd/yy): | Rush TAT: Yes ___ No X

BP Facility No: 374 | Lab Work Order Number: 440-55267

Lab Name: Test America	Facility Address: 6407 Telegraph Avenue	Consultant/Contractor: Broadbent and Associates, Inc.
Lab Address: 17461 Derian Avenue Suite #100, Irvine, CA 92641	City, State, ZIP Code: Oakland, CA	Consultant/Contractor Project No: 06-88-602
Lab PM: Kathleen Robb	Lead Regulatory Agency: ACEH	Address: 875 Cotting Lane, Suite G, Vacaville, CA 95688
Lab Phone: 949-261-1022	California Global ID No.: T0600100106	Consultant/Contractor PM: Kristene Tidwell
Lab Shipping Accnt: 1103-6633-7	Enfos Proposal No: 005TP-0001	Phone: 707-455-7290 Fax: 707-455-7295
Lab Bottle Order No:	Accounting Mode: Provision x OOC-BU ___ OOC-RM ___	Email EDD To: ktidwell@broadbentinc.com and to lab.enfosdoc@bp.com
Other Info:	Stage: Execute (40) Activity: Project Spend (80)	Invoice To: BP x Contractor ___
BP Project Manager (PM): Chuck Carmel		
BP PM Phone: 925-275-3804		
BP PM Email: chuck.carmel@bp.com		

Lab No.	Sample Description	Date	Time	Matrix: Soil / Solid	Matrix: Water / Liquid	Matrix: Air / Vapor	Is this location a well?	No. Containers / Preservative: Total Number of Container	Unpreserved	H2SO4	HNO3	HCl	Methanol	Requested Analyses: GRO by 8015M	BTEX/5 FO & EDB by 8260	1,2-DCA & Ethanol by 8260	Report Type & QC Level / Comments
	MW-1	8/22/2013	0315		x		y	6				x		x	x	x	
	MW-2	8/22/2013	0840		x		y	6				x		x	x	x	
	MW-3	8/22/2013	1040		x		y	6				x		x	x	x	
	MW-4	8/22/2013	1135		x		y	6				x		x	x	x	
	MW-5	8/22/2013	1105		x		y	6				x		x	x	x	
	~~MW-6~~	~~8/22/2013~~			x		y	6				x		x	x	x	
	MW-7	8/22/2013	1010		x		y	6				x		x	x	x	
	MW-8	8/22/2013	0945		x		y	6				x		x	x	x	
	MW-9	8/22/2013	0915		x		n	6				x		x	x	x	
	TB-374-08222013	-	-		x		n	2				x					On Hold

Standard x

Full Data Package ___

Comments

Note: If sample not collected, indicate "No Sample" in comments and single-strike out and initial any preprinted sample description.

440-55267 Chain of Custody

Sampler's Name:	Alex Martinez & Alejandro Hernandez	Relinquished By / Affiliation	Date	Time	Accepted By / Affiliation	Date	Time
Sampler's Company:	Broadbent and Associates	[signature] BAI	8/22/13	1700	VnBaull TAI	8/23/13	9:50
Shipment Method:	Fed Ex Ship Date: ~~8/22/2013~~ 8/23/13						
Shipment Tracking No:	8010 3695 0384						

Special Instructions:

THIS LINE - LAB USE ONLY: Custody Seals In Place: Yes / No | Temp Blank: Yes / No | Cooler Temp on Receipt: 2.4+2.2 °F/C | Trip Blank: Yes / No | MS/MSD Sample Submitted: Yes / No

8/23/13 19:10

Login Sample Receipt Checklist

Client: Broadbent & Associates, Inc.

Job Number: 440-55267-1

Login Number: 55267

List Source: TestAmerica Irvine

List Number: 1

Creator: Perez, Angel

Question	Answer	Comment
Radioactivity wasn't checked or is </= background as measured by a survey meter.	N/A	
The cooler's custody seal, if present, is intact.	True	
Sample custody seals, if present, are intact.	True	
The cooler or samples do not appear to have been compromised or tampered with.	True	
Samples were received on ice.	True	
Cooler Temperature is acceptable.	True	
Cooler Temperature is recorded.	True	
COC is present.	True	
COC is filled out in ink and legible.	True	
COC is filled out with all pertinent information.	True	
Is the Field Sampler's name present on COC?	True	Alex Martinez & Alejandra Hernandez
There are no discrepancies between the containers received and the COC.	True	
Samples are received within Holding Time.	True	
Sample containers have legible labels.	True	
Containers are not broken or leaking.	True	
Sample collection date/times are provided.	True	
Appropriate sample containers are used.	True	
Sample bottles are completely filled.	True	
Sample Preservation Verified.	N/A	
There is sufficient vol. for all requested analyses, incl. any requested MS/MSDs	True	
Containers requiring zero headspace have no headspace or bubble is <6mm (1/4").	True	
Multiphasic samples are not present.	True	
Samples do not require splitting or compositing.	True	
Residual Chlorine Checked.	N/A	

APPENDIX D

GEOTRACKER UPLOAD CONFIRMATION RECEIPTS

STATE WATER RESOURCES CONTROL BOARD

GEOTRACKER ESI

UPLOADING A EDF FILE

SUCCESS

Processing is complete. No errors were found!
Your file has been successfully submitted!

Submittal Type:	**EDF**
Report Title:	**3Q13 GW Monitoring**
Report Type:	**Monitoring Report - Semi-Annually**
Facility Global ID:	**T0600100106**
Facility Name:	**ARCO #0374**
File Name:	**440-55267-1_03 Sep 13 1802_EDF.zip**
Organization Name:	**Broadbent & Associates, Inc.**
Username:	**BROADBENT-C**
IP Address:	**216.241.56.58**
Submittal Date/Time:	**10/11/2013 10:50:39 AM**
Confirmation Number:	**8553559780**

VIEW QC REPORT

VIEW DETECTIONS REPORT

STATE WATER RESOURCES CONTROL BOARD

GEOTRACKER ESI

UPLOADING A GEO_WELL FILE

SUCCESS

Processing is complete. No errors were found!
Your file has been successfully submitted!

Submittal Type:	**GEO_WELL**
Report Title:	**3Q13 GEO_WELL 374**
Facility Global ID:	**T0600100106**
Facility Name:	**ARCO #0374**
File Name:	**GEO_WELL.zip**
Organization Name:	**Broadbent & Associates, Inc.**
Username:	**BROADBENT-C**
IP Address:	**216.241.56.58**
Submittal Date/Time:	**10/11/2013 10:53:22 AM**
Confirmation Number:	**5719379484**
