ENVIRONMENTAL PROTECTION

99 DEC 13 PM 4:54

Chevron

Chevron U.S.A. Products Company
6001 Bollinger Canyon Rd. Bldg. L
P. O. Box 6004
San Ramon, CA 94583-0804

Site Assessment and
Remediation Group
Phone (510) 842-9500
Fax (510) 842-8370

Date: December 3, 1999

To: Distribution

Re: Groundwater Monitoring Report , 9-6991

The enclosed groundwater monitoring report has been properly reviewed by a Chevron authorized representative. Agency guidelines have been followed. Blaine Tech Services is authorized to distribute the report directly to interested parties.

If you have any questions, please call me at (510) 842-8695.

Sincerely,

Brent L. Hunter

Brent Hunter
Site Assessment and Remediation
Project Manager

BLAINE
TECH SERVICES INC.

1680 ROGERS AVENUE
SAN JOSE, CALIFORNIA 95112-1105
(408) 573-7771 FAX
(408) 573-0555 PHONE

December 2, 1999

Brett Hunter
Chevron U.S.A. Products Company
P.O. Box 6004
San Ramon, CA 94583-0904

3rd Quarter 1999 Monitoring at 9-6991

Third Quarter 1999 Groundwater Monitoring at
Chevron Service Station Number 9-6991
2920 Castro Valley Blvd.
Castro Valley, CA

Monitoring Performed on September 16, 1999

Groundwater Sampling Report **990916-P-3**

This report covers the routine monitoring of groundwater wells at this Chevron facility. Blaine Tech Services, Inc.'s work at the site includes inspection, gauging, evacuation, purgewater containment, sample collection and sample handling in accordance with standard procedures that conform to Regional Water Quality Control Board requirements.

Routine field data collection includes depth to water, total well depth, thickness of any separate immiscible layer, water column volume, calculated volume of a three-case volume purge, elapsed evacuation time, total volume of water removed, and standard water parameter instrument readings. Sample material is collected, contained, stored, and transported to the laboratory in conformance with EPA standards. Purgewater is, likewise, collected and transported to McKittrick Waste Treatment Site for disposal.

Basic field information is presented alongside analytical values excerpted from the laboratory report in the cumulative table of **WELL DATA AND ANALYTICAL RESULTS**. The full analytical report for the most recent samples is located in the **Analytical Appendix**. The table also contains new groundwater elevation calculations taken from the computer plotted gradient map which is

located in the **Professional Engineering Appendix**.

At a minimum, Blaine Tech Services, Inc. field personnel are certified upon completion of a forty-hour Hazardous Materials and Emergency Response training course per 29 CFR 1910.120. Field personnel are also enrolled in annual eight hour refresher courses.

Blaine Tech Services, Inc. conducts sampling and documentation assignments of this type as an independent third party. In order to avoid compromising the objectivity necessary for the proper and disinterested performance of this work, Blaine Tech Services, Inc. concentrates on objective data collection and does not participate in the interpretation of analytical results, the definition of geological or hydrological conditions, the formulation of recommendations, or the marketing of remedial systems.

Please call if you have any questions.

Yours truly,



Scott Boor
Project Coordinator

SB/ew

attachments: Professional Engineering Appendix
Cumulative Table of Well Data and Analytical Results
Analytical Appendix
Field Data Sheets

cc: **Scott Seery, Alameda County Health Care Services**
Chuck Headlee, RWQCB-San Francisco Bay Region
Greg Gurss, Gettler-Ryan, Inc.
Bill Scudder, Chevron Products Company (w/o enclosure)

Professional Engineering Appendix

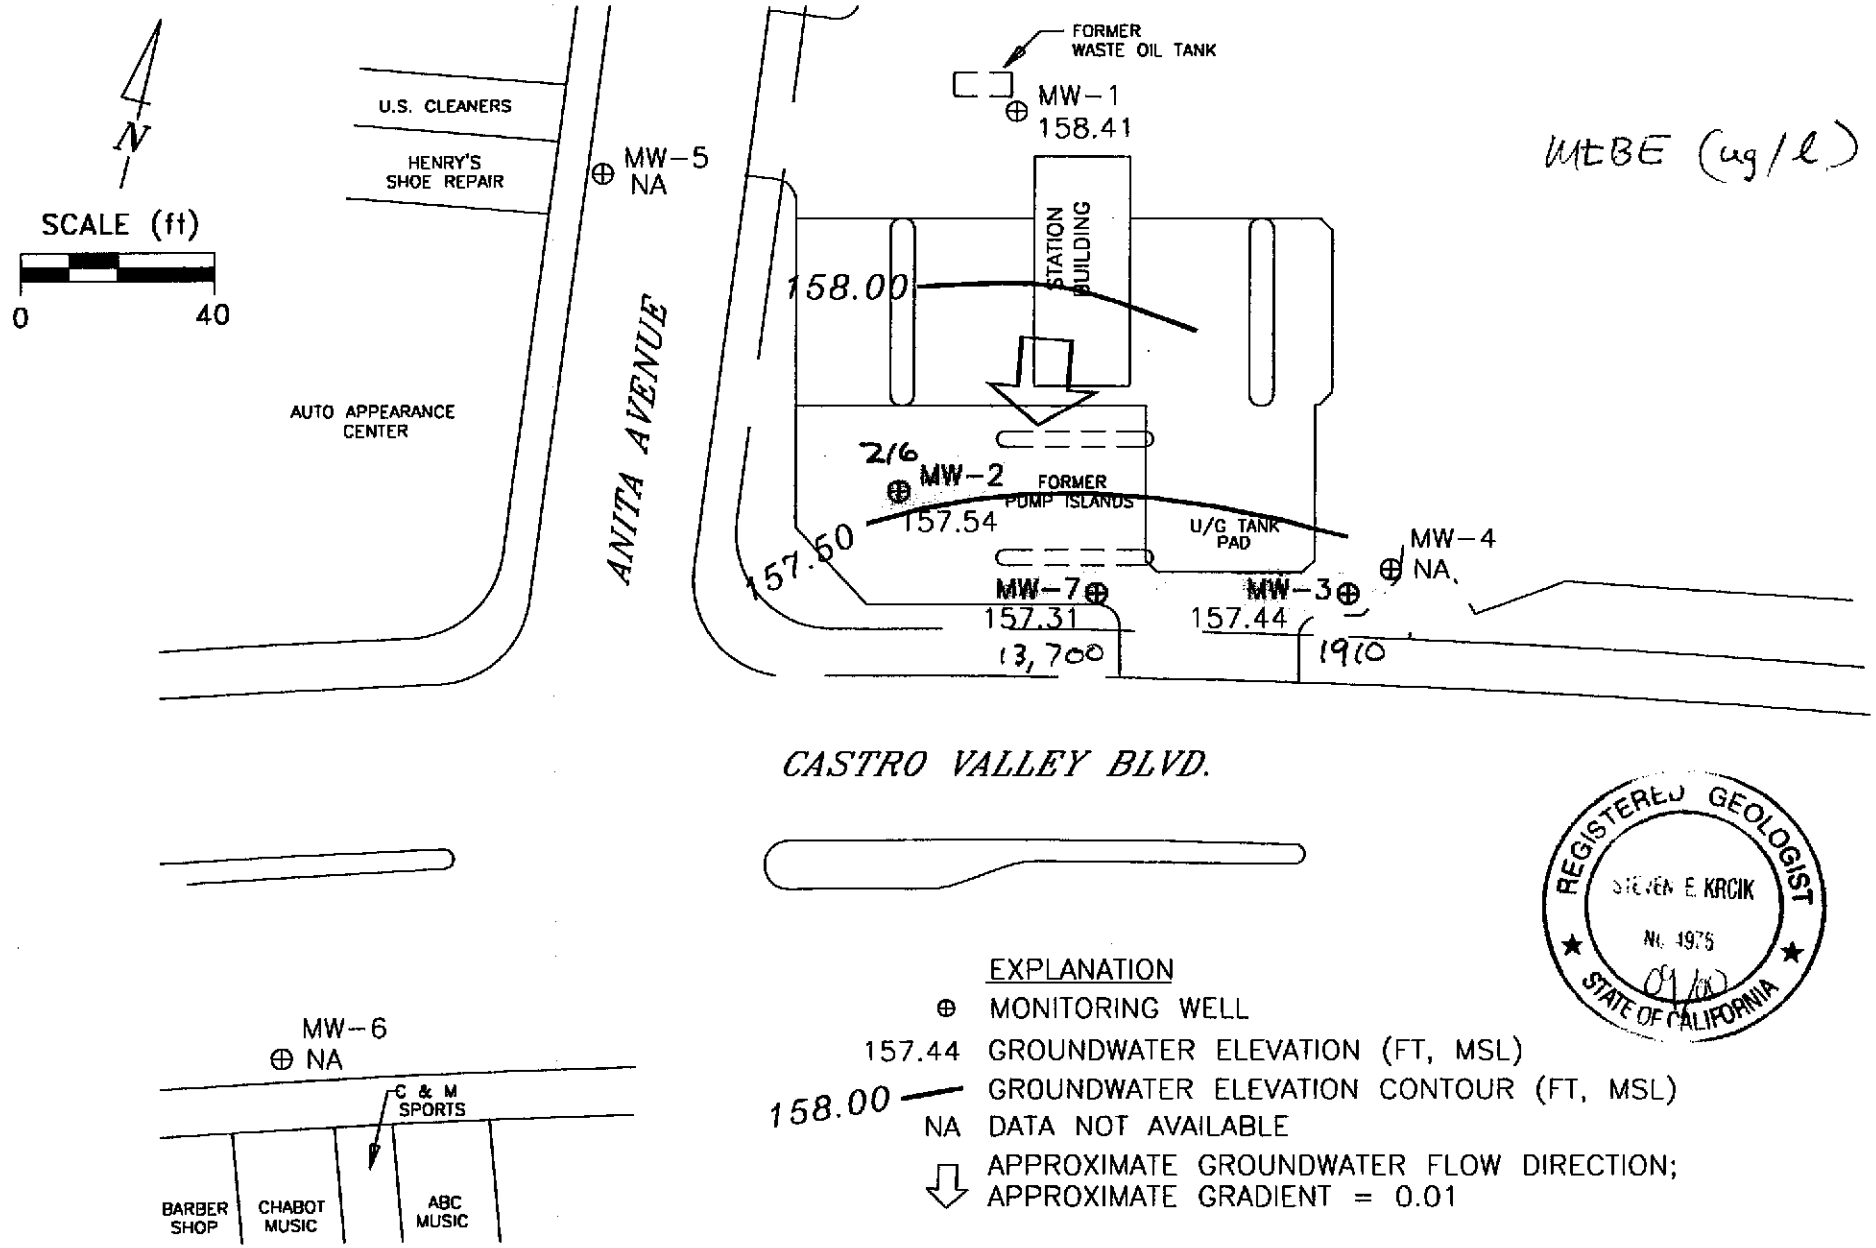

REGISTERED GEOLOGIST
STEVEN E. KRCIK
No. 1975
STATE OF CALIFORNIA

Basemap from Geoconsultants, Inc.

PREPARED BY
RRM
engineering contracting firm

Chevron Station 9-6991
2920 Castro Valley Boulevard
Castro Valley, California

GROUNDWATER ELEVATION CONTOUR MAP, SEPTEMBER 16, 1999

FIGURE:
1
PROJECT:
DAC04

Table of
Well Data and
Analytical Results

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE	TPH-Diesel	TOG
MW-1												
10/08/91	169.30	158.20	11.10	--	230	45	<0.5	0.9	9.1	--	--	<5000
11/04/91	169.30	158.27	11.03	--	340	120	<0.5	<0.5	6.1	--	--	--
12/04/91	169.30	158.25	11.05	--	<50	3.9	<0.5	<0.5	<0.5	--	170	<5000
06/05/92	169.30	158.26	11.04	--	100	26	0.6	0.5	1.0	--	<50	--
10/27/92	169.30	158.20	11.10	--	<50	11	<0.5	<0.5	<0.5	--	54	--
12/30/92	169.30	--	--	--	<50	24	<0.5	<0.5	<0.5	--	170	--
01/27/93	169.30	158.67	10.63	--	--	--	--	--	--	--	--	--
03/05/93	169.30	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	<50	--
03/17/93	169.30	158.59	10.71	--	--	--	--	--	--	--	--	--
06/18/93	169.30	158.29	11.01	--	<50	0.6	<0.5	<0.5	<1.5	--	<50	--
09/28/93	169.30	157.35	11.95	--	<50	0.8	<0.5	<0.5	<1.5	--	<50	--
12/30/93	169.30	158.34	10.96	--	<50	8.5	<0.5	<0.5	<0.5	--	<50	--
04/07/94	169.30	158.49	10.81	--	<50	<0.5	<0.5	<0.5	<0.5	--	<10	--
05/31/94	169.30	158.38	10.92	--	<50	1.0	<0.5	<0.5	<0.5	--	<50	--
09/23/94	169.30	158.40	10.90	--	<50	1.3	<0.5	<0.5	<0.5	--	<50	--
11/30/94	169.30	158.76	10.54	--	<50	8.9	<0.5	<0.5	<0.5	--	570*	--
03/30/95	169.30	158.60	10.70	--	<50	<0.5	<0.5	<0.5	<0.5	--	110**	--
06/06/95	169.30	158.38	10.92	--	61	15	<0.5	<0.5	<0.5	--	570**	--
09/25/95	169.30	158.30	11.00	--	<50	4.7	<0.5	<0.5	<0.5	--	550**	--
12/28/95	169.30	158.50	10.80	--	72	9.1	0.65	<0.5	<0.5	6.0	330**	--
03/05/96	169.30	159.20	10.10	Sampled annually	<50	7.8	<0.5	<0.5	<0.5	<2.5	780**	--
09/13/96	169.30	158.28	11.02	--	--	--	--	--	--	--	--	--
12/19/96	169.30	158.08	11.22	--	--	--	--	--	--	--	--	--
03/20/97	169.30	158.40	10.90	--	<50	2.2	<0.5	<0.5	<0.5	<2.5	350**	--
06/27/97	169.30	158.27	11.03	--	--	--	--	--	--	--	--	--
09/19/97	169.30	158.34	10.96	--	--	--	--	--	--	--	--	--
12/05/97	169.30	158.62	10.68	--	--	--	--	--	--	--	--	--
03/31/98	169.30	158.67	10.63	--	<50	6.7	<0.5	<0.5	<0.5	<2.5	760**	--
06/19/98	169.30	159.62	9.68	--	--	--	--	--	--	--	--	--
08/13/98	169.30	157.67	11.63	--	--	--	--	--	--	--	--	--
12/17/98	169.30	158.25	11.05	--	--	--	--	--	--	--	--	--
03/19/99	169.30	158.35	10.95	--	124	14.8	<0.5	<0.5	<0.5	6.49	890**	--
03/19/99	169.30	158.35	10.95	Confirmation Run	--	--	--	--	--	<2.5	--	--
06/23/99	169.30	158.23	11.07	--	--	--	--	--	--	--	--	--
09/16/99	169.30	158.41	10.89	--	--	--	--	--	--	--	--	--

* Chromatogram pattern indicates a non-diesel mix.

** Chromatogram pattern indicates an unidentified hydrocarbon.

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE	TPH-Diesel	TOG
MW-2												
10/08/91	169.15	157.20	11.95	--	110	5.1	1.1	0.8	26	--	--	--
11/19/91	169.15	157.40	11.75	--	120	11	1.1	<0.5	17	--	--	--
12/04/91	169.15	157.35	11.80	--	440	30	2.5	<0.5	52	--	130	--
06/05/92	169.15	157.35	11.80	--	80	13	<0.5	<0.5	1.0	--	130	--
10/27/92	169.15	157.15	12.00	--	54	13	<0.5	<0.5	<0.5	--	110	--
12/30/92	169.15	--	--	--	180	30	<0.5	<0.5	1.0	--	92	--
01/27/93	169.15	158.24	10.91	--	--	--	--	--	--	--	--	--
03/05/93	169.15	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	<50	--
03/17/93	169.15	158.26	10.89	--	--	--	--	--	--	--	--	--
06/18/93	169.15	157.41	11.74	--	<50	1.4	<0.5	<0.5	<1.5	--	<50	--
09/28/93	169.15	157.97	11.18	--	<50	0.6	<0.5	<0.5	<1.5	--	<50	--
12/30/93	169.15	158.34	21.00	--	<50	0.9	<0.5	<0.5	<0.5	--	<50	--
04/07/94	169.15	158.40	10.75	--	<50	<0.5	<0.5	<0.5	<0.5	--	<10	--
05/31/94	169.15	158.35	10.80	--	<50	<0.5	<0.5	<0.5	<0.5	--	<50	--
09/23/94	169.15	157.50	11.65	--	<50	0.7	<0.5	<0.5	<0.5	--	120	--
11/30/94	169.15	158.41	10.74	--	55	2.9	<0.5	1.4	0.94	--	570*	--
03/30/95	169.15	158.25	10.90	--	91	4.5	<0.5	3.8	<0.5	--	430**	--
06/06/95	169.15	157.73	11.42	--	<50	<0.5	<0.5	<0.5	<0.5	--	410**	--
09/25/95	169.15	157.52	11.63	--	<50	<0.5	<0.5	<0.5	<0.5	--	220**	--
12/28/95	169.15	157.98	11.17	--	<2000	<20	<20	<20	<20	5000	120**	--
03/05/96	169.15	159.09	10.06	Sampled biannually	<2000	<20	<20	<20	<20	10,000	860**	--
09/13/96	169.15	157.37	11.78	--	1100	25	<10	<10	<10	20,000	1300	--
12/19/96	169.15	158.30	10.85	--	--	--	--	--	--	--	--	--
03/20/97	169.15	157.75	11.40	--	2400	<10	<10	46	<10	6200	190**	--
06/27/97	169.15	157.35	11.80	--	--	--	--	--	--	--	--	--
09/19/97	169.15	157.43	11.72	--	<50	<0.5	<0.5	<0.5	<0.5	280	60**	--
12/08/97	169.15	158.27	10.88	--	--	--	--	--	--	--	--	--
03/31/98	169.15	158.46	10.69	--	110	30	0.74	0.74	0.59	1000	220**	--
06/19/98	169.15	159.31	9.84	--	--	--	--	--	--	--	--	--
08/31/98	169.15	157.43	11.72	--	<100	3.4	<1.0	<1.0	<1.0	980	380**	--
12/17/98	169.15	157.60	11.55	--	--	--	--	--	--	480	--	--
03/19/99	169.15	158.63	10.52	--	<250	12.7	<2.5	<2.5	<2.5	1040	107*	--
03/19/99	169.15	158.63	10.52	Confirmation Run	--	--	--	--	--	819	--	--
06/23/99	169.15	159.61	9.54	--	--	--	--	--	--	--	--	--
09/16/99	169.15	157.54	11.61	--	<100	<1.0	<1.0	<1.0	<1.0	216	84.9	--

* Chromatogram pattern indicates a non-diesel mix + discrete peaks.

** Chromatogram pattern indicates an unidentified hydrocarbon.

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE	TPH-Diesel	TOG
MW-3												
10/08/91	169.11	160.84	8.27	--	81	1.9	0.7	0.8	2.4	--	--	--
11/04/91	169.11	158.26	10.85	--	60	<0.5	<0.5	<0.5	<0.5	--	--	--
12/04/91	169.11	158.06	11.05	--	<50	<0.5	<0.5	<0.5	<0.5	--	<50	--
06/05/92	169.11	157.96	11.15	--	<50	<0.5	<0.5	<0.5	<0.5	--	170	--
10/27/92	169.11	157.51	11.60	--	<50	<0.5	<0.5	<0.5	<0.5	--	120	--
12/30/92	169.11	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	170	--
01/27/93	169.11	160.00	9.11	--	--	--	--	--	--	--	--	--
03/05/93	169.11	--	--	--	--	--	--	--	--	--	--	--
03/17/93	169.11	159.16	9.95	--	--	--	--	--	--	--	--	--
06/18/93	169.11	158.22	10.89	--	<50	<0.5	<0.5	<0.5	<1.5	--	<50	--
09/28/93	169.11	159.49	9.62	--	<50	<0.5	<0.5	<0.5	<1.5	--	<50	--
12/30/93	169.11	159.80	9.31	--	<50	<0.5	<0.5	<0.5	<0.5	--	<50	--
04/07/94	169.11	160.30	8.81	--	<50	<0.5	<0.5	<0.5	<0.5	--	<10	--
05/31/94	169.11	160.21	8.90	--	<50	<0.5	<0.5	<0.5	<0.5	--	<50	--
09/23/94	169.11	158.48	10.63	--	<50	<0.5	<0.5	<0.5	<0.5	--	<50	--
11/30/94	169.11	160.19	8.92	Inaccessible	--	--	--	--	--	--	--	--
03/30/95	169.11	160.01	9.10	--	<50	<0.5	<0.5	<0.5	<0.5	--	290*	--
06/06/95	169.11	158.79	10.32	--	<50	<0.5	<0.5	<0.5	<0.5	--	150*	--
09/25/95	169.11	158.11	11.00	--	<50	<0.5	<0.5	<0.5	<0.5	--	260*	--
12/28/95	169.11	158.96	10.15	--	<250	<2.5	<2.5	<2.5	<2.5	1400	200*	--
12/17/98	169.11	158.86	10.25	--	<250	<2.5	<2.5	<2.5	<2.5	62,000	130*	--
03/19/99	169.11	159.37	9.74	--	<1000	<10	<10	<10	<10	5650	139*	--
03/19/99	169.11	159.37	9.74	Confirmation Run	--	--	--	--	--	5850	--	--
06/23/99	169.11	158.40	10.71	--	<2000	<20	<20	<20	<20	6700	61.6*	--
09/16/99	169.11	157.44	11.67	--	<1000	<10	<10	<10	<10	1910	122	--

* Chromatogram pattern indicates an unidentified hydrocarbon.

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE	TPH-Diesel	TOG
MW-7												
09/25/95	168.80	157.20	11.60	--	220	0.79	<0.5	0.67	<0.5	--	1400*	--
12/28/95	168.80	158.14	10.66	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	590*	--
03/05/96	168.80	159.74	9.06	--	1400	<10	<10	47	<10	5300	320*	--
06/27/96	168.80	157.27	11.53	--	<2500	<25	<25	<25	<25	14,000	630*	--
09/13/96	168.80	156.88	11.92	--	1100	26	<10	24	<10	20,000	1400	--
12/19/96	168.80	158.29	10.51	--	<5000	<50	<50	<50	<50	12,000	1100**	--
03/20/97	168.80	157.84	10.96	--	<1000	<10	<10	<10	<10	2100	1600**	--
03/20/97	168.80	157.84	10.96	Confirmation run	--	--	--	--	--	2000	--	--
06/27/97	168.80	157.02	11.78	--	2000	<20	<20	<20	<20	11,000	1600*	--
09/19/97	168.80	156.87	11.93	--	<1000	35	<10	<10	<10	13,000	1900*	--
12/05/97	168.80	158.40	10.40	--	2100	47	2.7	28	<2.5	15,000	1100*	--
03/31/98	168.80	158.89	9.91	--	410	4.0	0.61	2.2	<0.5	<2.5	780*	--
06/19/98	168.80	159.09	9.71	--	1100	16	<10	17	<10	12,000	480*	--
08/31/98	168.80	157.11	11.69	--	<500	350	22	<5.0	<5.0	47,000	580*	--
12/17/98	168.80	157.70	11.10	--	1800	<10	<10	24	<10	13,000	970	--
12/17/98	168.80	157.70	11.10	Confirmation run	--	--	--	--	--	14,000	--	--
03/19/99	168.80	158.51	10.29	--	1280	<5.0	5.0	16.3	<5.0	2240	615*	--
03/19/99	168.80	158.51	10.29	Confirmation run	--	--	--	--	--	2910	--	--
06/23/99	168.80	157.25	11.55	--	<5000	<50	<50	<50	<50	18,000	1240*	--
09/16/99	168.80	157.31	11.49	--	<5000	<50	<50	<50	<50	13,700	2230	--

* Chromatogram pattern indicates an unidentified hydrocarbon.

** Chromatogram pattern indicates an unidentified hydrocarbon and weathered diesel.

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE	TPH-Diesel	TOG
TRIP BLANK												
10/08/91	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
11/04/91	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
12/04/91	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	<50	--
06/05/92	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
12/30/92	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
01/27/93	--	--	--	--	--	--	--	--	--	--	<50	--
03/05/93	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
03/17/93	--	--	--	--	--	--	--	--	--	--	--	--
06/18/93	--	--	--	--	<50	<0.5	<0.5	<0.5	<1.5	--	--	--
09/28/93	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
12/30/93	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
04/07/94	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
05/31/94	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
09/23/94	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
11/30/94	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
03/30/95	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
06/06/95	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
09/25/95	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
12/28/95	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
03/05/96	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
06/27/96	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
09/13/96	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--	--	--
12/19/96	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--
03/20/97	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--
06/27/97	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--
09/19/97	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--
12/05/97	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--

CONTINUED ON NEXT PAGE

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE	TPH-Diesel	TOG
TRIP BLANK (CONT'D)												
03/31/98	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--
06/19/98	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--
08/31/98	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--
03/19/99	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.0	--	--
09/16/99	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5	--	--

Note: Blaine Tech Services, Inc. began routine monitoring of the groundwater wells at this site on November 1, 1994.
Earlier field data and analytical results are drawn from the September 27, 1994 Groundwater Technology, Inc. report.

ABBREVIATIONS

TPH = Total Petroleum Hydrocarbons
MTBE = Methyl t-butyl Ether
TOG = Total Oil and Grease

Analytical Appendix

Sequoia Analytical

1455 McDowell Blvd. North, Ste. D
Petaluma, CA 94954
(707) 792-1865
FAX (707) 792-0342

October 8, 1999

Christine Lillie
Blaine Tech/Chevron
1680 Rogers Ave.
San Jose, CA 95112

RE: Chevron/P909483

Dear Christine Lillie

Enclosed are the results of analyses for sample(s) received by the laboratory on September 17, 1999. If you have any questions concerning this report, please feel free to contact me.

Sincerely,

Marvin Heskett
Project Manager

CA ELAP Certificate Number I-2374

Sequoia Analytical

1455 McDowell Blvd. North, Ste. D
Petaluma, CA 94954
(707) 792-1865
FAX (707) 792-0342

Blaine Tech/Chevron	Project:	Chevron	Sampled:	9/16/99
1680 Rogers Ave.	Project Number:	990916-P3	Received:	9/17/99
San Jose, CA 95112	Project Manager:	Christine Lillie	Reported:	10/8/99

ANALYTICAL REPORT FOR P909483

Sample Description	Laboratory Sample Number	Sample Matrix	Date Sampled
MW-2	P909483-01	Water	9/16/99
MW-3	P909483-02	Water	9/16/99
MW-7	P909483-03	Water	9/16/99
TB	P909483-04	Water	9/16/99

Sequoia Analytical

1455 McDowell Blvd. North, Ste. D
Petaluma, CA 94954
(707) 792-1865
FAX (707) 792-0342

Blaine Tech/Chevron	Project:	Chevron	Sampled: 9/16/99
1680 Rogers Ave.	Project Number:	990916-P3	Received: 9/17/99
San Jose, CA 95112	Project Manager:	Christine Lillie	Reported: 10/8/99

Total Petroleum Hydrocarbons as Gasoline and BTEX by EPA 8015M/8020M
Sequoia Analytical - Petaluma

Analyte	Batch Number	Date Prepared	Date Analyzed	Surrogate Limits	Reporting Limit	Result	Units	Notes*
MW-2			**P909483-01**				**Water**	
Gasoline	9090554	9/22/99	9/22/99		100	ND	ug/l	
Benzene	"	"	"		1.00	ND	"	
Toluene	"	"	"		1.00	ND	"	
Ethylbenzene	"	"	"		1.00	ND	"	
Xylenes (total)	"	"	"		1.00	ND	"	
Methyl tert-butyl ether	"	"	"		5.00	**216**	"	
Surrogate: a,a,a-Trifluorotoluene	"	"	"	*65.0-135*		*98.0*	*%*	
Surrogate: 4-Bromofluorobenzene	"	"	"	*65.0-135*		*96.7*	"	
MW-3			**P909483-02**				**Water**	
Gasoline	9090554	9/22/99	9/22/99		1000	ND	ug/l	
Benzene	"	"	"		10.0	ND	"	
Toluene	"	"	"		10.0	ND	"	
Ethylbenzene	"	"	"		10.0	ND	"	
Xylenes (total)	"	"	"		10.0	ND	"	
Methyl tert-butyl ether	"	"	"		50.0	**1910**	"	
Surrogate: a,a,a-Trifluorotoluene	"	"	"	*65.0-135*		*95.3*	*%*	
Surrogate: 4-Bromofluorobenzene	"	"	"	*65.0-135*		*94.7*	"	
MW-7			**P909483-03**				**Water**	
Gasoline	9090554	9/22/99	9/22/99		5000	ND	ug/l	
Benzene	"	"	"		50.0	ND	"	
Toluene	"	"	"		50.0	ND	"	
Ethylbenzene	"	"	"		50.0	ND	"	
Xylenes (total)	"	"	"		50.0	ND	"	
Methyl tert-butyl ether	"	"	"		250	**13700**	"	
Surrogate: a,a,a-Trifluorotoluene	"	"	"	*65.0-135*		*96.7*	*%*	
Surrogate: 4-Bromofluorobenzene	"	"	"	*65.0-135*		*93.3*	"	
TB			**P909483-04**				**Water**	
Gasoline	9090554	9/22/99	9/22/99		50.0	ND	ug/l	
Benzene	"	"	"		0.500	ND	"	
Toluene	"	"	"		0.500	ND	"	
Ethylbenzene	"	"	"		0.500	ND	"	
Xylenes (total)	"	"	"		0.500	ND	"	
Methyl tert-butyl ether	"	"	"		2.50	ND	"	
Surrogate: a,a,a-Trifluorotoluene	"	"	"	*65.0-135*		*101*	*%*	
Surrogate: 4-Bromofluorobenzene	"	"	"	*65.0-135*		*94.0*	"	

Sequoia Analytical

1455 McDowell Blvd. North, Ste. D
Petaluma, CA 94954
(707) 792-1865
FAX (707) 792-0342

Blaine Tech/Chevron	Project:	Chevron	Sampled: 9/16/99
1680 Rogers Ave.	Project Number:	990916-P3	Received: 9/17/99
San Jose, CA 95112	Project Manager:	Christine Lillie	Reported: 10/8/99

Total Petroleum Hydrocarbons as Diesel & others by EPA 8015M
Sequoia Analytical - Petaluma

Analyte	Batch Number	Date Prepared	Date Analyzed	Surrogate Limits	Reporting Limit	Result	Units	Notes*
MW-2			**P909483-01**				**Water**	
Diesel (C10-C24)	9100158	9/30/99	10/7/99		0.0500	**0.0849**	mg/l	
Surrogate: o-Terphenyl	"	"	"	*50.0-150*		*88.9*	*%*	
MW-3			**P909483-02**				**Water**	
Diesel (C10-C24)	9100158	9/30/99	10/7/99		0.0500	**0.122**	mg/l	
Surrogate: o-Terphenyl	"	"	"	*50.0-150*		*62.2*	*%*	
MW-7			**P909483-03**				**Water**	
Diesel (C10-C24)	9100158	9/30/99	10/7/99		0.0500	**2.23**	mg/l	1
Surrogate: o-Terphenyl	"	"	"	*50.0-150*		*90.5*	*%*	

Sequoia Analytical

1455 McDowell Blvd. North, Ste. D
Petaluma, CA 94954
(707) 792-1865
FAX (707) 792-0342

Blaine Tech/Chevron	Project:	Chevron	Sampled: 9/16/99
1680 Rogers Ave.	Project Number:	990916-P3	Received: 9/17/99
San Jose, CA 95112	Project Manager:	Christine Lillie	Reported: 10/8/99

Total Petroleum Hydrocarbons as Gasoline and BTEX by EPA 8015M/8020M/Quality Control
Sequoia Analytical - Petaluma

Analyte	Date Analyzed	Spike Level	Sample Result	QC Result	Units	Reporting Limit Recov. Limits	Recov. %	RPD Limit	RPD %	Notes*
Batch: 9090554	**Date Prepared: 9/22/99**					**Extraction Method: EPA 5030 waters**				
Blank	**9090554-BLK1**									
Gasoline	9/22/99			**ND**	ug/l	**50.0**				
Benzene	"			**ND**	"	**0.500**				
Toluene	"			**ND**	"	**0.500**				
Ethylbenzene	"			**ND**	"	**0.500**				
Xylenes (total)	"			**ND**	"	**0.500**				
Methyl tert-butyl ether	"			**ND**	"	**2.50**				
Surrogate: a,a,a-Trifluorotoluene	"	*300*		*302*	"	*65.0-135*	*101*			
Surrogate: 4-Bromofluorobenzene	"	*300*		*274*	"	*65.0-135*	*91.3*			
LCS	**9090554-BS1**									
Gasoline	9/22/99	1000		1110	ug/l	65.0-135	111			
Surrogate: 4-Bromofluorobenzene	"	*300*		*295*	"	*65.0-135*	*98.3*			
Matrix Spike	**9090554-MS1**		**P909474-27**							
Gasoline	9/22/99	1000	ND	1130	ug/l	65.0-135	**113**			
Surrogate: 4-Bromofluorobenzene	"	*300*		*291*	"	*65.0-135*	*97.0*			
Matrix Spike Dup	**9090554-MSD1**		**P909474-27**							
Gasoline	9/22/99	1000	ND	1140	ug/l	65.0-135	**114**	20.0	**0.881**	
Surrogate: 4-Bromofluorobenzene	"	*300*		*288*	"	*65.0-135*	*96.0*			

Sequoia Analytical

1455 McDowell Blvd. North, Ste. D
Petaluma, CA 94954
(707) 792-1865
FAX (707) 792-0342

Blaine Tech/Chevron	Project:	Chevron	Sampled: 9/16/99
1680 Rogers Ave.	Project Number:	990916-P3	Received: 9/17/99
San Jose, CA 95112	Project Manager:	Christine Lillie	Reported: 10/8/99

Notes and Definitions

#	Note
1	Hydrocarbon pattern is present in the requested fuel quantitation range but does not resemble the pattern of the requested fuel.
2	Non-diesel contamination in method blank.
3	The RPD result exceeded the QC control limits; however, both percent recoveries were acceptable. Sample results for the QC batch were accepted based on percent recoveries and completeness of QC data.
DET	Analyte DETECTED
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
dry	Sample results reported on a dry weight basis
Recov.	Recovery
RPD	Relative Percent Difference

Fax copy of Lab Report and COC to Chevron Contact: ☐ Yes ☐ No

Chain-of-Custody-Record

Chevron Products Co.
P.O. BOX 6004
San Ramon, CA 94583
FAX (925)842-8370

Chevron Facility Number 9-6991
Facility Address 2920 Castro Valley Blvd., Castro Valley
Consultant Project Number 990916-P3
Consultant Name BLAINE TECH SERVICE, INC.
Address 1680 ROGERS AVE., SAN JOSE
Project Contact (Name) CHRISTINE LILLIE
(Phone) 408-573-0555 (Fax Number) 408-573-7771

Chevron Contact (Name) PHIL BRIGGS
(Phone) (925) 842-9136
Laboratory Name SEQUOIA
Laboratory Service Order 9144488
Laboratory Service Code ZZ02800
Samples Collected by (Name) 990916-P Phil Sammut
Signature

State Method: ☐ CA ☐ OR ☐ WA ☐ NW Series ☐ CO ☐ UT

Sample Number	Number of Containers	Matrix S = Soil A = Air W = Water C = Charcoal	Sample Preservation	Date/Time	BTEX/MTBE+TPH GAS (8020 + 8015)	BTEX + TPH GAS (8020 + 8015)	TPH Diesel (8015)	Oxygenates (8260)	Purgeable Halocarbons (8010)	Purgeable Organics (8260)	Extractable Organics (8270)	Oil and Grease (5520)	Metals (ICAP or AA) Cd,Cr,Pb,Zn,Ni	BTEX (8020)	BTEX/MTBE/Naph. (8020)	TPH - HCID	TPH-D Extended	Remarks / Lab Sample No.
MW-2	4	W		9/16 15:10	X		X											
MW-3	4	W		" 15:48														
MW-7	5	W		" 16:05														
TB	2	W		" —				P.S.										

COOLER CUSTODY SEALS INTACT ☐ NOT INTACT ☐
COOLER TEMPERATURE 6°C

Relinquished By (Signature)	Organization	Date/Time	Received By (Signature)	Organization	Date/Time	Iced Y/N
	Blaine	9/17/99 9:14		SEQ	9/17	
Relinquished By (Signature)	Organization	Date/Time	Received By (Signature)	Organization	Date/Time	Iced Y/N
Relinquished By (Signature)	Organization	Date/Time 05:00	Received For Laboratory By (Signature)		Date/Time	Iced Y/N

Turn Around Time (Circle Choice)
24 Hrs.
48 Hrs.
5 Days
10 Days
As Contracted

Field
Data
Sheets

WELL GAUGING DATA

Project # 990916-93 Date 9-16-99 Client Chevron

Site 2920 Castro Valley Blvd. Castro Valley

Well ID	Well Size (in.)	Sheen / Odor	Depth to Immiscible Liquid (ft.)	Thickness of Immiscible Liquid (ft.)	Volume of Immiscibles Removed (ml)	Depth to water (ft.)	Depth to well bottom (ft.)	Survey Point: TOB or TOC	
MW-1	3/4"					10.89	17.80		
MW-2	1					11.61	17.36		
MW-3	↓					11.67	17.00		
MW-7	2					11.49	19.65		

CHEVRON WELL MONITORING DATA SHEET

Project #: 990916-P3	Station #: 9-6991
Sampler: PAT	Date: 9-16-99
Well I.D.: MW-2	Well Diameter: 2 3 4 6 8 3/4
Total Well Depth: 17.36	Depth to Water: 11.61
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: (PVC) Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
2"	0.16	5"	1.02
3"	0.37	6"	1.47
4"	0.65	Other	radius^2 * 0.163

Purge Method: Bailer / Disposable Bailer / Middleburg / Electric Submersible / Extraction Pump / Other: 1/2 Hose

Sampling Method: Bailer / Disposable Bailer / Extraction Port / Other: 1/2 Hose

0.1 (1 Case Volume (Gals.)) x 3 (Specified Volumes) = .3 (Calculated Volume) Gals.

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
14:46	71.4	7.3	1096	.1	turbid
14:52	70.2	7.2	945	.2	
15:00	69.8	7.2	896	.3	

Did well dewater? Yes (No) Gallons actually evacuated: .3

Sampling Time: 15:10 Sampling Date: 9-16-99

Sample I.D.: MW-2 Laboratory: (Sequoia) CORE N. Creek Assoc. Labs

Analyzed for: (TPH-G BTEX MTBE TPH-D) Other:

Duplicate I.D.: Analyzed for: TPH-G BTEX MTBE TPH-D Other:

D.O. (if req'd):	Pre-purge:	mg/L	Post-purge:	mg/L
O.R.P. (if req'd):	Pre-purge:	mV	Post-purge:	mV

CHEVRON WELL MONITORING DATA SHEET

Project #: 990910-P3	Station #: 9-6991
Sampler: Pam I	Date: 9-16-95
Well I.D.: MW-3	Well Diameter: 2 3 4 6 8 3/4
Total Well Depth: 17.00	Depth to Water: 11.67
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: PVC Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
2"	0.16	5"	1.02
3"	0.37	6"	1.47
4"	0.65	Other	radius^2 * 0.163

Purge Method: Bailer / Disposable Bailer / Middleburg / Electric Submersible / Extraction Pump / Other: 1/2 Hose

Sampling Method: Bailer / Disposable Bailer / Extraction Port / Other: 1/2 Hose

.8	X	3	=	.24 Gals.
1 Case Volume (Gals.)		Specified Volumes		Calculated Volume

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
15:27	70.8	7.1	1006	.8	turbid
15:30	70.2	7.0	977	.16	
15:40	70.0	7.0	959	.24	

Did well dewater? Yes (No) Gallons actually evacuated: .24

Sampling Time: 15:48 Sampling Date: 9-16-95

Sample I.D.: MW-3 Laboratory: (Sequoia) CORE N. Creek Assoc. Labs

Analyzed for: TPH-G BTEX MTBE TPH-D Other:

Duplicate I.D.: Analyzed for: TPH-G BTEX MTBE TPH-D Other:

D.O. (if req'd):	Pre-purge:	mg/L	Post-purge:	mg/L
O.R.P. (if req'd):	Pre-purge:	mV	Post-purge:	mV

CHEVRON WELL MONITORING DATA SHEET

Project #: 990916-P3	Station #: 9-6991
Sampler: Paul	Date: 9-16-99
Well I.D.: MW-7	Well Diameter: (2) 3 4 6 8 ___
Total Well Depth: 19.65	Depth to Water: 11.49
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: (PVC) Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
(2")	0.16	5"	1.02
3"	0.37	6"	1.47
4"	0.65	Other	radius^2 * 0.163

Purge Method: Bailer / Disposable Bailer ✓ / Middleburg / Electric Submersible / Extraction Pump / Other: ___

Sampling Method: Bailer / Disposable Bailer ✓ / Extraction Port / Other: ___

1.2 (1 Case Volume (Gals.)) X 3 (Specified Volumes) = 3.8 (Calculated Volume) Gals.

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
15:56	71.4	6.9	1129	1.5	odor
15:58	70.8	7.0	1086	3.0	
16:00	70.6	7.0	1027	4.0	

Did well dewater? Yes (No) Gallons actually evacuated: 4.0

Sampling Time: 16:05 Sampling Date: 9-16-99

Sample I.D.: MW-7 Laboratory: (Sequoia) CORE N. Creek Assoc. Labs

Analyzed for: (TPH-G BTEX MTBE TPH-D) Other:

Duplicate I.D.: Analyzed for: TPH-G BTEX MTBE TPH-D Other:

D.O. (if req'd):	Pre-purge:	mg/L	Post-purge:	mg/L
O.R.P. (if req'd):	Pre-purge:	mV	Post-purge:	mV
