SECOR
INTERNATIONAL
INCORPORATED

www.secor.com
3017 Kilgore Road, Suite 100
Rancho Cordova, CA 95670
916-861-0400 TEL
916-861-0430 FAX

July 27, 2007

Ms. Donna Drogos, P.E.
Alameda County Environmental Health Services
1131 Harbor Bay Parkway Suite 250
Alameda, CA 94502

RE: **Quarterly Monitoring and Summary Report – Second Quarter 2007**
SECOR Project No.: 77CP.01634.03.0303

Dear Ms. Drogos:

On behalf of ConocoPhillips, SECOR International Incorporated (SECOR) is forwarding the quarterly summary report for the following location:

Service Station	**Location**
Former 76 Service Station No. 7124	10151 International Boulevard Oakland, California

If there are questions or comments regarding this quarterly summary report, please contact me at (916) 861-0400.

Sincerely,
SECOR International Incorporated

Sean Coyle
Project Manager

Attachments: SECOR's *Quarterly Monitoring and Summary Report – Second Quarter 2007.*

cc: Mr. Bill Borgh, ConocoPhillips

QUARTERLY SUMMARY REPORT
Second Quarter 2007

Former 76 Service Station No. 7124
10151 International Boulevard
Oakland, California

City/County ID #: Oakland/RO0002444
County: Alameda

SITE DESCRIPTION

The site is currently an active Royal Gasoline Station located on the northwestern corner of the intersection of International Boulevard and 102nd Avenue in Oakland, California. Site facilities include three underground storage tanks (USTs) and associated piping and fuel dispensers. A detailed site plan is included in TRC's *Quarterly Monitoring Report April through June 2007* dated April 26, 2007 (Attachment 1).

PREVIOUS ASSESSMENT

On March 22, 2000, SECOR supervised the removal and replacement of product lines and dispensers by Balch Petroleum of Milpitas, California. Soil samples collected from beneath the dispensers and product lines revealed the presence of total petroleum hydrocarbons as gasoline (TPHg) at a maximum concentration of 6,200 milligrams per kilogram (mg/kg), methyl tertiary butyl ether (MtBE) up to120 mg/kg, and up to 7.4 mg/kg. Excavation and sampling activities were observed and approved by Inspector Gomez of the City of Oakland Fire Services Agency.

On March 27, 2000, SECOR observed the over-excavation of approximately 60 cubic yards of soil from the beneath those portions of the dispensers and product lines where soil samples with elevated concentrations of petroleum hydrocarbons were located. Areas measuring approximately 8-10 feet long by 8-10 feet wide were over-excavated to an approximate depth of 8 feet below ground surface (bgs) in each of these areas. Additional over-excavation in these areas was not possible due to their proximity to the footings of the service station canopy. TPHg was detected in two of the three samples at a concentration of 108 mg/kg; benzene was detected in one of the three samples at 0.162 mg/kg; and MtBE was detected in all three samples at a maximum concentrations of up to 43.8 mg/kg. Lead was not detected at or above laboratory reporting limits in any samples.

During February 2002, SECOR supervised the installation of four on-site groundwater monitoring wells. Prior to well installation, all borings were advanced to 26.5 feet bgs, and subsurface soil samples were collected every five feet. Soil samples were analyzed for gasoline range organics (GRO), benzene, toluene, ethylbenzene, total xylenes (BTEX), and fuel oxygenates via EPA Method 8260B. The maximum reported concentrations were 42 mg/kg GRO, 0.36 mg/kg ethylbenzene, 0.26 mg/kg xylenes, and 1.2 mg/kg MtBE.

SENSITIVE RECEPTORS

During the third quarter 2004, SECOR completed a ½-mile radius agency receptor survey and obtained an Environmental Data Resources (EDR) radius map for the site from Environmental Data Resources, Incorporated. The agency survey identified two industrial supply wells, three cathodic protection wells, and two wells of unknown type within the search radius. The survey also identified twelve wells of unknown type that could not be located precisely because the records on file with DWR did not include this information. These wells may or may not be located within the search radius. The EDR radius map did not identify any water supply wells within the search radius, but did identify two water supply wells within one mile of the site.

MONITORING AND SAMPLING

The site has been monitored and sampled since the third quarter 2002. Currently, four wells are monitored quarterly (MW-1 through MW-4). Samples are analyzed for TPHg, BTEX, and the fuel oxygenates tert-butyl alcohol (TBA), MtBE, di-isopropyl ether (DIPE), ethyl tert-butyl ether (EtBE), tert-amyl methyl ether (TAME), and ethanol, as well as, ethylene di-bromide (EDB) by EPA Method 8260B.

DISCUSSION

During the second quarter 2007, depth to groundwater ranged between 15.31 and 17.84 feet below top of casing (toc), which is slightly lower than historical low levels. Historical groundwater depths have been reported between 15.11 and 17.26 feet below toc. The direction of groundwater flow is toward the southwest at a gradient of 0.03 foot/foot (Attachment 1).

The highest concentrations of petroleum hydrocarbons and MtBE continue to be detected in on-site wells MW-3 and MW-4. This quarter, the maximum concentrations of TPHg and MtBE were reported to be in well MW-3 at 1,700 µg/L, and 650 µg/L respectively (Attachment 1); however, the reported TPPH concentrations may actually be MTBE, as the BC Laboratories includes MtBE in their TPPH concentrations. Lack of detectable levels of BTEX indicates that TPHg is probably not a major contaminant at the site. The downgradient/crossgradient extent of the dissolved plume remains undefined by the existing monitoring well network.

On October 14, 2004, SECOR submitted a work plan for the installation of monitoring wells offsite to delineate the dissolved phase hydrocarbons in groundwater; however, in a letter dated April 12, 2005, the Alameda County Environmental Health Services (ACEHS) disapproved the work plan stating that it was premature to install more monitoring wells without additional groundwater sampling to determine the location of the plume for optimal well locations. Therefore, an addendum to the October 14, 2004 work plan was submitted on July 22, 2005 and has never been approved.

CHARACTERIZATION STATUS

None of the groundwater samples collected showed detections at or above MCL levels for any BTEX components. The highest concentrations of residual MtBE contamination are localized in the northeastern area of the site in the vicinity of MW-3 and MW-4. The extent of dissolved contamination is undefined in the downgradient (northwest) direction, but MTBE concentrations continue declining, and variable TBA levels in MW-4 may indicate active degradation of MTBE.

REMEDIATION STATUS

Currently, there is no active remediation at this site.

RECENT SUBMITTALS/CORRESPONDENCE

Submitted: *Quarterly Summary and Monitoring Report – First Quarter 2007,* dated April 25, 2007

WASTE DISPOSAL SUMMARY

The volume of purged groundwater generated and disposed of during the quarterly groundwater monitoring event is documented in TRC's *Quarterly Monitoring Report, April through June 2007,* dated April 26, 2007 (Attachment 1).

THIS QUARTER ACTIVITIES (Second Quarter 2007)

1. TRC performed quarterly groundwater monitoring and sampling event.

2. SECOR prepared and submitted the first quarter 2007 summary report.

NEXT QUARTER ACTIVITIES (Third Quarter 2007)

1. TRC to perform coordinated groundwater monitoring and sampling event.

2. SECOR to prepare and submit quarterly summary and monitoring report.

3. SECOR to discuss site path forward with the agency, including any required revisions to the work plan submitted approximately one year ago. After discussions, if no additional comments to the work plan are forthcoming, the proposed scope of work will be implemented within 60 days of discussion, as it has been well over 60 days since the work plan was first submitted.

LIMITATIONS

This report has been prepared for the exclusive use of ConocoPhillips and its representatives as it pertains to the property located at 10151 International Boulevard, Oakland, California. The evaluation of subsurface conditions at the site for the purpose of this investigation is inherently limited due to the number of points of investigation. There are no representations, warranties, or guarantees that the results are representative of the entire site. Data from this report reflects the conditions at locations at a specified time. No other interpretation, representations, warranties, guarantees, express or implied, are included or intended in the report findings. SECOR makes no warranties or guarantees for the groundwater monitoring report (Attachment 1) prepared by TRC.

Sincerely,
SECOR International Incorporated

Ed Simonis P.G.
Senior Geologist

Wesley Snyder
Staff Scientist

Attachment 1: TRC's *Quarterly Monitoring Report – April through June 2007*, dated April 26, 2007

ATTACHMENT 1
TRC'S *QUARTERLY MONITORING REPORT APRIL THROUGH JUNE 2007*

Quarterly Monitoring and Summary Report
76 Service Station No. 7124
10151 International Boulevard
Oakland, California

21 Technology Drive
Irvine, CA 92618

949.727.9336 PHONE
949.727.7399 FAX

www.TRCsolutions.com

DATE: May 2, 2007

TO: ConocoPhillips Company
76 Broadway
Sacramento, CA 95818

ATTN: MR. ERIC HETRICK

SITE: 76 STATION 7124
10151 INTERNATIONAL BOULEVARD
OAKLAND, CALIFORNIA

RE: QUARTERLY MONITORING REPORT
APRIL THROUGH JUNE 2007

Dear Mr. Hetrick:

Please find enclosed our Quarterly Monitoring Report for 76 Station 7124, located at 10151 International Bouelvard, Oakland, California. If you have any questions regarding this report, please call us at (949) 727-9336.

Sincerely,

TRC

Anju Farfan
Groundwater Program Operations Manager

CC: Mr. Sean Coyle, SECOR International, Inc (2 copies)

Enclosures
200400/7124R015.QMS.doc

QUARTERLY MONITORING REPORT
APRIL THROUGH JUNE 2007

76 STATION 7124
10151 International Boulevard
Oakland, California

Prepared For:

Mr. Eric Hetrick
CONOCOPHILLIPS COMPANY
76 Broadway
Sacramento, California 95818

By:

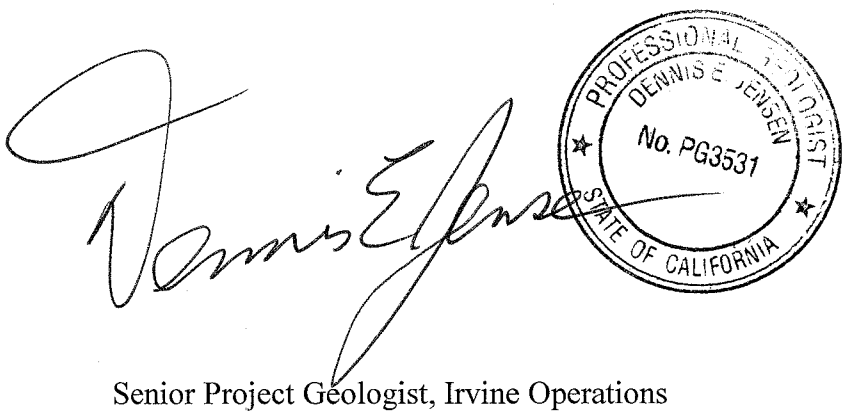

Senior Project Geologist, Irvine Operations
April 26, 2007

TRC

LIST OF ATTACHMENTS	
Summary Sheet	Summary of Gauging and Sampling Activities
Tables	Table Key Contents of Tables Table 1: Current Fluid Levels and Selected Analytical Results Table 1a: Additional Current Analytical Results Table 2: Historic Fluid Levels and Selected Analytical Results Table 2a: Additional Historic Analytical Results
Figures	Figure 1: Vicinity Map Figure 2: Groundwater Elevation Contour Map Figure 3: Dissolved-Phase TPH-G (GC/MS) Concentration Map Figure 4: Dissolved-Phase Benzene Concentration Map Figure 5: Dissolved-Phase MTBE Concentration Map
Graphs	Groundwater Elevations vs. Time MTBE 8260B Concentrations vs. Time
Field Activities	General Field Procedures Field Monitoring Data Sheet – 4/4/07 Groundwater Sampling Field Notes – 4/4/07
Laboratory Reports	Official Laboratory Reports Quality Control Reports Chain of Custody Records
Statements	Purge Water Disposal Limitations

Summary of Gauging and Sampling Activities
April 2007 through June 2007
76 Station 7124
10151 International Boulevard
Oakland, CA

Project Coordinator: **Eric Hetrick**
Telephone: **916-558-7604**
Water Sampling Contractor: ***TRC***
Compiled by: **Daniel Lee**
Date(s) of Gauging/Sampling Event: **04/04/07**

Sample Points

Groundwater wells: **4** onsite, **0** offsite
Wells gauged: **4** Wells sampled: **4**
Purging method: **Submersible pump**
Purge water disposal: **Onyx/Rodeo Unit 100**
Other Sample Points: **0** Type: **n/a**

Liquid Phase Hydrocarbons (LPH)

Wells with LPH: **0** Maximum thickness (feet): **n/a**
LPH removal frequency: **n/a** Method: **n/a**
Treatment or disposal of water/LPH: **n/a**

Hydrogeologic Parameters

Depth to groundwater (below TOC): Minimum: **15.31 feet** Maximum: **17.84 feet**
Average groundwater elevation (relative to available local datum): **21.04 feet**
Average change in groundwater elevation since previous event: **-0.03 feet**
Interpreted groundwater gradient and flow direction:
Current event: **0.03 ft/ft, southwest**
Previous event: **0.01 ft/ft, west (01/12/07)**

Selected Laboratory Results

Wells with detected **Benzene:** **0** Wells above MCL (1.0 µg/l): **n/a**
Maximum reported benzene concentration: **n/a**

Wells with **TPH-G by GC/MS** **3** Maximum: **1,700 µg/l (MW-3)**
Wells with **MTBE 8260B** **3** Maximum: **650 µg/l (MW-3)**

Notes:

This report presents the results of groundwater monitoring and sampling activities performed by TRC. Please contact the primary consultant for other specific information on this site.

TABLES

TABLE KEY

STANDARD ABBREVIATIONS

--	=	not analyzed, measured, or collected
LPH	=	liquid-phase hydrocarbons
Trace	=	less than 0.01 foot of LPH in well
ug/l	=	micrograms per liter (approx. equivalent to parts per billion, ppb)
mg/l	=	milligrams per liter (approx. equivalent to parts per million, ppm)
ND<	=	not detected at or above laboratory detection limit
TOC	=	top of casing (surveyed reference elevation)

ANALYTES

BTEX	=	benzene, toluene, ethylbenzene, and (total) xylenes
DIPE	=	di-isopropyl ether
ETBE	=	ethyl tertiary butyl ether
MTBE	=	methyl tertiary butyl ether
PCB	=	polychlorinated biphenyls
PCE	=	tetrachloroethene
TBA	=	tertiary butyl alcohol
TCA	=	trichloroethane
TCE	=	trichloroethene
TPH-G	=	total petroleum hydrocarbons with gasoline distinction
TPH-G (GC/MS)	=	total petroleum hydrocarbons with gasoline distinction utilizing EPA Method 8260B
TPH-D	=	total petroleum hydrocarbons with diesel distinction
TRPH	=	total recoverable petroleum hydrocarbons
TAME	=	tertiary amyl methyl ether
1,1-DCA	=	1,1-dichloroethane
1,2-DCA	=	1,2-dichloroethane (same as EDC, ethylene dichloride)
1,1-DCE	=	1,1-dichloroethene
1,2-DCE	=	1,2-dichloroethene (cis- and trans-)

NOTES

1. Elevations are in feet above mean sea level. Depths are in feet below surveyed top-of-casing.
2. Groundwater elevations for wells with LPH are calculated as: Surface Elevation – Measured Depth to Water + (Dp x LPH Thickness), where Dp is the density of the LPH, if known. A value of 0.75 is used for gasoline and when the density is not known. A value of 0.83 is used for diesel.
3. Wells with LPH are generally not sampled for laboratory analysis (see General Field Procedures).
4. Comments shown on tables are general. Additional explanations may be included in field notes and laboratory reports, both of which are included as part of this report.
5. A "J" flag indicates that a reported analytical result is an estimated concentration value between the method detection limit (MDL) and the practical quantification limit (PQL) specified by the laboratory.
6. Other laboratory flags (qualifiers) may have been reported. See the official laboratory report (attached) for a complete list of laboratory flags.
7. Concentration graphs based on tables (presented following Figures) show non-detect results prior to the Second Quarter 2000 plotted at fixed values for graphical display. Non-detect results reported since that time are plotted at reporting limits stated in the official laboratory report.
8. Groundwater vs. Time graphs may be corrected for apparent level changes due to resurvey

REFERENCE

TRC began groundwater monitoring and sampling for 76 Station 7124 in October 2003. Historical data compiled prior to that time were provided by Gettler-Ryan Inc.

Contents of Tables 1 and 2
Site: 76 Station 7124

Current Event

Table 1	Well/ Date	Depth to Water	LPH Thickness	Ground-water Elevation	Change in Elevation	TPH-G (8015M)	TPH-G (GC/MS)	Benzene	Toluene	Ethyl-benzene	Total Xylenes	MTBE (8021B)	MTBE (8260B)	Comments
Table 1a	Well/ Date	TBA	Ethanol (8260B)	Ethylene-dibromide (EDB)	1,2-DCA (EDC)	DIPE	ETBE	TAME						

Historic Data

Table 2	Well/ Date	Depth to Water	LPH Thickness	Ground-water Elevation	Change in Elevation	TPH-G (8015M)	TPH-G (GC/MS)	Benzene	Toluene	Ethyl-benzene	Total Xylenes	MTBE (8021B)	MTBE (8260B)	Comments
Table 2a	Well/ Date	TBA	Ethanol (8015B)	Ethanol (8260B)	Ethylene-dibromide (EDB)	1,2-DCA (EDC)	DIPE	ETBE	TAME					

Table 1

CURRENT FLUID LEVELS AND SELECTED ANALYTICAL RESULTS

April 4, 2007

76 Station 7124

Date Sampled	TOC Elevation (feet)	Depth to Water (feet)	LPH Thickness (feet)	Ground-water Elevation (feet)	Change in Elevation (feet)	TPH-G (8015M) (µg/l)	TPH-G (GC/MS) (µg/l)	Benzene (µg/l)	Toluene (µg/l)	Ethyl-benzene (µg/l)	Total Xylenes (µg/l)	MTBE (8021B) (µg/l)	MTBE (8260B) (µg/l)	Comments
MW-1														
04/04/07	37.37	15.31	0.00	22.06	0.24	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	ND<0.50	
MW-2														
04/04/07	37.87	17.84	0.00	20.03	-0.77	--	110	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	2.5	
MW-3														
04/04/07	37.72	16.62	0.00	21.10	0.23	--	1700	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	650	
MW-4														
04/04/07	38.36	17.40	0.00	20.96	0.17	--	460	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	41	

Table 1 a
ADDITIONAL CURRENT ANALYTICAL RESULTS
76 Station 7124

Date Sampled	TBA	Ethanol (8260B)	Ethylene-dibromide (EDB)	1,2-DCA (EDC)	DIPE	ETBE	TAME
	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)
MW-1							
04/04/07	ND<10	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
MW-2							
04/04/07	ND<10	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
MW-3							
04/04/07	130	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
MW-4							
04/04/07	260	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50

Table 2

HISTORIC FLUID LEVELS AND SELECTED ANALYTICAL RESULTS

April 2002 Through April 2007

76 Station 7124

Date Sampled	TOC Elevation (feet)	Depth to Water (feet)	LPH Thickness (feet)	Ground-water Elevation (feet)	Change in Elevation (feet)	TPH-G (8015M) (µg/l)	TPH-G (GC/MS) (µg/l)	Benzene (µg/l)	Toluene (µg/l)	Ethyl-benzene (µg/l)	Total Xylenes (µg/l)	MTBE (8021B) (µg/l)	MTBE (8260B) (µg/l)	Comments
MW-1														
04/08/02	37.37	14.27	0.00	23.10	--	ND<50	--	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<2.5	ND<2.0	
07/28/02	37.37	15.88	0.00	21.49	-1.61	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<2.0	
11/03/02	37.37	16.75	0.00	20.62	-0.87	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<2.0	
01/24/03	37.37	13.94	0.00	23.43	2.81	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<2.0	
04/02/03	37.37	14.99	0.00	22.38	-1.05	--	460	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<2.0	
07/01/03	37.37	15.48	0.00	21.89	-0.49	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<2.0	
10/02/03	37.37	16.68	0.00	20.69	-1.20	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<2.0	
01/09/04	37.37	13.79	0.00	23.58	2.89	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1	--	ND<2	
04/26/04	37.37	15.21	0.00	22.16	-1.42	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
07/22/04	37.37	16.43	0.00	20.94	-1.22	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
10/29/04	37.37	16.14	0.00	21.23	0.29	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
01/12/05	37.37	12.83	0.00	24.54	3.31	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
06/20/05	37.37	14.38	0.00	22.99	-1.55	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
09/23/05	37.37	15.92	0.00	21.45	-1.54	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
12/13/05	37.37	16.09	0.00	21.28	-0.17	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
03/24/06	37.37	11.85	0.00	25.52	4.24	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
05/30/06	37.37	13.30	0.00	24.07	-1.45	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	ND<0.50	
08/22/06	37.37	15.11	0.00	22.26	-1.81	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	ND<0.50	
10/31/06	37.37	16.11	0.00	21.26	-1.00	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	ND<0.50	
01/12/07	37.37	15.55	0.00	21.82	0.56	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	ND<0.50	
04/04/07	37.37	15.31	0.00	22.06	0.24	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	ND<0.50	
MW-2														
04/08/02	37.87	15.86	0.00	22.01	--	4400	--	ND<2.5	ND<2.5	6.4	ND<2.5	380	490	

Table 2

HISTORIC FLUID LEVELS AND SELECTED ANALYTICAL RESULTS

April 2002 Through April 2007

76 Station 7124

Date Sampled	TOC Elevation (feet)	Depth to Water (feet)	LPH Thickness (feet)	Ground-water Elevation (feet)	Change in Elevation (feet)	TPH-G (8015M) (µg/l)	TPH-G (GC/MS) (µg/l)	Benzene (µg/l)	Toluene (µg/l)	Ethyl-benzene (µg/l)	Total Xylenes (µg/l)	MTBE (8021B) (µg/l)	MTBE (8260B) (µg/l)	Comments
MW-2 continued														
07/28/02	37.87	17.28	0.00	20.59	-1.42	--	3200	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	170	
11/03/02	37.87	18.03	0.00	19.84	-0.75	--	3800	ND<5.0	ND<5.0	ND<5.0	ND<10	--	72	
01/24/03	37.87	15.59	0.00	22.28	2.44	--	410	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	490	
04/02/03	37.87	16.50	0.00	21.37	-0.91	--	1000	ND<5.0	ND<5.0	ND<5.0	ND<10	--	180	
07/01/03	37.87	16.94	0.00	20.93	-0.44	--	1900	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	120	
10/02/03	37.87	17.93	0.00	19.94	-0.99	--	6900	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	32	
01/09/04	37.87	15.42	0.00	22.45	2.51	--	1000	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	300	
04/26/04	37.87	--	--	--	--	--	--	--	--	--	--	--	--	Covered with asphalt
07/22/04	37.87	--	--	--	--	--	--	--	--	--	--	--	--	Covered with asphalt
10/29/04	37.87	--	0.00	--	--	--	--	--	--	--	--	--	--	Well is paved over.
01/12/05	37.87	--	--	--	--	--	--	--	--	--	--	--	--	Well was paved over.
06/20/05	37.87	15.94	0.00	21.93	--	--	120	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	46	
09/23/05	37.87	17.29	0.00	20.58	-1.35	--	120	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	10	
12/13/05	37.87	17.41	0.00	20.46	-0.12	--	ND<50	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	11	
03/24/06	37.87	13.77	0.00	24.10	3.64	--	190	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	15	
05/30/06	37.87	15.16	0.00	22.71	-1.39	--	120	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	6.6	
08/22/06	37.87	16.49	0.00	21.38	-1.33	--	81	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	3.0	
10/31/06	37.87	17.15	0.00	20.72	-0.66	--	93	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	2.0	
01/12/07	37.87	17.07	0.00	20.80	0.08	--	230	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	4.3	
04/04/07	37.87	17.84	0.00	20.03	-0.77	--	110	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	2.5	
MW-3														
04/08/02	37.72	15.86	0.00	21.86	--	8700	--	65	ND<25	400	ND<25	6500	8300	
07/28/02	37.72	17.22	0.00	20.50	-1.36	--	4500	ND<25	ND<25	ND<25	ND<50	--	1100	
11/03/02	37.72	17.90	0.00	19.82	-0.68	--	25000	ND<5.0	ND<5.0	25	ND<10	--	470	

Table 2

HISTORIC FLUID LEVELS AND SELECTED ANALYTICAL RESULTS

April 2002 Through April 2007

76 Station 7124

Date Sampled	TOC Elevation (feet)	Depth to Water (feet)	LPH Thickness (feet)	Ground-water Elevation (feet)	Change in Elevation (feet)	TPH-G (8015M) (µg/l)	TPH-G (GC/MS) (µg/l)	Benzene (µg/l)	Toluene (µg/l)	Ethyl-benzene (µg/l)	Total Xylenes (µg/l)	MTBE (8021B) (µg/l)	MTBE (8260B) (µg/l)	Comments
MW-3 continued														
01/24/03	37.72	15.57	0.00	22.15	2.33	--	6000	ND<25	ND<25	94	ND<50	--	10000	
04/02/03	37.72	16.45	0.00	21.27	-0.88	--	130000	ND<100	ND<100	ND<100	ND<200	--	4400	
07/01/03	37.72	16.88	0.00	20.84	-0.43	--	9400	ND<10	ND<10	ND<10	ND<20	--	2200	
10/02/03	37.72	17.85	0.00	19.87	-0.97	--	73000	ND<50	ND<50	ND<50	ND<100	--	460	
01/09/04	37.72	15.31	0.00	22.41	2.54	--	8700	ND<25	ND<25	98	ND<50	--	3800	
04/26/04	37.72	16.62	0.00	21.10	-1.31	--	6700	ND<25	ND<25	ND<25	ND<50	--	3900	
07/22/04	37.72	17.62	0.00	20.10	-1.00	--	13000	ND<25	ND<25	ND<25	ND<50	--	980	
10/29/04	37.72	17.29	0.00	20.43	0.33	--	4600	ND<5.0	ND<5.0	13	ND<10	--	640	
01/12/05	37.72	14.64	0.00	23.08	2.65	--	6100	0.88	0.99	30	2.2	--	6900	
06/20/05	37.72	15.91	0.00	21.81	-1.27	--	1900	ND<0.50	0.21J	0.52	0.46J	--	960	
09/23/05	37.72	17.20	0.00	20.52	-1.29	--	2400	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	160	
12/13/05	37.72	17.32	0.00	20.40	-0.12	--	2100	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	340	
03/24/06	37.72	13.86	0.00	23.86	3.46	--	2200	ND<5.0	ND<5.0	ND<5.0	ND<10	--	970	
05/30/06	37.72	15.69	0.00	22.03	-1.83	--	1500	ND<12	ND<12	ND<12	ND<25	--	760	
08/22/06	37.72	16.51	0.00	21.21	-0.82	--	1900	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	160	
10/31/06	37.72	17.36	0.00	20.36	-0.85	--	2200	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	58	
01/12/07	37.72	16.85	0.00	20.87	0.51	--	2600	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	680	
04/04/07	37.72	16.62	0.00	21.10	0.23	--	1700	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	650	
MW-4														
04/08/02	38.36	16.59	0.00	21.77	--	13000	--	ND<5.0	ND<5.0	28	ND<5.0	790	980	
07/28/02	38.36	17.93	0.00	20.43	-1.34	--	18000	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	170	
11/03/02	38.36	18.66	0.00	19.70	-0.73	--	220	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	5.7	
01/24/03	38.36	16.27	0.00	22.09	2.39	--	ND<1000	ND<10	ND<10	ND<10	ND<20	--	1000	
04/02/03	38.36	17.19	0.00	21.17	-0.92	--	130000	ND<100	ND<100	ND<100	ND<200	--	ND<400	

Table 2

HISTORIC FLUID LEVELS AND SELECTED ANALYTICAL RESULTS

April 2002 Through April 2007

76 Station 7124

Date Sampled	TOC Elevation (feet)	Depth to Water (feet)	LPH Thickness (feet)	Ground-water Elevation (feet)	Change in Elevation (feet)	TPH-G (8015M) (µg/l)	TPH-G (GC/MS) (µg/l)	Benzene (µg/l)	Toluene (µg/l)	Ethyl-benzene (µg/l)	Total Xylenes (µg/l)	MTBE (8021B) (µg/l)	MTBE (8260B) (µg/l)	Comments
MW-4 continued														
07/01/03	38.36	17.61	0.00	20.75	-0.42	--	15000	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	170	
10/02/03	38.36	18.58	0.00	19.78	-0.97	--	7100	ND<10	ND<10	ND<10	ND<20	--	70	
01/09/04	38.36	16.15	0.00	22.21	2.43	--	18000	ND<10	ND<10	ND<10	ND<20	--	530	
04/26/04	38.36	17.20	0.00	21.16	-1.05	--	6500	ND<10	ND<10	ND<10	ND<20	--	240	
07/22/04	38.36	18.34	0.00	20.02	-1.14	--	18000	ND<10	ND<10	ND<10	ND<20	--	48	
10/29/04	38.36	18.13	0.00	20.23	0.21	--	2700	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	76	
01/12/05	38.36	15.22	0.00	23.14	2.91	--	1300	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	620	
06/20/05	38.36	16.63	0.00	21.73	-1.41	--	980	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	110	
09/23/05	38.36	17.93	0.00	20.43	-1.30	--	1500	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	34	
12/13/05	38.36	18.04	0.00	20.32	-0.11	--	3900	ND<0.50	ND<0.50	ND<0.50	ND<1.0	--	36	
03/24/06	38.36	14.48	0.00	23.88	3.56	--	1500	ND<12	ND<12	ND<12	ND<25	--	200	
05/30/06	38.36	15.79	0.00	22.57	-1.31	--	1200	ND<2.5	ND<2.5	ND<2.5	ND<5.0	--	130	
08/22/06	38.36	17.26	0.00	21.10	-1.47	--	980	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	33	
10/31/06	38.36	18.08	0.00	20.28	-0.82	--	1300	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	10	
01/12/07	38.36	17.57	0.00	20.79	0.51	--	820	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	28	
04/04/07	38.36	17.40	0.00	20.96	0.17	--	460	ND<0.50	ND<0.50	ND<0.50	ND<0.50	--	41	

Table 2 a
ADDITIONAL HISTORIC ANALYTICAL RESULTS
76 Station 7124

Date Sampled	TBA	Ethanol (8015B)	Ethanol (8260B)	Ethylene-dibromide (EDB)	1,2-DCA (EDC)	DIPE	ETBE	TAME
	(µg/l)	(mg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)
MW-1								
07/28/02	ND<100	ND<500	--	ND<2.0	ND<2.0	ND<2.0	ND<2.0	ND<2.0
11/03/02	ND<100	ND<500	--	ND<2.0	ND<2.0	ND<2.0	ND<2.0	ND<2.0
01/24/03	ND<100	ND<500	--	ND<2.0	ND<2.0	ND<2.0	ND<2.0	ND<2.0
04/02/03	ND<100	ND<500	--	ND<2.0	ND<2.0	ND<2.0	ND<2.0	ND<2.0
07/01/03	ND<100	ND<500	--	ND<2.0	ND<2.0	ND<2.0	ND<2.0	ND<2.0
10/02/03	ND<100	--	ND<500	ND<2.0	ND<2.0	ND<2.0	ND<2.0	ND<2.0
01/09/04	ND<100	--	ND<500	ND<2	ND<2.0	ND<2	ND<2	ND<2
04/26/04	ND<5.0	--	ND<50	ND<0.50	ND<0.50	ND<1.0	ND<0.50	ND<0.50
07/22/04	ND<5.0	--	ND<50	ND<0.50	ND<0.50	ND<1.0	ND<0.50	ND<0.50
10/29/04	ND<5.0	--	ND<50	ND<0.50	ND<0.50	ND<1.0	ND<0.50	ND<0.50
01/12/05	ND<5.0	--	ND<50	ND<0.50	ND<0.50	ND<1.0	ND<0.50	ND<0.50
06/20/05	ND<10	--	ND<1000	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
09/23/05	ND<10	--	ND<1000	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
12/13/05	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
03/24/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
05/30/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
08/22/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
10/31/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
01/12/07	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
04/04/07	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
MW-2								
04/08/02	ND<2000	ND<10000	--	ND<40	ND<40	ND<40	ND<40	ND<40
07/28/02	ND<500	ND<2500	--	ND<10	ND<10	ND<10	ND<10	ND<10
11/03/02	ND<1000	ND<5000	--	ND<20	ND<20	ND<20	ND<20	ND<20
01/24/03	ND<500	ND<2500	--	ND<10	ND<10	ND<10	ND<10	ND<10
04/02/03	ND<1000	ND<5000	--	ND<20	ND<20	ND<20	ND<20	ND<20

Table 2 a
ADDITIONAL HISTORIC ANALYTICAL RESULTS
76 Station 7124

Date Sampled	TBA	Ethanol (8015B)	Ethanol (8260B)	Ethylene-dibromide (EDB)	1,2-DCA (EDC)	DIPE	ETBE	TAME
	(µg/l)	(mg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)
MW-2 continued								
07/01/03	ND<500	ND<2500	--	ND<10	ND<10	ND<10	ND<10	ND<10
10/02/03	ND<100	--	ND<500	ND<2.0	ND<2.0	ND<2.0	ND<2.0	ND<2.0
01/09/04	ND<500	--	ND<2500	ND<10	ND<10	ND<10	ND<10	ND<10
06/20/05	25	--	ND<1000	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
09/23/05	ND<10	--	ND<1000	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
12/13/05	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
03/24/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
05/30/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
08/22/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
10/31/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
01/12/07	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
04/04/07	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
MW-3								
10/02/03	ND<10000	--	ND<50000	ND<200	ND<200	ND<200	ND<200	ND<200
01/09/04	ND<5000	--	ND<25000	ND<100	ND<100	ND<100	ND<100	ND<100
04/26/04	ND<250	--	ND<2500	ND<25	ND<25	ND<50	ND<25	ND<25
07/22/04	ND<250	--	ND<2500	ND<25	ND<25	ND<50	ND<25	ND<25
10/29/04	ND<50	--	ND<500	ND<5.0	ND<5.0	ND<10	ND<5.0	ND<5.0
01/12/05	1300	--	ND<2500	ND<25	ND<25	ND<50	ND<25	ND<25
06/20/05	39	--	ND<1000	ND<0.50	ND<0.50	ND<0.50	ND<0.50	0.31J
09/23/05	ND<10	--	ND<1000	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
12/13/05	ND<50	--	ND<1200	ND<2.5	ND<2.5	ND<2.5	ND<2.5	ND<2.5
03/24/06	ND<100	--	ND<2500	ND<5.0	ND<5.0	ND<5.0	ND<5.0	ND<5.0
05/30/06	ND<250	--	ND<6200	ND<12	ND<12	ND<12	ND<12	ND<12
08/22/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
10/31/06	ND<10	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50

Table 2 a
ADDITIONAL HISTORIC ANALYTICAL RESULTS
76 Station 7124

Date Sampled	TBA	Ethanol (8015B)	Ethanol (8260B)	Ethylene-dibromide (EDB)	1,2-DCA (EDC)	DIPE	ETBE	TAME
	(µg/l)	(mg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)	(µg/l)
MW-3 continued								
01/12/07	43	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
04/04/07	130	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
MW-4								
04/08/02	ND<5000	ND<25000	--	ND<100	ND<100	ND<100	ND<100	ND<100
07/28/02	ND<500	ND<2500	--	ND<10	ND<10	ND<10	ND<10	ND<10
11/03/02	ND<100	ND<500	--	ND<2.0	ND<2.0	ND<2.0	ND<2.0	ND<2.0
01/24/03	ND<2000	ND<10000	--	ND<40	ND<40	ND<40	ND<40	ND<40
04/02/03	ND<20000	ND<100000	--	ND<400	ND<400	ND<400	ND<400	ND<400
07/01/03	ND<500	ND<2500	--	ND<10	ND<10	ND<10	ND<10	ND<10
10/02/03	ND<2000	--	ND<10000	ND<40	ND<40	ND<40	ND<40	ND<40
01/09/04	ND<2000	--	ND<10000	ND<40	ND<40	ND<40	ND<40	ND<40
04/26/04	430	--	ND<1000	ND<10	ND<10	ND<20	ND<10	ND<10
07/22/04	ND<100	--	ND<1000	ND<10	ND<10	ND<20	ND<10	ND<10
10/29/04	63	--	ND<250	ND<2.5	ND<2.5	ND<5.0	ND<2.5	ND<2.5
01/12/05	1300	--	ND<250	ND<10	ND<2.5	ND<5.0	ND<2.5	ND<2.5
06/20/05	580	--	ND<1000	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
09/23/05	92	--	ND<1000	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
12/13/05	50	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
03/24/06	1900	--	ND<6200	ND<12	ND<12	ND<12	ND<12	ND<12
05/30/06	ND<50	--	ND<1200	ND<2.5	ND<2.5	ND<2.5	ND<2.5	ND<2.5
08/22/06	150	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
10/31/06	43	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
01/12/07	72	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50
04/04/07	260	--	ND<250	ND<0.50	ND<0.50	ND<0.50	ND<0.50	ND<0.50

FIGURES

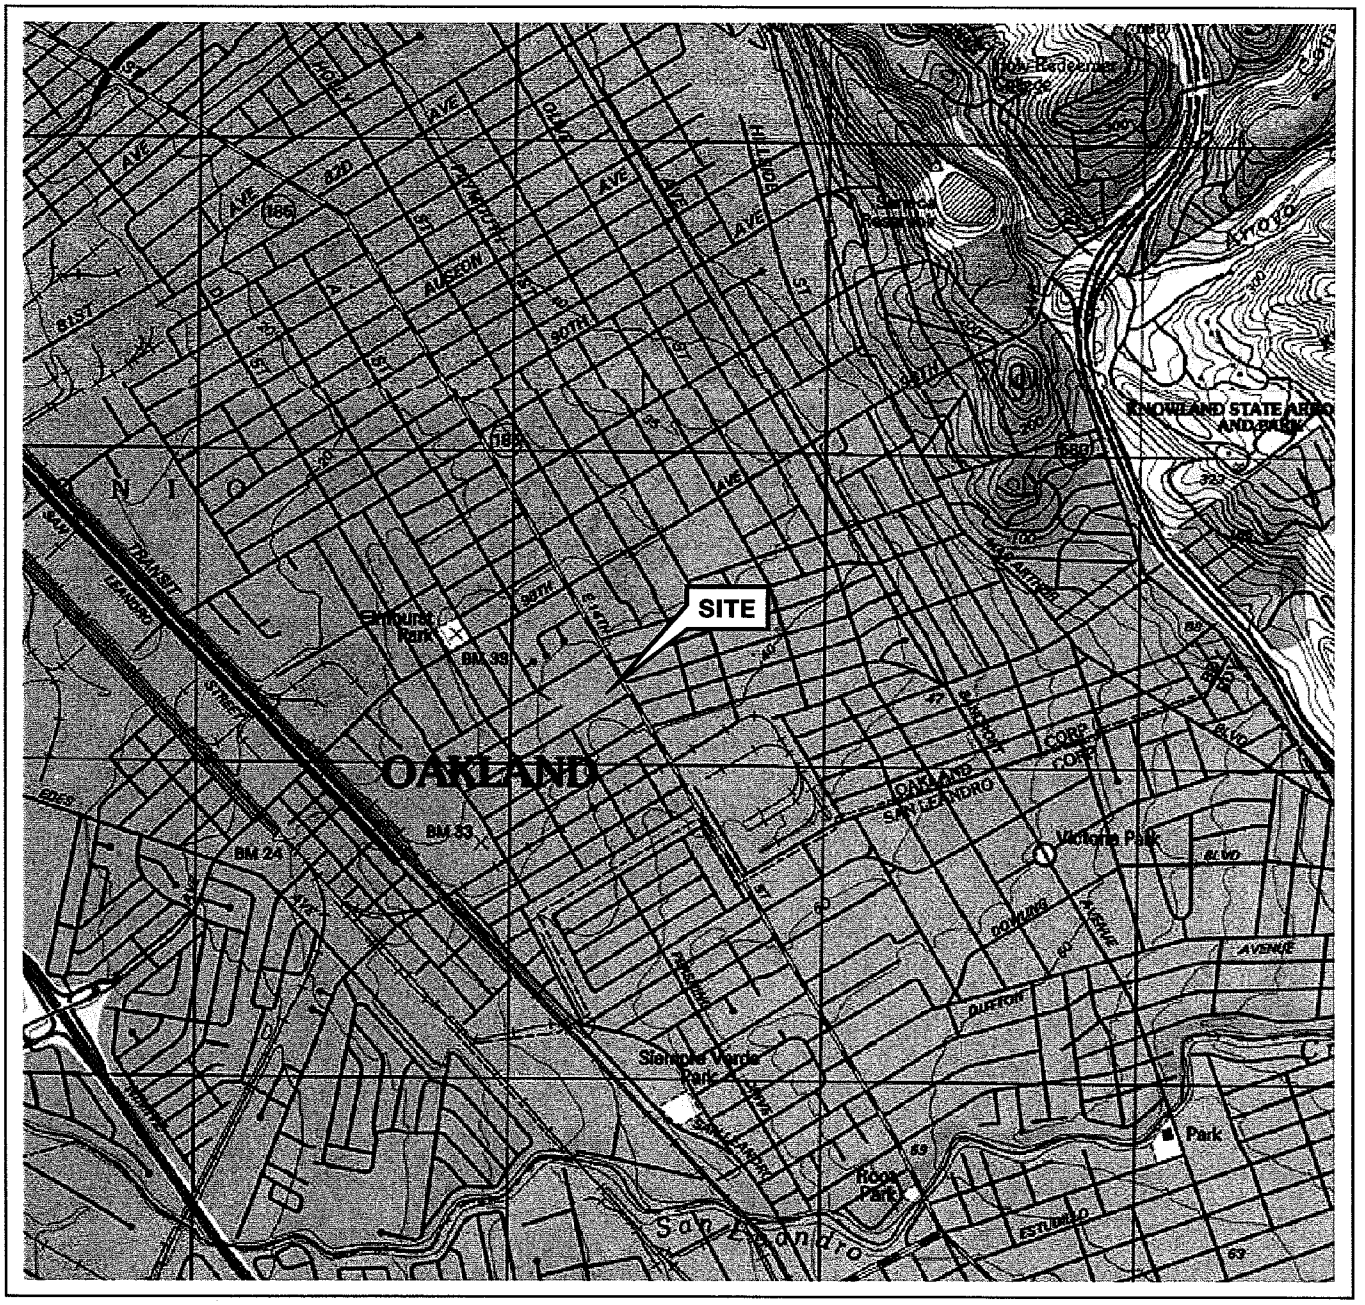

0 1/4 1/2 3/4 1 MILE

SCALE 1:24,000

N

SOURCE:

United States Geological Survey
7.5 Minute Topographic Map:
Oakland West Quadrangle

QUADRANGLE LOCATION

TRC	PROJECT: 41060002	VICINITY MAP
	FACILITY: 76 STATION 7124 10151 INTERNATIONAL BOULEVARD OAKLAND, CALIFORNIA	FIGURE 1

PS=1:1 L:\DMS VICINITY MAPS\7124vm.dwg Apr 11, 2007 - 2:40pm oakers

LEGEND

MW-4 ⊕ Monitoring Well with Groundwater Elevation (feet)

22.00 — Groundwater Elevation Contour

General Direction of Groundwater Flow

N

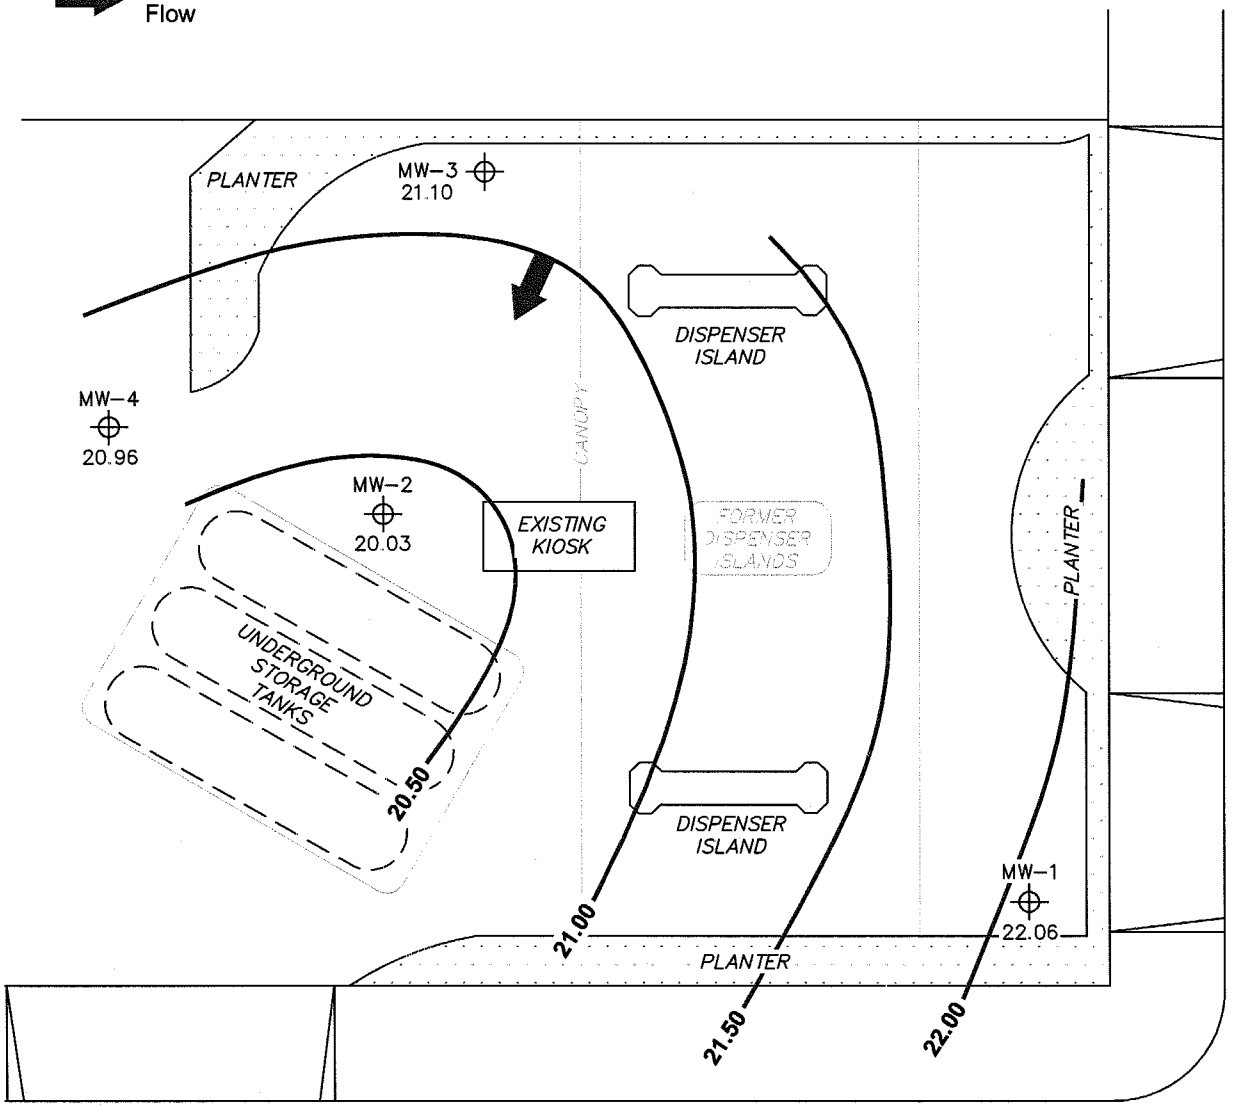

NOTES:

Contour lines are interpretive and based on fluid levels measured in monitoring wells. Elevations are in feet above mean sea level.

SCALE (FEET)

0 20

TRC

PROJECT: 41060002

FACILITY:

76 STATION 7124
10151 INTERNATIONAL BOULEVARD
OAKLAND, CALIFORNIA

GROUNDWATER ELEVATION CONTOUR MAP
April 4, 2007

FIGURE 2

MS=1:1 7124-003 L:\Graphics\ProjectsByNumber\20-xxxx\20-0400(UnocalQMS)\x-7000\7124+\7124QMS.DWG Apr 24, 2007 - 8:43am cvuong

LEGEND

MW-4 ⊕ Monitoring Well with Dissolved-Phase TPH-G (GC/MS) Concentration (µg/l)

—1,000— Dissolved-Phase TPH-G (GC/MS) Contour (µg/l)

N

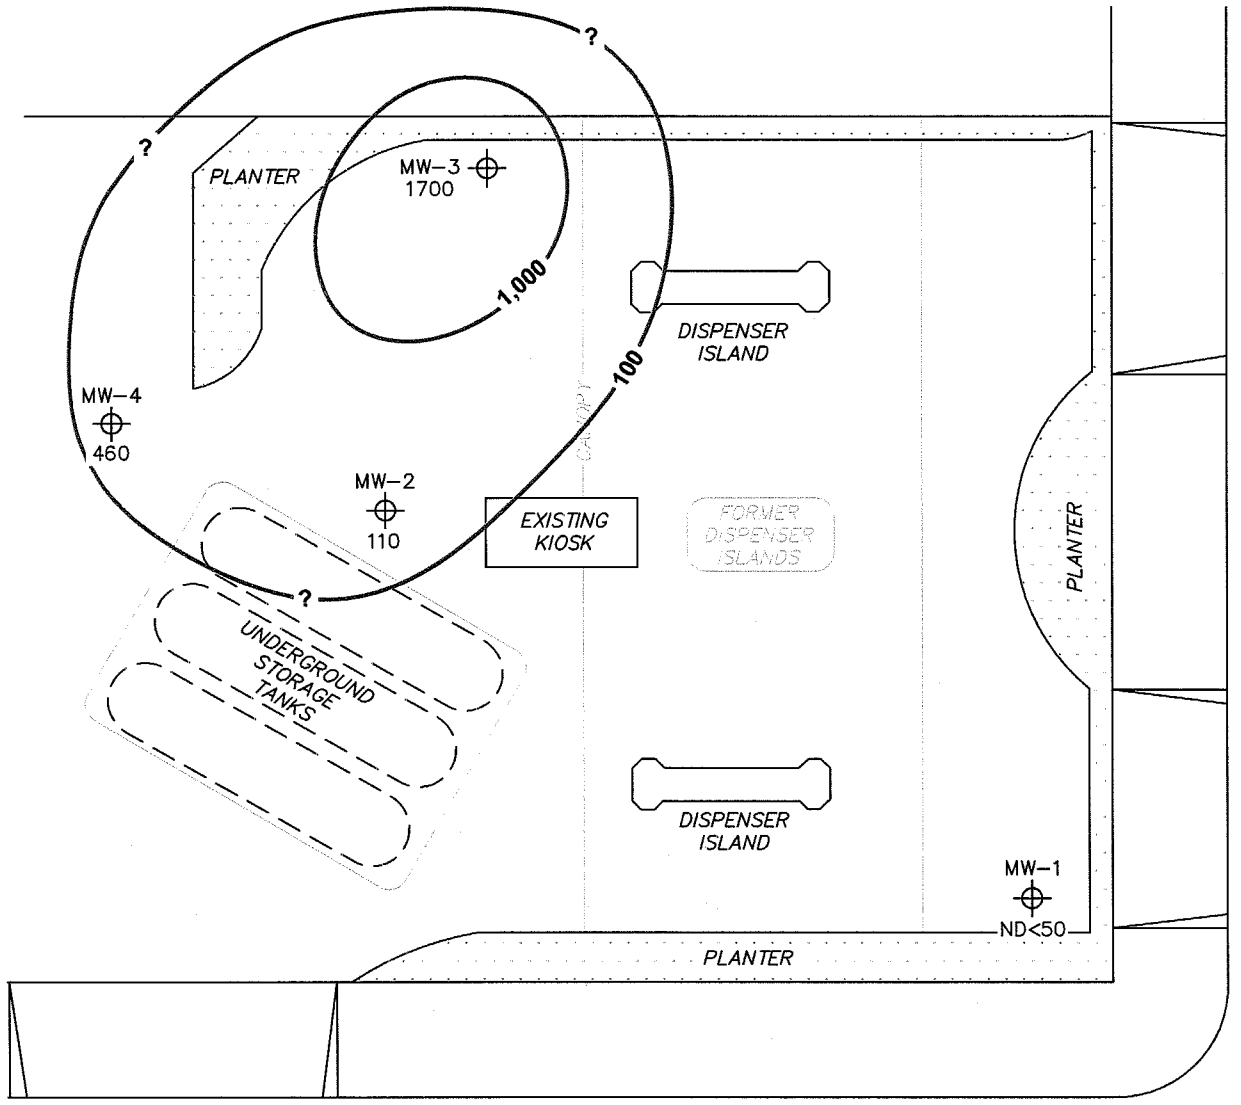

NOTES:

Contour lines are interpretive and based on laboratory analysis results of groundwater samples. TPH-G (GC/MS) = total petroleum hydrocarbons with gasoline distinction utilizing EPA Method 8260B. µg/l = micrograms per liter. ND = not detected at limit indicated on official laboratory report.

SCALE (FEET)

0 20

TRC

PROJECT: 41060002

FACILITY:

76 STATION 7124
10151 INTERNATIONAL BOULEVARD
OAKLAND, CALIFORNIA

DISSOLVED-PHASE TPH-G (GC/MS) CONCENTRATION MAP
April 4, 2007

FIGURE 3

MS=1:1 7124-003 L:\Graphics\ProjectsByNumber\20-xxxx\20-0400(UnocalQMS)\x-7000\7124+\71240MS.DWG Apr 23, 2007 - 2:50pm cvuong

LEGEND

MW-4 ⊕ Monitoring Well with Dissolved-Phase Benzene Concentration (µg/l)

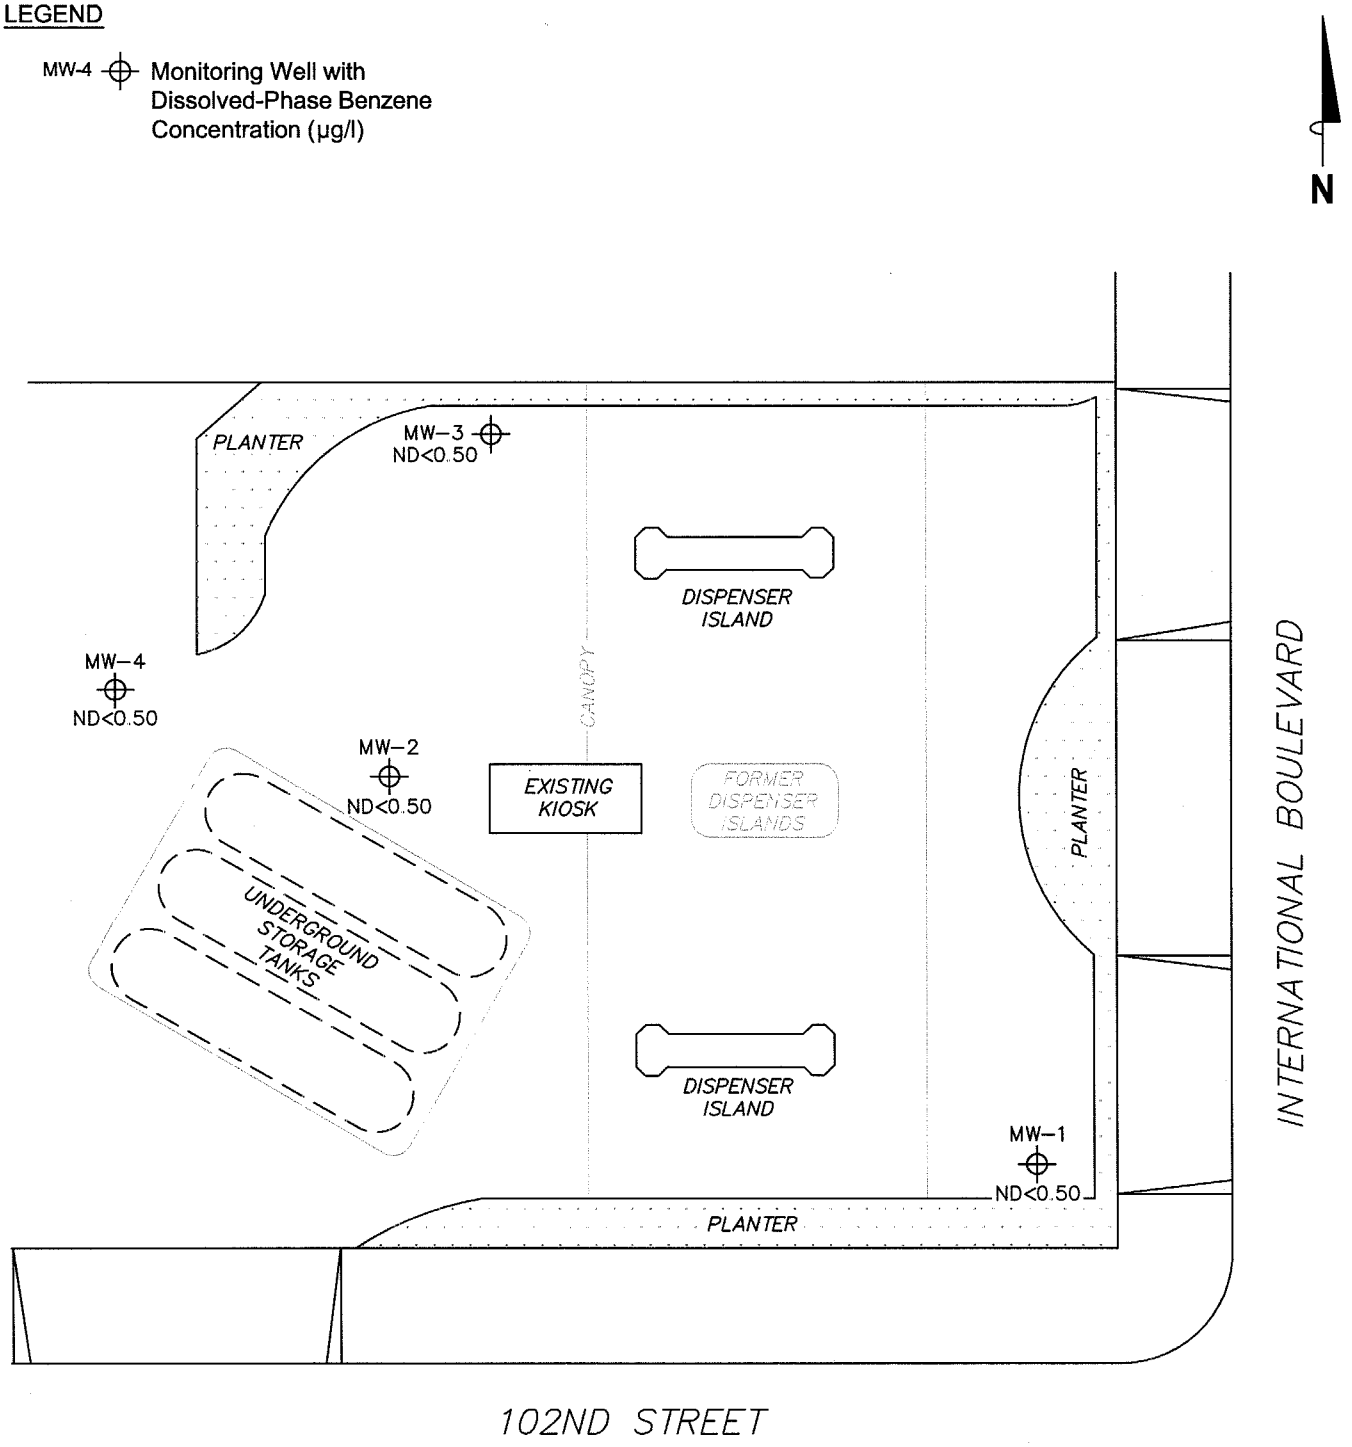

NOTES:

µg/l = micrograms per liter. ND = not detected at limit indicated on official laboratory report.

SCALE (FEET)

0 20

TRC

PROJECT: 41060002

FACILITY:

76 STATION 7124
10151 INTERNATIONAL BOULEVARD
OAKLAND, CALIFORNIA

DISSOLVED-PHASE BENZENE CONCENTRATION MAP
April 4, 2007

FIGURE 4

MS=1:1 7124-003 L:\Graphics\ProjectsByNumber\20-xxxx\20-0400(UnocalQMS)\x-7000\7124+\7124QMS.DWG Apr 23, 2007 - 2:50pm cvuong

LEGEND

MW-4 ⊕ Monitoring Well with Dissolved-Phase MTBE Concentration (µg/l)

100 Dissolved-Phase MTBE Contour (µg/l)

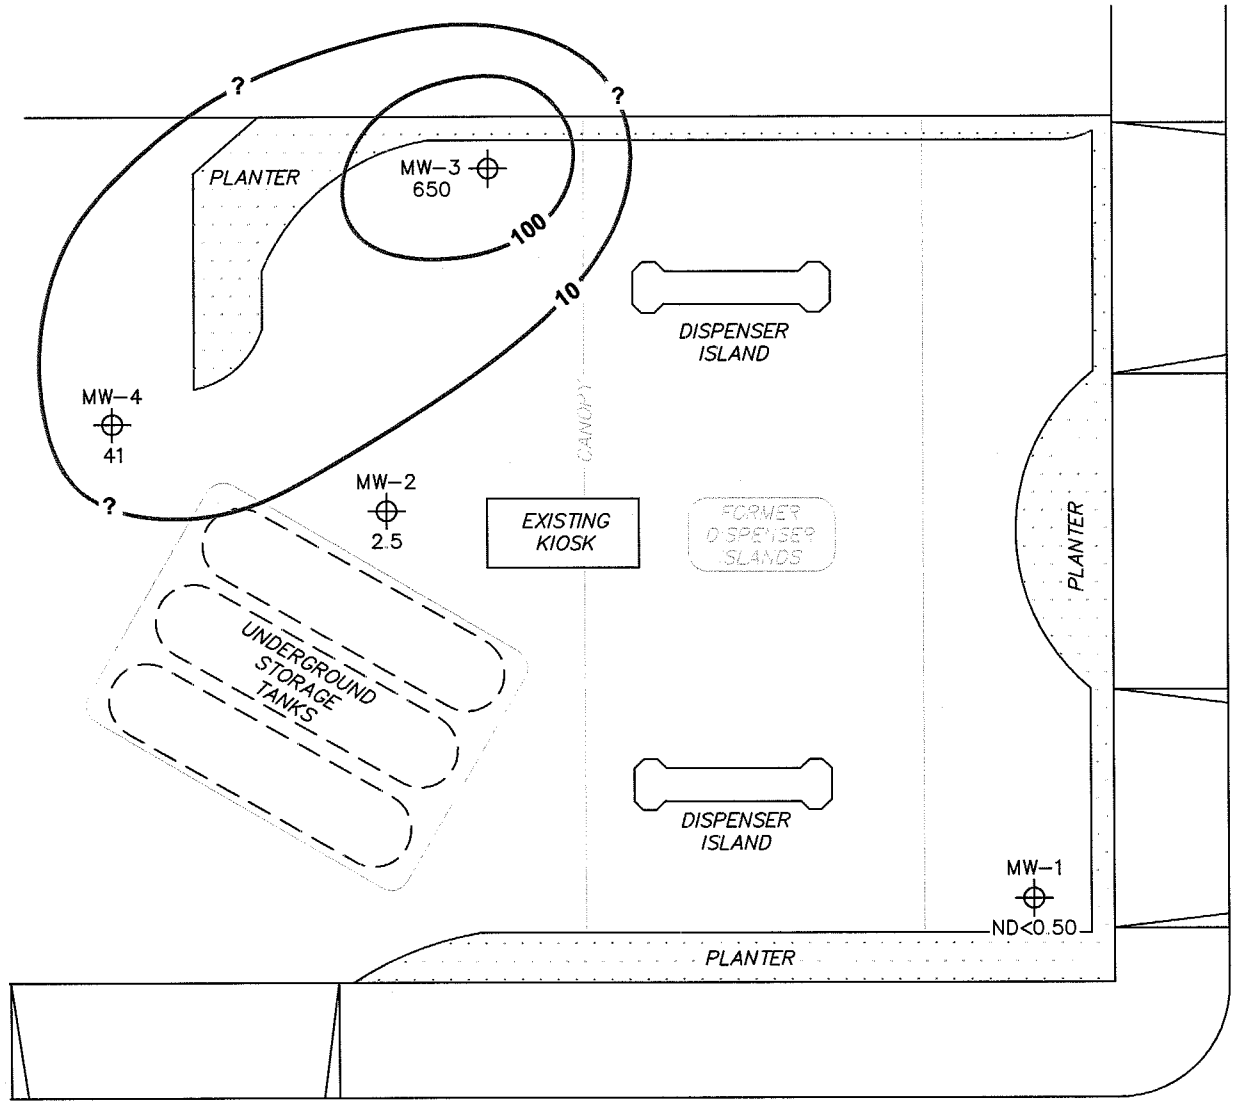

NOTES:

Contour lines are interpretive and based on laboratory analysis results of groundwater samples. MTBE = methyl tertiary butyl ether. µg/l = micrograms per liter. ND = not detected at limit indicated on official laboratory report. UST = underground storage tank. Results obtained using EPA Method 8260B.

SCALE (FEET)

0 20

TRC

PROJECT: 41060002

FACILITY:

76 STATION 7124
10151 INTERNATIONAL BOULEVARD
OAKLAND, CALIFORNIA

DISSOLVED-PHASE MTBE CONCENTRATION MAP
April 4, 2007

FIGURE 5

MS=1:1 7124-003 L:\Graphics\ProjectsByNumber\20-xxxx\20-0400(Unocal0MS)\x-7000\7124+\71240MS.DWG Apr 23, 2007 - 2:50pm cvuong

GRAPHS

Groundwater Elevations vs. Time
76 Station 7124

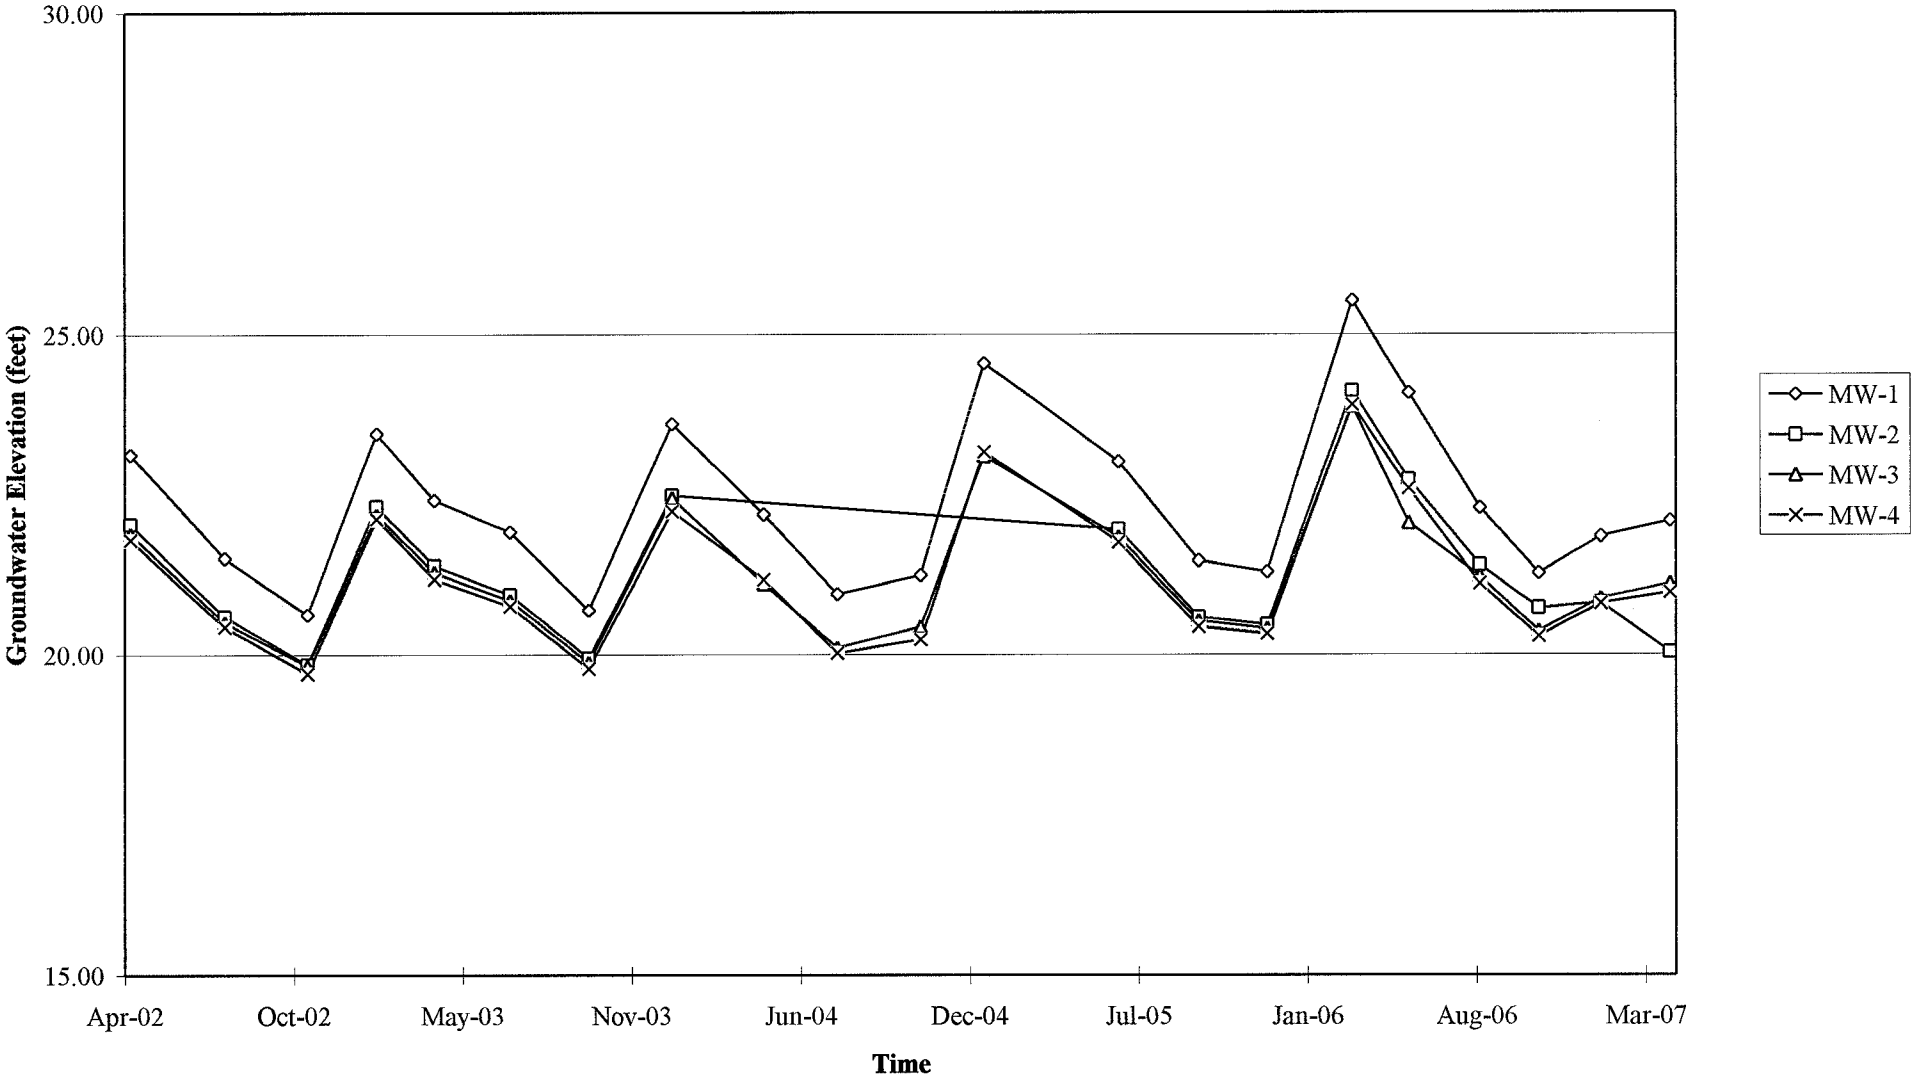

Elevations may have been corrected for apparent changes due to resurvey

MTBE 8260B Concentrations vs Time

76 Station 7124

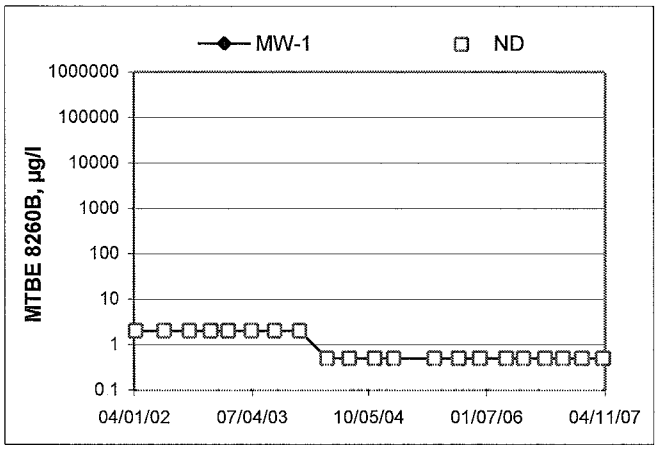

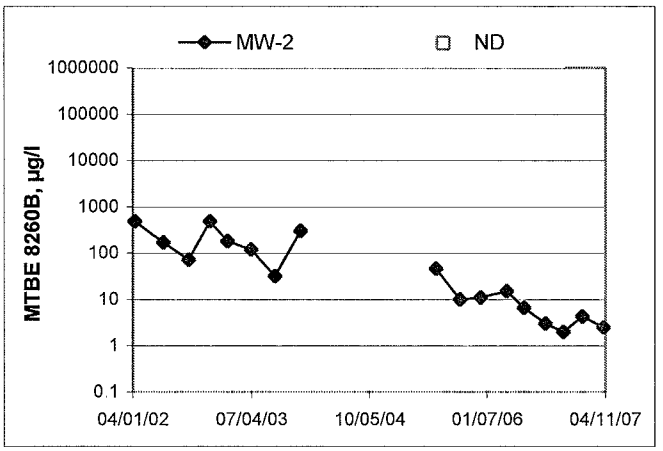

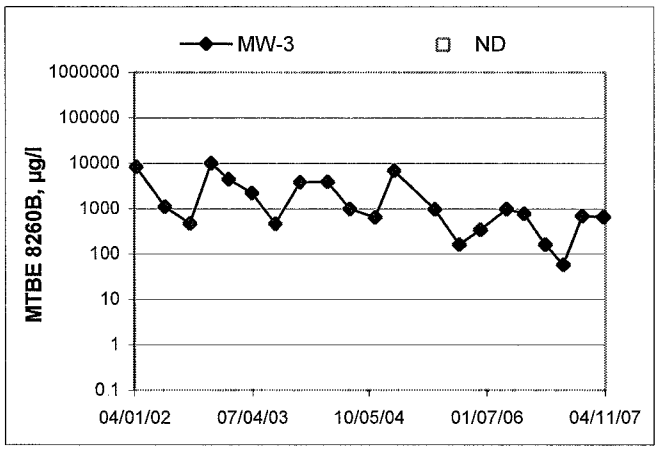

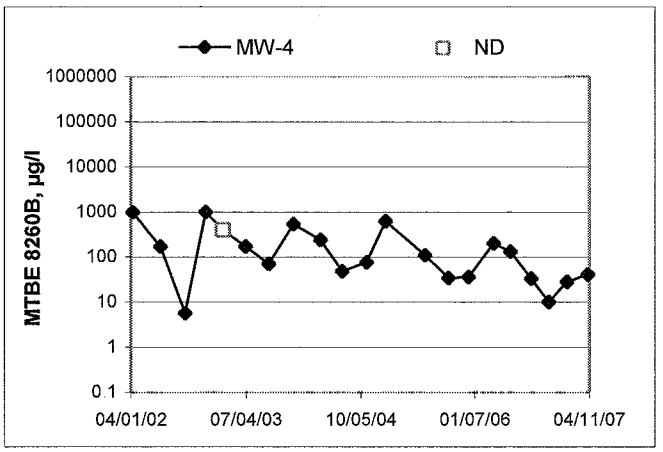

GENERAL FIELD PROCEDURES

Groundwater Monitoring and Sampling Assignments

For each site, TRC technicians are provided with a Technical Service Request (TSR) that specifies activities required to complete the groundwater monitoring and sampling assignment for the site. TSRs are based on client directives, instructions from the primary environmental consultant for the site, regulatory requirements, and TRC's previous experience with the site.

Fluid Level Measurements

Initial site activities include determination of well locations based on a site map provided with the TSR. Well boxes are opened and caps are removed. Indications of well or well box damage or of pressure buildup in the well are noted.

Fluid levels in each well are measured using a coated cloth tape equipped with an electronic interface probe, which distinguishes between liquid phase hydrocarbon (LPH) and water. The depth to LPH (if it is present), to water, and to the bottom of the well are measured from the top of the well casing (surveyors mark or notch if present) to the nearest 0.01 foot. Unless otherwise instructed, a well with less than 0.67 foot between the measured top of water and the measured bottom of the well casing is considered dry, and is not sampled. If the well contains 0.67 foot or more of water, an attempt is made to bail and/or sample as specified on the TSR.

Wells that are found to contain LPH are not purged or sampled. Instead, one casing volume of fluid is bailed from the well and the well is re-sealed. Bailed fluids are placed in a container separate from normal purge water, and properly disposed.

Purging and Groundwater Parameter Measurement

TSR instructions may specify that a well not be purged (no-purge sampling), be purged using low-flow methods, or be purged using conventional pump and/or bail methods. Conventional purging generally consists of pumping or bailing until a minimum of three casing volumes of water have been removed or until the well has been pumped dry. Pumping is generally accomplished using submersible electric or pneumatic diaphragm pumps.

During conventional purging, three groundwater parameters (temperature, pH, and conductivity) are measured after removal of each casing volume. Stabilization of these parameters, to within 10 percent, confirm that sufficient purging has been completed. In some cases, the TSR indicates that other parameters are also to be measured during purging. TRC commonly measures dissolved oxygen (DO), oxidation-reduction potential (ORP), and/or turbidity. Instruments used for groundwater parameter measurements are calibrated daily according to manufacturer's instructions.

Low-flow purging utilizes a bladder or peristaltic pump to remove water from the well at a low rate. Groundwater parameters specified by the TSR are measured continuously until they become stable in general accordance with EPA guidelines.

Purge water is generally collected in labeled drums for disposal. Drums may be left on site for disposal by others, or transported to a collection location for eventual transfer to a licensed treatment or recycling facility. In some cases, purge water may be collected directly from the site by a licensed vacuum truck company, or may be treated on site by an active remediation system, if so directed.

Groundwater Sample Collection

After wells are purged, or not purged, according to TSR instructions, samples are collected for laboratory analysis. For wells that have been purged using conventional pump or bail methods, sampling is conducted after the well has recovered to 80 percent of its original volume or after two hours if the well does not recover to at least 80 percent. If there is insufficient recharge of water in the well after two hours, the well is not sampled.

Samples are collected by lowering a new, disposable, ½-inch to 4-inch polyethylene bottom-fill bailer to just below the water level in the well. The bailer is retrieved and the water sample is carefully transferred to containers specified for the laboratory analytical methods indicated by the TSR. Particular care is given to containers for volatile organic analysis (VOAs) which require filling to zero headspace and fitting with Teflon-sealed caps.

After filling, all containers are labeled with project number (or site number), well designation, sample date, sample time, and the sampler's initials, and placed in an insulated chest with ice. Samples remain chilled prior to and during transport to a state-certified laboratory for analysis. Sample container descriptions and requested analyses are entered onto a chain-of-custody form in order to provide instructions to the laboratory. The chain-of-custody form accompanies the samples during transportation to provide a continuous record of possession from the field to the laboratory. If a freight or overnight carrier transports the samples, the carrier is noted on the form.

For wells that have been purged using low-flow methods, sample containers are filled from the effluent stream of the bladder or peristaltic pump. In some cases, if so specified by the TSR, samples are taken from the sample ports of actively pumping remediation wells.

Sequence of Gauging, Purging and Sampling

The sequence in which monitoring activities are conducted are specified on the TSR. In general, wells are gauged beginning with the least affected well and ending with the well that has the highest concentration based on previous analytic results. After all gauging for the site is completed, wells are purged and/or sampled from the least-affected to the most-affected well.

Decontamination

In order to reduce the possibility of cross contamination between wells, strict isolation and decontamination procedures are observed. Portable pumps are not used in wells with LPH. Technicians wear nitrile gloves during all gauging, purging and sampling activities. Gloves are changed between wells and more often if warranted. Any equipment that could come in contact with fluids are either dedicated to a particular wells, decontaminated prior to each use, or discarded after a single use. Decontamination consists of washing in a solution of Liqui-nox and water and rinsing twice. The final rinse is in deionized water.

Exceptions

Additional tasks or non-standard procedures, if any, that may be requested or required for a particular site, and noted on the site TSR, are documented in field notes on the following pages.

FIELD MONITORING DATA SHEET

Technician: DAMIAN Job #/Task #: 41060001/FA80 Date: 4/4/07

Site # 7134 Project Manager SEAN COYLE Page 1 of 1

Well #	Time Gauged	TOC	Total Depth	Depth to Water	Depth to Product	Product Thickness (feet)	Time Sampled	Misc. Well Notes
MW-1	0612		24.98	15.31	—	—	0948	4"
MW-2	0622		25.45	17.84	—	—	1002	4"
MW-4	0631		25.0	17.40	—	—	1010	4"
MW-3	0639		25.30	16.62	—	—	1032	4"

FIELD DATA COMPLETE ✓ QA/QC ✓ COC ✓ WELL BOX CONDITION SHEETS ✓

WTT CERTIFICATE MANIFEST DRUM INVENTORY ✓ TRAFFIC CONTROL

GROUNDWATER SAMPLING FIELD NOTES

Technician: DAMIAN

Site: 7124 Project No.: 41060001/FA20 Date: 4/4/07

Well No. MW-1 Purge Method: SUB

Depth to Water (feet): 15.31 Depth to Product (feet): —

Total Depth (feet) 24.98 LPH & Water Recovered (gallons): —

Water Column (feet): 9.67 Casing Diameter (Inches): 4

80% Recharge Depth(feet) 17.24 1 Well Volume (gallons): 6

Time Start	Time Stop	Depth to Water (feet)	Volume Purged (gallons)	Conduc-tivity (uS/cm)	Temperature (F ©)	pH	D.O.	ORP	Turbidity
0749			6	445 MS	19.0	6.57			
			12	441 MS	19.8	6.55			
	0806		18	444 MS	19.8	6.58			

Static at Time Sampled	Total Gallons Purged	Sample Time
1545	18	0948

Comments:

Well No. MW-2 Purge Method: SUB

Depth to Water (feet): 17.84 Depth to Product (feet) —

Total Depth (feet) 23.45 LPH & Water Recovered (gallons): —

Water Column (feet) 7.61 Casing Diameter (Inches): 4

80% Recharge Depth(feet) 19.36 1 Well Volume (gallons): 5

Time Start	Time Stop	Depth to Water (feet)	Volume Purged (gallons)	Conduc-tivity (uS/cm)	Temperature (F ©)	pH	D.O.	ORP	Turbidity
0819		5	5	475 MS	19.0	6.74			
		10	10	452 MS	20.0	6.61			
	0825	15	15	458 MS	20.5	6.62			

Static at Time Sampled	Total Gallons Purged	Sample Time
1680	15	1002

Comments:

GROUNDWATER SAMPLING FIELD NOTES

Technician: DAMIAN

Site: 7124 Project No.: 41060001/FA80 Date: 4/4/07

Well No. MW-4 Purge Method: SUB

Depth to Water (feet): 17.40 Depth to Product (feet): —

Total Depth (feet) 25.00 LPH & Water Recovered (gallons): —

Water Column (feet): 7.60 Casing Diameter (Inches): 4

80% Recharge Depth(feet): 18.92 1 Well Volume (gallons): 39

Time Start	Time Stop	Depth to Water (feet)	Volume Purged (gallons)	Conductivity (uS/cm)	Temperature (F, C)	pH	D.O.	ORP	Turbidity
0838			13	486 MS	20.5	6.71			
			26	483 MS	20.7	6.67			
	0856		39	479 MS	20.7	6.70			

Static at Time Sampled	Total Gallons Purged	Sample Time
	39	1010

Comments: MW-4 NEEDS LOCK FOR WELL CAP (MASTER LOCK) TO BE FOR EXP.

Well No. MW-3 Purge Method: SUB

Depth to Water (feet): 16.62 Depth to Product (feet): —

Total Depth (feet) 25.30 LPH & Water Recovered (gallons): —

Water Column (feet) 8.98 Casing Diameter (Inches) 4

80% Recharge Depth(feet): 18.11 1 Well Volume (gallons): 13

Time Start	Time Stop	Depth to Water (feet)	Volume Purged (gallons)	Conductivity (uS/cm)	Temperature (F, C)	pH	D.O.	ORP	Turbidity
0905			13	486 MS	20.3	6.64			
			26	493 MS	20.6	6.61			
	0925		39	495 MS	20.5	6.64			

Static at Time Sampled	Total Gallons Purged	Sample Time
1671	39	1032

Comments:

BC LABORATORIES, INC.

Date of Report: 04/17/2007

Anju Farfan

TRC Alton Geoscience
21 Technology Drive
Irvine, CA 92618-2302

RE: 7124
BC Work Order: 0703998

Enclosed are the results of analyses for samples received by the laboratory on 04/04/2007 21:10. If you have any questions concerning this report, please feel free to contact me.

Sincerely,

Contact Person: Vanessa Hooker
Client Service Rep

Steven Bennett
Authorized Signature

BC LABORATORIES, INC.

TRC Alton Geoscience 21 Technology Drive Irvine, CA 92618-2302	Project: 7124 Project Number: [none] Project Manager: Anju Farfan	**Reported:** 04/17/2007 13:34

Laboratory / Client Sample Cross Reference

Laboratory	Client Sample Information				
0703998-01	**COC Number:**	---	**Receive Date:**	04/04/2007 21:10	Delivery Work Order:
	Project Number:	7124	**Sampling Date:**	04/04/2007 09:48	Global ID: T0600173591
	Sampling Location:	MW-1	**Sample Depth:**	---	Matrix: W
	Sampling Point:	MW-1	**Sample Matrix:**	Water	Samle QC Type (SACode): CS
	Sampled By:	Damian B. of TRCI			Cooler ID:
0703998-02	**COC Number:**	---	**Receive Date:**	04/04/2007 21:10	Delivery Work Order:
	Project Number:	7124	**Sampling Date:**	04/04/2007 10:02	Global ID: T0600173591
	Sampling Location:	MW-2	**Sample Depth:**	---	Matrix: W
	Sampling Point:	MW-2	**Sample Matrix:**	Water	Samle QC Type (SACode): CS
	Sampled By:	Damian B. of TRCI			Cooler ID:
0703998-03	**COC Number:**	---	**Receive Date:**	04/04/2007 21:10	Delivery Work Order:
	Project Number:	7124	**Sampling Date:**	04/04/2007 10:10	Global ID: T0600173591
	Sampling Location:	MW-4	**Sample Depth:**	---	Matrix: W
	Sampling Point:	MW-4	**Sample Matrix:**	Water	Samle QC Type (SACode): CS
	Sampled By:	Damian B. of TRCI			Cooler ID:
0703998-04	**COC Number:**	---	**Receive Date:**	04/04/2007 21:10	Delivery Work Order:
	Project Number:	7124	**Sampling Date:**	04/04/2007 10:32	Global ID: T0600173591
	Sampling Location:	MW-3	**Sample Depth:**	---	Matrix: W
	Sampling Point:	MW-3	**Sample Matrix:**	Water	Samle QC Type (SACode): CS
	Sampled By:	Damian B. of TRCI			Cooler ID:

4100 Atlas Court • Bakersfield, CA 93308 • (661) 327-4911 • FAX (661) 327-1918 • www.bclabs.com

TRC Alton Geoscience 21 Technology Drive Irvine, CA 92618-2302	Project: 7124 Project Number: [none] Project Manager: Anju Farfan	**Reported:** 04/17/2007 13:34

Volatile Organic Analysis (EPA Method 8260)

BCL Sample ID: 0703998-01 | **Client Sample Name:** 7124, MW-1, MW-1, 4/4/2007 9:48:00AM, Damian B.

Constituent	Result	Units	PQL	MDL	Method	Prep Date	Run Date/Time	Analyst	Instru-ment ID	Dilution	QC Batch ID	MB Bias	Lab Quals
Benzene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
1,2-Dibromoethane	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
1,2-Dichloroethane	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
Ethylbenzene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
Methyl t-butyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
Toluene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
Total Xylenes	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
t-Amyl Methyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
t-Butyl alcohol	ND	ug/L	10		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
Diisopropyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
Ethanol	ND	ug/L	250		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
Ethyl t-butyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
Total Purgeable Petroleum Hydrocarbons	ND	ug/L	50		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495	ND	
1,2-Dichloroethane-d4 (Surrogate)	104	%	76 - 114 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495		
Toluene-d8 (Surrogate)	102	%	88 - 110 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495		
4-Bromofluorobenzene (Surrogate)	99.6	%	86 - 115 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 04:52	DKC	MS-V12	1	BQD0495		

TRC Alton Geoscience
21 Technology Drive
Irvine, CA 92618-2302

Project: 7124
Project Number: [none]
Project Manager: Anju Farfan

Reported: 04/17/2007 13:34

Volatile Organic Analysis (EPA Method 8260)

BCL Sample ID: 0703998-02 | **Client Sample Name:** 7124, MW-2, MW-2, 4/4/2007 10:02:00AM, Damian B.

Constituent	Result	Units	PQL	MDL	Method	Prep Date	Run Date/Time	Analyst	Instrument ID	Dilution	QC Batch ID	MB Bias	Lab Quals
Benzene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
1,2-Dibromoethane	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
1,2-Dichloroethane	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
Ethylbenzene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
Methyl t-butyl ether	2.5	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
Toluene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
Total Xylenes	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
t-Amyl Methyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
t-Butyl alcohol	ND	ug/L	10		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
Diisopropyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
Ethanol	ND	ug/L	250		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
Ethyl t-butyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
Total Purgeable Petroleum Hydrocarbons	110	ug/L	50		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495	ND	
1,2-Dichloroethane-d4 (Surrogate)	102	%	76 - 114 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495		
Toluene-d8 (Surrogate)	101	%	88 - 110 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495		
4-Bromofluorobenzene (Surrogate)	105	%	86 - 115 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 05:15	DKC	MS-V12	1	BQD0495		

BC LABORATORIES, INC.

TRC Alton Geoscience 21 Technology Drive Irvine, CA 92618-2302	Project: 7124 Project Number: [none] Project Manager: Anju Farfan	**Reported:** 04/17/2007 13:34

Volatile Organic Analysis (EPA Method 8260)

BCL Sample ID: 0703998-03 | **Client Sample Name:** 7124, MW-4, MW-4, 4/4/2007 10:10:00AM, Damian B.

Constituent	Result	Units	PQL	MDL	Method	Prep Date	Run Date/Time	Analyst	Instrument ID	Dilution	QC Batch ID	MB Bias	Lab Quals
Benzene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
1,2-Dibromoethane	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
1,2-Dichloroethane	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
Ethylbenzene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
Methyl t-butyl ether	41	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
Toluene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
Total Xylenes	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
t-Amyl Methyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
t-Butyl alcohol	260	ug/L	10		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
Diisopropyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
Ethanol	ND	ug/L	250		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
Ethyl t-butyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
Total Purgeable Petroleum Hydrocarbons	460	ug/L	50		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495	ND	
1,2-Dichloroethane-d4 (Surrogate)	105	%	76 - 114 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495		
Toluene-d8 (Surrogate)	99.5	%	88 - 110 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495		
4-Bromofluorobenzene (Surrogate)	118	%	86 - 115 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 05:39	DKC	MS-V12	1	BQD0495		A19,S09

TRC Alton Geoscience 21 Technology Drive Irvine, CA 92618-2302	Project: 7124 Project Number: [none] Project Manager: Anju Farfan	**Reported:** 04/17/2007 13:34

Volatile Organic Analysis (EPA Method 8260)

BCL Sample ID: 0703998-04 | **Client Sample Name:** 7124, MW-3, MW-3, 4/4/2007 10:32:00AM, Damian B.

Constituent	Result	Units	PQL	MDL	Method	Prep Date	Run Date/Time	Analyst	Instru-ment ID	Dilution	QC Batch ID	MB Bias	Lab Quals
Benzene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
1,2-Dibromoethane	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
1,2-Dichloroethane	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
Ethylbenzene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
Methyl t-butyl ether	650	ug/L	5.0		EPA-8260	04/13/07	04/14/07 23:42	DKC	MS-V12	10	BQD0495	ND	A01
Toluene	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
Total Xylenes	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
t-Amyl Methyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
t-Butyl alcohol	130	ug/L	10		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
Diisopropyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
Ethanol	ND	ug/L	250		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
Ethyl t-butyl ether	ND	ug/L	0.50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
Total Purgeable Petroleum Hydrocarbons	1700	ug/L	50		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495	ND	
1,2-Dichloroethane-d4 (Surrogate)	104	%	76 - 114 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495		
1,2-Dichloroethane-d4 (Surrogate)	97.7	%	76 - 114 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 23:42	DKC	MS-V12	10	BQD0495		
Toluene-d8 (Surrogate)	104	%	88 - 110 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495		
Toluene-d8 (Surrogate)	101	%	88 - 110 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 23:42	DKC	MS-V12	10	BQD0495		
4-Bromofluorobenzene (Surrogate)	98.6	%	86 - 115 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 23:42	DKC	MS-V12	10	BQD0495		
4-Bromofluorobenzene (Surrogate)	125	%	86 - 115 (LCL - UCL)		EPA-8260	04/13/07	04/14/07 06:03	DKC	MS-V12	1	BQD0495		A19,S09

TRC Alton Geoscience
21 Technology Drive
Irvine, CA 92618-2302

Project: 7124
Project Number: [none]
Project Manager: Anju Farfan

Reported: 04/17/2007 13:34

Volatile Organic Analysis (EPA Method 8260)

Quality Control Report - Precision & Accuracy

Constituent	Batch ID	QC Sample Type	Source Sample ID	Source Result	Result	Spike Added	Units	RPD	Percent Recovery	Control Limits RPD	Control Limits Percent Recovery	Lab Quals
Benzene	BQD0495	Matrix Spike	0703711-15	0	26.830	25.000	ug/L		107		70 - 130	
		Matrix Spike Duplicate	0703711-15	0	27.150	25.000	ug/L	1.9	109	20	70 - 130	
Toluene	BQD0495	Matrix Spike	0703711-15	0	26.580	25.000	ug/L		106		70 - 130	
		Matrix Spike Duplicate	0703711-15	0	26.930	25.000	ug/L	1.9	108	20	70 - 130	
1,2-Dichloroethane-d4 (Surrogate)	BQD0495	Matrix Spike	0703711-15	ND	10.510	10.000	ug/L		105		76 - 114	
		Matrix Spike Duplicate	0703711-15	ND	9.8400	10.000	ug/L		98.4		76 - 114	
Toluene-d8 (Surrogate)	BQD0495	Matrix Spike	0703711-15	ND	9.8400	10.000	ug/L		98.4		88 - 110	
		Matrix Spike Duplicate	0703711-15	ND	9.9200	10.000	ug/L		99.2		88 - 110	
4-Bromofluorobenzene (Surrogate)	BQD0495	Matrix Spike	0703711-15	ND	10.220	10.000	ug/L		102		86 - 115	
		Matrix Spike Duplicate	0703711-15	ND	10.180	10.000	ug/L		102		86 - 115	

4100 Atlas Court • Bakersfield, CA 93308 • (661) 327-4911 • FAX (661) 327-1918 • www.bclabs.com

TRC Alton Geoscience
21 Technology Drive
Irvine, CA 92618-2302

Project: 7124
Project Number: [none]
Project Manager: Anju Farfan

Reported: 04/17/2007 13:34

Volatile Organic Analysis (EPA Method 8260)

Quality Control Report - Laboratory Control Sample

Constituent	Batch ID	QC Sample ID	QC Type	Result	Spike Level	PQL	Units	Percent Recovery	RPD	Control Limits Percent Recovery	Control Limits RPD	Lab Quals
Benzene	BQD0495	BQD0495-BS1	LCS	26.620	25.000	0.50	ug/L	106		70 - 130		
Toluene	BQD0495	BQD0495-BS1	LCS	27.890	25.000	0.50	ug/L	112		70 - 130		
1,2-Dichloroethane-d4 (Surrogate)	BQD0495	BQD0495-BS1	LCS	9.8200	10.000		ug/L	98.2		76 - 114		
Toluene-d8 (Surrogate)	BQD0495	BQD0495-BS1	LCS	10.110	10.000		ug/L	101		88 - 110		
4-Bromofluorobenzene (Surrogate)	BQD0495	BQD0495-BS1	LCS	10.500	10.000		ug/L	105		86 - 115		

4100 Atlas Court • Bakersfield, CA 93308 • (661) 327-4911 • FAX (661) 327-1918 • www.bclabs.com

TRC Alton Geoscience
21 Technology Drive
Irvine, CA 92618-2302

Project: 7124
Project Number: [none]
Project Manager: Anju Farfan

Reported: 04/17/2007 13:34

Volatile Organic Analysis (EPA Method 8260)

Quality Control Report - Method Blank Analysis

Constituent	Batch ID	QC Sample ID	MB Result	Units	PQL	MDL	Lab Quals
Benzene	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
1,2-Dibromoethane	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
1,2-Dichloroethane	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
Ethylbenzene	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
Methyl t-butyl ether	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
Toluene	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
Total Xylenes	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
t-Amyl Methyl ether	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
t-Butyl alcohol	BQD0495	BQD0495-BLK1	ND	ug/L	10		
Diisopropyl ether	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
Ethanol	BQD0495	BQD0495-BLK1	ND	ug/L	250		
Ethyl t-butyl ether	BQD0495	BQD0495-BLK1	ND	ug/L	0.50		
Total Purgeable Petroleum Hydrocarbons	BQD0495	BQD0495-BLK1	ND	ug/L	50		
1,2-Dichloroethane-d4 (Surrogate)	BQD0495	BQD0495-BLK1	93.9	%	76 - 114 (LCL - UCL)		
Toluene-d8 (Surrogate)	BQD0495	BQD0495-BLK1	97.5	%	88 - 110 (LCL - UCL)		
4-Bromofluorobenzene (Surrogate)	BQD0495	BQD0495-BLK1	98.4	%	86 - 115 (LCL - UCL)		

TRC Alton Geoscience	Project: 7124	**Reported:** 04/17/2007 13:34
21 Technology Drive	Project Number: [none]	
Irvine, CA 92618-2302	Project Manager: Anju Farfan	

Notes And Definitions

MDL	Method Detection Limit
ND	Analyte Not Detected at or above the reporting limit
PQL	Practical Quantitation Limit
RPD	Relative Percent Difference
A01	PQL's and MDL's are raised due to sample dilution.
A19	Surrogate is high due to matrix interference. Interferences verified through second extraction/analysis.
S09	The surrogate recovery on the sample for this compound was not within the control limits.

BC LABORATORIES INC. **SAMPLE RECEIPT FORM** Rev. No. 10 01/21/04 Page 1 Of 1

Submission #: 07-03998 | Project Code: | TB Batch #

SHIPPING INFORMATION
Federal Express ☐ UPS ☐ Hand Delivery ☐
BC Lab Field Service ☑ Other ☐ (Specify)_____

SHIPPING CONTAINER
Ice Chest ☑ None ☐
Box ☐ Other ☐ (Specify)_____

Refrigerant: Ice ☑ Blue Ice ☐ None ☐ Other ☐ Comments:

Custody Seals: Ice Chest ☐ Intact? Yes ☐ No ☐ | Containers ☐ Intact? Yes ☐ No ☐ | None ☑ Comments:

All samples received? Yes ☒ No ☐ All samples containers intact? Yes ☑ No ☐ Description(s) match COC? Yes ☑ No ☐

COC Received ☑ YES ☐ NO

Ice Chest ID R/U Emissivity 0.95
Temperature: 3.0 °C Container VOA
Thermometer ID: 48

Date/Time 4/14/17
Analyst Init

SAMPLE CONTAINERS	SAMPLE NUMBERS 1	2	3	4	5	6	7	8	9	10
QT GENERAL MINERAL/ GENERAL PHYSICAL										
PT PE UNPRESERVED										
QT INORGANIC CHEMICAL METALS										
PT INORGANIC CHEMICAL METALS										
PT CYANIDE										
PT NITROGEN FORMS										
PT TOTAL SULFIDE										
2oz. NITRATE / NITRITE										
100ml TOTAL ORGANIC CARBON										
QT TOX										
PT CHEMICAL OXYGEN DEMAND										
PtA PHENOLICS										
40ml VOA VIAL TRAVEL BLANK										
40ml VOA VIAL	A(3)	A(3)	A(3)	A(2)	( )	( )	( )	( )	( )	( )
QT EPA 413.1, 413.2, 418.1										
PT ODOR										
RADIOLOGICAL										
BACTERIOLOGICAL										
40 ml VOA VIAL- 504										
QT EPA 508/608/8080										
QT EPA 515.1/8150										
QT EPA 525										
QT EPA 525 TRAVEL BLANK										
100ml EPA 547										
100ml EPA 531.1										
QT EPA 548										
QT EPA 549										
QT EPA 632										
QT EPA 8015M										
QT QA/QC										
QT AMBER										
8 OZ. JAR										
32 OZ. JAR										
SOIL SLEEVE										
PCB VIAL										
PLASTIC BAG										
FERROUS IRON										
ENCORE										

Comments:
Sample Numbering Completed By: _____ Date/Time: 4/15/17 0940

[H:\DOCS\WP80\LAB_DOCS\FORMS\SAMREC2.WPD]

07-03998

BC LABORATORIES, INC.

4100 Atlas Court □ Bakersfield, CA 93308
(661) 327-4911 □ FAX (661) 327-1918

CHAIN OF CUSTODY

Analysis Requested

Bill to: Conoco Phillips/ TRC	**Consultant Firm: TRC**
Address: 10151 INTERNATIONAL BLVD	21 Techology Drive Irvine, CA 92618-2302 Attn: Anju Farfan
City: OAKLAND	**4-digit site#:** 7124 **Workorder #** 01634-4507923519
State: CA **Zip:**	**Project #:** 41060001
Conoco Phillips Mgr: ERIK HETRICK	**Sampler Name:** DAMIAN

MATRIX: (GW) Groundwater, (S) Soil, (WW) Wastewater, (SL) Sludge

Lab#	Sample Description	Field Point Name	Date & Time Sampled	Matrix	BTEX/MTBE by 8021B, Gas by 8015	TPH GAS by 8015M	TPH DIESEL by 8015	8260 full list w/ oxygenates	BTEX/MTBE/OXYS BY 8260B	ETHANOL by 8260B	TPH –G by GC/MS	EDB/EDC			Turnaround Time Requested
	-1	MW-1	4/4/07 0948	GW					X	X	X	X			STD
	-2	MW-2	↓ 1002	↓					↓	↓	↓	↓			↓
	-3	MW-4	↓ 1010	↓					↓	↓	↓	↓			↓
	-4	MW-3	↓ 1032	↓					↓	↓	↓	↓			↓

CHK BY: SL03 DISTRIBUTION: [signature] SUB-OUT

Comments: TPH-g BY GC/MS; BTEX/MTBE/OXYS BY 8260B, EDB/EDC BY 8260B

GLOBAL ID: T0600173591

Relinquished by: (Signature)	Received by:	Date & Time
D Bruguand	ERIC	4/4/07 1237
[signature]	Ross Widey	4/4/07 1340
Ross Widey 4/4/07	R Raymond	4-4-07 1800

(A) = ANALYSIS (C) = CONTAINER (P) = PRESERVATIVE

R Raymond 4-4-07 2110 [signature] 4/4/7 2110

STATEMENTS

Purge Water Disposal

Non-hazardous groundwater produced during purging and sampling of monitoring was accumulated at TRC's groundwater monitoring facility at Concord, California, for transportation by a licensed carrier, to the ConocoPhillips Refinery at Rodeo, California. Disposal at the Rodeo facility was authorized by ConocoPhillips in accordance with "ESD Standard Operating Procedures – Water Quality and Compliance", as revised on February 7, 2003. Documentation of compliance with ConocoPhillips requirements is provided by an ESD Form R-149, which is on file at TRC's Concord Office. Purge water suspected of containing potentially hazardous material, such as liquid-phase hydrocarbons, was accumulated separately in a drum for transportation and disposal by others.

Limitations

The fluid level monitoring and groundwater sampling activities summarized in this report have been performed under the responsible charge of a California Registered Geologist or Registered Civil Engineer and have been conducted in accordance with current practice and the standard of care exercised by geologists and engineers performing similar tasks in this area. No warranty, express or implied, is made regarding the conclusions and professional opinions presented in this report. The conclusions are based solely upon an analysis of the observed conditions. If actual conditions differ from those described in this report, our office should be notified.
