ID	Task Name	Duration	Start	Finish
1	**Corrective Action Implementation Plan (CAIP)**	**85 days**	**Wed 8/15/18**	**Fri 12/14/18**
2	Draft CAIP to County (Initial Submittal)	8 days	Wed 8/15/18	Fri 8/24/18
3	County Review and Approval	24 days	Mon 8/27/18	Fri 9/28/18
4	Draft CAIP to County (Final Submittal)	45 days	Mon 10/1/18	Tue 12/4/18
5	County Review and Approval	8 days	Wed 12/5/18	Fri 12/14/18
6	**Soil Groundwater Management Plan (SGMP)**	**90 days**	**Wed 8/15/18**	**Fri 12/21/18**
7	Draft SGMP to County	77 days	Wed 8/15/18	Tue 12/4/18
8	County Review and Approval	8 days	Wed 12/5/18	Fri 12/14/18
9	SGMP Certification	5 days	Mon 12/17/18	Fri 12/21/18
10	**Vapor Mitigation Engineering Control (VMEC) Documents**	**106 days**	**Mon 10/15/18**	**Fri 3/15/19**
11	VMEC Submittal to County	52 days	Mon 10/15/18	Fri 12/28/18
12	County Review and Approval	29 days	Mon 12/31/18	Fri 2/8/19
13	City of Oakland Permit Approval	25 days	Mon 2/11/19	Fri 3/15/19
14	**Anticipated Demolition and Remediation Activities**	**146 days**	**Wed 1/2/19**	**Fri 7/26/19**
15	72-hour Notice to ACDEH	3 days	Wed 1/2/19	Fri 1/4/19
16	Monitoring Well Destruction (by Exxon)	10 days	Mon 1/7/19	Fri 1/18/19
17	Demolition and Remediation Activities	40 days	Mon 1/21/19	Fri 3/15/19
18	Draft Results of Remediation To County	5 days	Mon 2/25/19	Fri 3/1/19
19	County Approval of Draft Results/Approval to Commence Construction	10 days	Mon 3/4/19	Fri 3/15/19
20	Corrective Action Completion Report (Submittal to County)	30 days	Mon 3/18/19	Fri 4/26/19
21	County Review and Approval of Completion Report	63 days	Mon 4/29/19	Fri 7/26/19
22	**Anticipated Construction**	**376 days**	**Mon 12/3/18**	**Fri 5/22/20**
23	Building Permits and GeoTracker Upload	5 days	Mon 12/3/18	Fri 12/7/18
24	72-hour Notice to ACDEH	3 days	Mon 3/18/19	Wed 3/20/19
25	Begin Construction, including VIMS Installation	265 days	Thu 3/21/19	Fri 4/3/20
26	VMEC Completion Documents (Submittal to County)	30 days	Mon 4/6/20	Fri 5/15/20
27	Institutional Controls - Land Use Covenant	35 days	Mon 4/6/20	Fri 5/22/20
28	Financial Assurance	35 days	Mon 4/6/20	Fri 5/22/20
29	Long Term SMP	35 days	Mon 4/6/20	Fri 5/22/20

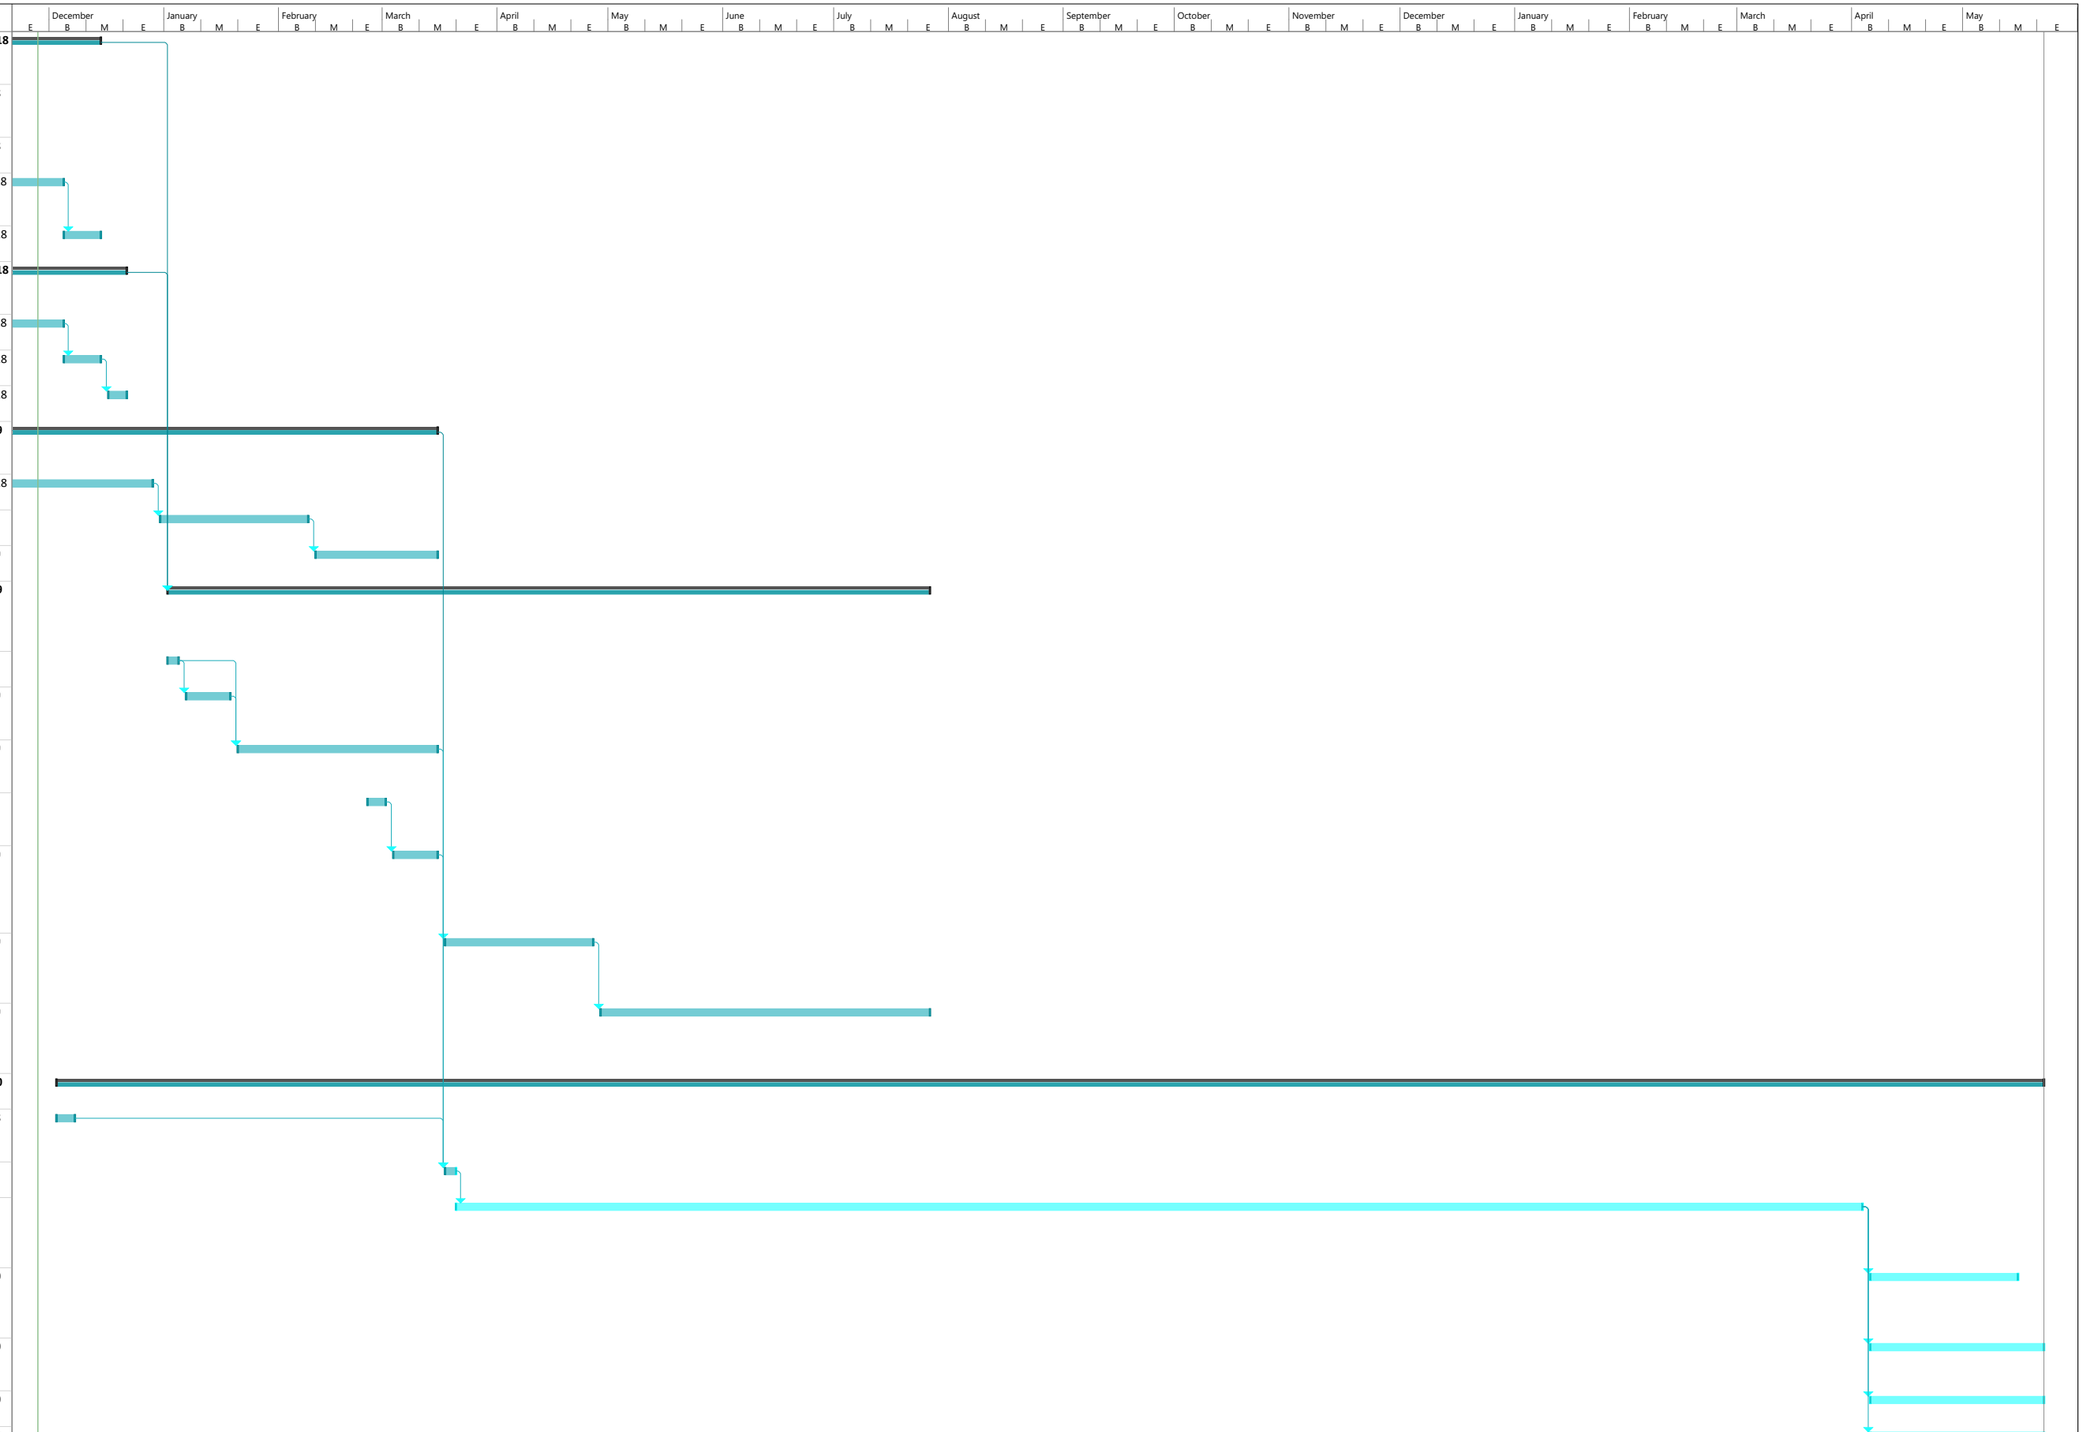

Project: 2018 11 27 Telegraph R
Date: Wed 11/28/18

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
