Chevron

Chevron

Chevron Products Company
6001 Bollinger Canyon Road
Building L
San Ramon, CA 94583
P.O. Box 6004
San Ramon, CA 94583-0904

Marketing – Sales West
Phone 510 842-9500

May 13, 1997

Dr. Ravi Arulanantham
RWQCB- San Francisco Bay Region
2101 Webster Street, Suite 500
Oakland, CA 94612

Re: Former Chevron Service Station #9-3864
5101 Telegraph Avenue, Oakland, CA

Dear Dr. Arulanantham:

Enclosed is the First Quarter Groundwater Monitoring Report for 1997, that was prepared by our consultant Blaine Tech Services, Inc. for the above noted site. Ground water samples were collected and analyzed for TPH-g, BTEX and MtBE constituents.

Concentrations of dissolved TPH-g, BTEX and MtBE constituents were below method detection limits for monitoring wells MW-1, MW-2, and MW-5. Benzene constituents decreased in monitoring wells C-3 and increased slightly in wells MW-3 and MW-4. Note that monitoring well MW-4 is upgradient of the site.

Depth to ground water varied from 10.92 to 15.45 feet below grade, with a direction of flow southwesterly.

Note that monitoring wells C-1, C-2 and C-4 have been abandoned due to proposed development of the site and as approved in Susan Hugo's, ACHCS, letter of February 24,1997.

Since monitoring wells MW-2 and MW-5 are crossgradient of the site, and have been below method detection limits for the TPH-g and BTEX constituents for at least the last eight quarters, and six quarters for the MtBE constituent, Chevron requests that these wells be sampled annually. Chevron would continue to sample the remaining wells quarterly. If you have any questions or comments, call me at (510) 842-9136.

Sincerely,
CHEVRON PRODUCTS COMPANY

Philip R. Briggs
Site Assessment and Remediation Project Manger

Enclosure

cc. Mr. Bette Owen, Chevron

Ms. Susan Hugo
Alameda County Health Care Services
Department of Environmental Health
1131 Harbor Bay Parkway, Suite 250
Alameda, CA 94502-6577

Mr. Howard Schindler and Mr. Saul Gevertz & Mr. Jon Eager
Temescal Triangle Investors
4179 Piedmont Avenue
Oakland, CA 94611

Mr. Breece Sloan
2057 Vanderslice Avenue
Walnut Creek, CA 94596

Mr. John Gwynn
Gwynn-Schields & Associates
300 Lakeside Drive, Suite 1980
Oakland, CA 94612

BLAINE
TECH SERVICES inc.

1680 ROGERS AVENUE
SAN JOSE, CALIFORNIA 95112
(408) 573-7771 FAX
(408) 573-0555 PHONE

April 29, 1997

Phil Briggs
Chevron U.S.A. Products Company
P.O. Box 6004
San Ramon, CA 94583-0904

1st Quarter 1997 Monitoring at 9-3864

First Quarter 1997 Groundwater Monitoring at
Chevron Service Station Number 9-3864
5101 Telegraph Avenue
Oakland, CA

Monitoring Performed on March 31, 1997

Groundwater Sampling Report **970331-J-1**

This report covers the routine quarterly monitoring of groundwater wells at this Chevron facility. Blaine Tech Services, Inc.'s work at the site includes inspection, gauging, evacuation, purgewater containment, sample collection and sample handling in accordance with standard procedures that conform to Regional Water Quality Control Board requirements.

Routine field data collection includes depth to water, total well depth, thickness of any separate immiscible layer, water column volume, calculated volume of a three-case volume purge, elapsed evacuation time, total volume of water removed, and standard water parameter instrument readings. Sample material is collected, contained, stored, and transported to the laboratory in conformance with EPA standards. Purgewater is, likewise, collected and transported to McKittrick Waste Treatment Site for disposal.

Basic field information is presented alongside analytical values excerpted from the laboratory report in the cumulative table of **WELL DATA AND ANALYTICAL RESULTS.** The full analytical report for the most recent samples is located in the **Analytical Appendix.** The table

also contains new groundwater elevation calculations taken from the computer plotted gradient map which is located in the **Professional Engineering Appendix.**

At a minimum, Blaine Tech Services, Inc. field personnel are certified upon completion of a forty-hour Hazardous Materials and Emergency Response training course per 29 CFR 1910.120. Field personnel are also enrolled in annual eight hour refresher courses.

Blaine Tech Services, Inc. conducts sampling and documentation assignments of this type as an independent third party. In order to avoid compromising the objectivity necessary for the proper and disinterested performance of this work, Blaine Tech Services, Inc. concentrates on objective data collection and does not participate in the interpretation of analytical results, the definition of geological or hydrological conditions, the formulation of recommendations, or the marketing of remedial systems.

Please call if you have any questions.

Yours truly,

Francis Thie
Vice President

FPT/cg

attachments: Professional Engineering Appendix
Cumulative Table of Well Data and Analytical Results
Analytical Appendix
Field Data Sheets

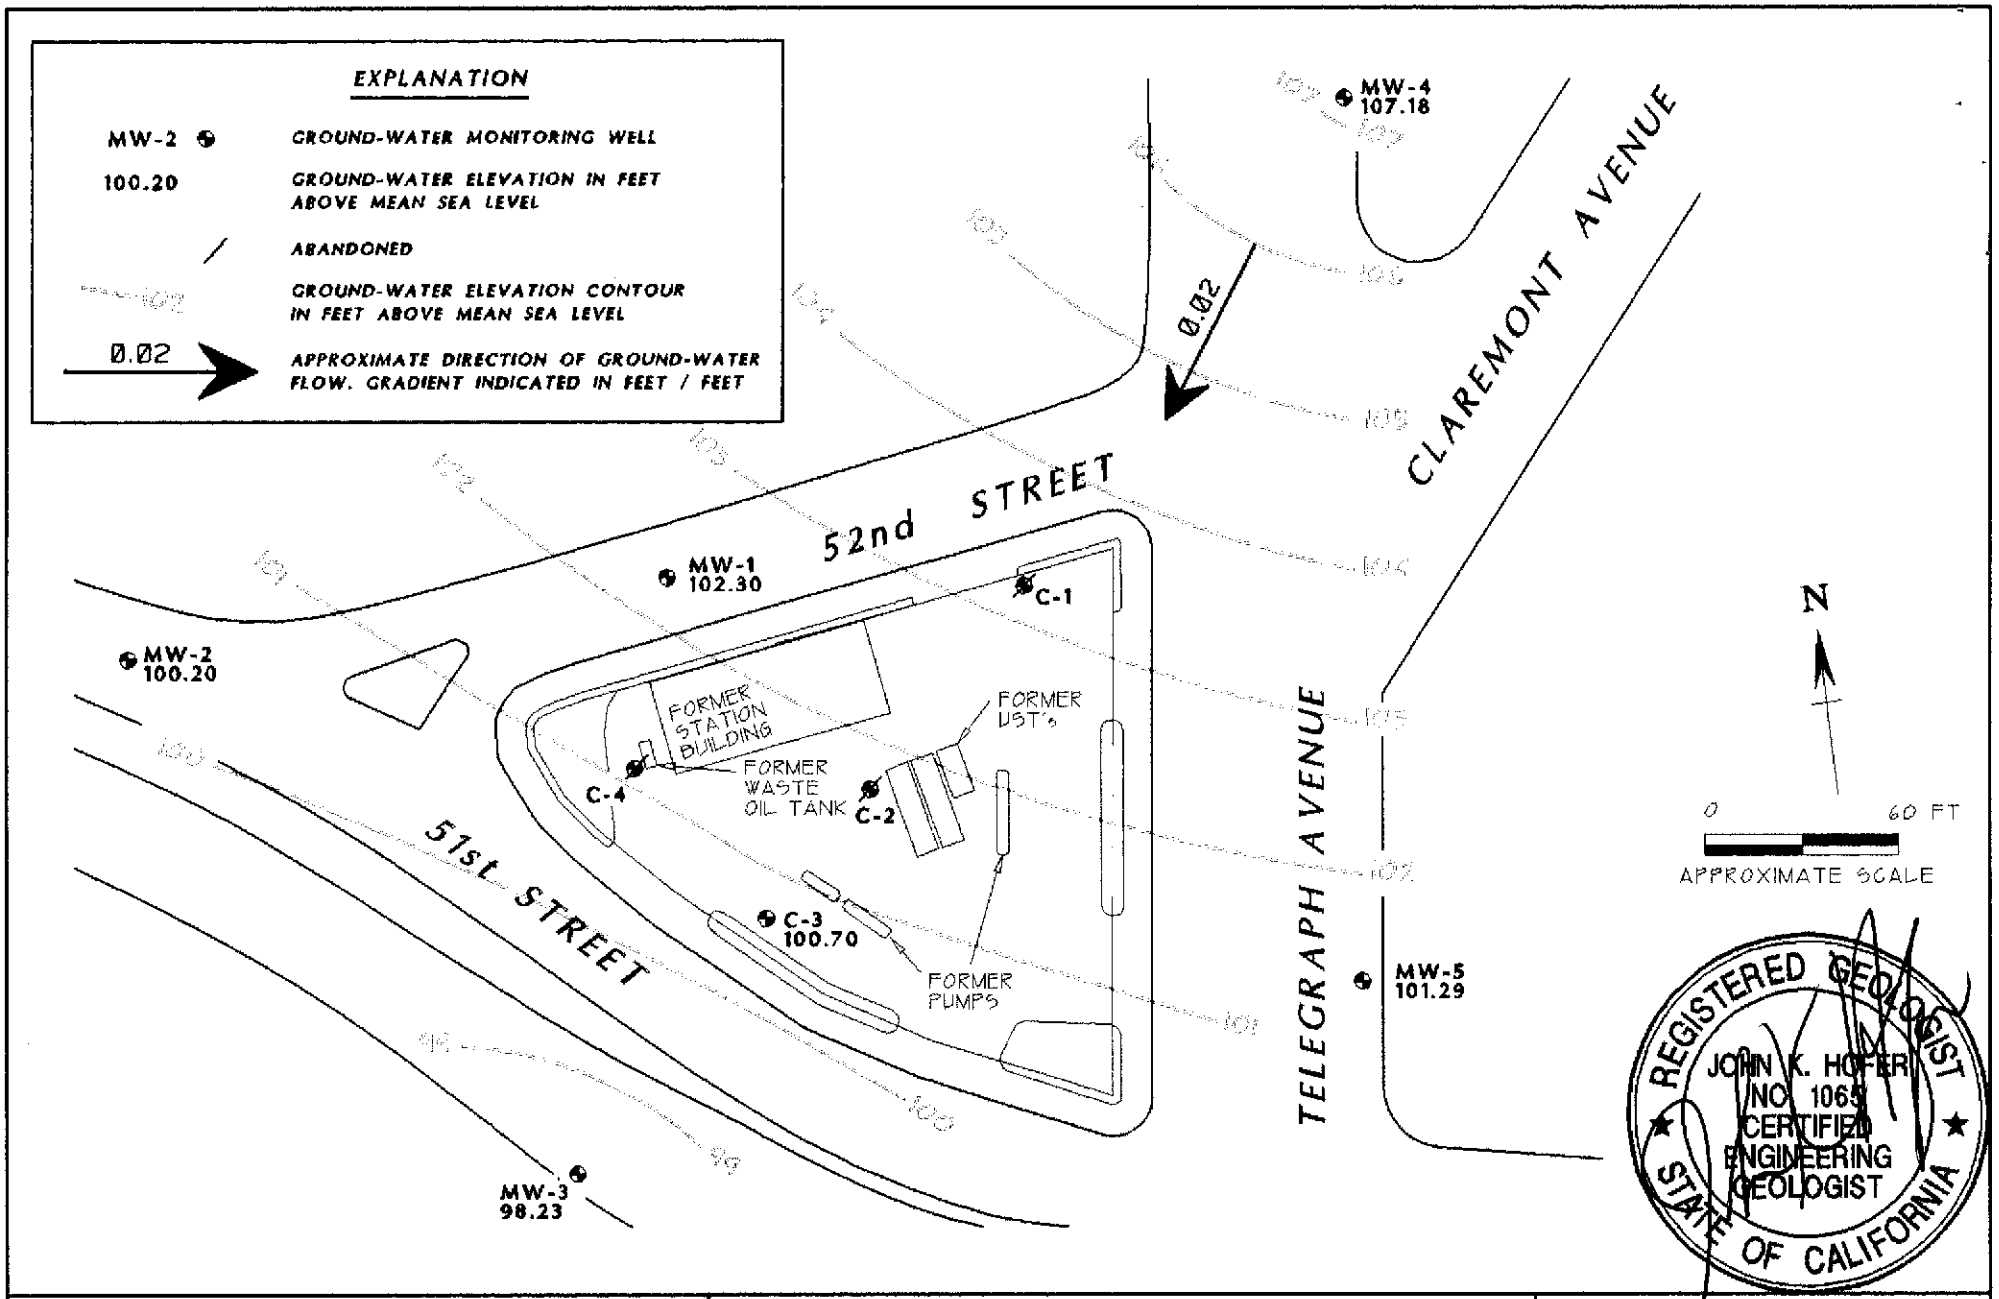

NOTES:

TITLE : GROUND-WATER ELEVATION CONTOUR MAP - MARCH 31, 1997

LOCATION : FORMER CHEVRON SERVICE STATION 9-3864
5101 TELEGRAPH AVENUE, OAKLAND, CALIFORNIA

SOURCE : CAMBRIA ENVIRONMENTAL TECHNOLOGY, INC.

GEOCONSULTANTS, INC
SAN JOSE, CALIFORNIA
Project No. G758-09
DRWG NO: W033197 REV:

Table of
Well Data and
Analytical Results

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE
C-1										
12/06/90	117.45	102.11	15.34	--	1900	17	11	3.0	21	--
06/06/91	117.45	102.83	14.62	--	3400	21	15	11	18	--
12/04/91	117.45	102.97	14.48	--	2700	22	16	13	23	--
06/02/92	117.45	102.92	14.53	--	1900	170	170	13	83	--
09/16/92	117.45	102.52	14.93	--	810	5.8	5.7	2.0	6.3	--
12/21/92	117.45	103.72	13.73	--	75	2.4	2.9	1.4	4.7	--
03/11/93	117.45	103.62	13.83	--	150	2.4	20	3.3	23	--
06/11/93	117.45	103.26	14.19	--	400	4.3	2.3	1.0	3.5	--
09/13/93	117.45	102.85	14.60	--	4100	62	43	34	57	--
12/14/93	117.45	103.67	13.78	--	3100	9.5	4.5	1.2	11	--
03/16/94	117.45	103.44	14.01	--	410	6.3	3.1	1.3	4.5	--
06/17/94	117.45	102.90	14.55	--	3700	100	42	30	91	--
08/29/94	117.45	102.96	14.49	--	2600	15	<0.5	6.7	9.7	--
12/06/94	117.45	104.04	13.41	--	510	2.0	2.2	1.7	9.4	--
03/31/95	117.45	105.33	12.12	--	5440	9.0	2.3	2.0	3.6	--
06/24/95	117.45	103.45	14.00	--	260	5.8	1.0	0.94	0.88	--
09/12/95	117.45	103.42	14.03	--	650	14	1.1	1.6	2.4	--
12/29/95	117.45	104.50	12.95	--	990	32	6.3	4.0	3.2	46
02/29/96	117.45	105.27	12.18	--	840	2.5	<1.0	2.6	7.3	<5.0
06/26/96	117.45	103.72	13.73	--	290	3.6	0.73	1.0	1.1	9.9
09/12/96	117.45	103.32	14.13	--	1200	17	1.8	4.0	4.4	24
12/11/96	117.45	104.66	12.79	--	7700	<10	53	19	44	87
03/31/97	117.45	--	--	Abandoned	--	--	--	--	--	--

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE
C-2										
12/06/90	116.16	100.82	15.34	--	210	140	9.0	2.0	11	--
06/06/91	116.16	101.54	14.62	--	4800	340	23	19	23	--
12/04/91	116.16	100.73	15.43	--	3900	85	15	9.1	15	--
06/02/92	116.16	101.74	14.42	--	3300	76	9.2	14	15	--
09/16/92	116.16	101.35	14.81	--	3000	16	15	3.4	7.5	--
12/21/92	116.16	102.79	13.37	--	2200	21	12	7.1	15	--
03/11/93	116.16	102.69	13.47	--	2200	33	24	12	25	--
06/11/93	116.16	102.18	13.98	--	2600	21	25	11	26	--
09/13/93	116.16	101.61	14.55	--	2100	31	25	18	39	--
12/14/93	116.16	102.46	13.70	--	3800	<2.5	24	12	20	--
03/16/94	116.16	102.51	13.65	--	2600	12	15	10	17	--
06/17/94	116.16	102.87	13.29	--	2400	17	19	28	71	--
08/29/94	116.16	111.60	4.56	--	3000	29	15	20	4.2	--
12/06/94	116.16	102.98	13.18	--	1900	7.9	30	14	31	--
03/31/95	116.16	104.10	12.06	--	890	<1.3	<1.3	2.6	<1.3	--
06/24/95	116.16	102.19	13.97	--	730	4.8	<0.5	5.4	0.96	--
09/12/95	116.16	102.28	13.88	--	1600	<2.5	<2.5	5.4	<2.5	--
12/29/95	116.16	103.31	12.85	--	1000	9.1	2.7	8.7	2.7	19
02/29/96	116.16	104.09	12.07	--	850	<2.5	<2.5	8.7	11	<12
06/26/96	116.16	102.50	13.66	--	2500	14	<5.0	13	6.3	<25
09/12/96	116.16	102.25	13.91	--	1800	26	19	17	31	37
12/11/96	116.16	103.82	12.34	--	2800	<5.0	34	14	<5.0	41
03/31/97	116.16	--	--	Abandoned	--	--	--	--	--	--

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE
C-3										
12/06/90	115.70	98.84	16.86	--	210	2.0	<0.5	<0.5	1.0	--
12/06/90	115.70	--	--	Duplicate	220	2.0	0.6	<0.5	2.0	--
06/06/91	115.70	100.01	15.69	--	6400	310	21	16	21	--
09/16/92	115.70	99.81	15.89	--	7100	130	26	12	30	--
12/04/91	115.70	100.32	15.38	--	5100	120	18	17	20	--
06/02/92	115.70	100.30	15.40	--	6700	140	44	17	37	--
12/21/92	115.70	101.79	13.91	--	13,000	390	360	100	410	--
03/11/93	115.70	101.95	13.75	--	5100	86	20	12	23	--
06/11/93	115.70	101.03	14.67	--	7200	91	38	19	38	--
09/13/93	115.70	100.17	15.53	--	6800	100	52	41	75	--
12/14/93	115.70	101.30	14.40	--	8600	74	23	18	36	--
03/16/94	115.70	101.44	14.26	--	6000	100	42	27	30	--
06/17/94	115.70	100.60	15.10	--	15,000	170	120	120	270	--
08/29/94	115.70	100.30	15.40	--	26,000	51	<0.5	58	107	--
12/06/94	115.70	101.90	13.80	--	34,000	88	140	98	390	--
03/31/95	115.70	102.91	12.79	--	2800	42	<5.0	<5.0	6.6	--
06/24/95	115.70	100.84	14.86	--	5200	34	<10	<10	13	--
09/12/95	115.70	100.76	14.94	--	7000	45	<10	28	42	--
12/29/95	115.70	102.12	13.58	--	5100	20	<10	<10	19	<50
02/29/96	115.70	102.88	12.82	--	2600	15	<5.0	17	16	<25
06/26/96	115.70	101.32	14.38	--	4400	<10	<10	<10	<10	<50
09/12/96	115.70	100.75	14.95	--	5800	73	22	18	17	61
12/11/96	115.70	103.08	12.62	--	8800	81	<20	<20	37	200
03/31/97	115.70	100.70	15.00	--	8100	38	62	30	42	38

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE
C-4										
12/06/90	116.10	98.42	17.68	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/18/90	116.10	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/06/91	116.10	99.61	16.49	--	<50	1.0	1.0	<0.5	0.7	--
12/04/91	116.10	99.28	16.82	--	70	6.5	9.8	1.7	8.6	--
06/02/92	116.10	99.18	16.92	--	70	3.0	4.4	1.8	9.0	--
09/16/92	116.10	98.39	17.71	--	<50	1.4	1.8	<0.5	1.1	--
12/21/92	116.10	100.74	15.36	--	<50	0.6	0.7	<0.5	1.5	--
03/11/93	116.10	100.61	15.49	--	<50	<0.5	<0.5	<0.5	<1.5	--
06/11/93	116.10	99.83	16.27	--	52	0.9	3.1	0.7	3.8	--
09/13/93	116.10	98.92	17.18	--	64	0.9	1.0	<0.5	1.7	--
12/14/93	116.10	101.03	15.07	--	<50	<0.5	0.8	<0.5	0.7	--
03/16/94	116.10	100.19	15.91	--	<50	<0.5	1.0	<0.5	0.8	--
06/17/94	116.10	99.46	16.64	--	230	0.6	2.2	2.2	11	--
08/29/94	116.10	99.05	17.05	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/06/94	116.10	101.52	14.58	--	<50	<0.5	<0.5	<0.5	<0.5	--
03/31/95	116.10	102.26	13.84	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/24/95	116.10	100.05	16.05	--	<50	<0.5	<0.5	<0.5	<0.5	--
09/12/95	116.10	99.87	16.23	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/29/95	116.10	101.35	14.75	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
02/29/96	116.10	102.40	13.70	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
06/26/96	116.10	100.30	15.80	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
09/12/96	116.10	99.67	16.43	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
12/11/96	116.10	103.18	12.92	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
03/31/97	116.10	--	--	Abandoned	--	--	--	--	--	--

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE
MW-1										
09/20/93	115.05	102.37	12.68	--	<50	<0.5	<0.5	<0.5	<1.5	--
12/14/93	115.05	105.01	10.04	--	<50	<0.5	<0.5	<0.5	<0.5	--
03/16/94	115.05	103.10	11.95	--	<50	<0.5	1.7	<0.5	2.1	--
06/17/94	115.05	102.51	12.54	--	350	1.2	3.7	2.0	12	--
08/29/94	115.05	101.98	13.07	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/06/94	115.05	104.45	10.60	--	140	0.9	2.8	1.1	4.2	--
03/31/95	115.05	104.74	10.31	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/24/95	115.05	102.44	12.61	--	<50	<0.5	<0.5	<0.5	<0.5	--
09/12/95	115.05	102.00	13.05	--	<50	<0.5	<0.5	<0.5	<0.5	--
02/02/96	115.05	106.19	8.86	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
02/29/96	115.05	105.39	9.66	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
06/26/96	115.05	102.85	12.20	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
09/12/96	115.05	101.55	13.50	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
12/11/96	115.05	105.90	9.15	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
03/31/97	115.05	102.30	12.75	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
MW-2										
09/20/93	112.08	99.93	12.15	--	<50	<0.5	<0.5	<0.5	<1.5	--
12/14/93	112.08	97.36	14.72	--	<50	<0.5	<0.5	<0.5	<0.5	--
03/16/94	112.08	100.92	11.16	--	<50	<0.5	1.1	<0.5	0.9	--
06/17/94	112.08	100.41	11.67	--	330	1.4	3.3	1.9	11	--
08/29/94	112.08	100.08	12.00	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/06/94	112.08	102.57	9.51	--	<50	<0.5	<0.5	<0.5	<0.5	--
03/31/95	112.08	103.24	8.84	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/24/95	112.08	100.44	11.64	--	<50	<0.5	<0.5	<0.5	<0.5	--
09/12/95	112.08	100.00	12.08	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/29/95	112.08	101.58	10.50	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
02/29/96	112.08	104.08	8.00	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
06/26/96	112.08	100.58	11.50	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
09/12/96	112.08	99.81	12.27	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
12/11/96	112.08	104.17	7.91	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
03/31/97	112.08	100.20	11.88	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE
MW-3										
09/20/93	113.67	97.25	16.42	--	6600	400	11	32	23	--
12/14/93	113.67	98.95	14.72	--	8400	390	9.4	13	<2.5	--
03/16/94	113.67	98.45	15.22	--	6900	260	30	32	27	--
06/17/94	113.67	97.62	16.05	--	10,000	190	61	58	190	--
08/29/94	113.67	97.44	16.23	--	7200	74	9.8	26	24	--
12/06/94	113.67	99.35	14.32	--	13,000	610	86	88	140	--
03/31/95	113.67	99.98	13.69	--	4300	120	<10	12	<10	--
06/24/95	113.67	98.02	15.65	--	6200	210	24	29	12	--
09/12/95	113.67	97.68	15.99	--	7200	190	<20	<20	<20	--
12/29/95	113.67	99.67	14.00	--	7100	200	<10	45	24	<50
02/29/96	113.67	100.91	12.76	--	1200	30	<5.0	<5.0	<5.0	<25
06/26/96	113.67	98.44	15.23	--	7900	180	<20	35	28	240
09/12/96	113.67	97.73	15.94	--	11,000	150	<5.0	35	28	170
12/11/96	113.67	99.86	13.81	--	7500	75	8.8	30	45	110
03/31/97	113.67	98.23	15.44	--	8700	100	<10	20	23	50
MW-4										
09/20/93	118.10	107.17	10.93	--	5800	16	4.2	35	48	--
12/14/93	118.10	108.33	9.77	--	7100	19	6.5	24	35	--
03/16/94	118.10	107.99	10.11	--	8500	83	43	60	70	--
06/17/94	118.10	107.20	10.90	--	21,000	150	20	140	350	--
08/29/94	118.10	107.28	10.82	--	10,000	86	71	44	85	--
12/06/94	118.10	108.70	9.40	--	13,000	68	56	67	110	--
03/31/95	118.10	109.31	8.79	--	6700	100	9.4	26	23	--
06/24/95	118.10	107.60	10.50	--	6300	<20	<20	<20	24	--
09/12/95	118.10	107.90	10.20	--	7100	65	16	<10	21	--
12/29/95	118.10	108.86	9.24	--	3300	<10	<10	12	14	720
02/29/96	118.10	111.85	6.25	--	5100	<10	37	23	21	85
06/26/96	118.10	107.92	10.18	--	6800	<20	<20	<20	<20	<100
09/12/96	118.10	107.53	10.57	--	13,000	150	<10	38	35	240
12/11/96	118.10	109.39	8.71	--	26,000	<20	<20	<20	170	<100
03/31/97	118.10	107.18	10.92	--	12,000	120	74	45	70	240

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE
MW-5										
09/20/93	116.74	101.43	15.31	--	590	25	1.8	0.6	2.0	--
12/14/93	116.74	102.19	14.55	--	210	11	6.3	2.3	6.1	--
03/16/94	116.74	101.77	14.97	--	270	12	16	4.8	17	--
06/17/94	116.74	101.36	15.38	--	220	24	17	6.7	28	--
08/29/94	116.74	101.54	15.20	--	1000	<0.5	<0.5	<0.5	<0.5	--
12/06/94	116.74	102.09	14.65	--	110	9.2	9.7	2.2	11	--
03/31/95	116.74	103.04	13.70	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/24/95	116.74	101.95	14.79	--	<50	<0.5	<0.5	<0.5	<0.5	--
09/12/95	116.74	102.15	14.59	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/29/95	116.74	101.76	14.98	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
02/29/96	116.74	103.07	13.67	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
06/26/96	116.74	102.50	14.24	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
09/12/96	116.74	102.12	14.62	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
12/11/96	116.74	102.93	13.81	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
03/31/97	116.74	101.29	15.45	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5

Cumulative Table of Well Data and Analytical Results

Vertical Measurements are in feet. Analytical results are in parts per billion (ppb)

DATE	Well Head Elev.	Ground Water Elev.	Depth To Water	Notes	TPH-Gasoline	Benzene	Toluene	Ethyl-Benzene	Xylene	MTBE
TRIP BLANK										
12/06/90	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/18/90	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/06/91	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/04/91	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/02/92	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
09/16/92	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/21/92	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
03/11/93	--	--	--	--	<50	<0.5	<0.5	<0.5	<1.5	--
06/11/93	--	--	--	--	<50	<0.5	<0.5	<0.5	<1.5	--
09/13/93	--	--	--	--	<50	<0.5	<0.5	<0.5	<1.5	--
12/14/93	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
03/16/94	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/17/94	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
08/29/94	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/06/94	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
03/31/95	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
06/24/95	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
09/12/95	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/29/95	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
02/29/96	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
06/26/96	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
09/12/96	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	--
12/11/96	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5
03/31/97	--	--	--	--	<50	<0.5	<0.5	<0.5	<0.5	<2.5

Note: Blaine Tech Services, Inc. began routine monitoring of the groundwater wells at this site on March 31, 1995. Earlier field data and analytical results provided by Sierra Environmental.

ABBREVIATIONS:
TPH = Total Petroleum Hydrocarbons
MTBE = Methyl t-butyl ether

Analytical Appendix

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services	Client Proj. ID: Chevron 9-3864/970331-J1	Sampled: 03/31/97
1680 Rogers Avenue	Sample Descript: C-3	Received: 04/01/97
San Jose, CA 95112	Matrix: LIQUID	
	Analysis Method: 8015Mod/8020	Analyzed: 04/07/97
Attention: Fran Thie	Lab Number: 9704056-01	Reported: 04/09/97

QC Batch Number: GC040797BTEX06A
Instrument ID: GCHP06

Total Purgeable Petroleum Hydrocarbons (TPPH) with BTEX and MTBE

Analyte	Detection Limit ug/L	Sample Results ug/L
TPPH as Gas	**500**	**8100**
Methyl t-Butyl Ether	**25**	**38**
Benzene	**5.0**	**38**
Toluene	**5.0**	**62**
Ethyl Benzene	**5.0**	**30**
Xylenes (Total)	**5.0**	**42**
Chromatogram Pattern:		**Gas**

Surrogates	Control Limits %		% Recovery
Trifluorotoluene	70	130	427 Q

Analytes reported as N.D. were not present above the stated limit of detection.

SEQUOIA ANALYTICAL - ELAP #1210

Peggy Penner
Project Manager

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services	Client Proj. ID: Chevron 9-3864/970331-J1	Sampled: 03/31/97
1680 Rogers Avenue	Sample Descript: MW-1	Received: 04/01/97
San Jose, CA 95112	Matrix: LIQUID	
	Analysis Method: 8015Mod/8020	Analyzed: 04/04/97
Attention: Fran Thie	Lab Number: 9704056-02	Reported: 04/09/97

QC Batch Number: GC040497BTEX06A
Instrument ID: GCHP06

Total Purgeable Petroleum Hydrocarbons (TPPH) with BTEX and MTBE

Analyte	Detection Limit ug/L	Sample Results ug/L
TPPH as Gas	50	N.D.
Methyl t-Butyl Ether	2.5	N.D.
Benzene	0.50	N.D.
Toluene	0.50	N.D.
Ethyl Benzene	0.50	N.D.
Xylenes (Total)	0.50	N.D.
Chromatogram Pattern:		

Surrogates	Control Limits %		% Recovery
Trifluorotoluene	70	130	74

Analytes reported as N.D. were not present above the stated limit of detection.

SEQUOIA ANALYTICAL - ELAP #1210

Peggy Penner
Project Manager

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services	Client Proj. ID: Chevron 9-3864/970331-J1	Sampled: 03/31/97
1680 Rogers Avenue	Sample Descript: MW-2	Received: 04/01/97
San Jose, CA 95112	Matrix: LIQUID	
	Analysis Method: 8015Mod/8020	Analyzed: 04/04/97
Attention: Fran Thie	Lab Number: 9704056-03	Reported: 04/09/97

QC Batch Number: GC040497BTEX06A
Instrument ID: GCHP06

Total Purgeable Petroleum Hydrocarbons (TPPH) with BTEX and MTBE

Analyte	Detection Limit ug/L	Sample Results ug/L
TPPH as Gas	50	N.D.
Methyl t-Butyl Ether	2.5	N.D.
Benzene	0.50	N.D.
Toluene	0.50	N.D.
Ethyl Benzene	0.50	N.D.
Xylenes (Total)	0.50	N.D.
Chromatogram Pattern:		

Surrogates	Control Limits %		% Recovery
Trifluorotoluene	70	130	74

Analytes reported as N.D. were not present above the stated limit of detection.

SEQUOIA ANALYTICAL - ELAP #1210

Peggy Renner
Project Manager

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services	Client Proj. ID: Chevron 9-3864/970331-J1	Sampled: 03/31/97
1680 Rogers Avenue	Sample Descript: MW-3	Received: 04/01/97
San Jose, CA 95112	Matrix: LIQUID	
	Analysis Method: 8015Mod/8020	Analyzed: 04/07/97
Attention: Fran Thie	Lab Number: 9704056-04	Reported: 04/09/97

QC Batch Number: GC040797BTEX06A
Instrument ID: GCHP06

Total Purgeable Petroleum Hydrocarbons (TPPH) with BTEX and MTBE

Analyte	Detection Limit ug/L	Sample Results ug/L
TPPH as Gas	**1000**	**8700**
Methyl t-Butyl Ether	**50**	**50**
Benzene	**10**	**100**
Toluene	10	N.D.
Ethyl Benzene	**10**	**20**
Xylenes (Total)	**10**	**23**
Chromatogram Pattern:		**Gas**

Surrogates	Control Limits %		% Recovery
Trifluorotoluene	70	130	103

Analytes reported as N.D. were not present above the stated limit of detection.

SEQUOIA ANALYTICAL - ELAP #1210

Peggy Penner
Project Manager

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services	Client Proj. ID: Chevron 9-3864/970331-J1	Sampled: 03/31/97
1680 Rogers Avenue	Sample Descript: MW-4	Received: 04/01/97
San Jose, CA 95112	Matrix: LIQUID	
	Analysis Method: 8015Mod/8020	Analyzed: 04/07/97
Attention: Fran Thie	Lab Number: 9704056-05	Reported: 04/09/97

QC Batch Number: GC040797BTEX18A
Instrument ID: GCHP18

Total Purgeable Petroleum Hydrocarbons (TPPH) with BTEX and MTBE

Analyte	Detection Limit ug/L	Sample Results ug/L
TPPH as Gas	1000	12000
Methyl t-Butyl Ether	50	240
Benzene	10	120
Toluene	10	74
Ethyl Benzene	10	45
Xylenes (Total)	10	70
Chromatogram Pattern:		Gas

Surrogates	Control Limits %		% Recovery
Trifluorotoluene	70	130	480 Q

Analytes reported as N.D. were not present above the stated limit of detection.

SEQUOIA ANALYTICAL - ELAP #1210

Peggy Penner
Project Manager

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services
1680 Rogers Avenue
San Jose, CA 95112

Attention: Fran Thie

Client Proj. ID: Chevron 9-3864/970331-J1
Sample Descript: MW-5
Matrix: LIQUID
Analysis Method: 8015Mod/8020
Lab Number: 9704056-06

Sampled: 03/31/97
Received: 04/01/97

Analyzed: 04/04/97
Reported: 04/09/97

QC Batch Number: GC040497BTEX06A
Instrument ID: GCHP06

Total Purgeable Petroleum Hydrocarbons (TPPH) with BTEX and MTBE

Analyte	Detection Limit ug/L	Sample Results ug/L
TPPH as Gas	50	N.D.
Methyl t-Butyl Ether	2.5	N.D.
Benzene	0.50	N.D.
Toluene	0.50	N.D.
Ethyl Benzene	0.50	N.D.
Xylenes (Total)	0.50	N.D.
Chromatogram Pattern:		

Surrogates	Control Limits %		% Recovery
Trifluorotoluene	70	130	72

Analytes reported as N.D. were not present above the stated limit of detection.

SEQUOIA ANALYTICAL - ELAP #1210

Peggy Penner
Project Manager

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services
1680 Rogers Avenue
San Jose, CA 95112

Attention: Fran Thie

Client Proj. ID: Chevron 9-3864/970331-J1
Sample Descript: TB
Matrix: LIQUID
Analysis Method: 8015Mod/8020
Lab Number: 9704056-07

Sampled: 03/31/97
Received: 04/01/97

Analyzed: 04/04/97
Reported: 04/09/97

QC Batch Number: GC040497BTEX06A
Instrument ID: GCHP06

Total Purgeable Petroleum Hydrocarbons (TPPH) with BTEX and MTBE

Analyte	Detection Limit ug/L	Sample Results ug/L
TPPH as Gas	50	N.D.
Methyl t-Butyl Ether	2.5	N.D.
Benzene	0.50	N.D.
Toluene	0.50	N.D.
Ethyl Benzene	0.50	N.D.
Xylenes (Total)	0.50	N.D.
Chromatogram Pattern:		

Surrogates	Control Limits %		% Recovery
Trifluorotoluene	70	130	76

Analytes reported as N.D. were not present above the stated limit of detection.

SEQUOIA ANALYTICAL - ELAP #1210

Peggy Penner
Project Manager

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services 1680 Rogers Avenue San Jose, CA 95112 Attention: Fran Thie	Client Proj. ID: Chevron 9-3864/970331-J1 Lab Proj. ID: 9704056	Received: 04/01/97 Reported: 04/09/97

LABORATORY NARRATIVE

In order to properly interpret this report, it must be reproduced in its entirety. This report contains a total of 11 pages including the laboratory narrative, sample results, quality control, and related documents as required (cover page, COC, raw data, etc.).

TPPH Note: Sample 9704056-01 was diluted 10-fold.
Sample 9704056-04 was diluted 20-fold.
Sample 9704056-05 was diluted 20-fold.

SEQUOIA ANALYTICAL

Peggy Penner
Project Manager

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services, Inc.
1680 Rogers Avenue
San Jose, CA 95112
Attention: Fran Thie

Client Project ID: Chevron 9-3864/970331-J1
Matrix: Liquid
Work Order #: 9704056 -01, -04

Reported: Apr 14, 1997

QUALITY CONTROL DATA REPORT

Analyte:	Benzene	Toluene	Ethyl Benzene	Xylenes	Gas
QC Batch#:	GC040797BTEX06A	GC040797BTEX06A	GC040797BTEX06A	GC040797BTEX06A	GC040797BTEX06A
Analy. Method:	EPA 8020	EPA 8020	EPA 8020	EPA 8020	EPA 8015M
Prep. Method:	EPA 5030	EPA 5030	EPA 5030	EPA 5030	EPA 5030
Analyst:	A. Porter	A. Porter	A. Porter	A. Porter	A. Porter
MS/MSD #:	970405002	970405002	970405002	970405002	970405002
Sample Conc.:	N.D.	N.D.	N.D.	N.D.	N.D.
Prepared Date:	4/7/97	4/7/97	4/7/97	4/7/97	4/7/97
Analyzed Date:	4/7/97	4/7/97	4/7/97	4/7/97	4/7/97
Instrument I.D.#:	GCHP06	GCHP06	GCHP06	GCHP06	GCHP06
Conc. Spiked:	10µg/L	10µg/L	10µg/L	30 µg/L	60 µg./L
Result:	10	9.9	9.9	29	73
MS % Recovery:	100	99	99	97	122
Dup. Result:	9.9	9.9	10	29	79
MSD % Recov.:	99	99	100	97	132
RPD:	1.0	0.0	1.0	0.0	7.9
RPD Limit:	0-25	0-25	0-25	0-25	0-25
LCS #:	BLK040797	BLK040797	BLK040797	BLK040797	BLK040797
Prepared Date:	4/7/97	4/7/97	4/7/97	4/7/97	4/7/97
Analyzed Date:	4/7/97	4/7/97	4/7/97	4/7/97	4/7/97
Instrument I.D.#:	GCHP06	GCHP06	GCHP06	GCHP06	GCHP06
Conc. Spiked:	10µg/L	10µg/L	10µg/L	30 µg/L	60 µg./L
LCS Result:	9.4	9.4	9.4	28	75
LCS % Recov.:	94	94	94	93	125
MS/MSD Control Limits	60-140	60-140	60-140	60-140	60-140
LCS Control Limits	70-130	70-130	70-130	70-130	70-130

SEQUOIA ANALYTICAL

Peggy Penner
Project Manager

Please Note:
The LCS is a control sample of known, interferent-free matrix that is analyzed using the same reagents, preparation, and analytical methods employed for the samples. The matrix spike is an aliquot of sample fortified with known quantities of specific compounds and subjected to the entire analytical procedure. If the recovery of analytes from the matrix spike does not fall within specified control limits due to matrix interference, the LCS recovery is to be used to validate the batch.

** MS = Matrix Spike, MSD = MS Duplicate, RPD = Relative % Difference

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services, Inc.
1680 Rogers Avenue
San Jose, CA 95112
Attention: Fran Thie

Client Project ID: Chevron 9-3864/970331-J1
Matrix: Liquid
Work Order #: 9704056-02-03, -06-07

Reported: Apr 14, 1997

QUALITY CONTROL DATA REPORT

Analyte:	Benzene	Toluene	Ethyl Benzene	Xylenes	Gas
QC Batch#:	GC040497BTEX06A	GC040497BTEX06A	GC040497BTEX06A	GC040497BTEX06A	GC040497BTEX06A
Analy. Method:	EPA 8020	EPA 8020	EPA 8020	EPA 8020	EPA 8015M
Prep. Method:	EPA 5030	EPA 5030	EPA 5030	EPA 5030	EPA 5030
Analyst:	R. Geckler	R. Geckler	R. Geckler	R. Geckler	R. Geckler
MS/MSD #:	9703G1205	9703G1205	9703G1205	9703G1205	9703G1205
Sample Conc.:	N.D.	N.D.	N.D.	N.D.	N.D.
Prepared Date:	4/4/97	4/4/97	4/4/97	4/4/97	4/4/97
Analyzed Date:	4/4/97	4/4/97	4/4/97	4/4/97	4/4/97
Instrument I.D.#:	GCHP06	GCHP06	GCHP06	GCHP06	GCHP06
Conc. Spiked:	10µg/L	10µg/L	10µg/L	30 µg/L	60 µg./L
Result:	9.7	9.7	9.7	29	81
MS % Recovery:	97	97	97	97	135
Dup. Result:	10	9.8	9.8	29	81
MSD % Recov.:	100	98	98	97	135
RPD:	3.0	1.0	1.0	0.0	0.0
RPD Limit:	0-25	0-25	0-25	0-25	0-25
LCS #:	BLK040497	BLK040497	BLK040497	BLK040497	BLK040497
Prepared Date:	4/4/97	4/4/97	4/4/97	4/4/97	4/4/97
Analyzed Date:	4/4/97	4/4/97	4/4/97	4/4/97	4/4/97
Instrument I.D.#:	GCHP06	GCHP06	GCHP06	GCHP06	GCHP06
Conc. Spiked:	10µg/L	10µg/L	10µg/L	30 µg/L	60 µg./L
LCS Result:	9.5	9.4	9.5	28	77
LCS % Recov.:	95	94	95	93	128
MS/MSD Control Limits	60-140	60-140	60-140	60-140	60-140
LCS Control Limits	70-130	70-130	70-130	70-130	70-130

SEQUOIA ANALYTICAL

Peggy Penner
Project Manager

Please Note:
The LCS is a control sample of known, interferent-free matrix that is analyzed using the same reagents, preparation, and analytical methods employed for the samples. The matrix spike is an aliquot of sample fortified with known quantities of specific compounds and subjected to the entire analytical procedure. If the recovery of analytes from the matrix spike does not fall within specified control limits due to matrix interference, the LCS recovery is to be used to validate the batch.

** MS = Matrix Spike, MSD = MS Duplicate, RPD = Relative % Difference

Sequoia Analytical

680 Chesapeake Drive, Redwood City, CA 94063, (415) 364-9600, FAX (415) 364-9233
404 N. Wiget Lane, Walnut Creek, CA 94598, (510) 988-9600, FAX (510) 988-9673
819 Striker Avenue, Suite 8, Sacramento, CA 95834, (916) 921-9600, FAX (916) 921-0100

Blaine Tech Services, Inc.
1680 Rogers Avenue
San Jose, CA 95112
Attention: Fran Thie

Client Project ID: Chevron 9-3864/970331-J1
Matrix: Liquid
Work Order #: 9704056-05

Reported: Apr 14, 1997

QUALITY CONTROL DATA REPORT

Analyte:	Benzene	Toluene	Ethyl Benzene	Xylenes	Gas
QC Batch#:	GC040797BTEX18A	GC040797BTEX18A	GC040797BTEX18A	GC040797BTEX18A	GC040797BTEX18A
Analy. Method:	EPA 8020	EPA 8020	EPA 8020	EPA 8020	EPA 8015M
Prep. Method:	EPA 5030	EPA 5030	EPA 5030	EPA 5030	EPA 5030
Analyst:	A. Porter	A. Porter	A. Porter	A. Porter	A. Porter
MS/MSD #:	970405602	970405602	970405602	970405602	970405602
Sample Conc.:	N.D.	N.D.	N.D.	N.D.	N.D.
Prepared Date:	4/7/97	4/7/97	4/7/97	4/7/97	4/7/97
Analyzed Date:	4/7/97	4/7/97	4/7/97	4/7/97	4/7/97
Instrument I.D.#:	GCHP18	GCHP18	GCHP18	GCHP18	GCHP18
Conc. Spiked:	10µg/L	10µg/L	10µg/L	30 µg/L	60 µg./L
Result:	8.9	8.9	8.8	26	62
MS % Recovery:	89	89	88	87	103
Dup. Result:	9.6	9.7	9.6	28	65
MSD % Recov.:	96	97	96	93	108
RPD:	7.6	8.6	8.7	7.4	4.7
RPD Limit:	0-25	0-25	0-25	0-25	0-25
LCS #:	BLK040797	BLK040797	BLK040797	BLK040797	BLK040797
Prepared Date:	4/7/97	4/7/97	4/7/97	4/7/97	4/7/97
Analyzed Date:	4/7/97	4/7/97	4/7/97	4/7/97	4/7/97
Instrument I.D.#:	GCHP18	GCHP18	GCHP18	GCHP18	GCHP18
Conc. Spiked:	10µg/L	10µg/L	10µg/L	30 µg/L	60 µg./L
LCS Result:	9.8	9.8	9.8	29	68
LCS % Recov.:	98	98	98	97	113
MS/MSD Control Limits	60-140	60-140	60-140	60-140	60-140
LCS Control Limits	70-130	70-130	70-130	70-130	70-130

SEQUOIA ANALYTICAL

Peggy Penner
Project Manager

Please Note:
The LCS is a control sample of known, interferent-free matrix that is analyzed using the same reagents, preparation, and analytical methods employed for the samples. The matrix spike is an aliquot of sample fortified with known quantities of specific compounds and subjected to the entire analytical procedure. If the recovery of analytes from the matrix spike does not fall within specified control limits due to matrix interference, the LCS recovery is to be used to validate the batch.

** MS = Matrix Spike, MSD = MS Duplicate, RPD = Relative % Difference

Chain of Custody Record

Chevron U.S.A. Inc.
P.O. BOX 5004
San Ramon, CA 94583
FAX (415)842-9591

Chevron Facility Number: 9-3864
Facility Address: 5101 Telegraph, Oakland, CA
Consultant Project Number: 970331-J1
Consultant Name: Blaine Tech Services, Inc.
Address: 1680 Rogers Ave., San Jose, CA 95112
Project Contact (Name): Fran Thie
(Phone) 408-573-0555 (Fax Number) 408-573-7771

Chevron Contact (Name): Phil Briggs
(Phone) (510) 842-9136
Laboratory Name: Sequoia
Laboratory Release Number: 9034826
Samples Collected by (Name): Matt Jamos
Collection Date: 3/31/97
Signature:

Sample Number	Lab Sample Number	Number of Containers	Matrix S = Soil W = Water A = Air C = Charcoal	Type G = Grab C = Composite D = Discrete	Time	Sample Preservation	Iced (Yes or No)	Analyses To Be Performed: BTEX + TPH GAS (8020 + 8015) / MTBE	TPH Diesel (8015)	Oil and Grease (5520)	Purgeable Halocarbons (8010)	Purgeable Aromatics (8020)	Purgeable Organics (8240)	Extractable Organics (8270)	Metals Cd,Cr,Pb,Zn,Ni (ICAP or AA)					Remarks
C-3	01	3	W	D	1145	HCl	Y	X												DO NOT BILL FOR TB-LB 970456
MW-1	02	3			1035			X												
MW-2	03	3			1055			X												
MW-3	04	3			1010			X												
MW-4	05	3			1120			X												TR 1 12 16
MW-5	06	3			940			X												
TB	07	2	↓	↓	—	↓	↓	X												

Relinquished By (Signature)	Organization	Date/Time	Received By (Signature)	Organization	Date/Time
	BTS	4/1/97 1022		SEQ	4/1/97 1022
Relinquished By (Signature)	Organization	Date/Time	Received By (Signature)	Organization	Date/Time
	SEQ	4/1/97 1200			
Relinquished By (Signature)	Organization	Date/Time	Received For Laboratory By (Signature)		Date/Time
			Maria Gruslis		4/1/97 1216

Turn Around Time (Circle Choice)
24 Hrs.
48 Hrs.
5 Days
10 Days
As Contracted

Field
Data
Sheets

WELL GAUGING DATA

Project # 970331J Date 3/31/97 Client Chev 9-3864

Site 5101 Telegraph Ave., Oakland

Well I.D.	Well Size (in.)	Sheen/ Odor	Depth to Immiscible Liquid (feet)	Thickness of Immiscible Liquid (ft.)	Volume of Immiscibles Removed (ml)	Depth to Water (feet)	Depth to Well Bottom (feet)	Survey Point: TOB or TOC
C-3	2					15.00	29.19	TOC
MW-1	2					12.75 ~~11.88~~	23.86 ~~29.60~~	
MW-2	2					11.88	29.60	
MW-3	2					15.44	26.88	
MW-4	2					10.92	21.44	
MW-5	2					15.45	21.59	

5

CHEVRON WELL MONITORING DATA SHEET

Project #: 970331-J1	Station #: 9-3864
Sampler: MS	Date: 3/31/97
Well I.D.: C-3	Well Diameter: (2) 3 4 6 8 ____
Total Well Depth: 29.19	Depth to Water: 15.00
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: (PVC) Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
2"	0.16	5"	1.02
3"	0.37	6"	1.47
4"	0.65	Other	radius² * 0.163

Purge Method: Bailer / Disposable Bailer X / Middleburg / Electric Submersible / Extraction Pump / Other: _____

Sampling Method: Bailer / Disposable Bailer X / Extraction Port / Other: _____

2.3 (1 Case Volume (Gals.)) x 3 (Specified Volumes) = 6.8 (Calculated Volume) Gals.

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
1136	64.8	6.6	390	25	
1139	65.4	6.5	370	5	
1142	66.0	6.4	360	7	

Did well dewater? Yes (No)		Gallons actually evacuated: 7	
Sampling Time: 1145		Sampling Date: 3/31	
Sample I.D.: C-3		Laboratory: (Sequoia) GTEL N. Creek Assoc. Labs	
Analyzed for: (TPH-G BTEX MTBE) TPH-D		Other:	
Duplicate I.D.:	Analyzed for: TPH-G BTEX MTBE TPH-D	Other:	
D.O. (if req'd):	Pre-purge:	mg/L	Post-purge: mg/L
O.R.P. (if req'd):	Pre-purge:	mV	Post-purge: mV

5

CHEVRON WELL MONITORING DATA SHEET

Project #: 970331-J1	Station #: 9-3864
Sampler: MS	Date: 3/31/97
Well I.D.: MW-1	Well Diameter: (2) 3 4 6 8 ___
Total Well Depth: 23.86	Depth to Water: 12.75
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: (PVC) Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
2"	0.16	5"	1.02
3"	0.37	6"	1.47
4"	0.65	Other	radius² * 0.163

Purge Method: Bailer / Disposable Bailer X / Middleburg / Electric Submersible / Extraction Pump / Other: _____

Sampling Method: Bailer / Disposable Bailer ✓ / Extraction Port / Other: _____

1.8 (1 Case Volume (Gals.)) x 3 (Specified Volumes) = 5.3 (Calculated Volume) Gals.

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
1025	63.4	6.7	640	2	
1027	63.4	6.6	620	4	
1029	63.6	6.6	620	5.5	

Did well dewater? Yes (No)		Gallons actually evacuated: 5.5	
Sampling Time: 1035		Sampling Date: 3/31	
Sample I.D.: MW-1		Laboratory: (Sequoia) GTEL N. Creek Assoc. Labs	
Analyzed for: (TPH-G BTEX MTBE) TPH-D		Other:	
Duplicate I.D.:	Analyzed for: TPH-G BTEX MTBE TPH-D	Other:	
D.O. (if req'd):	Pre-purge:	mg/L	Post-purge: mg/L
O.R.P. (if req'd):	Pre-purge:	mV	Post-purge: mV

CHEVRON WELL MONITORING DATA SHEET

Project #: 970331-J1	Station #: 9-3864
Sampler: MJ	Date: 3/31/97
Well I.D.: MW-2	Well Diameter: (2) 3 4 6 8 ___
Total Well Depth: 29.60	Depth to Water: 11.88
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: (PVC) Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
2"	0.16	5"	1.02
3"	0.37	6"	1.47
4"	0.65	Other	radius² * 0.163

Purge Method: Bailer / Disposable Bailer X / Middleburg / Electric Submersible / Extraction Pump / Other: ___

Sampling Method: Bailer / Disposable Bailer X / Extraction Port / Other: ___

2.8 (1 Case Volume (Gals.)) x 3 (Specified Volumes) = 8.5 Gals. (Calculated Volume)

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
1042	61.6	6.6	410	3	
1046	61.6	6.5	400	6	
1050	61.8	6.6	400	8.5	

Did well dewater? Yes (No)		Gallons actually evacuated: 8.5	
Sampling Time: 1055		Sampling Date: 3/31	
Sample I.D.: MW-2		Laboratory: (Sequoia) GTEL N. Creek Assoc. Labs	
Analyzed for: (TPH-G BTEX MTBE) TPH-D		Other:	
Duplicate I.D.:	Analyzed for: TPH-G BTEX MTBE TPH-D	Other:	
D.O. (if req'd):	Pre-purge: ___ mg/L	Post-purge:	mg/L
O.R.P. (if req'd):	Pre-purge: ___ mV	Post-purge:	mV

CHEVRON WELL MONITORING DATA SHEET

Project #: 970331-J1	Station #: 9-3864
Sampler: MS	Date: 3/31/97
Well I.D.: MW-3	Well Diameter: (2) 3 4 6 8 ____
Total Well Depth: 76.88	Depth to Water: 15.44
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: (PVC) Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
2"	0.16	5"	1.02
3"	0.37	6"	1.47
4"	0.65	Other	radius² * 0.163

Purge Method: Bailer / Disposable Bailer ✗ / Middleburg / Electric Submersible / Extraction Pump / Other: _____

Sampling Method: Bailer / Disposable Bailer ✗ / Extraction Port / Other: _____

1.8 (1 Case Volume (Gals.)) X 3 (Specified Volumes) = 5.5 Gals. (Calculated Volume)

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
957	67.8	6.7	700	2	Odor
1000	68.2	6.6	650	4	
1004	68.0	6.6	650	5.5	

Did well dewater? Yes (No)		Gallons actually evacuated: 5.5	
Sampling Time: 1010		Sampling Date: 3/31	
Sample I.D.: MW-3		Laboratory: (Sequoia) GTEL N. Creek Assoc. Labs	
Analyzed for: (TPH-G BTEX MTBE) TPH-D	Other:		
Duplicate I.D.:	Analyzed for: TPH-G BTEX MTBE TPH-D	Other:	
D.O. (if req'd): Pre-purge:	mg/L	Post-purge:	mg/L
O.R.P. (if req'd): Pre-purge:	mV	Post-purge:	mV

-5

CHEVRON WELL MONITORING DATA SHEET

Project #: 970331-J1	Station #: 9-3864
Sampler: MS	Date: 3/31/97
Well I.D.: MW-5	Well Diameter: (2) 3 4 6 8 ____
Total Well Depth: 21.59	Depth to Water: 15.45
Depth to Free Product:	Thickness of Free Product (feet):
Referenced to: (PVC) Grade	D.O. Meter (if req'd): YSI HACH

Well Diameter	Multiplier	Well Diameter	Multiplier
2"	0.16	5"	1.02
3"	0.37	6"	1.47
4"	0.65	Other	radius² * 0.163

Purge Method: Bailer / Disposable Bailer X / Middleburg / Electric Submersible / Extraction Pump / Other: _____

Sampling Method: Bailer / Disposable Bailer X / Extraction Port / Other: _____

1.0 (1 Case Volume (Gals.)) x 3 (Specified Volumes) = 3.0 (Calculated Volume) Gals.

Time	Temp (°F)	pH	Cond.	Gals. Removed	Observations
930	69.2	6.9	430	1	
933	69.4	6.8	420	2	
936	70.0	6.7	410	3	

Did well dewater? Yes (No)		Gallons actually evacuated: 3	
Sampling Time: 940		Sampling Date: 3/31	
Sample I.D.: MW-5		Laboratory: (Sequoia) GTEL N. Creek Assoc. Labs	
Analyzed for: (TPH-G BTEX MTBE) TPH-D		Other:	
Duplicate I.D.:	Analyzed for: TPH-G BTEX MTBE TPH-D	Other:	
D.O. (if req'd):	Pre-purge:	mg/L	Post-purge: mg/L
O.R.P. (if req'd):	Pre-purge:	mV	Post-purge: mV
