

Detterman, Mark, Env. Health

From: Detterman, Mark, Env. Health
Sent: Monday, December 29, 2014 6:23 PM
To: 'Rachel Green'
Cc: Trisha Malone; Kyle Flory (kflory@pesenv.com); Robert S. Creps (RCreps@pesenv.com); Roe, Dilan, Env. Health
Subject: RE: 6701 Shellmound Street (Mike Roberts Color: RO548); Gantt Chart Response

Rachel,

Thanks for the Gantt Chart. We've had a chance to review it and there are a number of changes that appear warranted to reflect typical site progress and timeframes. I've used the various task names from the left side of the chart and have rearranged the order for some of them, have added task items, and, where noted, have changed the length of time that will be required to complete them. Hopefully this will sufficiently capture the site; however, some tasks can potentially be a tad shorter. Let's see where the time frame falls out and see if any time estimate modifications are required to reach your goal.

- 1 Prepare CSM
 - a. Prepare CSM
 - b. Client Review
 - c. CSM Revision
 - d. CSM to ACEH
 - e. ACEH Review
 - f. Final CSM
- 2 Soil Management Plan
 - a. Prepare SMP
 - b. Draft SMP to Client
 - c. SMP Revision
 - d. SMP to ACEH
 - e. ACEH Review
 - f. Final SMP
- 3 Land Use Covenant
 - a. Prepare LUC
 - b. Draft LUC to Client
 - c. LUC Revision
 - d. LUC to ACEH
 - e. ACEH Review
 - f. Final LUC
- 4 ACEH & PES Meeting
- 5 Closure Request
 - a. Prepare Closure Request
 - b. Closure Request to Client
 - c. Closure Request Revision
 - d. ACEH Review
- 6 Public Comment Period (new)
 - a. Notification Letter and Mailing – 7 days (new)
 - b. Public Comment Period – 30 days
 - c. Response to Comments (Contingency) – 14 days (new)
 - d. Notification to Proceed with Well Destruction – 5 days (new)
- 7 Well Destructions
- 8 Submit Well Destruction and Waste Disposal Report – 5 days (new)
 - a. ACEH Review – 5 days (new)
- 9 Case Closure – 5 days

Mark Detterman
Senior Hazardous Materials Specialist, PG, CEG
Alameda County Environmental Health
1131 Harbor Bay Parkway
Alameda, CA 94502
Direct: 510.567.6876
Fax: 510.337.9335
Email: mark.detterman@acgov.org

PDF copies of case files can be downloaded at:

<http://www.acgov.org/aceh/lop/ust.htm>


From: Rachel Green [<mailto:rgreen@anton.co>]
Sent: Friday, December 19, 2014 4:04 PM
To: Roe, Dilan, Env. Health; Detterman, Mark, Env. Health
Cc: Trisha Malone; Kyle Flory (kflory@pesenv.com); Robert S. Creps (RCreps@pesenv.com)
Subject: 6701 Shellmound Street


Mark,

Attached is our proposed project schedule for the 6701 Shellmound street soils management project. Additionally I received your request for funds and am processing those. We look forward to working with you in the New Year.


Thank you,

Rachel Green
Development Manager

 **Anton** DEVELOPMENT
COMPANY
1415 L Street, Suite 450
Sacramento, CA 95814
916-444-9887 Phone
www.anton.co

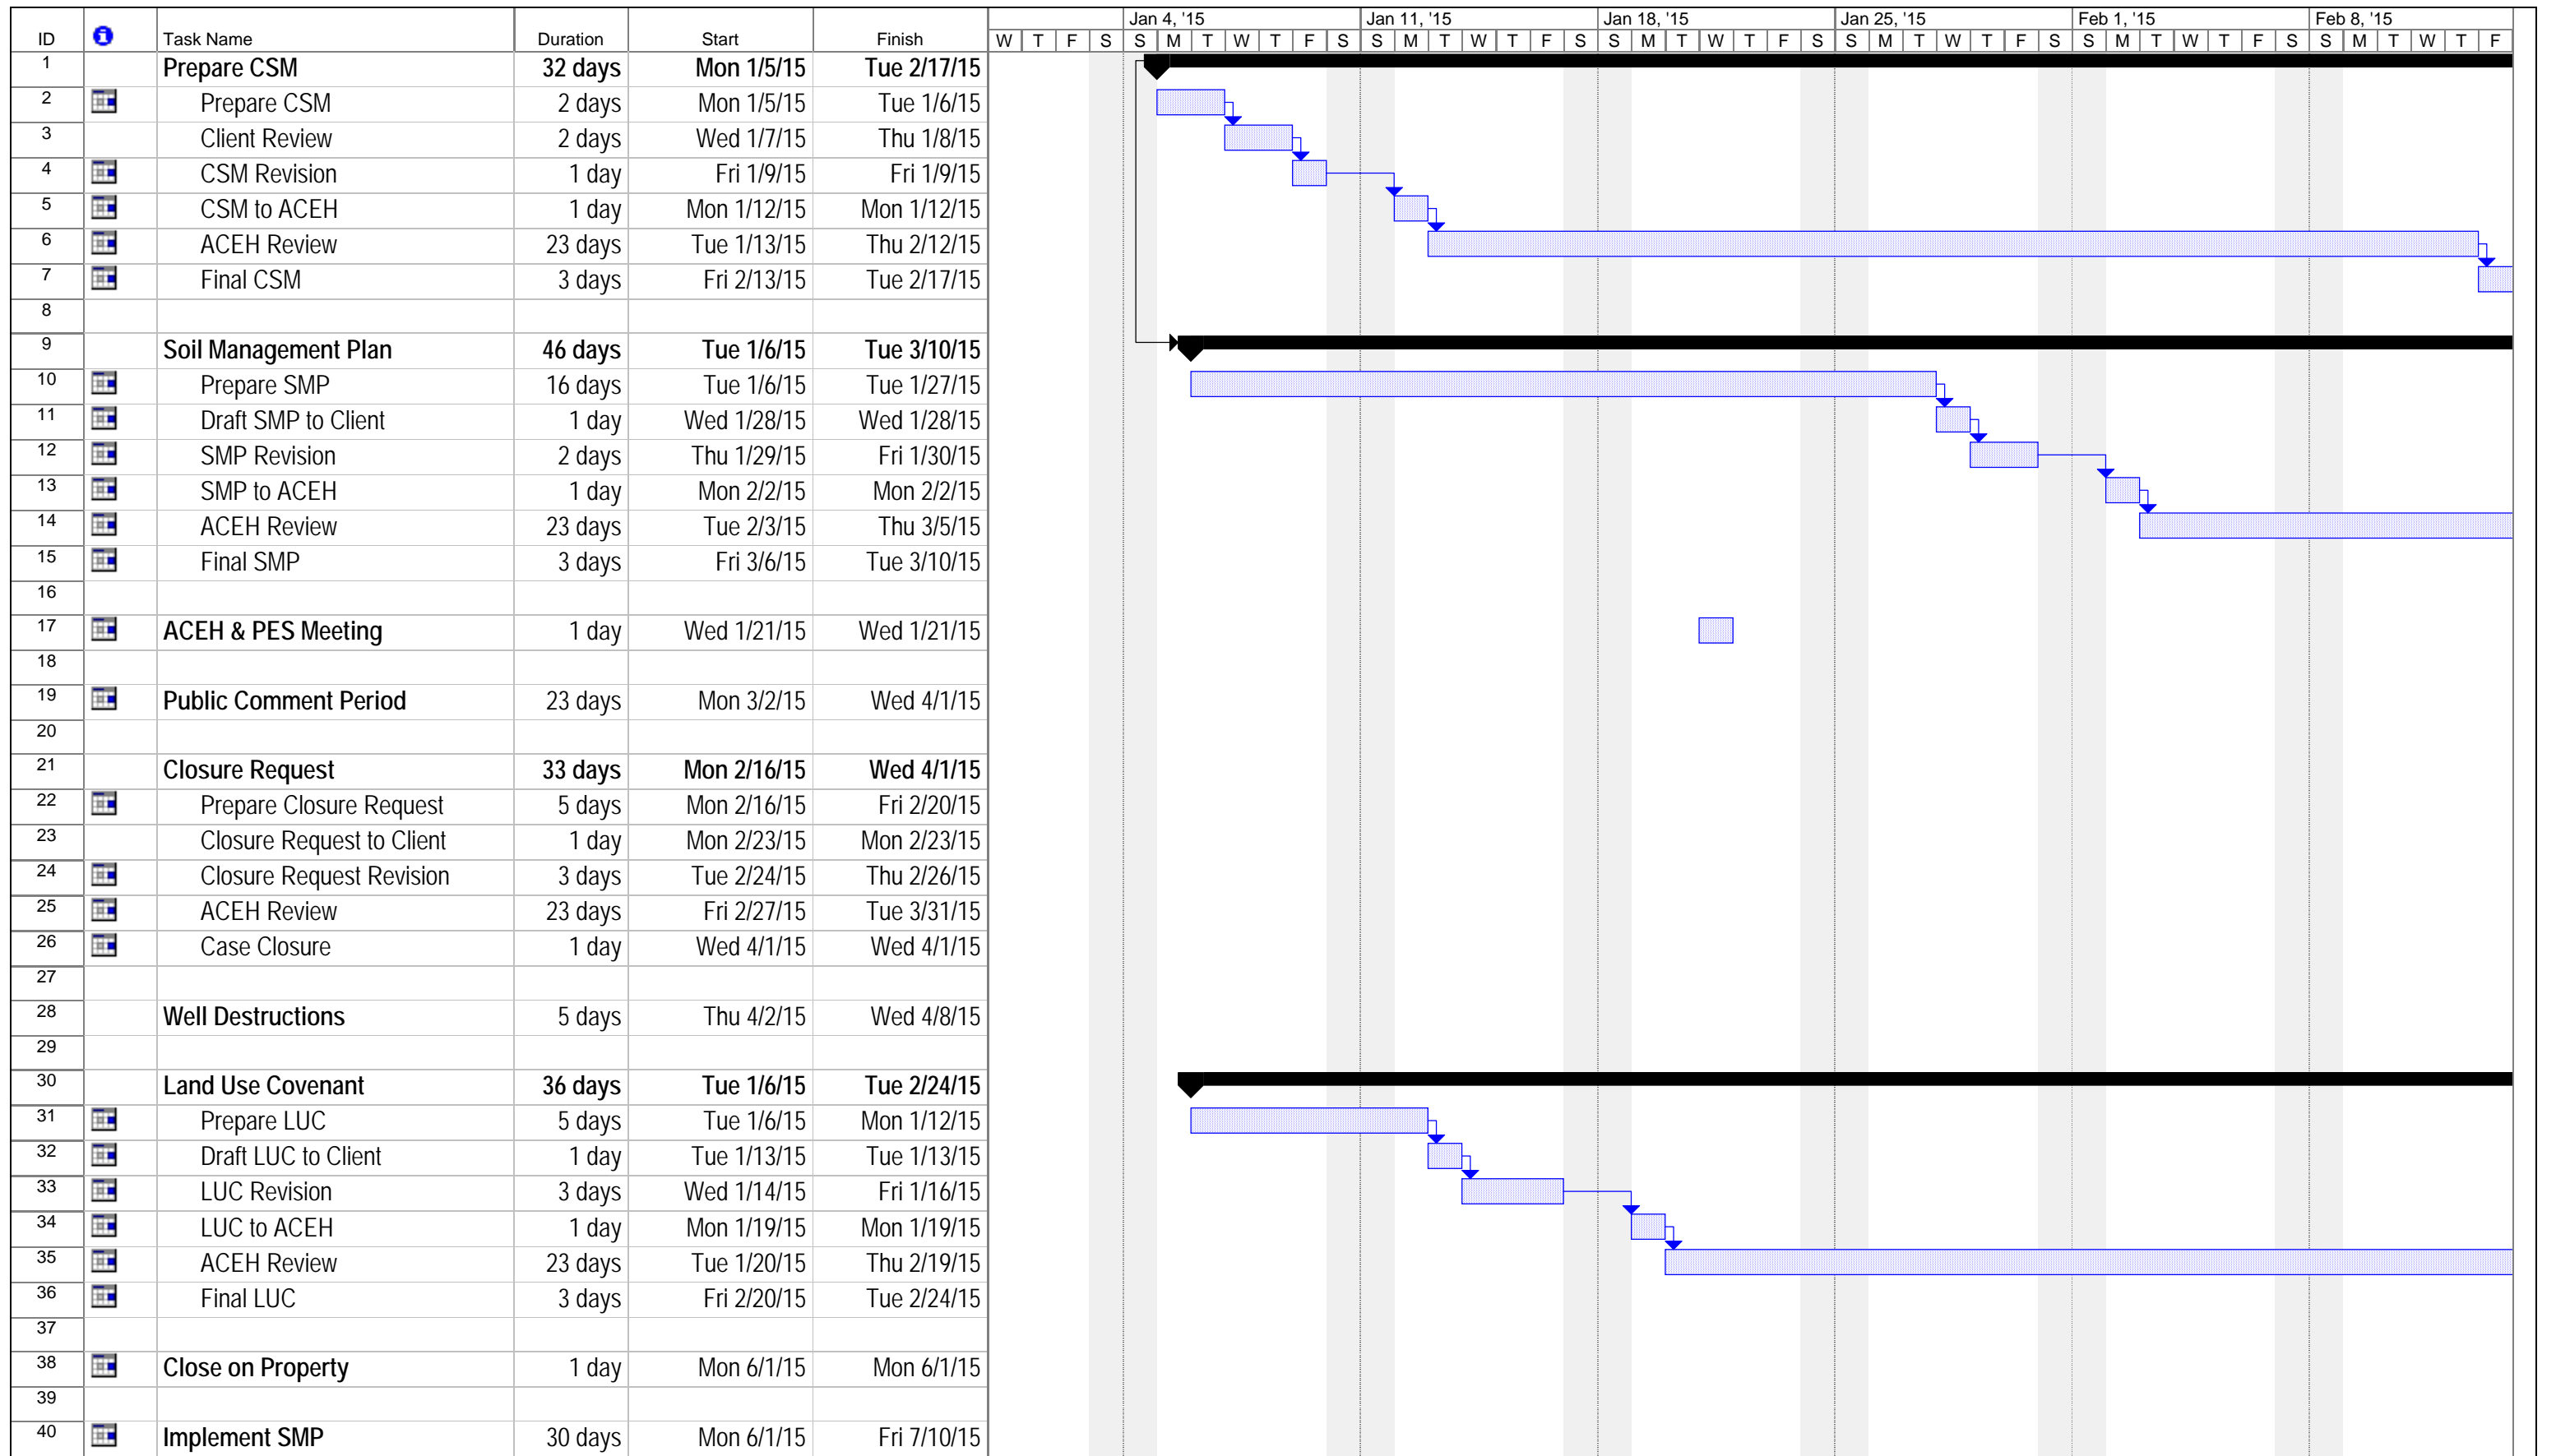

Project: Nady_Schedule_121914 Date: Fri 12/19/14	Task: [Blue box]	Progress: [Black bar]	Summary: [Black bar]	External Tasks: [Grey bar]	Deadline: [Green arrow]
	Split: [Dotted line]	Milestone: [Black diamond]	Project Summary: [Grey bar]	External Milestone: [Black diamond]	

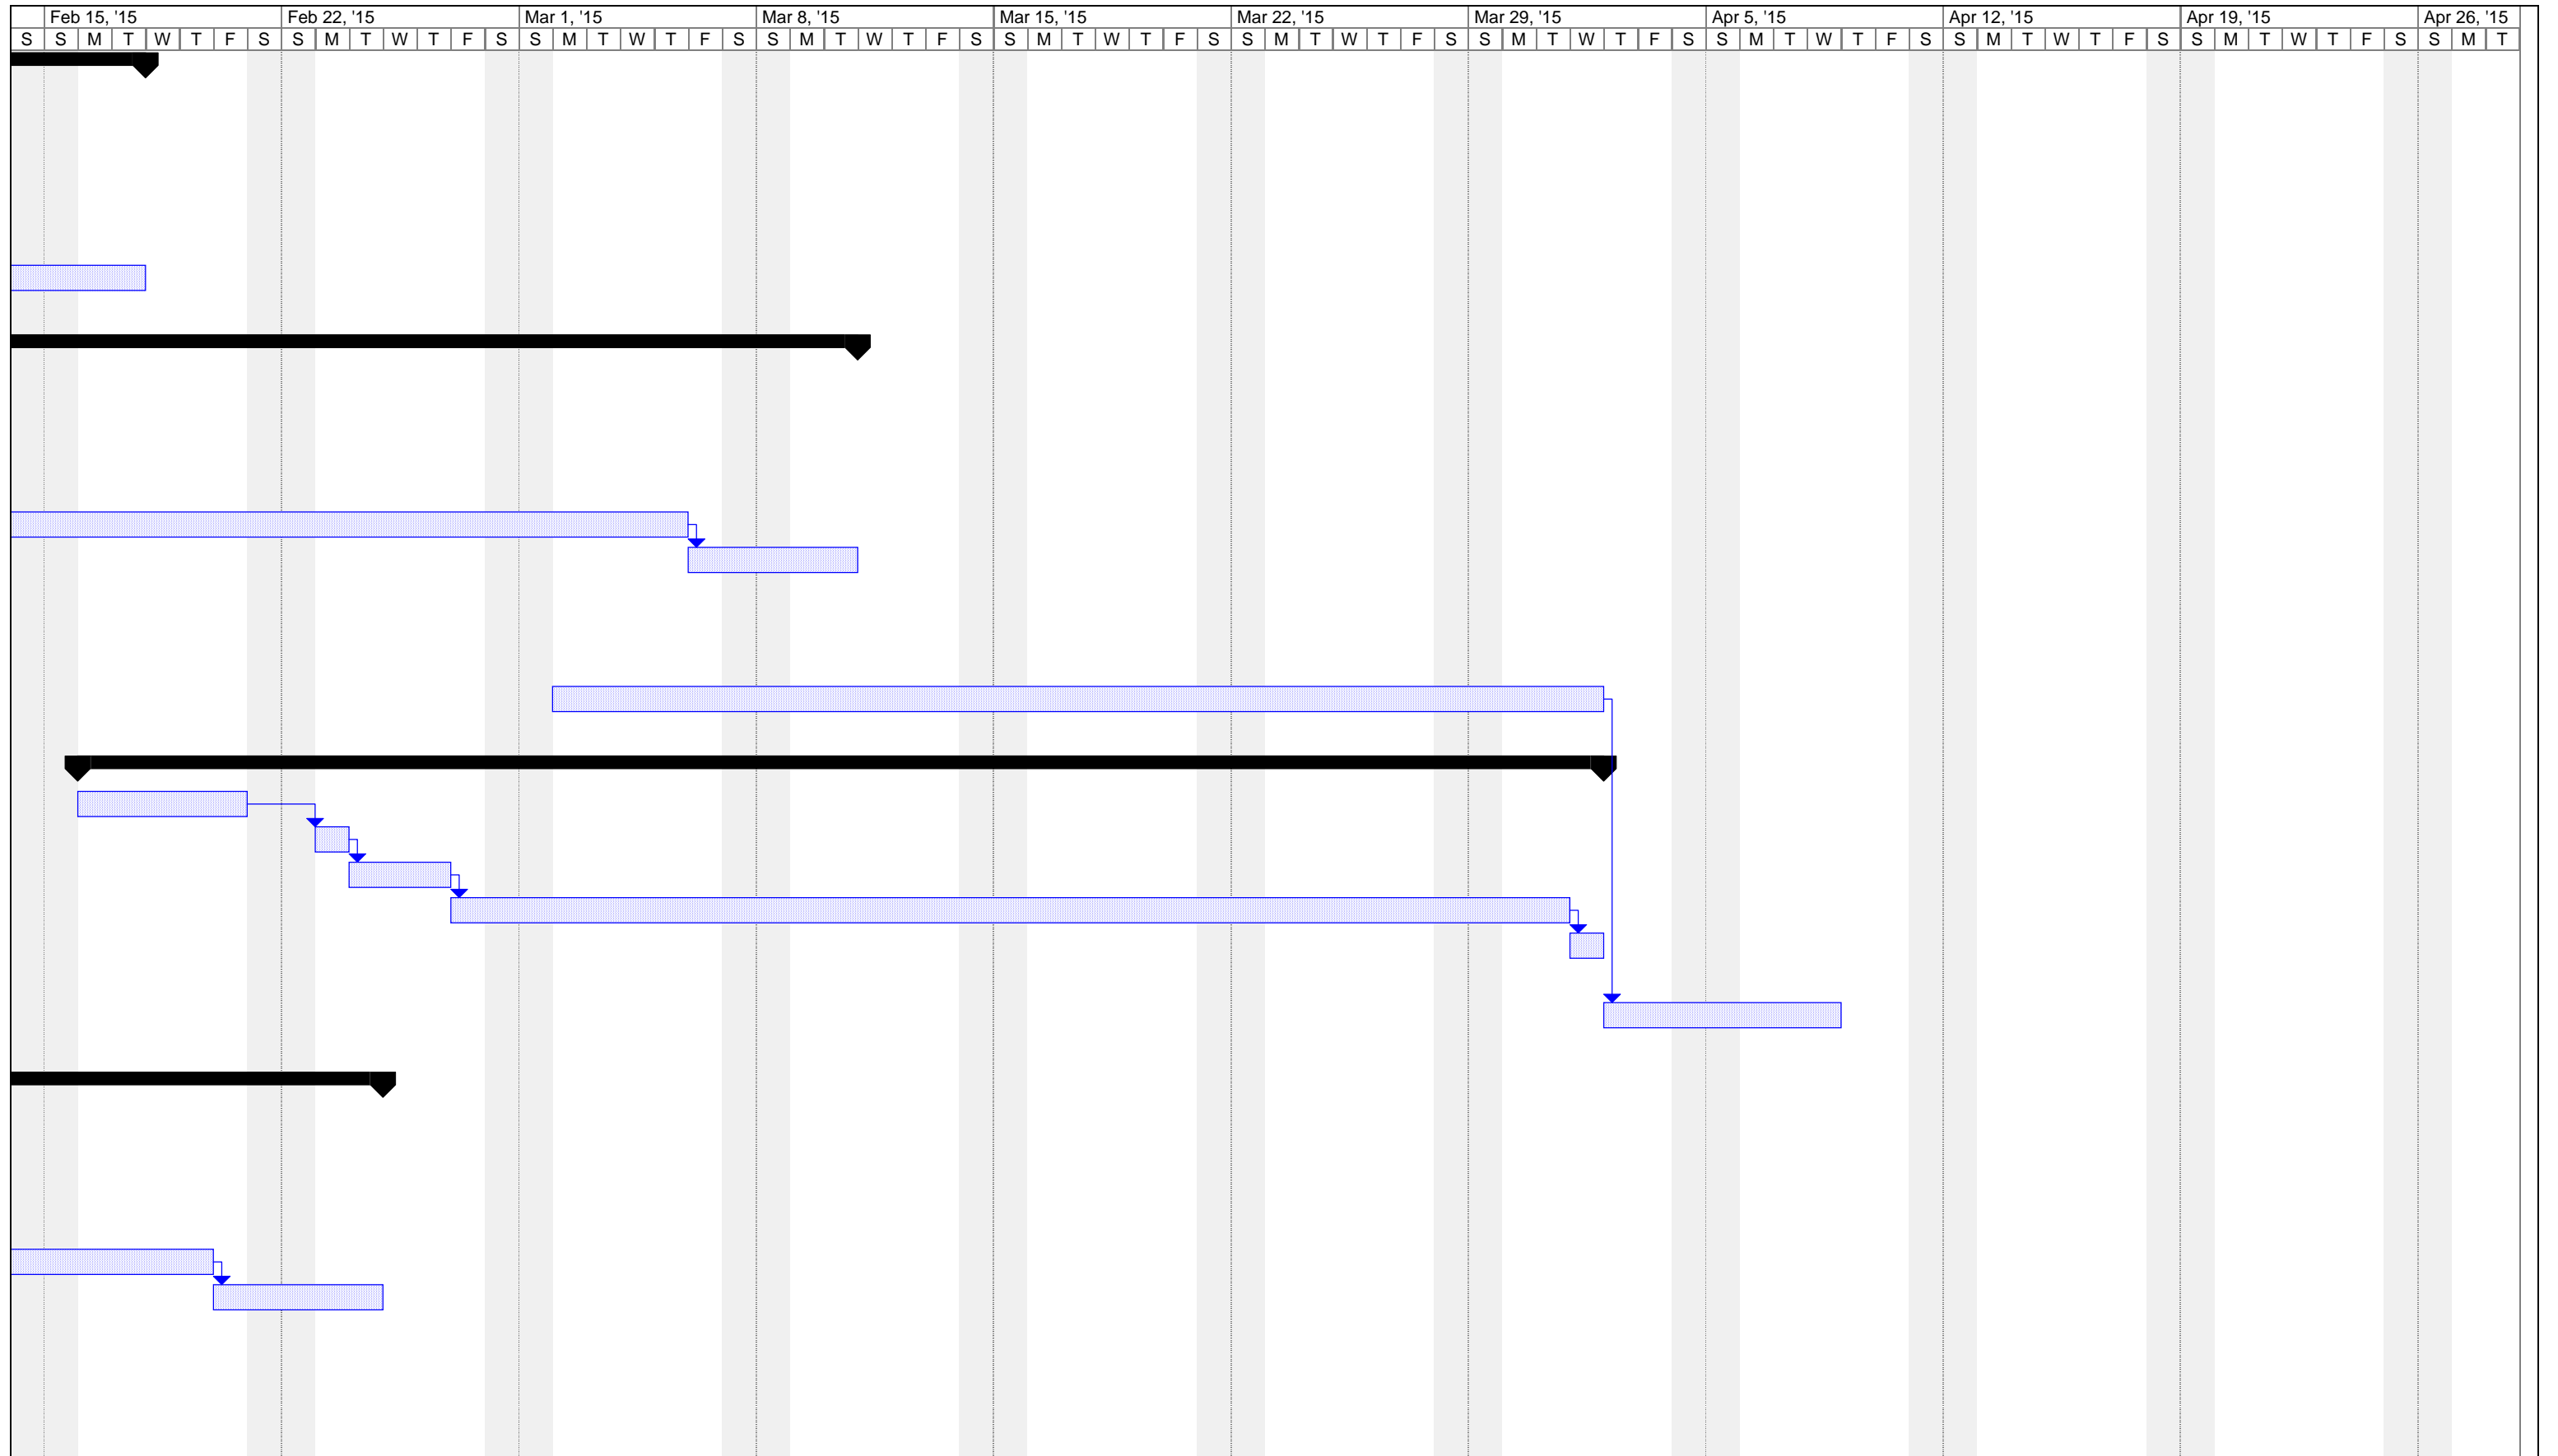









Project: Nady_Schedule_121914
 Date: Fri 12/19/14

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			



Project: Nady_Schedule_121914
 Date: Fri 12/19/14

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone	
